SAN FRANCISCO PUBLIC LIBRARY
3 1223 06446 5223

5/S

5/S

San Francisco Public Library

Government Information Center
San Francisco Public Library
100 Larkin Street, 5th Floor
San Francisco, CA 94102

REFERENCE BOOK

Not to be taken from the Library

Digitized by the Internet Archive
in 2015

https://archive.org/details/minutesofmeetin1999sanf_0

A8H-5066
5.93
4/99

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Location: 1680 Mission, 4th floor conference room

Date: Thursday, January 14, 1999 10am to 11:30am.

Subject: **Committee Meeting 407-** Coordination of Street Construction

Agenda

DOCUMENTS DEPT.
JAN 05 1999
SAN FRANCISCO
PUBLIC LIBRARY

1. **Introduction**	
2. **Approval of Minutes for November 11th Meeting**	enclosed is 12/10/98 Minutes
3. **Electronic Permitting Update**	Cynthia Chono
4. **Development of a Policy on Signing of Permit Application drawings by a Civil Engineer**	Vitaly Troyan
5. **Question and Answer about Implementation of the Revised Excavation Code and DPW Order**	Cynthia Chono
6. **February 17, 1999 Teleconference on "Pavement Excavation Damage"**	Vitaly Troyan
7. **Other New Business**	All

Next Meeting: 2nd Thursday of Each Month
Thursday February 11, 1999 at 10:00 A. M.
Conference Room
1680 Mission Street, 4th Floor

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American sign language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-8274, at leaStreet72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-8274.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 1680 Mission Street, the Fourth Floor Conference Room. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L on Mission Street; # 42 on Van Ness Avenue;
   #26 on Valencia Street; #71 on Noriega Street; #9 on Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

3 1223 06446 5223

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 406

Ms. Chono announced the next electronic permitting meeting at 1:30 pm, 12-17-98, at 30 Van Ness. She needs a contact for each participating organization and its password administrator.

Announcements for the Director's hearing on December 16 have been sent to the CULCOP distribution list.

The meeting consisted of Ms. Chono's discussion of the draft Regulations for Excavating and Restoring Streets in San Francisco.

The discussion followed through the comments Ms. Chono had received, as summarized in the handout. The comments had been of four types: typographical and grammatical errors, clarifications, objections, and suggested additions (such as a definitions page). Items requiring comment or explanation not given in the handout were:

Section 1.1: "Resurfacing" means repaving the whole street. It does not mean trench restoration or mitigation, unless the mitigation amounts to a new excavation.

Section 1.9: The intent of the State policy is still being clarified with the Board of Registration.

Section 1.11 D: Recent permit conditions for PG&E and SFWD work in the same part of California Street illustrate the kind of situation the 5 Year Plan requirement is intended to capture, and the special conditions to address. Ideally, complete and accurate 5 Year Plans would prompt coordination before the organizations applied for permits.

Section 1.12 B: The purpose of the tighter definition of start date and duration is to enable coordination with other work in the area. A last minute change in one agency's schedule can impact others. The plans are re-checked for permit renewals or changes to capture conflicts with other work, whether already scheduled or in applications filed after the original permit dates. Cases like Fillmore Street illustrate the need for this requirement, both for particular blocks and for the wider area.

Section 23: The focus of the 3' rule is structural integrity, not appearance. The aim is to minimize the number of discontinuities in the concrete base, whether at expansion joints or existing trench edges.

Section 9.2 A2: The diagrams give examples of the "best of 13'" principle: whichever edges give the cleanest final shape. If the 3' rule applies, it is counted as part of the 13'.

Comment 33: Our requirement intends the restoration to be to California PUC standard or better.

In answer to questions:

BSM is considering requirements for work mandated by the City, such as Rule 20 projects.

The City may consider requests to vary from the 72 hour backfill / restoration requirement on very large projects that include paving.

Does the Code require an excavation permit for X-1104 repairs? Yes. It includes any repair to the wearing surface, because of the coordination aspect. If another permit applies nearby, the two agencies could benefit by cooperating.

The City will devote January 1999 to education and facilitating adjustment. Full enforcement will begin in February.

The next meeting will be at 10:00 am Thursday, December 10, 1998, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, AIA, Director and City Architect

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

December 8, 1998

"Regulations for Excavating and Restoring Streets in San Francisco"
Summary of Comments

Comments were received from Pacific Gas & Electric Co., Pacific Bell, Television Signal Corporation, Department of Parking and Traffic, , San Francisco Municipal Railway, Department of Public Works Bureau of Street and Sewer Repair, Bureau of Engineering, and the Bureau of Construction Management. Comments fell roughly into four (4) general categories: 1) Punctuation and typos 2) Clarification questions 3) Objections and 4) Additions. The following summarizes comments received in categories 2, 3, and 4 and is organized according by Sections of the Order.

1. Section 1.1: Is an Excavation Permit required for:
    a. Installing bicycle racks?
    b. Potholing or patch paving?

    An Excavation Permit will not be required for the work stated above. These types of work would generally fall into work that will be completed within 24 hours. However, other types of permits such as a Special Traffic Permit or an encroachment may be required.

    c. Street resurfacing?

    The code (section 2.4.4 h) defines excavation as any work ***in the surface*** *or subsurface of the Public Right-of-Way. Based on this definition repaving or street resurfacing may be required to obtain excavation permits. This would be consistent with the spirit of the code to increase coordination of street excavation work.*

2. Section 1.3: All affected parties should be notified of an emergency excavation

    We will add "the excavator must notify all affected parties, including:
    The Department of Parking and Traffic at #_________
    The Police Department at #_________
    When MUNI service is affected contact MUNI at #__________.

3. Section 1.5 A 1 & 7: Will these sections apply for small contractors?

Yes, Section 2.4.2 of the Excavation Code authorizes DPW to issues excavation Permits "only if the Applicant has the legal authority to occupy and use the Public Right-of-Way for the purposes identified in the application".

The submittal of 5 year plans is required only of Utility and Municipal Excavators. The 5 year plans are required of major work anticipated to be done in the Public Right-of-Way.

4. Section 1.8 C: For Rule 20A project will the joint intent form meet this requirement?

Yes, the Joint Intent Form will meet this requirement.

5. Section 1.9: Do **all** permits need to be submitted with a plan or diagram?

Yes, please see the attached sketch. The plan must provide the location and size of the excavation. The plan does not need to be to scale.

6. Section 1.9: Do all plans need to be signed by a licensed civil engineer?

We will add, "when legally required". We are currently asking the Board of Registration for Professional Engineers and Land Surveyors for clarification on this issue.

7. Section 1.11 D: What type of special conditions can be imposed at our design stage?

The intent of a pre-permit meeting is to fine tune coordination. A permit may be conditioned to not start before a specific date and to be completed by a specific date. A special condition may also be required to coordinate with another specific project, such as agreement on schedules, distance to be maintained between the two project, if reasonable, determine if a single paving contractor can do work for both project

8. Section 1.12 B: If due to circumstances beyond our control such as a customer is not ready or inclement weather and construction does not begin within 30 days of the start date specified in the permit, the permit should NOT become void.

Section 2.4.20.2 of the Excavation Code specifically states that "Permit shall be void if the excavation has not begun within thirty (30) calendar days of the start date specified in the Permit."

If you are not able to start the project within the thirty (30) calendar days of the start date specified you should request an extension to the start date.

9. Section 1.13: How will the City Determine if a project is being prosecuted diligently?

Once a project begins work must continue on a daily basis, except for weekends, holidays, inclement weather or labor disputes.

10. Section 1.14 D: How will the administrative fee be determined if it is not $50?

Opps, this was an "typo". An extension to an approved permit will be treated as new permit. The extension request will be plan checked in the same manner as a new permit except that you will only be charged $25 to cover this additional plan checking costs.

11. Section 1.14 D: How much lead time is required for an extension request?

Requests for extensions need to be made prior to the permit expiring. If you need an extension to the duration time you should request an extension as soon as you know you will not be able to complete the project within the approved duration time. We recommend that you request an extension at least 5 working days before your permit expires.

12. Section 1.14 D: If an extension is not granted what will happen to the unfinished work?

The intent of this section is to inform the excavator that an extension is not automatically granted. Specific conditions will be considered and if an extension is granted special conditions may be imposed on the extension, such as prohibiting construction on specific dates that may conflict with community events or requiring scheduling coordination with another project.

13. Section 1.18 D5: If an 2 feet by 5 foot excavation is paved for the full width of the lane will the Street Damage Pavement Fee be waived?

No, to have the Street Damage Pavement Fee waived the asphalt wearing surface must be removed and replaced for a minimum of 50 feet in length and for the width of all affected lanes. See attached diagrams.

14. Section 4.1 A: Emergency excavations and excavation lasting between 2 to 14 days should be exempt from posting public notices.

This requirement can not be exempted. The Code (Section 2.4.50(a)) requires excavations exceeding 24 hours but lasting less than 14 calendar days to post notices at least 72 hours prior to the commencement of the excavation and for every 100 ' along any block where the excavation is to take place.

15. Will the "Tow Away No Parking Construction Zone" meet this excavation code requirement?

The excavation code requires the name, telephone number and address of the owner and permittee, a description of the excavation to be performed and the duration of the excavation.

If the information required can be placed on the "Tow Away No Parking Construction Zone" sign, then the "Tow Away No Parking Construction Zone" sign would also meet the public posting notification requirement for excavations lasting longer than 24 hour and less than 14 calendar days.

16. Section 4.1 B: If any affected blocks are on a designated bicycle route can notices also be mailed to the San Francisco Bicycle Advisory Committee and San Francisco Bicycle Coalition?

O.K. good idea, we will add this.

17. Section 4.1 B 2: Posting notices 10 day prior to construction every 100 feet for projects that will last longer than 15 calendar days and maintaining project signs is unnecessary.

The Excavation Code (Section 2.4.50(b)(ii)) requires the Permittee to post and maintain notice at the site of the excavation at least 10 calendar days prior to commencement of the excavation in the same manner and with the same information as required for posted notice pursuant to Subsection (a).

Section 2.4.50(b)(iii) of the Excavation Code requires posting ad maintaining Excavation project signs at the site of the excavation.

Perhaps "Tow Away No Parking Construction Zone" signs could be posted on the same barricade or parking meter as the Public Notice.

18. Section 5.5: The requirement of a locked container will take up additional space and dust control will provide adequate cover.

The Excavation Code, Section 2.4.53(c), allows fill material, sand, aggregate and asphalt-coated material to be stored at the site **only** if it is stored in covered locked containers. The concerns are not solely for dust control, but also for the safety of the general public.

We will propose that projects, where construction fences or barricading prohibit public access, materials may be stored if contained and covered.

19. Section 6.2 A: It will not be possible to meet this requirement if a single excavation is limited to 1,200 feet.

The Excavation Code, Section 2.4.52 (c) limits a single excavation site to 1,200 feet in length at any time except with the prior written approval of the Director.

If you wish an exception from this requirement, you must submit a written request specifying the exception you are requesting and explaining why an exception is needed. The Director will respond in writing.

20. Section 6.2 A 3 & 4: Areas were pavement has been removed or areas that have been saw cut should not be included in the 1,200 feet limitation.

O.K., we will also modify this section accordingly.

21. Section 6.3: When and excavation affect Transit Stops can specific language be included to require the excavator to restore the Stop?

O.K., we will modify this section accordingly.

22. Section 6.3: When and an excavation is in a designated BIKE LANE can specific language be included to require the excavator to restore the pavement the entire width f the bike lane?

O.K., we will modify this section accordingly.

23. Section 6.3 D: What is the definition of a concrete panel? Does the 4' rule still apply?

The intent of this section is to implement a "No New Joints" in concrete pavement. In San Francisco concrete streets are constructed with transverse joints placed every 15 feet on centers, for the full width of the pavement and at right angles to the centerline of the street.

If you excavate in one of these concrete sections (panel) you will have to remove the entire section from joint to joint. The old 4' rule is no longer applicable.

24. Section 6.4: Can the Director give annual permission for the use of specific boring methods?

The crowded underground conditions in some areas of the City and the various soils conditions does not make it possible to give general annual permission to use boring equipment. However, if you have a number of projects you wish to use specific equipment you can ask for to use the equipment for the various projects in one request prior to applying for an Excavation Permit.

25. Section 7.5 How is a curve for native soil established or do a compaction test?

There are established testing methods to establish the optimum moisture content and maximum density of a specific soil sample. We will include the ASTM standards. Soil compaction can be tested by various methods. The most common method is an in place density test by a nuclear gage. A certified material testing laboratory will provide you with more information.

If there is interest we will arrange for visit to DPW's Materials Testing Laboratory and a training class on soils and compaction.

26. Section 9.1 A & B: The 72 hour requirement to backfill, base and restore pavement is unnecessary. Temporary asphalt remains adequate for longer than 72 hours and we agree to inspect and maintain our excavations.

The Excavation Code, Section 2.4.55 (c) empowers the Director to grant modifications to the 72 hours requirements, upon written request from the Permittee.

If you wish to vary from the requirements, you must submit a written request specifying the modifications you are requesting and explaining why the modification is needed. The Director will respond in writing.

27. Section 9: Add a the restoration of traffic stripping and/or markings.

O.K., we will modify this section accordingly.

28. Section 9.2 A2: How will the 13 feet Rule be applied? Is there a defined distance between lateral trenches?

If lateral trenches are less than 50 feet apart you will be required to remove the and replace the asphalt wearing surface with the trench restoration to a maximum of 13 feet wide. See the attached diagrams.

29. Section 9.2 A3: The 3 feet Rule, does this mean removing both the concrete base and the asphalt wearing surface? Is this 3 feet included in the 13 feet Rule?

Yes, the requirement to remove and replace undamaged pavement of 3 feet or less from a joint (concrete curb, gutter, parking strip or other joint) includes the concrete base and the asphalt wearing surface. Yes, the footage that required to be restored under the 3 feet rule will be included in the maximum 13 feet. See attached drawings.

30. Section 9.2 A3: If a new trench is less than 3 feet away from an old trench, is the old trench line considered a joint and the pavement between the two trench have to be removed under the 3 feet Rule?

Yes, we consider the old trench to constitute a joint and would require the pavement between the new trench and old trench to be removed and replace in accordance with the 3 feet Rule.

General Comments

31. Add a definition Section

OK, we will add a section of definitions.

32. Add a section on notification process to notify owner of to repair trench detects.

33. Should a typical trench detail be included? The detail could indicate a minimum distance of the pipe or conduit from the top of the wearing surface to the top of the pipe and a minimum distance from other facilities.

Past practice we have asked for a minimum depth of 18 inches and a minimum of 12 inches from other facilities and consistent with California PUC Requirements and other legal requirements. We will look into adding a typical trench detail.

34. Plating requirements in the Order are consistent with requirements in DPTs "Blue Book".

Thanks, we will change the language in the Order to be consistent with DPT's "Blue Book".

If you have any comments or questions please call Cynthia Chono at 554-6196 or you may fax you comments to Cynthia at 554-5843.

35. Add a section on House keeping

Summary

- 50 feet rule (two cars length),
- The three feet rule, remove undamaged pavement (concrete base + asphalt wearing surface) for 3’ or less
- Old trench next to a new trench < 3’
- No new joint for concrete streets
- Street damage restoration fee waiver
- Multiple bellholes/potholes restoration
- T-trench for moratorium streets

Note: Drawings are not to scale.

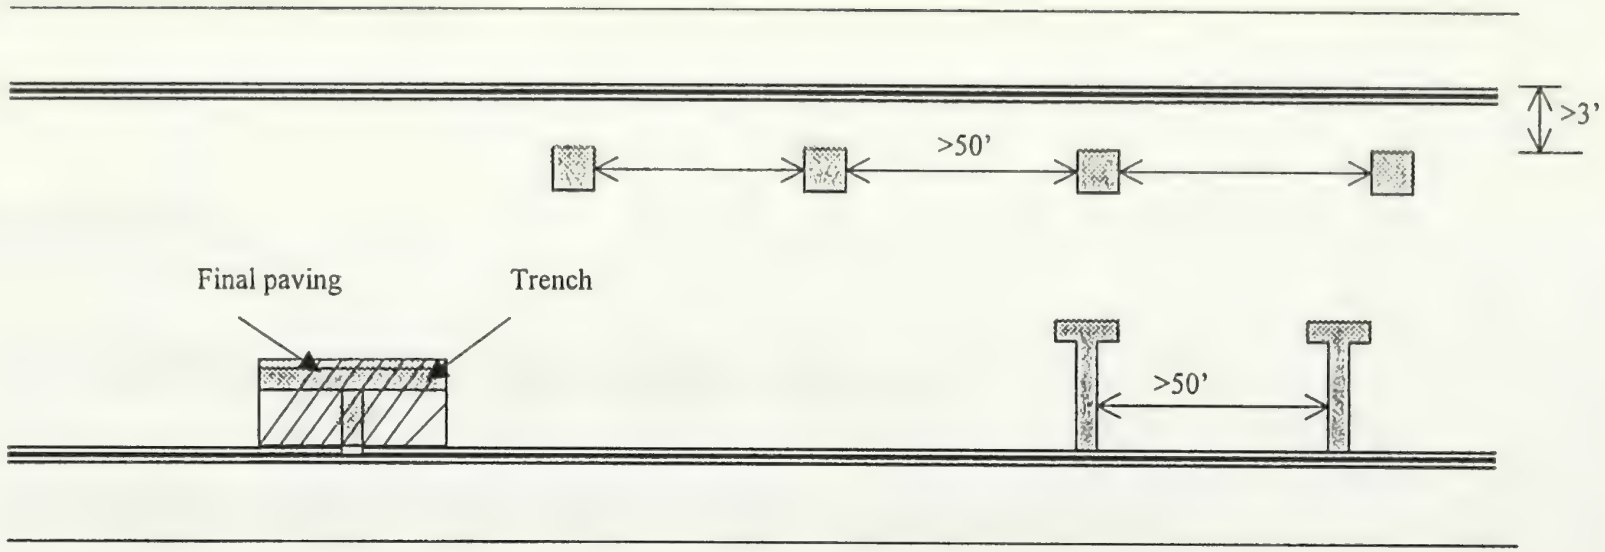
>3'
>50'
Final paving
Trench
>50'

Sample of new and old trench next each other and the three feet rule

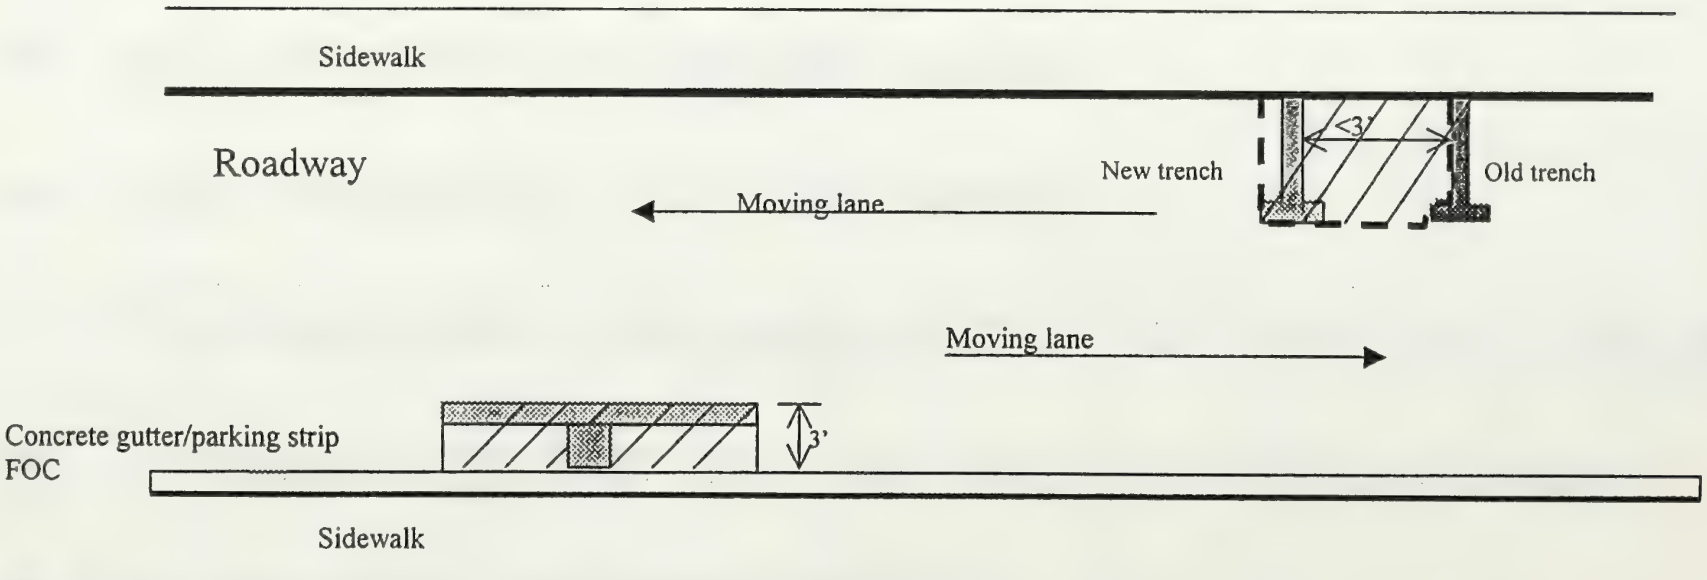
Sidewalk
Roadway
New trench
<3'
Old trench
Moving lane
Moving lane
Concrete gutter/parking strip
FOC
3'
Sidewalk

Three feet rule sample

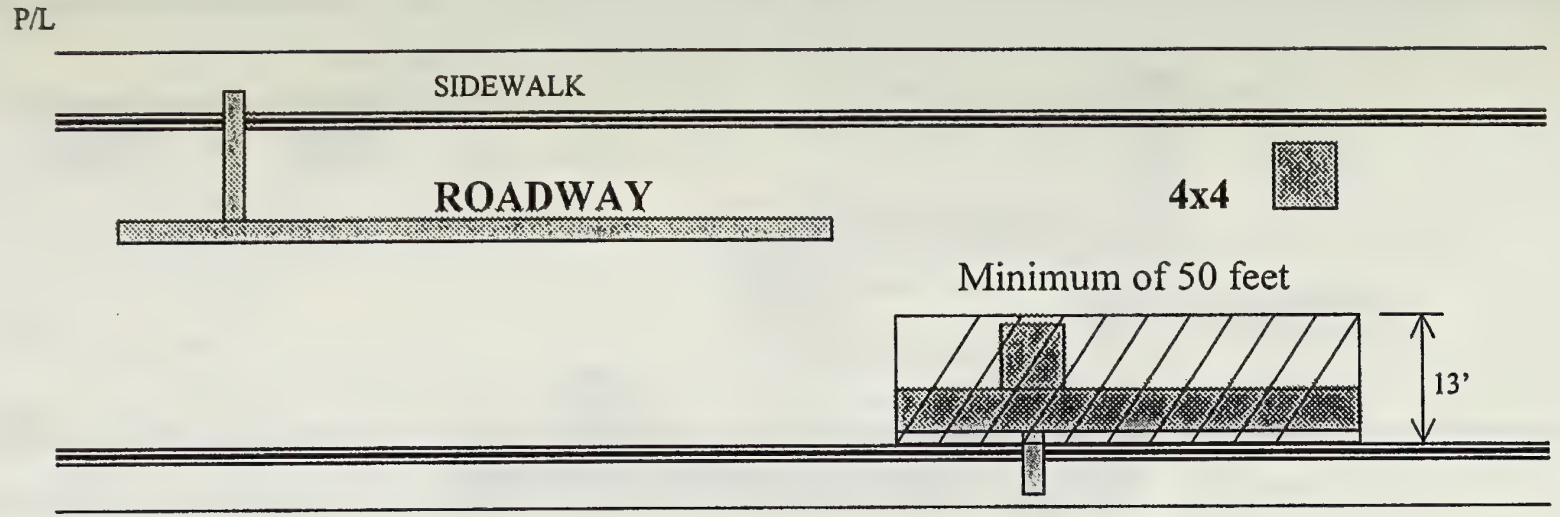
P/L
SIDEWALK
ROADWAY
4x4
Minimum of 50 feet
13’

DRAWINGS ARE NOT TO SCALE

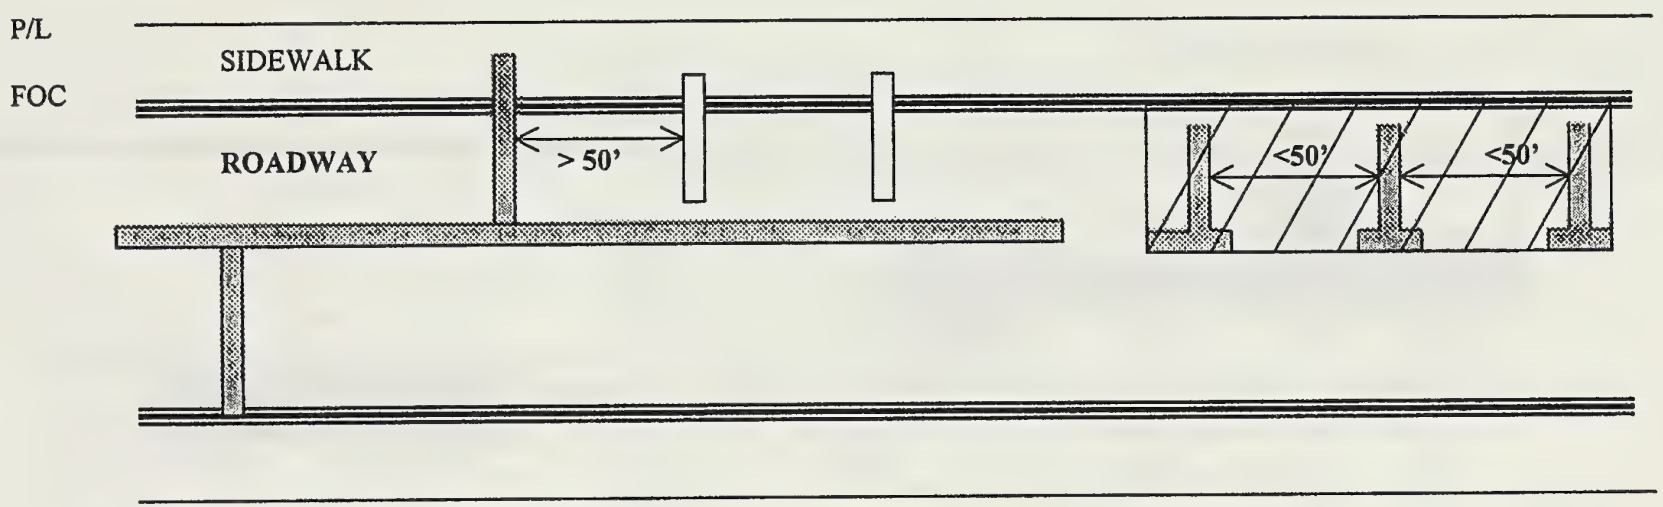
P/L
SIDEWALK
FOC
ROADWAY
> 50’
<50’
<50’

Minimum of 50 feet in length and all affected lanes must be paved in order to wave pavement damage restoration fee
At what point do they have to pave the entire trenches? at 50’ or less?

J:\BERHANE\temp now\Personal\Personal\Trench details.doc


Top ACWS
1 ½" Min. AC
Concrete base 6" MIN
1'
Moratorium Street
13'

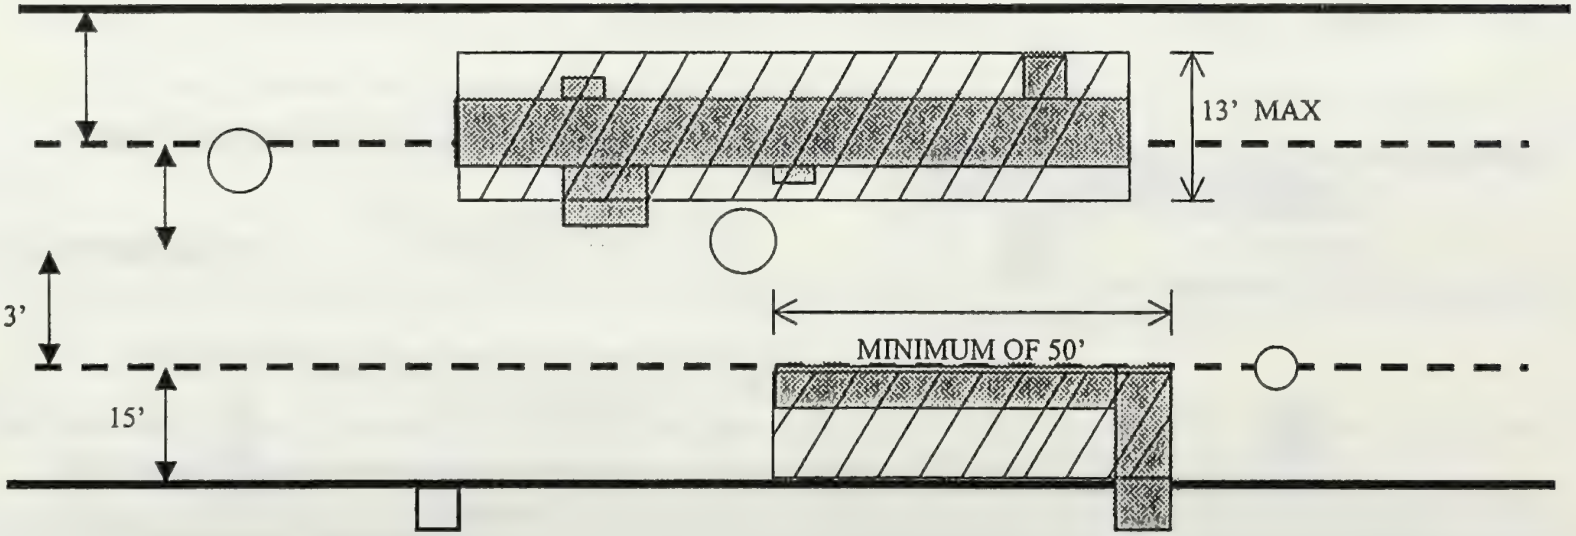
13' MAX
13'
MINIMUM OF 50'
15'


ACWS
Min. 1 ½" AC
Concrete base Min. 6"
1'


Moratorium Street
13'

Street shall be restored by "T-Section" by removing an additional one (1) foot of concrete base beyond the excavation.


SREET SURFACE
THIS AREA MUST BE CLEAR OF AWSS
New Trench

MUST BE CLEAR 45-DEGREE OFF AWSS FACILITIES

AWSS ATTACHEMENT

J:\BERHANE\temp now\Personal\Personal\Trench details.doc

Pre-construction meeting with Utility Inspection section is required.
Call 554-5863 UTILITY INSPECTION, five business days before start of work.

No Permit!

No Work!

Permit must be obtained before working in public right-of-way
Working with an expired permit is unacceptable
Night Noise Permit must be obtained for work between 7 Pm to 7 AM

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, AIA, Director and City Architect

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

December 9, 1998

ELECTRONIC PERMITTING UPDATE

Dear Applicant:

The time for the implementation of our electronic permitting program is rapidly approaching. We are anticipating your cooperation in getting the program up and running.

Over the course of the next few weeks informational meetings and training sessions are going to be provided for the people designated by your companies and organizations.

A meeting for users of the system will be held **December 17, 1998 from 1:30-3:00 PM. The meeting will be held at 30 Van Ness Avenue, 4th Floor Conference Room, Suite 4400**, San Francisco. At this meeting we will review the new Excavation Code and its impact on the application process. A demonstration of the new **ON LINE** application for permitting will be presented.

Four (4) training sessions will be held on December 21, 1998 and January 6, 1999. Times are available for both AM and PM sessions both days. Training will be held at **CIBER TRAINING**, 74 New Montgomery Street, Suite 780, San Francisco. To enroll please call Sean Brady @ (415) 554-5804. Please be prepared to be flexible on the limited slots that are available.

In order for you to participate by the proposed time the following requirements are necessary.

1. Computer Hardware and Software:
    - A. Microsoft Internet Explorer 4.0.
    - B. Pentium P.C.
    - C. Internet Connection-33K bps minimum modem speed.
2. Administration and Personnel:
    - A. A list of employees plus their functions and phone numbers who will need access to the permitting system.
    - B. Name of one person who will manage the users.
        1. Add users.
        2. Delete Users.
        3. Administer passwords of users for the company.

We here at BSM and some of the people from your companies and organizations who have been introduced to the system have all been impressed by the ease of use of this system. We look forward to introducing you to the system and anticipate a launch date of January 4, 1999.

If you have any question please give me a call at #554-6196 or Jeff Tilton at #554-5816.

Sincerely,

Cynthia N. Chono
Inspection Services Manager

City and County of San Francisco

DEC 0 9 1998

Department of Public Work
Bureau of Street-Use and Mappin

APPLICATION / PERMIT FOR UTILITY EXCAVATION

Permit No.: P98-20338
Date: DEC 0 9 1998
USA No.:

COMPANY NAME: San Francisco Water Department

ADDRESS: 1990 Newcomb Avenue, San Francisco, CA 94124

We hereby petition the Department of Public Works for permission to excavate the following named street(s) in compliance with the rules and regulations as set forth in Article 8 of the Department of Public Works Code, for the purpose of:
Installing water services 2-1" SERVICE

50[illegible]

The permittee by acceptance of this permit also agrees to the conditions as stated on the reverse side of this permit.

No. of Permits (Blocks): 1 x $50 = 50
Total Sq. Ft. of Trench: 17 x $0.80 = 13.6
Total Cost of Permit: $ 63.60

By (Rep. Name): Arleen Chan
Phone: (415) 550-4931
Construction- Begin: 12-21-98 End: 5-21-99

JOB LOCATION: 2955 -2957 JACKSON ST.

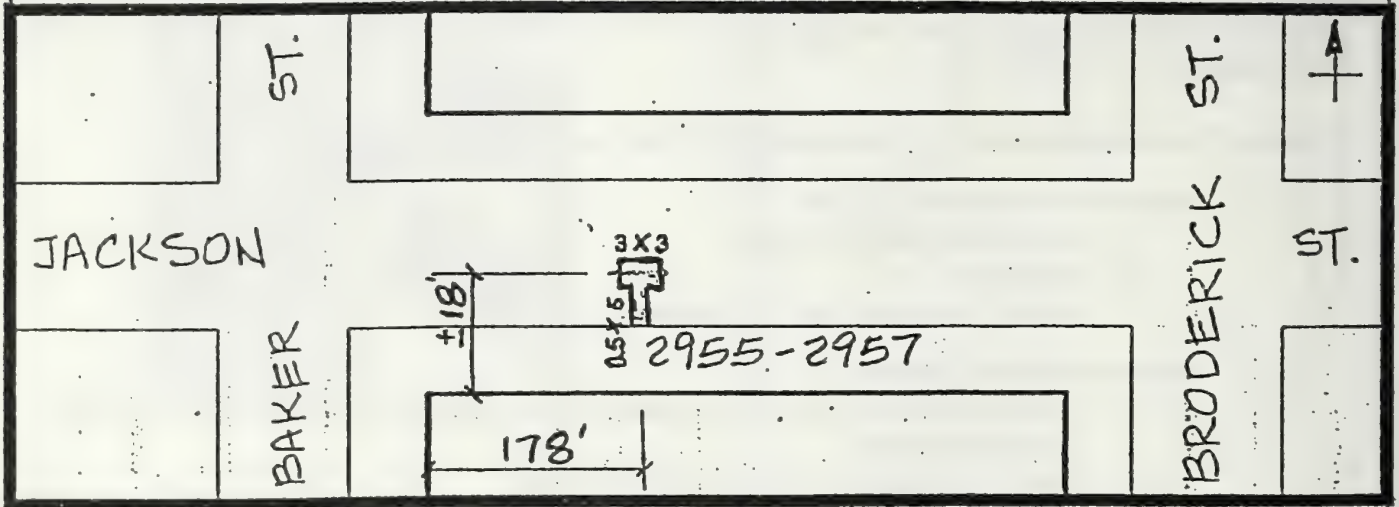

- ☐ Main
- ☑ New Construction
- ☐ Leak Repair
- ☑ Service
- ☐ Reconstruction
- ☐ Duct Repair
- ☐ Other

	Yes
Moratorium Street	☐
Rockwheel Use	☐

Resurfacing Date :
CCSF Job # :

Yes	
☐	Sidewalk Work Only
☐	AWSS
☐	FAU Street
☐	Traffic Var./Restriction
☐	Sawcut & Tee Patch Req.
☐	Night Noise Permit Req.

21

NOTICE :
This permit is in conflict with PG&E permit # P98-01389. Please contact Carlos Martinez @ 415-695-3536.

CCSF USE ONLY

SEE REGULATIONS FOR WORKING IN S.F. STREETS
4TH EDITION FOR TRAFFIC RESTRICTIONS
APPROVED
DEC 0 9 1998
DENISE M. BRADY
BUREAU CHIEF BSM
BY

Bureau of Street-Use and Mapp

APPLICATION / PERMIT FOR UTILITY EXCAVATION

Permit No.: P98 - 10390
Date: 11/27/98
USA No.: 1-800-642-2444

COMPANY NAME: PACIFIC BELL

[JOB NO: R2-8235R]

ADDRESS: 666 FOLSOM STREET - ROOM 1121A - SAN FRANCISCO, CA. 94107

We hereby petition the Department of Public Works for permission to excavate the following named street(s) in compliance with the rules and regulations as set forth in Article 8 of the Department of Public Works Code, for the purpose of: PLACING 9 FT. OF 2" CONDUIT FROM SB 9428 WEST ALONG JACKSON ST.

The permittee by acceptance of this permit also agrees to the conditions as stated on the reverse side of this permit.

No. of Permits (Blocks): 1 x $50 = 50.00	By (Rep. Name): WAI-LAN WOO
Total Sq. Ft. of Trench: 109 x $0.80 = 7.20	Phone: 542-8104
Total Cost of Permit: $ 57.20	Construction- Begin: 4/5/99 End: 4/20/99

JOB LOCATION: 3161 JACKSON   CODE 4C   GEO R2 CO 07

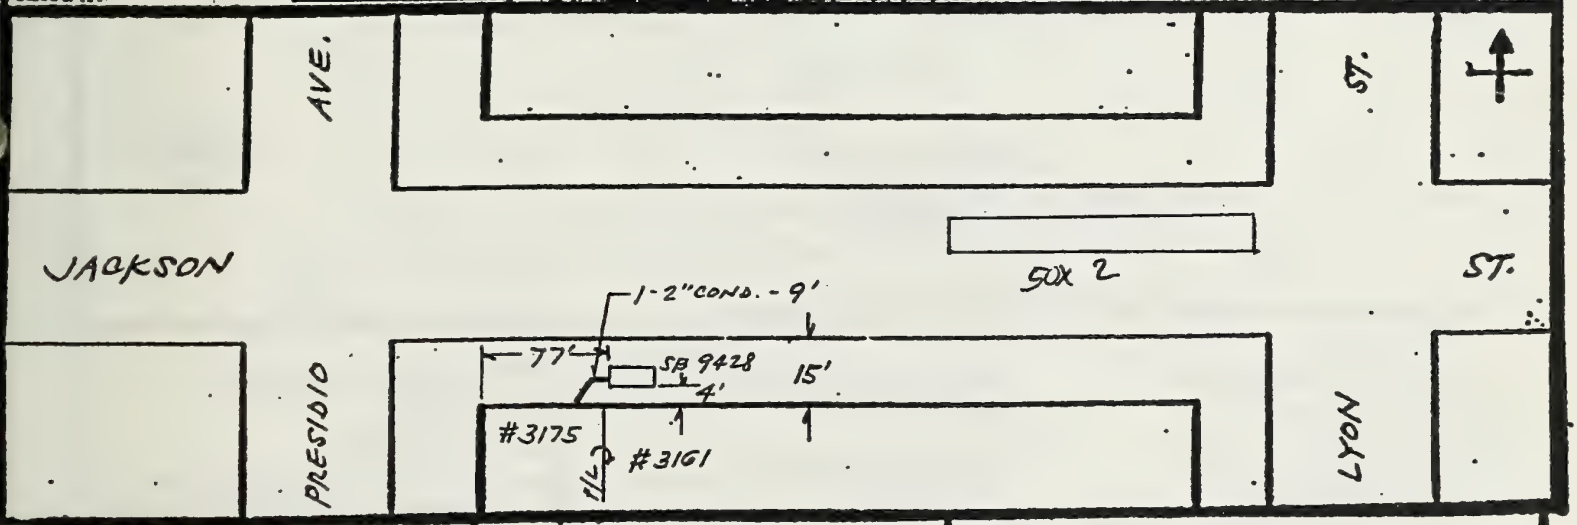

- ☐ Main
- ■ New Construction
- ☐ Leak Repair
- ☐ Service
- ☐ Reconstruction
- ☐ Duct Repair
- ☐ Other

Yes
- Moratorium Street ☐
- Rockwheel Use ☐
- Resurfacing Date: ______
- CCSF Job #: ______

Yes
- ■ Sidewalk Work Only
- ☐ AWSS
- ☐ FAU Street
- ☐ Traffic Var./Restriction
- ☐ Sawcut & Tee Patch Req.
- ☐ Night Noise Permit Req.

CCSF USE ONLY

SEE REGULATIONS FOR WORKING IN S.F. STREETS
4TH EDITION FOR TRAFFIC RESTRICTIONS
APPROVED
DEC 07 1998
DENISE M. BRADY
BUREAU CHIEF BSM
BY

RECEIVED
DEC 07 1998

City and County of San Francisco

RECEIVED
DEC 0 8 1998

PLS. XPD

Department of Public Works
Bureau of Street-Use and Mapping

APPLICATION / PERMIT FOR UTILITY EXCAVATION

Permit No.: P9802141
Date: 12/7/98
USA No.:
Job No.: 30046492

COMPANY NAME: PACIFIC GAS & ELECTRIC COMPANY
ADDRESS: 2180 HARRISON STREET, SAN FRANCISCO, CA. 94110

We hereby petition the Department of Public Works for permission to excavate the following named street(s) in compliance with the rules and regulations as set forth in Article 8 of the Department of Public Works Code, for the purpose of:

INSTALL NEW GAS SERVICE DUE TO NEW BUSINESS REQUEST: 114 DIAMOND ST.

The permittee by acceptance of this permit also agrees to the conditions as stated on the reverse side of this permit.

No. of Permits (Blocks): 1 x $50.00 = $ 50.00	By: DOUG CHANG	Rep:
Total Sq. Ft. of Trench: 56' x $0.80 = $ 44.80	Phone: 695-3679	Dept: GAS ENGINEERING
Total Cost of Permit: $ 94.80	Construction- Begin: 12/04/98	End: 01/30/99

JOB LOCATION: 114 DIAMOND ST. 180' S/S/L 18TH ST.



☐ Main
☒ New Construction
☐ Leak Repair
☒ Service
☐ Reconstruction
☐ Duct Repair
☐ Other

Moratorium Street Yes ☐
Rockwheel Use ☐
Resurfacing Date:
CCSF Job #:

Yes
☐ Sidewalk Work Only
☒ AWSS
☐ FAU Street
☐ Traffic Var./Restriction
☐ Sawcut & Tee Patch Required
☐ Night Noise Permit Required

PG&E ACCOUNTING INFORMATION: KEYPUNCH FORMAT 925 LEVEL 1

ELEM.	STANDING ORDER NO.	SIR	FAC.		ACCOUNT	SUB-ACCOUNT	PCC	AMOUNT
1-3	20 - 27	31	32 - 37		38 - 41	42 - 45	50 - 54	60 - 70
127	1006524		02				10984	$94.80

CCSF USE ONLY

AWSS/CISTERN PRESENT
SEE ATTACHED AWSS
REQUIREMENTS

This permit is in conflict with PG&E permit # P98-00828.

SEE REGULATIONS FOR WORKING IN S.F. STREETS
4TH EDITION FOR TRAFFIC RESTRICTIONS
APPROVED
DEC 0 9 1998
DENISE M. BRADY
BUREAU CHIEF BSM
BY

1999 One-Call Systems and Damage Prevention Symposium

April 25-28, 1999
Atlanta, Georgia

For information, contact the Meetings Department at (816) 472-6100, ext. 3520.

Link up with APWA for a valuable educational experience!

Deadline for downlink registration is January 25, 1999.

This Satellite Videoconference will be available on C-BAND.

Questions? Contact the Education Department at (816) 472-6100, ext. 3511 or via email at education@apwa.net.

www.apwa.net

www.agc.org

The Associated General Contractors of America also have resources available on excavation damage prevention, safety and risk allocation. To order these three products or obtain a copy of their catalog, contact the AGC Publications Department at (202) 393-2040.

Survival in Excavation: Safe Working Around Existing Utilities – 20 Minute Video
Members: $105 • Nonmembers: $157.50 • AGC product # 3205

Enlightened Risk Allocation: The Twenty-first Century Owners Guide to Cost Effectiveness - Booklet
Members: $9 • Nonmembers: $13.50 • AGC product #3539

Managed Risk or Wild Gamble: Enlightened Risk Allocation – 18 Minute Video (accompanies booklet)
Members: $40 • Nonmembers: $60 • AGC product #3940

American Public Works Association
2345 Grand Blvd., Suite 500
Kansas City, MO 64108-2625

Non-Profit
Organization
U.S. Postage
PAID
Kansas City, M
Permit No. 69

Vitaly B. Troyan
Deputy Public Service Dir
City & County Of San Francisco CA
875 Stevenson St Ste 460
San Francisco CA 94103-0903

The American Public Works Association and the
Associated General Contractors of America proudly present

Preventing Excavation Damage: What You Can't See Can Hurt You

A Satellite Videoconference

February 17, 1999
10:30 a.m. - 3:00 p.m. CT



"Full participation in excavation damage prevention programs by all excavators and underground facility owners is essential to achieve optimum effectiveness of these systems."

- National Transportation Safety Board (NTSB)

What You Can't See Can Hurt You!

Excavation operations bring with them a variety of contractual and physical concerns, which range from possible "differing site conditions," to potential environmental risks or damages to hazardous materials accidents. Misinformation and miscalculations can lead to litigation, financial loss, property damage, injury or even death. This satellite videoconference will identify concepts, resources and technologies to assist you in implementing proper risk allocation and reduction procedures and protocols.

A number of significant factors have radically changed the scenario for the construction industry over the years. Society has become more urbanized and left in its wake an intricate web of sewers, cables of all descriptions, power and telephone wires, and water supply lines—all of which are often covered by concrete and asphalt. When something unexpected is unearthed, what is the main issue at stake? Who pays for removing the rock or concrete, filling in the sinkhole or providing for adequate bearing? What contractual clauses will provide a measure of fairness to owners and contractors alike? As abandoned gas stations and waste dumps become more common, hazardous materials issues are a major concern.

The result of all these factors is a tremendous increase in costs dealing with underground risks. The present financial burden of these concerns is massive, but it has the potential of affecting future generations as well. To meet the challenge of such far-reaching proportions, a cooperative approach is required to adequately address the issues of proper risk allocation. It is the owners, contractors and design professionals, along with utility owners and operators who must find a way to work together to eliminate as many of the risks and hazards as possible.

This satellite videoconference brings together representatives of all those stakeholder groups to discuss the issues and allows you to ask them questions. It could well be the best investment you'll make in 1999!

Who Should Attend:

- Public Works Directors
- One-Call center personnel
- Construction Inspectors
- Local Officials
- Engineers - city, consulting, geo-technical and safety
- Senior level management personnel
- Contractors
- Construction crews
- Suppliers of construction materials

Attendees of this Satellite Videoconference will:

- Realize the benefits of a One-Call center and its importance for communities
- Gain a better understanding of the collection of subsurface utility data by utilizing standard guidelines and Subsurface Utility Engineering (SUE)
- Discover how proper utility coordination and notification can simplify the damage excavation process
- Learn how trenchless technology affects risk allocation
- Be able to identify the key elements necessary for an effective excavation damage prevention program

Program Agenda

Following each session, time has been allotted for questions from the viewing audience.

Introduction of Program and Speakers

Robert A. Martin, Esq., APWA/AGC Joint Committee, FH Martin Construction, Eastpointe, MI

Risk Allocation, One-Call Operations and Public Safety Panel Discussion

Robert A. Martin, Esq., APWA/AGC Joint Committee, FH Martin Construction, Eastpointe, MI • James Anspach, So Deep, Inc., Manassas Park, VA • Mark McAlpine, Esq., McAlpine and McAlpine, Bloomfield Hills, MI • Bob Rast, Rast Construction Company, Birmingham, AL • Jack D. Messer, Director of Utilities, City of Manhattan, Manhattan, KS • Kristine Young, President, Miller the Driller, Des Moines, IA • Donald R. Evans, APWA/OCSI Committee Chair, Operations Manager, Underground Service Alert/SC, Brea, CA • Thomas V. Jackson, Staff Engineer, Georgia Power, Atlanta, GA

Are owners, contractors and design professionals on the same page with respect to the issues involved and the project solutions to risk allocation? How effective are existing One-Call centers? What problems exist in these systems? How do parties address the problems of catastrophic loss and deal with overall responsibilities to the public? This session will provide answers to these questions as well as general information on risk allocation issues, one-call operations and general safety concerns and responsibilities for existing underground utilities.

The Collection of Subsurface Utility Data -
Utilizing Standard Guidelines and Subsurface Utility Engineering (SUE)

James Anspach, So Deep, Inc., Manassas Park, VA • Bob Rast, Rast Construction Company, Birmingham, AL

The first part of this presentation will focus on new national consensus standards, Standard Guidelines for the Collection and Depiction of Existing Subsurface Utility Data, being developed by the American Society of Civil Engineers (ASCE) for collection of existing subsurface utility data. These standards will better define the allocations of risk among engineers, contractors, and project owners for existing underground utility data. Although these standards are not yet in place, the concepts, definitions and use are already practiced in many sectors of construction. Learn how this standard will assist with classifying the quality of existing subsurface utility data.

The second half of this presentation will focus on the new emerging technology, Subsurface Utility Engineering (SUE). SUE combines the traditional disciplines of geophysics, surveying and civil engineering to provide data on existing utilities and other manmade subsurface structures at appropriate times in the design process. Through the use of this process, the owner and design professional are able to select appropriate design data to avoid many of the problems involved in underground construction operations. Through the usage of SUE it is anticipated that utility conflicts, construction delays, contractor claims, utility relocations, project redesigns and the time required to design project will greatly be reduced. Even more impressive, SUE can lead to better bid prices and a safer more economical excavation project.

This session will also address the relationship of utilizing standard guidelines and subsurface utility engineering in an overall damage prevention program.

Lunch Break (30 minutes)

Damage Prevention through the One-Call Function -
Utility Notification and Coordination

Donald R. Evans, APWA/OCSI Committee Chair, Operations Manager, Underground Service Alert/SC, Brea, CA • Thomas V. Jackson, Staff Engineer, Georgia Power, Atlanta, GA

Why is it necessary to notify utility companies? Why must notifying others be coordinated? This presentation will address the significance of One-Call centers and the importance of notifying owner/operators of underground line systems. By utilizing One-Call centers, a communication link is established between utility operators, contractors and the general public, providing utility companies sufficient time to locate and mark their facilities. In doing so, time and money are saved. Notification and coordination of efforts prevent excavation damage and reduce the potential loss of public services, and the need for expensive excavation equipment. Most importantly, however, threatening injuries and the loss of human life are drastically reduced.

Trenchless Technology and Its Effect on Risk Allocation

Kristine Young, President, Miller the Driller, Des Moines, IA

Trenchless technology has definitely had an impact on risk allocation. Through new cutting-edge technologies, underground installations are being made in more places than ever. It is predicted that the use of trenchless technology will continue to increase due to the advantages of minimizing disruption to society and reducing environmental impact.

For example, new advancements in directional tracking systems now allows contractors to work under and around some of the busiest roadways while still complying with dictated project restrictions and avoiding major traffic disruptions. With the use of new trenchless technologies, however, many questions are raised. Who is tracking the installations? Are the locations and depths of directional bores known? What risks are involved as a result of drilling blindfolded? What risks are increased due to trenchless technologies being utilized? This presentation will provide insight, answers and solutions to these challenging questions.

Keys to Effective Damage Prevention Programs Panel Discussion

Robert A. Martin, Esq., APWA/AGC Joint Committee, FH Martin Construction, Eastpointe, MI • James Anspach, So Deep, Inc., Manassas Park, VA • Mark McAlpine, Esq., McAlpine and McAlpine, Bloomfield Hills, MI • Bob Rast, Rast Construction Company, Birmingham, AL • Jack D. Messer, Director of Utilities, City of Manhattan, Manhattan, KS • Kristine Young, President, Miller the Driller, Des Moines, IA • Donald R. Evans, APWA/OCSI Committee Chair, Operations Manager, Underground Service Alert/SC, Brea, CA • Thomas V. Jackson, Staff Engineer, Georgia Power, Atlanta, GA

In this closing session, panelists will focus on the key components necessary for effective teamwork in damage prevention programs.

PLEASE CUT ALONG DOTTED LINE AND MAIL OR FAX TO ADDRESS LISTED ON FORM

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

UTILITY COORDINATION REPORT

for December 1, 1998 to December 31, 1998

Notice of Intent and Request for Information Issued (NOI):	**Date**
1589N – Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement (CW-165)	12/03/98
1734N – Franklin/Greenwich and Union Streets Pavement Renovation	12/04/98
1755N – Oak Street Pavement Renovation	12/17/98

Final Preliminary Plans Issued (LOT):	
1589N – Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement (CW-165)	12/15/98

State of California:

Other:

Projects in Progress (NOI)

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
—N	Greg Cruz	554-8268	Various Locations, Construction of Curb Ramps - STPL-5934(030)	Pav	09/04/1997
1034N	Ed Choy	554-8284	Chinatown Alleyway Improvements Phase 1 Commercial, Cordelia and Ross	STR	05/27/1998
1048N	Gene Handa	554-8341	Sunnydale Sewer Improvements	SW	07/03/1996
1076N	Arlen Ung	554-8263	West End Utilities	Pav	08/11/1997
1100N	Martha Ketterer	554-8296	Ecker Street, Mission Street to Elim Alley	Pav	01/08/1996
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements Locations #306 & 309	UG	02/15/1998
1145N	Naoki Kaku	554-8246	Bernal Heights Street Improvement, Banks/Chapman Area	Pav	12/02/1996
1202N	Linda Leong	648-6882	North Point Plant Improvement, Phase II	Pav	01/30/1996
1218N	Cliff Wong	554-8339	Market , Larkin and Harrison Streets Sewer Replacement	SW	03/29/1996
1243N	Ronald Cheng	558-4049	Marina Seawall and Roadway Improvement	Pav	04/12/1996
1277N(1)	Laarni Camerino	554-8256	Var Loc: As Needed Paving - McAllister, Polk, Grove & Van Ness Avenue	Pav	08/17/1998
1277N(2)	Pak Choi	554-8283	Various Locations: As Needed Paving - Stockton (Post to Market Street)	Pav	08/17/1998
1277N(3)	Greg Cruz	554-8268	Var Loc - As Needed Pav: Lake Merced from Skyline Blvd. To John Muir Drive	PAV	09/28/1998
1285N	Brian Gatter	554-8292	Pioneer Park Renovation – Telegraph Hill Stairways	Pav	11/14/1997
1294N	Leon Louie	558-4070	Fourth Street Bridge Fender Repair Project	Str	12/18/1996
1330N	Wallis Lee	554-8344	2nd / 9th Streets Sewer Abandonment Project	SW	06/27/1997
1349N	Saed Toloui	558-4084	12th Avenue/Quintara Street, Stairway Construction	Str	02/07/1997
1362N	Edward Choy	554-8284	Various Locations SOMA Street District Track Removal & Pavement Renovation Phase 2	PAV	01/07/1999
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	12/02/1996
1381N	Patrick Riviera	558-4045	Martin Luther King Utilities	Pav	09/12/1997
1385N	Laarni Camerino	554-8256	Various Locations: Concrete Street Reconstruction - Stillings Ave from Teresita to Congo	PAV	07/10/1998
1389N	Pak Choi	554-8283	Mission Street Pavement Renovation	Pav	06/13/1997
1395N	Cliff Wong	554-8339	Sacramento/ Larkin/ Pine Streets Sewer Replacement	SW	04/10/1998
1407N	Narciso Paderanga Jr.	554-8258	California Street Pavement Renovation, STP-17	Pav	02/13/1997
1409N	Pak Choi	554-8283	Sutter Street Pavement Renovation STP-19	Pav	04/13/1998
1415N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	Str	07/31/1997
1421N	Clifford Wong	554-8339	Green Street Sewer Replacement - Columbus Avenue to Powell Street	SW	01/17/1997
1423N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	SR	07/31/1997
1432N	Gene Handa	554-8341	Post Street Sewer Replacement	SW	02/07/1997
1459N	Narciso Paderanga, Jr.	554-8258	Fillmore Street Pavement Renovation and Muni Underground Ductbank System	Pav	08/29/1997
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	11/10/1997
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SR	09/30/1997
1549N	Thomas Won	554-8275	Ocean/Victoria/Everglade Sewer Replacement	SW	09/23/1997
1573N	Wallis Lee	554-8344	5th Street & Harrison Sewer Replacement	SW	02/17/1998
1583N	Thomas Won	554-8275	Everglade/ Victoria/ Revere/ Bridge View Sewer Replacement	SW	03/23/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	04/13/1998
1587N	Jean To	554-8298	7th Avenue and Kirkham Street Sewer Replacement	SW	12/11/1998
1588N	Thomas Won	554-8275	Joost Ave/Alemany Blvd/Mt. Vernon Ave/Kensington Way Sewer Replacement	SW	12/22/1998
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	01/04/1999
1590N	Thomas Won	554-8275	Ocean Avenue Sewer Replacement (Joint Venture with MUNI)	SW	07/13/1998
1605N	Bryan Dessaure	554-8299	Sacramento/Pierce/Wilmot Streets Sewer Replacement	SW	06/07/1998
1626N	Thomas Won	554-8275	4th/5th Ave/Stanyan St (easement) / Paris Street Sewer Replacement	SW	10/22/1998
1628N	Jean To	554-8298	Moraga Street Sewer Replacement: 17th to 18th Avenues	SW	09/16/1998
1629N	Peter Cheng	554-8348	Union/Kearny Streets Sewer Replacement	SW	10/28/1998
1630N	Birgit Chase	554-8336	Polk/Francisco/Quincy/Sacramento Streets Sewer Replacement	SW	11/09/1998
1631N	Jean To	554-8298	4th/10th Ave/Anza/Cabrillo Streets Sewer Replacement	SW	10/26/1998
1632N	Bhula Patel	554-8324	Post, Grove and Potomac Streets Sewer Replacement	SW	12/10/1998
1653N	Uday Prasad	558-4061	Demolition of North Beach Garage at 763 Vallejo Street	Str	09/15/1997
1655N	Lesley Wong	554-8252	Cezar Chavez Improvements Phase 2		07/27/1998
1667N	Lesley Wong	554-8252	Fourth Street Sidewalk Widening Project - Phase 2	Pav	03/10/1998
1668N	Ken Chu	554-8388	Golden Gate Avenue Pavement Renovation	Pav	01/02/1998
1674N	Joe Haas	558-4539	1680 Mission Street Secondary Power Source	SDV	05/27/1998
1678N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Street Reconstruction No. 15	Pav	04/13/1998
1680N	Lesley Wong	554-8252	Great Highway and Point Lobos Pavement Renovation	Pav	05/13/1998
1701N	Laarni Camerino	554-8256	Seventh Street Pavement Renovation	Pav	08/24/1998

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
1724N	Laami Camerino	554-8256	Various Locations: As Needed Paving - 2nd St. between Townsend & King Streets	Pav	07/10/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	10/28/1998
1729N	Narciso Paderanga, Jr.	558-8258	Brotherhood Way & Font Boulevard Pavement Renovation	Pav	09/08/1998
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	10/05/1998
1734N	Dimitrios Stavrakis	554-8271	Franklin/Greenwich and Union Streets Pavement Renovation	PAV	01/04/1999
1735N	Naoki Kaku	554-8246	Various Locations: Bayview District Pavement Renovation	PAV	10/13/1998
1748N	Carol Finucane	558-4581	Mid-Market Public Improvements		10/05/1998
1755N	David Pang	554-8278	Oak Street Pavement Renovation	PAV	02/02/1999
1759N	Pak Choi	554-8283	Mission Street Pavement Renovation Phase 2	PAV	12/30/1998
6618E	Leon L. Louie	558-4070	Seismic Retrofit of Third Street Bridge	Str	08/31/1997
6618N	Frank Piruzmand	558-4081	3rd Street Bridge Rehabilitation & Retrofit	Str	03/30/1998
7291E	Lynn Fong	554-8269	K-Line Rail Replacement & Ocean Avenue Improvements	Pav	11/03/1997
7361E	Fernando Cisneros	554-8278	Hunter's Point Naval Shipyard Infrastructure Backbone Phase I	Pav	11/25/1996
7416E	Deirdre Appel	558-4556	Golden Gate Park Reservoir and Pump Station		08/07/1998
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	12/22/1998
N	Linda DeBolt	554-8265	Surface Streets Improvement Project	Pav	02/06/1998

Projects in Progress (NOI)

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
---N	09/04/1997		08/07/1997	11/09/1998	10/20/1997	08/20/1997			09/04/1997
1034N	05/27/1998		05/06/1998	06/02/1998	05/11/1998	05/12/1998	04/30/1998	05/06/1998	05/13/1998
1048N	07/03/1996	Mar-99	07/11/1996	06/17/1996		07/16/1996			07/14/1996
1076N	08/11/1997	Jul-98	07/17/1997			07/23/1997	07/18/1997	07/29/1997	08/26/1997
1100N	01/08/1996	May-98		05/14/1996		12/18/1995			02/16/1996
1109K	02/15/1998		12/30/1997	04/27/1998	01/21/1998	01/09/1998	12/30/1997	01/09/1998	01/13/1998
1145N	12/02/1996	Nov-98	11/08/1996			12/03/1996			12/07/1996
1202N	01/30/1996	18-Nov-97		01/29/1996				01/16/1996	
1218N	03/29/1996	On hold	03/22/1996			03/20/1996	03/01/1996		
1243N	04/12/1996		03/29/1996				03/25/1996	03/19/1996	04/23/1996
1277N(1)	08/17/1998			07/24/1998	08/19/1998	07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(2)	08/17/1998			07/24/1998		07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(3)	09/28/1998		09/08/1998	09/10/1998	11/02/1998	09/09/1998	09/04/1998	09/23/1998	09/17/1998
1285N	11/14/1997	Jul-98	10/21/1997	04/13/1998		10/24/1997	10/16/1997	10/20/1997	11/06/1997
1294N	12/18/1996	May-98	10/25/1996	03/19/1997		10/18/1996		10/09/1996	12/07/1996
1330N	06/27/1997	Apr-98	06/16/1997	06/17/1997		06/17/1997	06/16/1997		
1349N	02/07/1997	Apr-98	01/09/1997			03/27/1997	01/10/1997	01/24/1997	02/07/1997
1362N	01/07/1999		12/02/1998			12/02/1998	12/01/1998		12/14/1998
1374N	12/02/1996		11/08/1996	02/24/1997		12/03/1996			12/07/1996
1381N	09/12/1997		08/18/1997			08/22/1997	08/18/1997	10/29/1997	09/15/1997
1385N	07/10/1998		06/12/1998	07/10/1998		06/22/1998	06/18/1998	07/17/1998	06/23/1998
1389N	06/13/1997	May-98	05/28/1997	06/02/1997			06/05/1997	05/28/1997	06/03/1997
1395N	04/10/1998			04/27/1998	04/17/1998	06/02/1998	04/08/1998	04/13/1998	04/20/1998
1407N	02/13/1997	On hold	01/17/1997			01/21/1997	01/15/1997	01/27/1997	02/18/1997
1409N	04/13/1998			05/15/1998		06/02/1998	04/08/1998	04/13/1998	04/20/1998
1415N	07/31/1997	Sep-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997	07/22/1997	07/28/1997
1421N	01/17/1997	Jan-98	01/09/1997	01/06/1997		01/23/1997	01/02/1997		02/07/1997
1423N	07/31/1997	Nov-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997		07/28/1997
1432N	02/07/1997	Jun-98		02/20/1997		02/11/1997	01/23/1997		02/18/1997
1459N	08/29/1997	May-98	08/05/1997	12/22/1997	10/20/1997	08/07/1997	08/01/1997		09/05/1997
1474N	11/10/1997	Jul-98	10/21/1997	06/17/1998	10/16/1997	10/24/1997	10/16/1997		11/06/1997
1548N	09/30/1997		09/08/1997	04/13/1998	09/24/1997	09/19/1997	09/09/1997		09/30/1997
1549N	09/23/1997					09/19/1997	09/11/1997		09/30/1997
1573N	02/17/1998		01/23/1998	06/17/1998	01/23/1998	02/12/1998	01/23/1998		02/12/1998
1583N	03/23/1998		03/23/1998		03/09/1998	03/05/1998	03/09/1998	03/11/1998	03/24/1998
1585N	04/13/1998		04/29/1998	04/30/1998	04/15/1998	05/12/1998	04/09/1998	04/13/1998	04/23/1998
1587N	12/11/1998		11/09/1998		11/09/1998	11/09/1998	11/02/1998		11/16/1998
1588N	12/22/1998					12/02/1998	12/01/1998		12/09/1998
1589N	01/04/1999		12/17/1998					12/17/1998	
1590N	07/13/1998			07/13/1998		06/19/1998	06/18/1998	07/16/1998	06/23/1998
1605N	06/07/1998		05/11/1998	05/15/1998	05/11/1998	05/13/1998	05/11/1998		05/20/1998
1626N	10/22/1998		10/16/1998	11/12/1998			10/06/1998		10/15/1998
1628N	09/16/1998		09/14/1998	09/10/1998	09/10/1998	09/10/1998	09/10/1998	09/15/1998	09/17/1998
1629N	10/28/1998			11/12/1998		10/02/1998	10/01/1998	10/09/1998	10/13/1998
1630N	11/09/1998				11/09/1998	11/09/1998	10/16/1998	10/13/1998	10/21/1998
1631N	10/26/1998		10/02/1998	11/12/1998	11/02/1998	10/08/1998	09/29/1998	10/09/1998	10/13/1998
1632N	12/10/1998		11/09/1998		11/09/1998	11/09/1998	11/02/1998		11/06/1998
1653N	09/15/1997		09/02/1997	09/09/1997		09/02/1997		09/09/1997	09/10/1997
1655N	07/27/1998		07/01/1998		07/06/1998		06/29/1998		07/20/1998
1667N	03/10/1998		02/20/1998		02/20/1998		02/20/1998	03/13/1998	03/05/1998
1668N	01/02/1998	Sep-98	12/04/1997	04/27/1998	12/12/1997	01/13/1998	12/03/1997	12/04/1997	12/16/1997
1674N	05/27/1998		05/15/1998		05/26/1998	05/22/1998	05/19/1998	06/02/1998	06/09/1998
1678N	04/13/1998								
1680N	05/13/1998		04/27/1998	06/02/1998	05/11/1998	05/26/1998		04/22/1998	05/06/1998
1701N	08/24/1998		07/29/1998	09/02/1998		08/04/1998	07/24/1998	10/15/1998	08/13/1998

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1724N	07/10/1998		06/22/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	06/22/1998	06/23/1998
1727N	10/28/1998		10/02/1998	11/06/1998		10/02/1998	10/01/1998	09/30/1998	10/13/1998
1729N	09/08/1998		08/12/1998	09/02/1998		08/12/1998	08/10/1998	09/15/1998	08/18/1998
1732N	10/05/1998		09/14/1998	11/06/1998	11/02/1998	09/22/1998	09/11/1998	10/15/1998	09/25/1998
1734N	01/04/1999		12/17/1998						
1735N	10/13/1998		09/14/1998	11/06/1998		09/22/1998	09/15/1998	09/25/1998	09/25/1998
1748N	10/05/1998		09/14/1998	11/06/1998		09/22/1998	09/14/1998	10/13/1998	09/25/1998
1755N	02/02/1999								
1759N	12/30/1998		11/23/1998			12/10/1998			12/09/1998
6618E	08/31/1997	Dec-98	07/16/1997		07/15/1997	07/18/1997	07/24/1997	07/28/1997	08/26/1997
6618N	03/30/1998		03/25/1998	03/23/1998		03/23/1998	03/24/1998	03/17/1998	03/30/1998
7291E	11/03/1997		10/21/1997	06/02/1998		10/24/1997	10/08/1997	10/09/1997	10/14/1997
7381E	11/25/1996		10/31/1996			11/13/1996	11/01/1996	10/30/1996	12/07/1996
7416E	08/07/1998		07/17/1998	07/10/1998		06/30/1998	07/13/1998	07/09/1998	07/29/1998
7458E	12/22/1998		11/25/1998			12/10/1998	12/01/1998		12/10/1998
N	02/06/1998		01/08/1998		01/23/1998	05/13/1998	01/08/1998	03/09/1998	01/26/1998

Projects in Progress (NOI)

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
---N	09/04/1997	08/26/1997	11/24/1998		08/19/1997		09/30/1997	09/30/1997
1034N	05/27/1998	05/06/1998	05/06/1998		06/02/1998		06/25/1998	06/25/1998
1048N	07/03/1996	06/18/1996	06/25/1996	07/16/1996	07/01/1996	06/21/1996		
1076N	08/11/1997	07/28/1997			08/04/1997	07/28/1997	07/28/1997	07/28/1997
1100N	01/08/1996	12/11/1995	12/21/1995	12/11/1995	12/28/1995	12/08/1995		
1109K	02/15/1998		01/14/1998		01/15/1998		01/27/1998	01/27/1998
1145N	12/02/1996	12/07/1996	12/02/1996		11/25/1996	12/03/1996	12/03/1996	12/03/1996
1202N	01/30/1996			01/18/1996	02/02/1996	01/18/1996		
1218N	03/29/1996	03/14/1996		03/14/1996	03/18/1996	03/18/1996		
1243N	04/12/1996	03/27/1996		04/15/1996	03/25/1996	04/02/1996		
1277N(1)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998			
1277N(2)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998	07/31/1998	08/13/1998	08/13/1998
1277N(3)	09/28/1998	09/09/1998	09/04/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1285N	11/14/1997	11/07/1997		02/11/1998	10/24/1997	10/17/1997	11/25/1997	11/25/1997
1294N	12/18/1996	10/24/1996		11/07/1996	10/28/1996	11/19/1996		
1330N	06/27/1997	07/01/1997		07/09/1997	06/27/1997	06/12/1997	07/10/1997	07/10/1997
1349N	02/07/1997	01/17/1997	01/22/1997	03/17/1997		01/13/1997	02/05/1997	02/05/1997
1362N	01/07/1999	12/01/1998			12/10/1998			
1374N	12/02/1996	11/07/1996			11/25/1996	11/07/1996	12/02/1996	12/02/1996
1381N	09/12/1997	08/26/1997			08/21/1997			09/24/1997
1385N	07/10/1998	06/15/1998	06/23/1998		06/25/1998	10/08/1998	07/29/1998	07/29/1998
1389N	06/13/1997	05/29/1997			05/23/1997	06/11/1997	05/23/1997	05/23/1997
1395N	04/10/1998	04/13/1998			04/22/1998	04/13/1998		05/14/1998
1407N	02/13/1997	02/24/1997	04/17/1997	03/19/1997	01/23/1997	02/03/1997	02/05/1997	02/05/1997
1409N	04/13/1998	04/13/1998	04/15/1998		04/14/1998		06/25/1998	06/25/1998
1415N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1421N	01/17/1997	01/10/1997		01/29/1997	02/19/1997	12/30/1996	01/22/1997	01/22/1997
1423N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1432N	02/07/1997	02/24/1997	02/10/1997	03/18/1997	01/31/1997	01/22/1997	02/24/1997	02/24/1997
1459N	08/29/1997	08/05/1997			08/13/1997		09/24/1997	09/24/1997
1474N	11/10/1997	11/07/1997			10/23/1997	10/14/1997	11/25/1997	11/25/1997
1548N	09/30/1997	09/12/1997			09/15/1997	09/29/1997	10/09/1997	10/09/1997
1549N	09/23/1997	09/24/1997			09/17/1997	09/15/1997	10/09/1997	10/09/1997
1573N	02/17/1998	01/26/1998	03/30/1998			01/22/1998		02/12/1998
1583N	03/23/1998	03/11/1998	03/30/1998		03/18/1998	03/09/1998	03/17/1998	
1585N	04/13/1998	04/13/1998			04/30/1998	04/13/1998	06/25/1998	06/25/1998
1587N	12/11/1998	11/13/1998		12/18/1998	11/13/1998			
1588N	12/22/1998	12/01/1998			12/02/1998			
1589N	01/04/1999	12/15/1998						
1590N	07/13/1998	06/17/1998	08/04/1998		06/29/1998	10/08/1998	07/29/1998	07/29/1998
1605N	06/07/1998	05/12/1998				05/15/1998	06/25/1998	06/25/1998
1626N	10/22/1998	10/06/1998		11/09/1998	10/13/1998			
1628N	09/16/1998	09/10/1998	09/08/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1629N	10/28/1998	10/06/1998		11/09/1998	10/08/1998		11/12/1998	11/12/1998
1630N	11/09/1998	10/15/1998			10/20/1998			
1631N	10/26/1998	10/06/1998		11/09/1998	10/02/1998			11/12/1998
1632N	12/10/1998				11/06/1998			
1653N	09/15/1997	09/12/1997			09/08/1997	09/04/1997	09/24/1997	09/24/1997
1655N	07/27/1998	07/01/1998			07/02/1998	07/01/1998	07/29/1998	07/29/1998
1667N	03/10/1998	02/20/1998			02/27/1998			
1668N	01/02/1998	12/04/1997			12/12/1997		01/27/1998	01/27/1998
1674N	05/27/1998	05/18/1998	05/19/1998		06/02/1998	05/14/1998	07/09/1998	07/09/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998	05/13/1998		04/30/1998		06/25/1998	06/25/1998
1701N	08/24/1998	07/24/1998	08/24/1998	11/09/1998			08/13/1998	08/13/1998

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1724N	07/10/1998	06/15/1998	06/23/1998		06/23/1998	10/08/1998	07/09/1998	07/09/1998
1727N	10/28/1998	10/02/1998		11/09/1998	10/13/1998			
1729N	09/08/1998	08/11/1998	08/12/1998	11/09/1998	08/18/1998	09/18/1998	09/01/1998	09/01/1998
1732N	10/05/1998	09/17/1998		11/09/1998	09/28/1998	09/11/1998		11/12/1998
1734N	01/04/1999	12/15/1998						
1735N	10/13/1998	09/18/1998		11/09/1998	09/18/1998	09/09/1998		11/12/1998
1748N	10/05/1998	09/18/1998		11/09/1998	09/24/1998	09/11/1998		11/12/1998
1755N	02/02/1999							
1759N	12/30/1998	12/01/1998	11/23/1998		12/14/1998			12/01/1998
6618E	08/31/1997	07/16/1997		07/30/1997	07/24/1997	07/28/1997	08/21/1997	08/21/1997
6618N	03/30/1998	03/25/1998			04/01/1998		05/14/1998	
7291E	11/03/1997	10/29/1997			10/20/1997		11/10/1997	11/10/1997
7381E	11/25/1996	11/06/1996	11/05/1996	11/14/1996	11/08/1996	12/18/1996	12/02/1996	12/02/1996
7416E	08/07/1998	07/13/1998		11/09/1998	07/20/1998	07/01/1998		07/29/1998
7458E	12/22/1998	12/01/1998	12/14/1998		12/15/1998			12/01/1998
N	02/06/1998	06/22/1998			01/26/1998	10/08/1998		02/12/1998

Projects in Progress (NOI)

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
---N	09/04/1997	08/12/1997		08/08/1997	08/13/1997	08/08/1997	08/08/1997	08/26/1997
1034N	05/27/1998	04/30/1998		05/19/1998	05/11/1998	05/20/1998		05/11/1998
1048N	07/03/1996		06/26/1996	07/01/1996		06/25/1996	07/03/1996	07/01/1996
1076N	08/11/1997	07/24/1997		07/24/1997	07/29/1997	08/08/1997	07/22/1997	08/15/1997
1100N	01/08/1996		12/20/1995	01/03/1996	12/14/1995	12/18/1995	12/27/1995	12/20/1995
1109K	02/15/1998	01/07/1998		01/14/1998	01/14/1998	05/20/1998	01/21/1998	01/21/1998
1145N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1202N	01/30/1996		01/16/1996	01/19/1996	01/31/1996	01/17/1996		02/06/1996
1218N	03/29/1996				03/12/1996	03/05/1996	03/27/1996	03/07/1996
1243N	04/12/1996		03/25/1996		03/27/1996	03/22/1996	03/27/1996	03/21/1996
1277N(1)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(2)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(3)	09/28/1998	09/03/1998		09/15/1998	09/17/1998			09/17/1998
1285N	11/14/1997	10/20/1997	10/28/1997	10/27/1997	10/23/1997	11/18/1997	11/10/1997	11/13/1997
1294N	12/18/1996		10/25/1996	10/25/1996	10/31/1996		12/02/1996	10/24/1996
1330N	06/27/1997	06/16/1997	07/02/1997	06/23/1997	06/23/1997	07/11/1997	08/08/1997	07/02/1997
1349N	02/07/1997	01/13/1997	01/13/1997	01/21/1997	02/12/1997	02/27/1997		01/22/1997
1362N	01/07/1999	12/01/1998	12/02/1998	12/10/1998	12/10/1998			12/14/1998
1374N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1381N	09/12/1997	08/15/1997		08/22/1997	08/22/1997	11/18/1997		08/26/1997
1385N	07/10/1998	06/15/1998		06/23/1998	06/19/1998			06/29/1998
1389N	06/13/1997	05/19/1997	05/29/1997	05/21/1997	05/23/1997	05/29/1997	06/26/1997	06/06/1997
1395N	04/10/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1407N	02/13/1997	01/17/1997	01/15/1997	01/24/1997	02/12/1997	02/27/1997	02/24/1997	01/22/1997
1409N	04/13/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1415N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1421N	01/17/1997	01/07/1997	01/06/1997		02/18/1997	02/27/1997		01/22/1997
1423N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1432N	02/07/1997	01/27/1997	01/27/1997	01/29/1997	02/12/1997	02/27/1997		01/30/1997
1459N	08/29/1997	08/05/1997		08/06/1997	08/12/1997	08/08/1997	11/10/1997	08/26/1997
1474N	11/10/1997	10/20/1997		10/21/1997	10/22/1997	11/18/1997	11/10/1997	11/13/1997
1548N	09/30/1997	09/19/1997		09/12/1997	09/12/1997	09/24/1997	09/11/1997	09/22/1997
1549N	09/23/1997	09/12/1997		09/18/1997	09/16/1997	09/24/1997	09/19/1997	09/22/1997
1573N	02/17/1998	01/26/1998		02/12/1998	02/12/1998			02/20/1998
1583N	03/23/1998		03/20/1998	03/24/1998	03/17/1998		04/08/1998	03/03/1998
1585N	04/13/1998	04/13/1998	04/28/1998	04/20/1998	04/28/1998	05/20/1998		04/28/1998
1587N	12/11/1998		11/12/1998	11/23/1998	11/19/1998			11/19/1998
1588N	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998			12/04/1998
1589N	01/04/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998			
1590N	07/13/1998	06/15/1998		07/08/1998	06/19/1998			07/07/1998
1605N	06/07/1998	05/13/1998		05/19/1998	05/20/1998	05/20/1998		06/02/1998
1626N	10/22/1998	10/05/1998			10/15/1998			10/15/1998
1628N	09/16/1998	09/08/1998	09/08/1998	09/15/1998	09/17/1998	09/16/1998	09/17/1998	09/17/1998
1629N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1630N	11/09/1998	10/09/1998			10/19/1998			10/27/1998
1631N	10/26/1998	09/28/1998		10/07/1998	10/06/1998			10/15/1998
1632N	12/10/1998	10/28/1998		11/23/1998	11/10/1998			11/10/1998
1653N	09/15/1997	09/02/1997		09/08/1997	09/12/1997		09/15/1997	09/22/1997
1655N	07/27/1998	06/29/1998	07/20/1998	07/10/1998	07/15/1998	07/29/1998		07/15/1998
1667N	03/10/1998	02/20/1998		02/20/1998	02/20/1998			02/20/1998
1668N	01/02/1998	12/03/1997		12/23/1997		02/12/1998	12/11/1997	12/12/1997
1674N	05/27/1998	05/19/1998			06/03/1998	05/20/1998		06/11/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998		05/06/1998	05/06/1998	06/02/1998		05/11/1998
1701N	08/24/1998	07/24/1998		08/04/1998	08/03/1998	07/24/1998		

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1724N	07/10/1998	06/22/1998		06/23/1998	06/19/1998			06/29/1998
1727N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1729N	09/08/1998	08/24/1998		09/01/1998	08/13/1998			09/17/1998
1732N	10/05/1998	09/11/1998		09/22/1998	09/17/1998			09/30/1998
1734N	01/04/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998			12/18/1998
1735N	10/13/1998	09/11/1998		09/22/1998	09/17/1998			09/24/1998
1748N	10/05/1998	09/11/1998		09/22/1998	09/17/1998			09/30/1998
1755N	02/02/1999							
1759N	12/30/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998			12/14/1998
6618E	08/31/1997	07/17/1997		07/21/1997	07/18/1997	03/24/1998	07/16/1997	07/18/1997
6618N	03/30/1998	03/26/1998	04/02/1998	04/02/1998		03/24/1998	04/01/1998	04/03/1998
7291E	11/03/1997	10/09/1997	10/16/1997	10/10/1997	10/15/1997	11/19/1997	11/10/1997	10/16/1997
7381E	11/25/1996	01/10/1997	11/13/1996	11/13/1996	11/07/1996		12/02/1996	11/19/1996
7416E	08/07/1998	07/21/1998		07/20/1998	07/20/1998			07/31/1998
7458E	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998			12/04/1998
N	02/06/1998	02/10/1998	01/16/1998	01/14/1998	01/21/1997	02/10/1998	01/21/1998	01/21/1998

Projects in Progress (LOT)

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1001H	Paul Travis	557-4631	911/OES Emergency Communications Center		12/06/1996
1036N	Lesley Wong	554-8252	Fourth Street Pavement Renovation	Pav	05/28/1997
1077N	Steve Bui	554-8298	Bowling Green Drive Contract	SW	09/30/1997
1091N	Ed Choy	554-8284	Various Locations South of Market Removal & Pavement Renovation	Pav	04/30/1997
1106N	Steve Bui	554-8298	Western Presidio Drainage Improvements (NOI/LOT)	SW	05/16/1997
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements, Various Locations	UG	04/28/1997
1109N	Linda DeBolt	554-8265	Cesar Chavez (Army) Street Widening	Pav	12/27/1996
1133N	Ellaine Taraya	554-8245	Fulton Street Roadway Widening	Pav	10/27/1997
1155N	E. Ho/Bhula Patel	554-8324	Grant/Chestnut Street Sewer Replacements	SW	10/21/1998
1195N	Gyee Yang	558-4553	Market and Steuart Streets, AWSS Relocation	AWSS	07/20/1996
1208K	Joe Haas	558-4539	San Francisco General Hospital Underground Storage Tank Replacement	UG	03/09/1998
1223W	Lesley Wong	554-8252	Islais Creek, Street Improvements	Pav	04/30/1997
1245N	Wallis Lee	554-8344	Yosemite/Egbert Sewer Enlargment Project (formerly 3180W)	SW	11/27/1996
1253N	Iqbal Dhapa	554-8337	Twelfth Street (SR)	SW	05/16/1997
1254N	Cliff Wong	554-8339	Eleventh Street Sewer Replacement - Harrison St. to Folsom St.	SW	05/23/1997
1272N	Steve Bui	554-8298	Illinois-Cesar Chavez (Army) Streets Sewer Construction	SW	08/08/1997
1322N	Lesley Wong	554-8252	Cabrillo Street, 9th and 16th Avenues Pavement Renovation	Pav	03/11/1997
1373N	Ken Chu	554-8388	Lower Great Highway, 46th, and 48th Avenues, Pavement Renovation	Pav	09/15/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	05/28/1997
1392N	Birgit Chase	554-8336	Bayshore Blvd. - U.S. 101 Off-Ramp...Sewer Repl. (1108N)	Pav & SW	02/28/1997
1393N	Thomas Won	554-8275	Bush/Kearny/Post Streets Sewer Replacement	SW	10/24/1997
1396N	Peter Cheng	554-8348	Sutter/Fell/Broederick Streets Sewer Replacement	SW	05/12/1997
1397N	Bhula Patel	554-8324	Douglass/Dolores/Ord/23rd/28th Streets, Sewer Replacement	SW	10/17/1997
1408N	Naoki Kaku	554-8246	Geneva Avenue, Pavement Renovation	Pav	02/06/1998
1411N	Peter Cheng	554-8348	Harding Park SR	SW	11/14/1997
1413N	Iqbal Dhapa	554-8337	Davis/Kearny/Francisco Streets Sewer Replacement	SW	06/25/1997
1414N	Thomas Won	554-8275	Treat / 22nd Streets Sewer Replacement	SW	02/28/1997
1426N	Ting He	554-8338	Dore/Valencia/Clinton Park SR	SW	12/08/1997
1433N	Peter Cheng	554-8348	Shotwell Street Sewer Replacement - Army Street to 26th St	SW	11/07/1997
1440N	Pak Choi	554-8283	Various Locations Concrete Street Reconstruction No. 13	Pav	02/06/1998
1453N	Naoki Kaku	554-8246	Montgomery, Kearny, & Sacramento, Pavement Renovation	Pav	02/06/1998
1454N	Ed Choy	554-8284	Potrero Hill District Track Removal and Pavement Renovation, Phase 3	SW	04/27/1998
1460N	Birgit Chase	554-8336	Church / Folsom / Harper Streets Sewer Replacement	SW	10/22/1997
1461N	Iqbal Dhapa	554-8337	Mason / Pine / Leavenworth Streets and Meacham Place Sewer Replacement	SW	03/06/1998
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	06/22/1998
1475N	Birgit Chase	554-8336	Virginia / Fair Avenues/Godeus Street SR	SW	12/24/1997
1477N	Lynn Fong	554-8269	Various Locations Concrete Street Pavement Renovation No. 14	Pav	11/09/1998
1488N	Peter Cheng	554-8348	24th Ave/California Street Sewer Replacement (1452N)	SW	06/20/1997
1491N	Peter Cheng	554-8348	Pacific Ave. Sewer Replacement - Grant Ave. to Stockton St.	SW	09/25/1997
1519N	Pak Choi	554-8283	Bus Bulb Improvement Project Phase 1	Pav	01/23/1998
1528N	Iqbal Dhapa	554-8337	501 Laguna Honda Boulevard Easement Sewer Replacement	SW	08/25/1997
1547N	Peter Cheng	554-8348	33rd Ave/Lyon Street/Molimo Dr SR	SW	01/16/1998
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SW	01/09/1998
1550N	Bhula Patel	554-8324	Day/Congo/Marston/Cuvier SR	SW	01/30/1998
1562N	Birgit Chase	554-8336	Broadway/Bryant/22nd/Sonoma Streets Sewer Replacement	SW	06/26/1998
1563N	Iqbal Dhapa	554-8337	Balboa St. and 3rd/20th/42nd Avenues Sewer Replacement	SW	06/25/1998
1566N	Peter Cheng	554-8243	Fillmore Street SR	SW	12/19/1997
1569N	Peter Cheng	554-8348	Dolores Street/Block 7044 Easement Sewer Replacement	SW	06/12/1998
1578N	Jean To	554-8329	Golden Gate Ave. Sewer Replacement-Polk St/Van Ness & Pierce/Scott Sts	SW	03/10/1998
1579N	Jean To	554-8329	Illinois Street Sewer Replacement-20th to 19th Street		04/17/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	09/15/1998
1586N	Jean To	437-7012	Geary, Eddy, Elm and Turk Sewer Replacement	SW	10/20/1998
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	
1602N	Jean To	437-7012	Howard, Minna and 2nd Streets Sewer Replacement	SW	11/09/1998
1603N	Jean To	554-8270	Broad Street, Capitol to Plymouth Avenue Sewer Replacement	SW	07/10/1998

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1606N	Jean To	554-8348	Cayuga/Laurel/Rondel and Douglass Sewer Replacement	SW	10/29/1998
1687N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 15	Pav	08/31/1998
6094Q	Deanna Calleros	554-8266	Mid Embarcadero Surface Rdwy and F-Line Extension	Pav	06/27/1997
7090E	Thinh Nguyen	558-4554	Various Locations Motorized Valves Contract #2	AWSS	03/19/1998
7437E	Laami Camerino	554-8256	Howard, Folsom & Hawthorne Streets (SR)	SW	08/29/1997
7474E	Peter Cheng	554-8348	Pine/California/Delancey Streets SR	SW	11/26/1997

Project in Progress (LOT)

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1001N	12/06/1996		12/03/1996	01/22/1997		12/05/1996		11/25/1996	12/16/1996
1036N	05/28/1997	Apr-98	05/15/1997	06/30/1997		05/09/1997	05/14/1997		
1077N	09/30/1997	Apr-98	09/08/1997	06/26/1998		09/24/1997	09/09/1997		09/05/1997
1091N	04/30/1997	15-Sep-97	04/04/1997	05/13/1997				04/11/1997	04/28/1997
1106N	05/16/1997	3-Nov-97	05/06/1997	05/13/1997		05/12/1997	05/06/1997		06/03/1997
1109K	04/28/1997		04/14/1997			04/16/1997		04/22/1997	05/08/1997
1109N	12/27/1996	Jun-98	12/05/1996				12/03/1996		02/07/1997
1133N	10/27/1997	May-98	10/21/1997		10/16/1997		10/10/1997		10/21/1997
1155N	10/21/1998		10/16/1998	11/09/1998		10/07/1998	10/06/1998		10/15/1998
1195N	07/20/1996						07/08/1996		
1208K	03/09/1998		03/24/1998	03/05/1998		03/18/1998	03/05/1998	03/12/1998	03/24/1998
1223W	04/30/1997	Jun-98	04/14/1997	05/13/1997		04/16/1997	04/21/1997		05/14/1997
1245N	11/27/1996		11/08/1996	02/24/1997					12/07/1996
1253N	05/16/1997	Apr-98	04/28/1997	05/13/1997		05/05/1997	04/29/1997		05/12/1997
1254N	05/23/1997	Jul-98	04/28/1997	05/13/1997		04/23/1997	04/22/1997		05/12/1997
1272N	08/08/1997	Jun-98	07/29/1997	06/15/1998		07/28/1997	07/28/1997		
1322N	03/11/1997	May-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997	02/14/1997	02/27/1997
1373N	09/15/1997	May-98	08/26/1997	04/22/1998			08/22/1997	08/28/1997	09/10/1997
1374N	05/28/1997	May-98	05/01/1997				04/30/1997	05/12/1997	05/14/1997
1392N	02/28/1997		02/20/1997				02/19/1997		02/27/1997
1393N	10/24/1997		10/21/1997			10/15/1997	10/08/1997		10/21/1997
1396N	05/12/1997	May-98	05/01/1997			05/28/1997			05/12/1997
1397N	10/17/1997		09/26/1997		10/20/1997	10/01/1997	09/26/1997		10/14/1997
1408N	02/06/1998	Jun-98	01/08/1998	04/22/1998	01/20/1998		01/08/1998	03/05/1998	01/21/1998
1411N	11/14/1997	Jul-98	10/23/1997			11/05/1997	10/24/1997		11/04/1997
1413N	06/25/1997	Jun-98	06/16/1997	06/17/1997		06/11/1997			07/11/1997
1414N	02/28/1997	Jul-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997		02/28/1997
1426N	12/08/1997	Sep-98	12/04/1997		12/03/1997	12/10/1997	12/03/1997		12/17/1997
1433N	11/07/1997	Jun-98	10/21/1997			10/24/1997	10/16/1997		11/13/1997
1440N	02/06/1998	Apr-98	01/08/1998	01/09/1998	01/20/1998	01/27/1998	01/08/1998		01/21/1998
1453N	02/06/1998	Jul-98	01/08/1998				01/08/1998	03/09/1998	01/26/1998
1454N	04/27/1998		04/27/1998			04/20/1998	04/16/1998	04/23/1998	07/09/1998
1460N	10/22/1997		10/21/1997			10/24/1997	10/10/1997		10/21/1997
1461N	03/06/1998	Jul-98	02/20/1998	04/02/1998			02/20/1998		
1474N	06/22/1998	Jul-98	06/03/1998	06/17/1998	06/02/1998	06/09/1998		06/02/1998	06/03/1998
1475N	12/24/1997		12/12/1997		01/20/1998	01/06/1998	12/15/1997		
1477N	11/09/1998	Jun-98	10/16/1998	11/12/1998	11/02/1998		10/16/1998	11/20/1998	10/20/1998
1488N	06/20/1997	Apr-98	06/09/1997			06/04/1997	06/03/1997		06/16/1997
1491N	09/25/1997	May-98	09/18/1997	06/30/1997		09/24/1997	09/16/1997		
1519N	01/23/1998	Jun-98	12/30/1997				12/30/1997	01/09/1998	01/26/1998
1528N	08/25/1997	Mar-98	08/20/1997		10/03/1997		08/21/1997		09/08/1997
1547N	01/16/1998		12/15/1997		01/20/1998	01/06/1998	12/17/1997		12/23/1997
1548N	01/09/1998		12/22/1997	04/13/1998	12/30/1997	01/09/1998	12/29/1997		01/06/1998
1550N	01/30/1998				01/20/1998	02/12/1998	01/14/1998		02/12/1998
1562N	06/26/1998		06/22/1998		06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1563N	06/25/1998		06/19/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1566N	12/19/1997		12/12/1997	12/19/1997	12/17/1997	12/17/1997	12/15/1997		
1569N	06/12/1998		05/15/1998	06/12/1998	06/17/1998	06/09/1998	05/19/1998	06/02/1998	06/09/1998
1578N	03/10/1998		03/24/1998	06/30/1998	03/09/1998		03/09/1998	03/11/1998	03/24/1998
1579N	04/17/1998			05/15/1998		04/14/1998	04/13/1998	04/13/1998	04/23/1998
1585N	09/15/1998		09/08/1998	09/02/1998	09/10/1998	09/17/1998	09/01/1998	09/21/1998	09/08/1998
1586N	10/20/1998		10/02/1998	11/06/1998	11/02/1998			10/09/1998	10/13/1998
1589N			12/17/1998					12/17/1998	
1602N	11/09/1998		10/16/1998				10/16/1998	10/13/1998	10/20/1998
1603N	07/10/1998		06/19/1998	07/10/1998		06/22/1998	06/18/1998	07/16/1998	06/23/1998

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1606N	10/29/1998		10/02/1998	11/09/1998	11/09/1998		10/06/1998	10/13/1998	10/13/1998
1687N	08/31/1998		08/12/1998	11/06/1998	08/05/1998	08/12/1998	08/03/1998	08/03/1998	08/13/1998
6094Q	06/27/1997	07/98							
7090E	03/19/1998		03/24/1998	04/22/1998				03/18/1998	
7437E	08/29/1997	Jul-98	08/05/1997	04/13/1998		08/08/1997	08/06/1997	09/23/1997	09/04/1997
7474E	11/26/1997		11/19/1997			12/04/1997	11/20/1997		12/10/1997

Project in Progress (LOT)

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1001H	12/06/1996	12/30/1996	01/22/1997		12/05/1996	12/03/1996	12/06/1996	12/06/1996
1036N	05/28/1997	05/23/1997				06/04/1997	06/12/1997	
1077N	09/30/1997	09/24/1997			10/07/1997		11/10/1997	01/27/1998
1091N	04/30/1997					04/14/1997	05/23/1997	05/23/1997
1106N	05/16/1997	05/20/1997			05/19/1997	05/13/1997	05/19/1997	05/19/1997
1109K	04/28/1997					04/22/1997	09/24/1997	09/04/1998
1109N	12/27/1996	12/14/1996	01/29/1997	01/09/1997			06/23/1997	
1133N	10/27/1997	10/16/1997			10/20/1997	10/17/1997	11/10/1997	11/10/1997
1155N	10/21/1998	10/06/1998		11/09/1998	10/13/1998			
1195N	07/20/1996			08/02/1996		07/23/1996		
1208K	03/09/1998	03/05/1998	03/30/1998		03/10/1998		05/14/1998	
1223W	04/30/1997	04/18/1997	04/17/1997			04/25/1997	05/23/1997	03/06/1998
1245N	11/27/1996			12/02/1996	12/05/1996	11/08/1996	04/15/1997	04/15/1997
1253N	05/16/1997	05/20/1997		05/14/1997		04/29/1997	05/16/1997	05/16/1997
1254N	05/23/1997	04/28/1997				04/24/1997	06/12/1997	
1272N	08/08/1997	08/05/1997			10/07/1997	07/30/1997	09/24/1997	09/24/1997
1322N	03/11/1997	03/11/1997	04/21/1997	03/25/1997		03/03/1997	04/18/1997	04/18/1997
1373N	09/15/1997	09/12/1997		11/07/1997	10/07/1997		11/10/1997	12/22/1997
1374N	05/28/1997	05/20/1997				04/29/1997	09/24/1997	03/06/1998
1392N	02/28/1997	02/28/1997	04/21/1997	03/18/1997		02/24/1997		
1393N	10/24/1997		10/22/1997		10/14/1997	10/16/1997	11/10/1997	
1396N	05/12/1997			05/14/1997		04/30/1997	06/12/1997	
1397N	10/17/1997	09/30/1997			10/07/1997	09/29/1997	11/10/1997	11/10/1997
1408N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1411N	11/14/1997	11/07/1997			10/29/1997	10/29/1997	12/22/1997	12/22/1997
1413N	06/25/1997				10/07/1997	06/09/1997	06/23/1997	
1414N	02/28/1997		04/17/1997	03/18/1997		02/13/1997	04/15/1997	04/15/1997
1426N	12/08/1997				12/12/1997	12/04/1997		02/20/1998
1433N	11/07/1997	11/07/1997			10/21/1997	10/16/1997	11/25/1997	12/22/1997
1440N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1453N	02/06/1998	01/13/1998			01/14/1998		02/12/1998	
1454N	04/27/1998		04/20/1998		04/23/1998		07/09/1998	07/09/1998
1460N	10/22/1997	10/16/1997			10/20/1997	10/08/1997	11/25/1997	12/22/1997
1461N	03/06/1998	02/20/1998	03/30/1998		02/27/1998		05/14/1998	
1474N	06/22/1998	06/18/1998	06/05/1998		06/03/1998	10/08/1998	07/13/1998	
1475N	12/24/1997		01/14/1998		12/19/1997		01/27/1998	
1477N	11/09/1998	10/15/1998			10/13/1998			12/01/1998
1488N	06/20/1997	06/19/1997			06/09/1997	06/02/1997	08/08/1997	
1491N	09/25/1997	09/24/1997			10/07/1997	09/15/1997	11/10/1997	02/12/1998
1519N	01/23/1998				01/06/1998		02/12/1998	
1528N	08/25/1997	08/26/1997			10/07/1997	08/20/1997	09/26/1997	09/26/1997
1547N	01/16/1998		03/30/1998			12/15/1997	02/12/1998	
1548N	01/09/1998	12/29/1997	01/14/1998		12/29/1997	12/19/1997	02/12/1998	
1550N	01/30/1998		03/30/1998		01/21/1998	01/23/1998	04/07/1998	
1562N	06/26/1998	06/22/1998	06/23/1998		06/19/1998	06/19/1998	09/25/1998	
1563N	06/25/1998	06/22/1998	06/23/1998		06/19/1998	06/16/1998	10/27/1998	
1566N	12/19/1997		01/14/1998		12/19/1997	12/10/1997	02/20/1998	
1569N	06/12/1998	06/08/1998	05/19/1998		05/21/1998	05/15/1998	07/13/1998	
1578N	03/10/1998	03/11/1998				03/09/1998	05/14/1998	
1579N	04/17/1998	04/20/1998	04/20/1998		04/20/1998			
1585N	09/15/1998		08/28/1998	11/09/1998	08/31/1998	09/10/1998	10/27/1998	

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1586N	10/20/1998			11/09/1998	10/01/1998			
1589N		12/21/1998						
1602N	11/09/1998	10/15/1998	12/02/1998		10/13/1998			
1603N	07/10/1998	06/17/1998	08/04/1998		06/16/1998	10/08/1998	11/12/1998	
1606N	10/29/1998			11/09/1998	10/13/1998			
1687N	08/31/1998	08/07/1998	08/04/1998	11/09/1998	08/07/1998		10/06/1998	
6094Q	06/27/1997	09/19/1998			10/07/1997	06/13/1997	09/24/1997	09/24/1997
7090E	03/19/1998				04/08/1998			
7437E	08/29/1997	08/26/1997			10/07/1997	08/07/1997	09/24/1997	09/24/1997
7474E	11/26/1997				11/25/1997	11/17/1997	02/12/1998	

Projects in Progress (LOT)

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1001H	12/06/1996	12/02/1996	12/02/1996		12/05/1996	12/23/1996	12/02/1996	12/05/1996
1036N	05/28/1997	05/19/1997	05/21/1997		05/23/1997	05/29/1997		05/28/1997
1077N	09/30/1997	09/19/1997			09/15/1997	09/24/1997	09/11/1997	10/02/1997
1091N	04/30/1997	04/09/1997			04/09/1997	04/14/1997	05/14/1997	04/10/1997
1106N	05/16/1997	05/06/1997		05/13/1997	05/13/1997	05/29/1997	05/14/1997	05/28/1997
1109K	04/28/1997	04/18/1997	04/24/1997	04/24/1997	04/16/1997	04/25/1997	05/14/1997	05/08/1997
1109N	12/27/1996	12/12/1996	01/06/1997		12/16/1996	12/23/1996	12/19/1996	12/10/1996
1133N	10/27/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1155N	10/21/1998	10/05/1998			10/15/1998			10/15/1998
1195N	07/20/1996		07/17/1996		07/19/1996		07/30/1996	07/15/1996
1208K	03/09/1998	03/06/1998	03/20/1998		03/17/1998		04/08/1998	04/03/1998
1223W	04/30/1997	05/05/1997	04/24/1997		04/16/1997		05/14/1997	04/24/1997
1245N	11/27/1996		11/13/1996		11/20/1996		12/02/1996	11/19/1996
1253N	05/16/1997	05/01/1997			05/02/1997	05/29/1997	05/14/1997	06/03/1998
1254N	05/23/1997	04/29/1997			04/29/1997	05/29/1997	05/14/1997	05/08/1997
1272N	08/08/1997	08/12/1997			08/05/1997	08/08/1997	08/08/1997	08/15/1997
1322N	03/11/1997	02/18/1997			03/13/1997	02/27/1997	04/21/1997	02/20/1997
1373N	09/15/1997	08/27/1997			09/04/1997	09/24/1997	09/15/1997	09/22/1997
1374N	05/28/1997	05/01/1997			05/06/1997	05/29/1997	05/14/1997	05/08/1997
1392N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1393N	10/24/1997	10/14/1997			10/15/1997	11/18/1997	12/11/1997	10/16/1997
1396N	05/12/1997	05/05/1997			05/13/1997	05/29/1997	05/14/1997	05/28/1997
1397N	10/17/1997	09/26/1997			10/02/1997	11/19/1997		10/16/1997
1408N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1411N	11/14/1997	10/28/1997	11/13/1997		10/31/1997	11/19/1997	11/10/1997	11/13/1997
1413N	06/25/1997	06/11/1997			06/19/1997	06/10/1997	08/08/1997	06/20/1997
1414N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1426N	12/08/1997	12/03/1997	12/20/1997		12/17/1997	02/12/1998	12/08/1997	12/12/1997
1433N	11/07/1997	10/20/1997	10/28/1997		10/23/1997	11/19/1997	11/10/1997	11/13/1997
1440N	02/06/1998	01/12/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1453N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1454N	04/27/1998	04/20/1998			04/28/1998	05/20/1998		05/11/1998
1460N	10/22/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1461N	03/06/1998	02/20/1998			02/20/1998	05/20/1998	04/08/1998	02/20/1998
1474N	06/22/1998				06/09/1998			06/03/1998
1475N	12/24/1997	12/13/1997	12/19/1997		12/19/1997	02/10/1998	12/29/1997	11/29/1908
1477N	11/09/1998	10/08/1998			10/19/1998		11/10/1997	10/27/1998
1488N	06/20/1997	06/04/1997			06/11/1997	07/11/1997	08/08/1997	06/20/1997
1491N	09/25/1997	09/19/1997			09/25/1997	11/19/1997	09/19/1997	09/22/1997
1519N	01/23/1998	01/07/1998			01/14/1998	05/20/1998	01/21/1998	01/21/1998
1528N	08/25/1997	08/22/1997			08/26/1997	08/21/1997	09/15/1997	09/22/1997
1547N	01/16/1998	12/19/1997			12/19/1997		12/29/1997	01/12/1998
1548N	01/09/1998	01/07/1998			01/14/1998	02/12/1998	12/29/1997	01/12/1998
1550N	01/30/1998	01/16/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1562N	06/26/1998	06/17/1998			06/19/1998			07/07/1998
1563N	06/25/1998	06/17/1998			06/19/1998			07/07/1998
1566N	12/19/1997	12/13/1997	12/19/1997		12/17/1997	02/10/1998	12/29/1997	01/12/1998
1569N	06/12/1998	05/19/1998			06/03/1998	05/20/1998		06/08/1998
1578N	03/10/1998	03/10/1998			03/17/1998		04/08/1998	04/03/1998
1579N	04/17/1998	04/13/1998	04/28/1998			05/20/1998		04/16/1998
1585N	09/15/1998		08/31/1998		09/15/1998			09/11/1998
1586N	10/20/1998	09/28/1998			10/06/1998			10/15/1998
1589N		12/11/1998	12/14/1998	12/16/1998	12/17/1998			
1602N	11/09/1998	10/08/1998			10/19/1998			10/27/1998
1603N	07/10/1998	06/15/1998			06/19/1998			07/07/1998

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1606N	10/29/1998	10/05/1998			10/06/1998			10/15/1998
1687N	08/31/1998	08/24/1998			08/13/1998			08/25/1998
6094Q	06/27/1997	06/27/1997			06/12/1997			
7090E	03/19/1998				03/24/1998		04/08/1998	04/03/1998
7437E	08/29/1997	08/06/1997			08/12/1997	08/08/1997	08/08/1997	08/26/1997
7474E	11/26/1997	11/25/1997	12/03/1997		12/01/1997	02/12/1998	12/12/1997	12/12/1997

SAN FRANCISCO
DPT
DEPARTMENT OF PARKING & TRAFFIC
Traffic Engineering Division
City and County of San Francisco

WILLIE LEWIS BROWN, JR., MAYOR
STUART R. SUNSHINE, EXECUTIVE DIRECTOR

FAX DISTRIBUTION LIST FOR UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS CALENDAR

JOHN BANNER, CITY TOW
JOHN BUSHER, DPW, BUREAU OF ENVIRONMENTAL SERVICES
AMY CHOW, DPW, PROJECT DEVELOPMENT SECTION
ADRIENNE FRAZIER, DPT, OPERATIONS
PETE HOWES, SFFD, EMS
WALTER HOO, DPW/BSM
CAPTAIN LI, SFFD, BUREAU OF FIRE PREVENTION AND INSPECTION
RICHARD SKAFF, DPW, DISABILITY ACCESS COORDINATOR
ANNA WONG, DPW, PUBLIC RELATIONS
ALISON HOOD, GGNRA, SPECIAL EVENTS OFFICE
MARIA TRAPALIS-BAIRD, MAYOR'S OFFICE OF RECYCLING
VIRGINIA RICHARDSON, PARK & REC
LEO PIERINI, STATE PAROLE DIVISION
JEFF BAUER, PORT OF SAN FRANCISCO
LT. JACK BALLENTINE, SFPD, FILM COORDINATOR
BILL WEBB, DPW, BCM
LYNNE PITTMAN, PRESS OFFICER, DPT
SHEILAH TUCKER, TRAVINFO
LAMONT DEBARBIE, FLYING DUTCHMAN

This list is a summary of the various street closures for special events which have been approved by the Interdepartmental Staff Committee on Traffic and Transportation (ISCOTT). I have also included other events which may impact traffic on City streets when I know of them. If you would like more details about any of the events, please give me a call at 415-554-2341. This list may not include events which have been permitted by the Port of San Francisco, Golden Gate National Recreational Area, or the Recreation & Park Department. If you know of other events which should be listed, please let me know. I have added a Temporary Street Closures for Special Events database on DPT's web page. Closures may be searched by date, event name and street name. You may find more detailed information about the events through this database. Our web site address is www.ci.sf.ca.us/dpt.

Cindy Shamban
Traffic Survey Technician

c:\myfiles\faxtecit.198

UPCOMING STREET CLOSURES

EVENT	START DATE	END DATE	TYPE	STREETS	OK	DENIED
DEDICATION OF SYNAGOGUE B	12/19/98	12/19/98		DOLORES (S/B ONLY): 15TH TO 16TH	11/12/98	
FILM SHOOT: THE BACHELORS	12/19/98	12/19/98	FILM	LEIDESDORFF: CA TO PIN	12/1/98	
TOY GIVEAWAY	12/19/98	12/19/98		JONES: TURK TO EDDY	10/22/98	
FILM SHOOT "THE BACHELORS"	12/20/98	12/20/98	FILM	PINE: FRONT TO DAVIS (RAIN DATE)		
FILM SHOOT: THE BACHELORS	12/20/98	12/20/98	FILM	BAT: SAC TO CA (6A TO 10A ONLY)	12/1/98	
49'ERS VS ST. LOUIS	12/27/98	12/27/98		CANDLESTICK (1 PM)		
BGP: NEW YEAR'S EVE	12/28/98	1/2/99		GROVE: LARKIN TO POLK	12/17/98	
BGP: NEW YEAR'S EVE	12/30/98	1/1/99		POK & LAR: GRO TO HAY parking lanes onl	12/17/98	
BGP: NEW YEAR'S EVE	12/30/98	1/1/99		POLK: MOST EASTERLY LANE ONLY	12/17/98	
UNION SQ. NEW YEAR'S EVE	12/31/98	1/1/99		STREETS SURROUNDING UNION SQ. 6PM		
FILM SHOOT "NASH BRIDGES"	1/4/99	1/5/99	FILM	FOL (WB ONLY) 11TH TO 12TH		
FILM SHOOT "NASH BRIDGES"	1/5/99	1/5/99	FILM	PERRY: 2ND TO 4TH (NO INTERSECTIONS		
FILM SHOOT "NASH BRIDGES"	1/5/99	1/5/99	FILM	ZOE: BRANNAN TO BRYANT		
FILM SHOOT "NASH BRIDGES"	1/6/99	1/6/99	FILM	PERRY: 2ND TO 4TH (NO INTERSECTIONS		
SF BALLET GRAND OPENING SE	1/18/99	1/29/99		FRA (E/S parking lane only): FUL to MCA	11/12/98	
SF BALLET GRAND OPENING GA	1/25/99	1/25/99				
S.F. HALF MARATHON	1/31/99	1/31/99	ATHLET	VARIOUS LOCATIONS: GGP AREA	11/12/98	
FLOWER STREET FAIR	2/12/99	2/14/99	FAIR	GRA:WAS TO BWD;PAC:COL TO STO ETC	9/24/98	
CHINESE NEW YEAR CARNIVAL	2/13/99	3/1/99		WALTER LUM PL.: WAS TO CLAY	11/12/98	
VIETNAMESE NEW YEAR'S CELE	2/14/99	2/14/99	FAIR	ELLIS: HYD TO POK; LAR:EDY TO OFA		
COMMUNITY STREET FAIR	2/26/99	2/28/99	FAIR	GRA:CLA TO BWD; PAC:STO TO COL ETC	9/24/98	
CHINESE NEW YEAR PARADE	2/27/99	2/27/99	PARADE	MKT:2ND TO STO;ETC		
HOULIHAN'S TO HOULIHAN'S	3/28/99	3/28/99	ATHLET	V ARIOUS LOCATIONS	9/24/98	
SISTERS OF P.I. BIRTHDAY BASI	4/4/99	4/4/99		CASTRO:18TH TO MARKET		
CHERRY BLOSSOM FESTIVAL	4/17/99	4/18/99	FAIR	POST: LAG TO FLM; WEB: GEA TO SUT		
SF INTERNATIONAL TRIATHLON	4/18/99	4/18/99	ATHLET	VARIOUS LOCATIONS: G.HWY, EL CAMINO	10/22/98	
CHERRY BLOSSOM FESTIVAL	4/24/99	4/25/99	FAIR	POST: LAG TO FLM; WEB: GEA TO SUT		
CHERRY BLOSSOM PARADE	4/25/99	4/25/99	PARADE	CIVIC CENTER TO POLK TO POST		
CALIFORNIA MILLE	4/25/99	4/26/99		MASON: CALIFORNIA TO SACRAMENTO	12/17/98	
CARNAVAL	5/29/99	5/30/99	FAIR	VARIOUS LOCATIONS: MISSION DISTRICT		
CARNAVAL PARADE	5/30/99	5/30/99	PARADE	24TH ST TO MISSION TO 14TH ST TO HAR		
ESCAPE FROM ALCATRAZ	6/5/99	6/5/99	ATHLET	VARIOUS LOCATIONS	7/23/98	
BLACK & WHITE BALL	6/5/99	6/6/99		VAN NESS: GRO TO MCA; ETC.		
SPCA ANIMAL WINGDING	6/5/99	6/6/99	FAIR	ALA:15 TO 17; FLA:15 TO 17; ETC	12/17/98	
UNION STREET ARTS FESTIVAL	6/5/99	6/6/99	FAIR	UN: GOU TO STEINER ETC.	12/17/98	
CA AIDS RIDE	6/6/99	6/6/99		VARIOUS LOCATIONS		
NORTH BEACH FESTIVAL	6/12/99	6/13/99		GRA:COL TO FIL;VJO&GRE:COL TO GRA		
HAIGHT STREET FAIR	6/13/99	6/13/99	FAIR	HAIGHT : MASONIC TO STANYAN ETC	11/13/98	
EXTREME GAMES	6/23/99	7/3/99		PIER 30-32		
GAY PRIDE CELEBRATION	6/26/99	6/27/99	FAIR	CIVIC CENTER AREA		
PINK SATURDAY	6/26/99	6/27/99		CAS:18TH TO MKT; 18TH: HFD TO CWD		
SF GAY DAY PARADE	6/27/99	6/27/99	PARADE	MKT: SPEAR TO CIVIC CENTER		
CHRONICLE'S 4TH OF JULY	7/3/99	7/4/99	FAIR	VARIOUS LOCATIONS: WHARF AREA	12/17/98	
JAZZ & ALL THAT ART ON FILLM	7/3/99	7/4/99	FAIR	FLM: JACKSON TO POST ETC.		

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, AIA, Director and City Architect

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

UNDERGROUND PLANNING MEETING

MEETING DATE: December 1, 1998

PRESENT:

Tom Trimbur	-	DPW/BSM	(554-6167)
John Fadeff	-	DPW/BSM	(554-5830)
Terry Bouey	-	TCI	(863-8500)
Carlos DeAnda	-	PG&E	(330-2138)
Cindy Vowell	-	PacBell	(542-9095)
José Saldaña	-	PG&E	(330-2249)
Don Hendricks	-	PG&E	(695-3394)
Scot Burbank	-	DPW/PMD	(558-4046)

DISCUSSION:

A. PROJECT STATUS

1. UGD 318 - DOLORES HEIGHTS DISTRICT

Dorland/Dolores Terrace – PacBell has another appointment with owner of 32 Dorland for hook-up. If that goes forward, poles could be removed in 3 weeks.

PHASE 2 – Project on target for beginning construction after the New Year. Only about 20-25 properties have not had work completed. Work to begin at 18th and Dolores to make gas main connection. In all, there will be 24 blocks of gas work; only 12 will have undergrounding.

2. UGD 310 - PRESIDIO HEIGHTS

PHASE 2 – Contractor trenching on Walnut near Sacramento. Five to six weeks of trenching work to complete. Lighting equipment has arrived. Approximately 6 properties, mainly on the 300 block of Laurel, have not had work completed.

California St. – Package to bid in mid-December and construction to begin after holidays.

3. UGD 320 - BREWSTER/JOY

Hearing held to begin abatement process for 316 Holladay and 124 Brewster. Work seems to be progressing on all properties except 316 Holladay, even though the work on that property seems to be minimal. City to proceed with abatement after the holidays.

4. UGD 321 - INDIANA STREET/ISLAIS CREEK & UGD 323 - CESAR CHAVEZ

On December 13 the freeway off-ramp will be closed for the removal of the overhead lines there and the train tracks. The major concern is Caltrain. PG&E to contact Caltrain to ascertain status. City may intervene politically if no movement evident.

5. UGD 324 - DUBOCE AVENUE

Overhead wires removed. Poles to be removed when work on and equipment for mural completed. Water finding its way into PG&E manhole being tested to see if it contains sewage. If so, City sewer folks to find source and repair.

6. UGD 311 - CORBETT AVENUE - PEMBERTON STAIRWAY

No word from BOE on progress. Landscape needs to provide schedule. Mr. Trimbur to send memo to MUNI regarding replacement of wooden poles along Clayton with new metal trolley poles. Existing streetlighting system to remain.

7. UGD 335 - UPPER FOLSOM

PG&E continuing to work up the hill to the south from Precita. Although City sent second letter to property owners, owner participation remains low. Some owners have requested additional names of contractors, saying that they cannot get bids. Mr. DeAnda stated that contractors may be less willing to visit some areas that are not perceived as wealthy because their profits would not be as high.

B. OTHER BUSINESS

1. Mr. Burbank inquired as to status of PG&E work on Clay east from Van Ness to the Bay. DPW will be paving 22 blocks in the spring.

2. Mr. DeAnda stated that PG&E will be ready for Inner Sunset 1 in April. Mr. Trimbur stated that the City will send a letter in January regarding a community meeting. The letter will include owner responsibilities.

THE NEXT MEETING WILL BE HELD ON TUESDAY, 5 JANUARY 1999, AT 9:00 A.M. AT 875 STEVENSON STREET, ROOM 460, BSM CONFERENCE ROOM.

cc: All Attendees
CULCOP - through Joe Norris
Ray Gigliati - BSM
Hin Lok Kung - BOE
Jack Donohoe - DET
Barbara Moy - BSM
Manfred Wong - CWP
Lynn Bunim - PacTel
Norman Chan - BOE
Dee Lemmon - BLHP
Lesley Wong - BOE/S&H
Patricia Healy - PG&E
Dave Bradley - PG&E
Amy Chow - PDS
Charles Yu - BOE/S&H
Amy Powell- DHIC
Brian Christiansen - Duboce
Carlos DeAnda - PG&E
Lynn Nakasato - BOE/S&H
Cynthia Chono - BSM
Ray Yamagishi - BLHP
Tom Flahavan - DET
Joe Ovadia - PMD
Kathy Devine - PG&E
Louis Victorio – TCI
John Katz - MUNI
Sam Lauter - PG&E
Carol Finucane - BOE
Don Stroh - DHIC
Brian Gatter - BOE/Landscape
Terry Bouey - TCI
Bob Striech - PG&E
Joe Marino - DHIC
Terry Elisaia - DET
Naoki Kaku - BOE
Richard Hong - PG&E
Ben Cruz – BOE

C:\My Documents\MEET12~1.DOC

CITY AND COUNTY OF SAN FRANCISCO
PUBLIC UTILITIES COMMISSION
UTILITIES ENGINEERING BUREAU

WILLIE L. BROWN, JR.
MAYOR

ANSON B. MORAN
GENERAL MANAGER

ANN MOLLER CAEN
PRESIDENT
DEPARTMENT
ROBERT K. WERBE
VICE PRESIDENT
E. DENNIS NORMANDY
VICTOR G. MAKRAS
FRANK L. COOK

SAN FRANCISCO
WATER

HETCH HETCHY
WATER AND POWER

SAN FRANCISCO
CLEAN WATER PROGRAM

RECEIVED
NOV 17 PM 12:40
PROJECT DEVELOPMENT

RECEIVED
98 NOV 19 AM 11:29
PROJECT DEVELOPMENT

Jor
please
outn
1. Sewer 5 yr plan
2. Sewer
TV → REL

TO: Vit Troyan Amy
SCCC

DATE: October 29, 1998

FROM: W Keaney W Kea
Manager, WPCD

RE: 5 year plan for Sewer Projects

We are hereby transmitting our 5 year plan of proposed sewer replacement projects. As discussed during the meeting last week, new emergency projects will take precedence over scheduled projects. Therefore, the schedule may change depending on the number of emergency projects. Additionally, MUNI's 3rd Street light rail project will require sewer relocations. This project is currently under study. Sewers recommended to MUNI for relocation will be included in the MUNI overall projects.

If you have any further questions regarding this memo please call Norman Chan at 554-8355 or Jim Walsh at 554-8272.

cc: N. Chan
A. Halstead
J. Walsh
C. O'neil

RECEIVED
NOV 16 1998
DEPUTY DIRECTOR PUBLIC SERVICES

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	P[illegible]'D PAVE DATE	PROJ. COST (000)
		SEW=SEWER										MF=Mill & Fill		
		S&H=STREETS AND HIGHWAYS						?	= Exact year of construction not known			OL=Overlay		
	FY 98-99											TR=Track Removval		-
1615N		SEW	1998	Jackson	Montgomery	Columbus	1876	?	4 x 6	BRICK	Bad shape, out of round, crown sagging	RE=Reconstructio		100
1615N		SEW	1998	Columbus	Jackson	Pacific	1900	?	16"/18"	CP/BRICK				100
1615N		SEW	1998	Kearny	Jackson	Pacific	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1615N		SEW	1998	Kearny	Jackson	Washington	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1619N		SEW	1998	60 Scenic Way Easement Sewer (Assessor's Block 1303)					8"	VCP	Cracks and collpased sections			50
1621N		SEW	1998	Anza	7th Ave	8th Ave	1908	?	2'6"x3'9	BRICK	Cracks and collpased sections			162
1622N		SEW	1998	3rd St	Jerrold	Kirkwood			18"	VCP	Many cracks, collapsing sections			250
1622N		SEW	1998	3rd St	Kirkwood	LaSalle			42"	CONC	Re-alignment			250
1622N		SEW	1998	3rd St	LaSalle	McKinnon			42"	CONC	Re-alignment			250
1622N		SEW	1998	3rd St	McKinnon	Newcomb			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998	3rd St	Newcomb	Oakdale			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998	3rd St	Oakdale	Palou			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998	Donner	Jennings	Ingalls			15"	ISP	Hydraulically inadequate sewer			250
1622N		SEW	1998	Jennings	Egbert	Donner			N/A		Hydraulically inadequate sewer			250
1623N		SEW	1998	Green	Polk	Van Ness	1890	?	16"	VCP				150
1218N	BSSR	SEW	1998	Harrison	5th St	Morris	1935		12/18/21	VCP	Severe cracks, many dips/debris restrict flow	MF	3/98	230
1433N		SEW	1998	Shotwell	26th St	Army St	1890	?	15"	VCP	Street Pavement & Sewer Collapsed			99
1433N	....N	SEW	1998	Moultrie	Eugenia	Cortland	1915	?	10"	VCP	Broken pipe, cracks, infiltration			111
1433N	....N	SEW	1998	26th St	Dolores	Church	1885		15"	VCP	Many medium & minor cracks, severe grout	MF		205
1432N	....N	SEW	1998	Post	Baker	Broderick	1900		18"	VCP	Joints open throughout, open ss, sand infiltration	MF	1/01	162
1432N	....N	SEW	1998	Post	Broderick	Divisadero	1900		18"	VCP	Collapsed @ 84-97' c-d, cracks @ 10-31'b-c	MF	1/01	162
1330N		SEW	1998	09th St	Harrison	McLea Ct MB	1900	?	24"	VCP	Crushed pipe @ 194-208, full of debris,dip			90
1547N	BSSR	SEW	1998	33rd Ave	Irving	Judah	1925	?	12"	ISP	Many St depressions, severe offsets, breaks @ ss's	MF	3/98	159
1547N		SEW	1998	Lyon	Hayes	Grove	1888		16"	ISP	Many St depressions, open joints, cracks, breaks; c-b			77
1547N		SEW	1998	Molimo	Bella Vista	Intersection	1946	?	12"/15"	VCP	Collapsed & crushed section @ 21'	MF		19
1569N		SEW	1998	Dolores	16th St	17th St	1889	?	18"	VCP	Egg shaped, Multiple cracks @ invert			168
1569N		SEW	1998	York	21st St	22nd St	1888		10"	VCP	Collapsed sections			135
1625N	1385N	JP/S&H	1998	Lombard	Leavenworth	Jones	1900	?	18"	ISP	Cracks, open joints, fast flow	RE	Jul-98	
1491N	BSSR	SEW	1998	Pacific	Stockton	Grant	1876		3'x5'	BRICK	Fairly bad shape, out of round, missing mortar	MF	1/98	134
1426N	BSSR	SEW	1998	Clinton Park	Guerrero	Valencia	1878		12"	ISP	Offsets, infiltration, many depressions	MF	7/98	139
1426N	....N	SEW	1998	Valencia	15th St	16th St	1890	?	3x5	BRICK	Bad shape, collapsed @ 447 Valencia			418
1426N		SEW	1998	Dore	Bryant	Harrison	1912	?	16"	VCP	Many cracks, offsets, dip, street depressions			140
1503N		SEW	1998	10th Ave	Kirkham	Judah MB	1902		12"	VCP	Cracked sections and many offsets b-c			75
1503N		SEW	1998	10th Ave	Pacheco	Ortega MB	1906	?	12"	ISP	Severe offsets, depressions, fast flow, worn invert			75
1461N	BSSR	SEW	1998	Mason	Ellis St.	Eddy St.	1880	?	3x5	BRICK	Severly deformed crown,missing bricks	OL		95
1461N	....N	SEW	1998	Pine	Hyde	Leavenworth	1880	?	3x5	BRICK	Fairly bad shape (oval), 3 broken s/s			280
1461N	1227N	SEW	1998	Leavenworth	O'Farrell	Geary	1900	?	3x5	BRICK	Bad shape	MF	7/99	221
1461N		SEW	1998	Meacham	Post	End: South		?	8"	VCP	Severe cracks and damaged ss connections			60
1488N		SEW	1998	California	10th Ave	11th Ave	1900	?	8"	VCP	St. depression; crushed / collapsed			65

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1488N		SEW	1998	24th Ave	California	Clement MB	1907		8"	ISP	Cracks, breaks, dip, street depressions			100
1550N		SEW	1998	Day St	Dolores	San Jose	1888		18"	ISP	Collapsed pipe			70
1550N		SEW	1998	Congo	Monterey	Hearst	1910	?	12"	VCP	Multiple cracks, st dep @ 147-159' b-c, infiltration			72
1550N	BSSR	SEW	1998	Congo	Melrose	Mangels	1910		8"	VCP	Many cracks over the block	OL		60
1550N	BSSR	SEW	1998	Marston	Circular	Edna	1910		8"	ISP	Many severe cracks	MF		114
1550N	BSSR	SEW	1998	Cuvier	Bosworth MB (m	Mirando (mhE)	1902		15"	VCP	Multiple cracks & egg shape @ 64-140' d-e	MF		90
1550N		SEW	1998	28th St	Noe	East Xing	1900	?	15"	VCP	Bad open joints @20-50'			139
1562N	....N	SEW	1998	Broadway	Taylor	Himmelmann	1952		16"	VCP	Collapsed & Crushed	RE	1/99	56
1562N	....N	SEW	1998	Broadway	Florence	Taylor	1900	?	12"	VCP	Crushed invert, mult cracks	RE	1/99	63
1562N	....N	SEW	1998	Broadway(N Sid	Cyrus Pl	Hyde MB	1952		21"	VCP	Mult cracks, ready to collapse a-b	MF	1/99	54
1562N		SEW	1998	Bryant	18th St	19th St	1889		14"	VCP	Many cracks; pipe collapses			108
1562N		SEW	1998	Sonoma	Union	Green		?	12/15"	VCP	Crushed,broken pipe, ready to collapse			75
1566N	1459N	JP/S&H	1998	Fillmore	Jackson	Washington	1900	?	12"	VCP	Continuous multiple cracks and offsets	RE	5/98	90
1566N	1459N	JP/S&H	1998	Fillmore	Pacific	Jackson	1888		16"	ISP	Multiple, continuous cracked sections	RE	5/98	92
1253N	1091N	SEW	1998	12th St	Folsom	Harrison	1875		3x5	BRICK	Bad shape, missing bricks, broken ss	TR/JP	9/97	370
1254N	....N	SEW	1998	11th St	Folsom	Harrison	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			360
1603N		SEW	1998	Broad	Capitol	Plymouth	1910	?	8"	ISP	Many depressions, complaints, MUNI track replmt			215
7474E	BSSR	SEW	1998	Delancey (1st St)	Townsend	Brannan	?		12"/15"	VCP	Collapsed sections	MO		207
7474E		SEW	1998	Pine	Battery	Front	1907		18"	ISP	Collapsed, Cracks			86
7474E	1407N	SEW	1998	California	Webster	Buchanan	1880	?	15"	CEM	Offsets, hole @ 104',open joints st depressions	MF	1/1/01	142
7474E	1407N	SEW	1998	California	Laguna	Buchanan	1876	?	16"	CEM	TV'd 35', Collapsed	MF	1/1/01	323
1392N	1108N	JP/S&H	1998	Bayshore E	Oakdale MB	Jerrold	1928		15"/12"	VCP	Cracked (replace a-c), dip, debris	MF	1/98	75
1392N	1108N	JP/S&H	1998	Bayshore E	Oakdale	Jerrold MB	1928		15"/12"	VCP	Cracked (replace a-e), damaged @ 3' e-f	MF	1/98	178
1393N		SEW	1998	Bush	Kearny	Montgomery	1880	?	3x5	BRICK	Fairly bad shape,bricks, plastering			250
1393N	1453N	SEW	1998	Kearny	Sutter	Bush	1890	?	3x5	BRICK	Fairly bad shape, loose bricks	OL	10/98	208
1393N	BSSR	SEW	1998	Post	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, missing & loose bricks	MF		274
1393N	1453N	SEW	1998	Kearny	Sutter	Post	1875	?	3x5	BRICK	Bad shape, debris, crown sagging	MF	10/98	77
1393N	....N	SEW	1998	Sutter	Montgomery	Intersection	1876	?	3x5	BRICK	Intersection in bad shape	MF	1/1/01	50
1393N		SEW	1998	Bush	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, crown sagging			115
1397N	....N	SEW	1998	Ord	Corbett	Market	1900	?	15"	VCP	Cracks, cracked invert, severe offsets	MF		43
1397N	7317E	SEW	1998	Dolores	28th St	Valley	1885	?	18"	VCP	Crushed and multiple cracks	MF/JP		89
1397N	BSSR	SEW	1998	23rd St	Castro	Diamond	1888	?	15"	VCP	Severe cracks @ 25-70', heavy debris, dip	MF		180
1411N		SEW	1998	Harding Park	Skyline	Zoo					New Sewer			
1413N	6094Q	S&H	1998	Davis (Blk #200	Clay	Washington	1878	?	3x5	BRICK	Bad shape, debris, missing bricks & mortar	RE/JP		167
1413N	BSSR	SEW	1998	Francisco	Stockton	Powell	1876	?	3x5	BRICK	Bad shape 1/2, fairly bad shape 1/2	MF		290
1413N	1453N	SEW	1998	Kearny	Green	Union	1900	?	12/8"	VCP	Crushed & cracked sections	MF	10/98	99
1474N	BSSR	SEW	1998	43rd Ave	Anza St	Balboa MB	1917	?	15"	VCP	Many cracks @ mh b-c exfiltration @ 120' b-c	OL		95
1474N	....N	SEW	1998	08th Ave	Fulton	Cabrillo	1907	?	8"	VCP	Numerous cracked sections, collapse			168
1474N	BSSR	SEW	1998	06th Ave	Cabrillo	Balboa	1902	?	12"	VCP	Many cracked sections; sev. open joints., bad ss & mh	MF		133
1474N	BSSR	SEW	1998	06th Ave	Fulton	Cabrillo	1907	?	8"	ISP	Many cracked sections, hole (repair done 1/12/96)	MF		168
1548N	....N	SEW	1998	O'Farrell	Anza Vista	Masonic	1947		15"	VCP	Numerous cracks			140
1548N	BSSR	SEW	1998	Deming	Clayton MB	Uranus	1920		12"	ISP	Ready to collapse	OL		105

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	P[illegible]D PAVE DATE	PROJ. COST (000)
1548N		SEW	1998	Iron Alley	Corbett	Clayton	1917	?	15"	VCP	Offsets, roots, Hole invert @ 140' b-c			129
1548N		SEW	1998	Farnsworth	Edgewood	Willard		?	12"	VCP	Severe cracks, stopped @ 83'; recommend lining			67
1579N	1454N	JP/S&H	1998	Illinois	20th St	19th St	1910	?	18"	VCP	Multi cracked, crushed sections b-c; TV'd 60' b-c	TR	5/98	132
1475N	1389N	JP/S&H	1998	Virginia	Coleridge	Mission St	1905	?	16"	VCP	BSSR RECOMMENDED REPLACEMENT			85
1475N	1389N	JP/S&H	1998	Fair St	Coleridge	Mission	1890		12"	VCP	Mult joint offsets,cracks, infiltration, st. depression		1/99	90
1475N	1389N	JP/S&H	1998	Godeus	Coleridge MB	Mission		?	15"	VCP	Cracks/crush @123'-145'; cracks; open joints b-c	MF	1/99	70
1563N	BSSR	SEW	1998	42nd Ave	Geary	Anza	1920	?	8"	VCP	Street depression, collapse; sev. open joints	MF		145
1563N	....N	SEW	1998	Balboa	Arguello	2nd Ave	1907	?	18"	ISP	Multiple cracks			107
1563N	BSSR	SEW	1998	03rd Ave	Balboa	Anza	1908	?	8"	VCP	Many street dep.; many cracks/holes ms/ss	MF		158
1563N		SEW	1998	20th Ave	Fulton	Cabrillo	1915		8"	ISP	Numerous street depressions			135
	98-99 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)													4,000
1626N		SEW	1999	05th Ave	Irving	Lincoln	1900	?	12"	ISP	Many cracks; repair @109', 242'			
1626N		SEW	1999	04th Ave	Lincoln	Hugo								
1626N		SEW	1999	Stanyan (west sid	Turk	Anza								
1626N		SEW	1999	Paris	Brazil	Excelsior								
	BSSR		1999	Kate	End South	Bryant	1900	?	16"	VCP	Severe cracks 162-170' b-a; TV'd 13' b-c, offset			
1606N	BSSR	SEW	1999	Douglass	23rd St	Elizabeth	1890	?	15"	VCP	Severe offsets, separated ss's, st depn	OL		111
1606N		SEW	1999	Cayuga	Seneca	Junior Terr	1939		8"	VCP	Many offsets, large street depressions, infiltration			50
1606N		SEW	1999	Laurel	Washington	Jackson	1900	?	12"	CP	Multiple severe offsets, street depressions			86
1606N		SEW	1999	Rondel Pl	End S(17th St)	16th St	1890	?	12"	ISP	Crushed, multi-cracked sections, severe offsets			138
			1999	Bertita	Seneca	end			8"	VCP	Street collapsing (field check) several bad sections			
1155N		SEW	1999	Chestnut	Culebra	Polk	1913		12"	ISP	Numerous Cracks, Collapsed Pipe			68
1155N		SEW	1999	Chestnut	Powell	Stockton	1890		16"	CEM	Cracks, invert erosion			140
1155N		SEW	1999	Grant	Chestnut	Francisco	1918	?	14"	VCP	Offsets, Crushed Pipe, Debris			99
1155N		SEW	1999	Grant	Greenwich	Lombard	1918	?	16"	VCP	Cracks, Dip, Cement Pipe			107
1218N?		SEW	1999	Market S. Side	9th Street	10th Street	1878		3x5	BRICK	Ready to collapse			353
START FY 99-00														
1218N?	....N	SEW	1999	Larkin	Golden Gate	McAllister	1874		18"	VCP	Collapsed, continuous cracks	MF		109
		SEW	1999	Eugenia	Prospect	Coleridge	1920	?	12"	ISP	Severe offsets, breaks, bad ss, rat, street depressions			
1578N	1668N	JP/S&H	1999	Golden Gate	Polk St	Van Ness	1873		3'x5'	BRICK	Many St. depressions, Rec. by BSSR	MF	6/99	146
1578N	W-2240	JP/WD	1999	Golden Gate	Scott MB	Pierce	1875		14"	ISP/CP	Cement pipe sections, badly cracked	MF	6/99	80
1628N		S&H	1999	Moraga St	17th Ave	18th Ave								
1583N		SEW	1999	Everglade	Gellert	Lake Merced		?	21"	VCP	Easement;collapsed @ 30-40' a -b; exfiltration(line?)			49
1583N	....N	SEW	1999	Victoria	Randolph	Brotherhood	1920	?	12"	ISP	Open break @112-115', cont. cracks, mh b-c			163
1583N	.......N	SEW	1999	Revere	Griffith	Hawes MB	1930		8"	VCP	Many severe cracks/crushed mh b-c	RE		70
1583N		SEW	1999	Bridgeview	Topeka	Thornton	1941		12"	VCP	Many cracks & ss problems, invert break			185
1395N		SEW	1999	Sacramento	Grant	Kearny	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			274
1395N		SEW	1999	Larkin	Pine	Bush	1875	?	3x5	BRICK	Bad shape, many loose bricks			208
1395N	1453N	SEW	1999	Sacramento	Sansome	Battery	1908		12"	ISP	Many cracks, crushed sections, debris	MF	10/98	80
1395N	....N	SEW	1999	Pine	Polk	Larkin	1880	?	3x5	BRICK	Fairly bad shape (230'), st. depression			280
		SEW	1999	Cesar Chavez (A	Bryant	York		?	12"	VCP	Many cracks and collapsed sections			60
		SEW	1999	Folsom	Bessie	Precita	1890	?	16"	VCP	Collapsed sections, severe offsets,open ss, fast flow			39

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
	....N	SEW	1999	Larkin	Grove	Hayes	1915		18"	VCP	TV'd 190', collapsed, dip, debris			92
		SEW	1999	Winding Way	Prague	Xing	1915	?	8"	VCP	Collapsed & crushed pipe, exfiltration			30
	6094Q	S&H	1999	Embarcadero	Broadway	Jackson MB		?	12"	VCP	Abandoned in Mid-Embarcadero project	RE	3/98	124
1585N	BSSR	SEW	1999	05th Ave	Balboa	Anza	1908	?	16"	VCP	Severe cracks, depn @ 8-37 c-b, many separated ss	MF		166
1585N		SEW	1999	21st Ave	Clement	California	1902	?	8"	VCP	Severe offsets,Separated ss's, st. depressions			122
1585N	1407N	SEW	1999	California	Parker	Maple	1900	?	16"	VCP	Severe open joints, st. depression; Lining rec.	MF	1/1/00	30
1586N	.....N	SEW	1999	Geary Bl. S. Side	Lyon	Baker	1879		18"	VCP	Severe multi cracks, fast flow, begin to collapse	MF		151
1586N	.....N	SEW	1999	Geary Bl. S. Side	Baker	Broderick	1879	?	18"	VCP	Multi cracks, roots, fast flow	MF		138
1586N	1732N	SEW	1999	Turk	Broderick	Divisadero	1881		16"	ISP	Cracks, collapsed section	MF	7/99	152
	99-00 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)													4,000
1586N	....N	SEW	2000	Eddy	Pierce	Steiner	1875		3x5	BRICK	Bad shape (50'), rest needs plastering	MF		280
1586N		SEW	2000	Elm	Scott MB	Pierce	1908	?	15"	ISP	Egg shape cracks & offsets			55
1587N		SEW	2000	07th Ave	Moraga	Lincoln	1890	?	3'x5'	Conc/Br	Fairly bad shape; Install spray-on mortar lining.			100
1587N	....N	SEW	2000	Kirkham	6th Ave MB	7th Ave	1906		18"	VCP	43 foot run with cracks throughout			107
1590N	7291E	SEW	2000	Ocean	San Leandro	San Fernando	1913		15"	VCP	Many severe cracks @ 1-90' a-b	MO	4/99	40
1590N	7291E	SEW	2000	Ocean	San Fernando	Junipero Serra	1913		18"	VCP	Severe Offsets & many cracked sections	MO	4/99	40
1590N	7291E	SEW	2000	Ocean	Pinehurst	Manor	1913		18"	VCP	Many cracked sections	MO	4/99	56
1589N		SEW	2000	Clipper	Douglass	Diamond MB	1962		15"	VCP	No TV Log; Many large cracks invert, exfiltration; fast flow			82
1589N	....N	SEW	2000	Noe	26th St.	Clipper MB	1888		18"	VCP	Cracks throughout, 33' run(debris)			101
1589N	BSSR	SEW	2000	Fair Oaks	22nd St	23rd St	1878		15"	ISP	Submerged, pipe coming apart. Rec by PUC	MF		144
1589N		SEW	2000	Kingston	Mission	San Jose	1910	?	12"	VCP	Many cracks , dip, size changed to 6"			40
1588N		SEW	2000	Joost	Acadia	Brompton	1926	?	12"	ISP	Many open joints, infiltration, street depresions			150
1588N	6680E	S&H	2000	Alemany	Prentiss	Putnam		?	12"	VCP	Badly crushed pipe	MF		110
START FY 00-01														
1588N	BSSR	SEW	2000	Mt Vernon	Delano	Cayuga	1927		12"	VCP	Crushed sections @ 88-103' a-b; st. depression	MF		81
1588N		SEW	2000	Kensington	Merced	Claremont	1915		12"	VCP	Replace mh a-b, otherwise fair condition			100
1602N	BSSR	SEW	2000	Minna	6th St	Russ	1908	?	18"	VCP	Cracked invert @ 76-78' c-d, st depressions	MF		112
1602N	....N	SEW	2000	02nd St	Brannan	Townsend	1890	?	18"	VCP	Many cracks / replace lower 1/2 block			160
1602N		SEW	2000	Howard	01st St	Fremont	1880	?	3'x5'	BRICK	Bad shape, needs cleaning, plaster and bricks	MF		100
1605N	BSSR	SEW	2000	Sacramento	Spruce	Maple	1890	?	8"	ISP	Many seaprated ss's; infiltration	MF		110
1605N	BSSR	SEW	2000	Pierce	Green MB	Union	1885		18"	VCP	May collapse @219'-238', 0-110' replaced	MF		96
1605N	....N	SEW	2000	Wilmot	Webster	Fillmore	1900	?	10"	ISP/CP	Multiple extensive cracks/ cement pipe			120
1629N	1734N	SEW	2000	Union	Hyde	Larkin	1900	?	12"/18"	ISP	Crushed invert; multiple cracks, exfiltration	MF	7/99	115
1629N	......N	SEW	2000	Union	Hyde	Leavenworth	1900	?	8"/15"	ISP	3pt cracks, errosion of cement pipe sections, hole	OL	1/99	51
		SEW	2000	Union	Divisadero	Broderick	1885	?	8"/12"	VCP	Cracks/collapse, offsets, open joints		done 4/95	125
	......N	SEW	2000	Union	Jones St	Taylor St	1900		16"	CEM	Many sections collapsed, fast flow, rat	MF	7/99	130
1629N		SEW	2000	Kearny	Filbert	Union	1900	?	15"	VCP	Severe offsets, crushed sections, exfiltration			78
1630N	....N	SEW	2000	Polk	Greenwich MB	Filbert	1890	?	10"/18"	VCP	Continuous cracks, offsets			109
1630N		SEW	2000	Francisco	Polk	Van Ness	1914		12"	VCP	Many offsets & cracks; fast flow; lining recommended			50
1630N		SEW	2000	Quincy	Pine	California	1900	?	15"	VCP	Many severe cracks, breaks			84
	00-01 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)													4,000
1630N	....N	SEW	2001	Sacramento	Taylor	Mason	1875		16"	ISP	Many cracks, open joint			138

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	F P'D PAVE DATE	PROJ. COST (000)
1631N		SEW	2001	04th Avenue	Cabrillo	Balboa	1908	?	8"	VCP	Street depressions, separated ss's, open breaks			166
1631N		SEW	2001	10th Ave	Clement MB	Geary	1912	?	8"	ISP	Separated ss's, st depressions, low spots, exfiltration			.
1631N	......N	SEW	2001	Anza	9th Avenue	10th Avenue	1907		8"	VCP	Many separated side sewers, exfiltration	MF	1/00	55
1631N	......N	S &H	2001	Cabrillo St	6th Ave	7th Ave	1908	?	8"	VCP	Severe open breaks, street depressions	MF		63
1632N	......N	SEW	2001	Post	Lyon	Baker	1900		18"	VCP	ss separated ; hole invert 233-239' a-b, offses, fast flov	MF	1/01	146
1632N	1732N	SEW	2001	Eddy	Steiner	Fillmore	1875		3'x5'	BRICK	Bad shape, missing bricks, mortar crown & walls; dirt	MF	7/99	153
1632N	BSSR	SEW	2001	Grove	Baker	Broderick	1890		16"	ISP	Severe offsets, cracks; crushed section	OL		119
1632N		SEW	2001	Potomac St	Waller St	End South	1930	?	8"	VCP	Mult cracks, separated ss, infiltrtion, st. depn			79
1633N		SEW	2001	Greenwich	Webster	Fillmore								
1633N		SEW	2001	Precita South	Coso	Emmet Pl								
		SEW	2001	Precita South	Treat	Harrison	1900	?	16"	ISP	Multi cracks, loosing shape, fast flow, rat			
		SEW	2001	Precita South	Harrison	Alabama	1900	?	16"/18"	ISP	Many cracks, ss open @ 79' & 148' a-b, rat, replace a-b			
		SEW	2001	Pacific	Walnut	Laurel	1900	?	15"/12"	VCP	Cracks and open joints, street depressions, fast flow			
	......N	SEW	2001	Clement	27th Ave	26th Ave	1908	?	15"	ISP	Offset joints, many cracked sections			
START FY 01-02														
		SEW	2001	3rd St	4th St MB	16th St	1911		12"	VCP	Many cracked sections, collapse @ 27' b-a			
		SEW	2001	Hayes	Larkin	Polk	1890	?	3x5	BRICK	Bad shape, severe sags, missing bricks,bulging			190
	BSSR	SEW	2001	Sterling	I-80 ramp	Bryant	1900	?	12"	CEM	Multi cracks; ready to collapse; Rec. lining	MO	10/98	56
	BSSR	SEW	2001	Jones	Bernard	Pacific	1906	?	12"	VCP	Multiple cracked & collapsed sections	MF	n/a	40
	....N	SEW	2001	Bryant	7th St	Gilbert	1876	?	3x5	BRICK	Bad shape, cracks on crown, ready to cave in	MF		119
	1453N	SEW	2001	Kearny	Maiden Ln	Geary	1875	?	3'x5'	Brick	Bad shape, crown sagging, missing bricks	RE	7/98	77
	....N	SEW	2001	Townsend	7th St Mb	8th St Mb	1921		12"	VCP	Dips, Cracks, Crushed			167
		SEW	2001	Esmt blk #4315/1	Minnesota	3rd St	1949		12"	VCP	Several severe cracks & collapses			145
		SEW	2001	Esmt Blk #4317	Indiana	Minnesota	1949		12"	VCP	Severe multiple cracks			74
		SEW	2001	22nd Ave	Irving	Lincoln	1910	?	18"	VCP	Many active street depressions.			190
		SEW	2001	Folsom	18th St MB	17th St	1946		15"	VCP	Cont cracks 55-130', depression 157' b-c			145
	....N	SEW	2001	Rincon	Bay Bridge	Bryant	1917	?	12"	VCP	Collapsed			70
	....N	SEW	2001	Harrison	8th St	7th St	1880	?	3x5	BRICK	Missing mortar, loose bricks, out of round			550
	....N	SEW	2001	08th St	Market	Intersection	?		15"	VCP	Cracked sects. replace (a-b) across Market	RE		50
	01-02 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)													4,000
	1727N	SEW	2002	Leavenworth	Washington	Jackson	1900	?	16"	VCP	Many cracks; invert break	MF	7/99	68
	....N	SEW	2002	Leavenworth	Greenwich	Lombard	1890	?	16"	VCP	Crushed Pipe, Numerous Cracks			110
	....N	SEW	2002	Mission	13th St	14th St	1875	?	3'x5'	Brick	Bad shape, crown sagging, ready to collapse	MF		205
	....N	SEW	2002	Geary	Mason	Powell	1880		3x5	BRICK	Bad shape, crown buckled, mortar, bricks missing	MF		115
	....N	SEW	2002	Jones	Filbert	Lombard	1919		12"	VCP	Numerous Cracks			213
	....N	SEW	2002	Buchanan	Greenwich	Lombard St	1887		18"	VCP	Cracks, offsets, open joints			120
			2002	Stonestown Trestle Removal							Trestle is an attractive nuisance			286
			2002	Chinatown Alleys(3)										150
	BSSR	SEW	2002	South Hill	Prague	Geneva	1915		8"	ISP	Broken sections, cracks	MF/OL		60
	....N	SEW	2002	Washburn	Howard	Mission	1900	?	3x5	BRICK	Fairly bad shape, bricks, broken s/s			350
	BSSR	SEW	2002	Bayshore(W Side	Cortland	Oakdale	1928		12"	VCP	Many bad cracks & breaks	MF		93
START FY 02-03														

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
		SEW	2002	Esmt Block#113	End North	Anza	1935		8"	VCP	Many separated ss's from main, exfiltration			75
		SEW	2002	City View Way	Skyview	Knollview	1951		8"	VCP	Street depressions; crushed, open joints, exfiltration, fast flow			57
		SEW	2002	19th St	Collingwood	Castro	1887		18"	ISP	Open joints, bad cracks			90
		SEW	2002	O'Shaughnessy	Portola	Del Vale MB	1939		15"	VCP	Badly cracked, no tv log, sewer lining recommended		paved '96	70
		SEW	2002	Capp	21st St	20th St	1874	?	15"	CEM	Cement pipe, cracks			145
		SEW	2002	Liberty	Guerrero	Valencia	1875		15"	VCP/CP	SS discont'd @173', cracked sections			150
		SEW	2002	37th Ave	Balboa St	Cabrillo St	1920	?	18"	ISP	Offsets, several cracked sections, fast flow			207
		SEW	2002	Folsom	Precita	Army MB	1890	?	16"	VCP	Severe offsets, open invert, exfiltration, fast flow			49
		SEW	2002	Ashbury	Waller	Haight	1890		18"	VCP	Open joints, cracks; Replace Haig-Ash int.; fast flow			111
	BSSR	SEW	2002	Walter	Duboce	14th St	1890	?	8"	VCP	Many open breaks, separated ss, exfiltration	OL		148
		SEW	2002	Cole	Carl	Frederick	1888		3'x5'	BRICK	Bad shape			96
		SEW	2002	Pacific Ave	Presidio	Walnut	1900	?	12"	VCP	Crushed sections, bad side sewer, fast flow			112
		SEW	2002	26th Street	San Jose	Valencia	1889	?	15"	VCP	Open breaks, separated ss's, fast flow			64
	02-03 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)													4,000
	BSSR	SEW	2003	Moraga	23rd Ave	22nd Ave	1926		12"	ISP		MF		77
		SEW	2003	Lawton	21st Ave	23rd Ave	1925		15"/21"	VCP				177
		SEW	2003	11th Ave	Irving	Lincoln	1903	?	10"/12"	VCP	Many active street depressions, severe offsets,ss problems			
		SEW	2003	21st Ave	Moraga	Lawton	1925		15"	ISP				190
		SEW	2003	Russia	Madrid	Lisbon	1907	?	16"	VCP	Cracks, larghe street depression'			
1394N		SEW	hold	Kirkham	21st Ave	26th Ave					New Auxiliary Sewer 12"? VCP			216

F
85.93
2
1/14/99

DPW

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

DOCUMENTS DEPT.
FEB 10 1999
SAN FRANCISCO
PUBLIC LIBRARY

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 407
January 14, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4004
Thinh Nguyen	558-4554
Carmen Talavera	558-4012
James Walsh	554-8272

Street Construction Coordination Center

Kim Huynh	554-8260
Nancy Lynch	554-8870
Joe Norris	554-8274
Vitaly Troyan	554-5803

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Cynthia Chono	554-6196
Berhane Gaime	554-5841
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

Charles Kascal	554-1803

PUC Sewer R&R

(Representative not present)

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

(Representative not present)

Redevelopment Agency

(Representative not present)

Caltrans

Matt Abel	(510) 286-5188
Karen Ashe	557-7052
Dean Drablos	330-6537
Don Manning	557-4021
Erica Rankins	(510) 286-5517
Fernando Velez	(510) 286-6035

Caltrans Public Information

(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric

Gilbert Munoz	695-3550

S F Thermal

Charles Cotton	777-3415
Mike Eurkus	777-3415

Allstar / Metro Media

Nick Araujo	431-2510
Tom Stames	(510)-782-0900

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

RCN

(Representative not present)

TCG

(Representative not present)

TCI

Louis Victorio	863-8500

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 407

1. Mr. Troyan introduced Ms. Nancy Lynch, our new Service Representative, who will perform liaison and outreach for neighborhoods affected by DPW projects.

2. The December 10, 1998 Minutes were approved.

3. Mr. Troyan discussed our attempt to clarify the State Registration Board's requirement for a civil engineer's signature on drawings. His letter to the Board enclosed examples of the permit diagrams for a large project, a single trench within a block, and a service repair. The reply required interpretation by the City Attorney, whose opinion is that, narrowly construed, the requirement applies only to municipal improvements, including joint projects. It seems to exempt telecommunications projects. The City's projects are already stamped routinely. P G & E and San Francisco Thermal are still determining their positions. For Rule 20 undergrounding, the utility that does the composites is responsible for compliance, if applicable. Mr. Troyan will draft a letter for inclusion with these minutes, to be discussed at the next meeting.

4. Ms. Chono reported that the electronic permit system is up to do single blocks, but the multiple block feature is not ready yet. Multiple block permits still need to be done on paper. We expect the complete system to be active by January 25. Call Ephrem Naizghi at 554-6198 for user passwords.

Mr. Troyan asked which utilities are ready and equipped to use the system. Pacific Bell, TCI, S F thermal, and the Water Department are ready. P G & E is equipped but still deciding who their users will be. Mr. Walsh will check with Mr. Cunningham about his status, and Mr. Broady will check with DPT.

5. Ms. Chono distributed copies of the new handbook containing the DPW Order, the Code, specifications for barricades and dust control, and the applicable sections of the DPW Standard Plans and Specifications. It reflects the outcome of numerous meetings with interested parties, and contains some changes from the previous draft.

During January, BSM's inspectors are touring the City with checklists of the new requirements to visit work sites and make the contractors familiar with them. Starting February 1, they will begin citing infractions. BSM has been conducting orientation meetings with the major players, and we encourage any interested party to ask for such a meeting.

Ms. Lynch is in the process of setting up a one-stop information line and web site. Until the new number is arranged, please address questions to BSM at 554-5800.

The handbook contains a sample of the new X-1104 form; please note the new features. Mr. Troyan discussed the data base of all X-1104 citations issued since July 1, 1998. The inspectors are revisiting the sites to note compliance or to mark the locations (dark gray paint, to avoid confusion with USA markings) and remind the owners. BSM will issue a monthly reminder list of outstanding items.

6. Mr. Troyan called attention to the flyer in the Minutes, repeated in this month's issue, for the APWA's satellite teleconference on Preventing Excavation Damage: What You Can't See Can Hurt You. DPW will host the session at no cost to attendees, in the training trailer at the DPW yard at 2323 Cesar Chavez Blvd. Note the time on the flyer is CENTRAL time; locally, it is 8:30 a.m. to 1:00 p.m. Please call Debbie Kennedy at 554-5805 if you will attend, so we can set up for the right number of people.

New Business

Montgomery Street Paving Mr. Troyan reported that Mayor Brown walked down Montgomery St. last Thursday, accompanied by DPW officials. He has ordered it paved as soon as possible, each block begun and finished within 24 hours, coordinated to guarantee no utility work will be done within the moratorium period. We will contact all potential excavators that we know of to confirm clearance. The paving contract has been awarded, and a start date is being determined. Note the contract also includes parts of Post and Sutter Streets. Please examine the map included with these minutes and tell us immediately if you expect to do any work in or near the affected area.

THE PROJECT AREA WILL BE ASSUMED CLEAR UNLESS WE ARE TOLD OTHERWISE. ALL UTILITY WORK MUST BE COMPLETED BEFORE THE PAVING START DATE.

Please note that the coordination is mandatory not only in the project blocks themselves but also in the surrounding area. Traffic control will be a major concern, and ANY street opening near enough to affect it, on any day of the week and at any time, must be scheduled to avoid conflicts.

Mr. Troyan added that we will begin the work on some blocks at the north end of the Kearny Street project area as a rehearsal for the more critical area.

The next meeting will be at 10:00 am Thursday, February 11, 1998, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

City and County of San Francisco **Department of Public Works**
Street Construction Coordination Center

DOCUMENTS DE
FEB 10 1999
SAN FRANCISCO
PUBLIC LIBRARY

F
35.93
1
/11/99

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Location: 1680 Mission, 4th floor conference room

Date: Thursday, February 11, 1999 10am to 11:30am.

Subject: Committee Meeting 408- Coordination of Street Construction

1. Introduction	
2. Approval of Minutes for January 14th Meeting	
3. X1104 Monthly Report	Cynthia Chono
4. Electronic Permit Update	Cynthia Chono
5. Signing of Permit Application Drawings by Civil Engineer	Vitaly Troyan
6. Montgomery Street Construction Activity Update	Vitaly Troyan
7. Paving Program Clearance Issues	Joe Ovadia
8. Earth Quake Retrofit Project in San Francisco Caltrans Community Awareness Program	Jeff Weiss Veronica Faisant
9. Final CULCOP 5 Year Plan Due 4/1/99	Amy Chow
10. February 17, 1999 Teleconference on "Pavement Excavation Damage"	Vitaly Troyan
11. New Meeting Location for CULCOP	Vitaly Troyan
12. Other New Business	All

Next Meeting: 2nd Thursday of Each Month
Thursday March 11, 1999 at 10:00 A. M.
Conference Room
1680 Mission Street, 4th Floor

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-8274, at leaStreet72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-8274.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 1680 Mission Street, the Fourth Floor Conference Room. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L on Mission Street; # 42 on Van Ness Avenue;
   #26 on Valencia Street; #71 on Noriega Street; #9 on Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 407

January 14, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4004
Thinh Nguyen	558-4554
Carmen Talavera	558-4012
James Walsh	554-8272

Street Construction Coordination Center

Kim Huynh	554-8260
Nancy Lynch	554-8870
Joe Norris	554-8274
Vitaly Troyan	554-5803

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Cynthia Chono	554-6196
Berhane Gaime	554-5841
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

Charles Kascal	554-1803

PUC Sewer R&R

(Representative not present)

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

(Representative not present)

Redevelopment Agency

(Representative not present)

Caltrans

Matt Abel	(510) 286-5188
Karen Ashe	557-7052
Dean Drablos	330-6537
Don Manning	557-4021
Erica Rankins	(510) 286-5517
Fernando Velez	(510) 286-6035

Caltrans Public Information

(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric

Gilbert Munoz	695-3550

S F Thermal

Charles Cotton	777-3415
Mike Eurkus	777-3415

Allstar / Metro Media

Nick Araujo	431-2510
Tom Stames	(510)-782-0900

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

RCN

(Representative not present)

TCG

(Representative not present)

TCI

Louis Victorio	863-8500

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 407

1. Mr. Troyan introduced Ms. Nancy Lynch, our new Service Representative, who will perform liaison and outreach for neighborhoods affected by DPW projects.

2. The December 10, 1998 Minutes were approved.

3. Mr. Troyan discussed our attempt to clarify the State Registration Board's requirement for a civil engineer's signature on drawings. His letter to the Board enclosed examples of the permit diagrams for a large project, a single trench within a block, and a service repair. The reply required interpretation by the City Attorney, whose opinion is that, narrowly construed, the requirement applies only to municipal improvements, including joint projects. It seems to exempt telecommunications projects. The City's projects are already stamped routinely. P G & E and San Francisco Thermal are still determining their positions. For Rule 20 undergrounding, the utility that does the composites is responsible for compliance, if applicable. Mr. Troyan will draft a letter for inclusion with these minutes, to be discussed at the next meeting.

4. Ms. Chono reported that the electronic permit system is up to do single blocks, but the multiple block feature is not ready yet. Multiple block permits still need to be done on paper. We expect the complete system to be active by January 25. Call Ephrem Naizghi at 554-6198 for user passwords.

Mr. Troyan asked which utilities are ready and equipped to use the system. Pacific Bell, TCI, S F thermal, and the Water Department are ready. P G & E is equipped but still deciding who their users will be. Mr. Walsh will check with Mr. Cunningham about his status, and Mr. Broady will check with DPT.

5. Ms. Chono distributed copies of the new handbook containing the DPW Order, the Code, specifications for barricades and dust control, and the applicable sections of the DPW Standard Plans and Specifications. It reflects the outcome of numerous meetings with interested parties, and contains some changes from the previous draft.

During January, BSM's inspectors are touring the City with checklists of the new requirements to visit work sites and make the contractors familiar with them. Starting February 1, they will begin citing infractions. BSM has been conducting orientation meetings with the major players, and we encourage any interested party to ask for such a meeting.

Ms. Lynch is in the process of setting up a one-stop information line and web site. Until the new number is arranged, please address questions to BSM at 554-5800.

The handbook contains a sample of the new X-1104 form; please note the new features. Mr. Troyan discussed the data base of all X-1104 citations issued since July 1, 1998. The inspectors are revisiting the sites to note compliance or to mark the locations (dark gray paint, to avoid confusion with USA markings) and remind the owners. BSM will issue a monthly reminder list of outstanding items.

6. Mr. Troyan called attention to the flyer in the Minutes, repeated in this month's issue, for the APWA's satellite teleconference on Preventing Excavation Damage: What You Can't See Can Hurt You. DPW will host the session at no cost to attendees, in the training trailer at the DPW yard at 2323 Cesar Chavez Blvd. Note the time on the flyer is CENTRAL time; locally, it is 8:30 a.m. to 1:00 p.m. Please call Debbie Kennedy at 554-5805 if you will attend, so we can set up for the right number of people.

New Business

Montgomery Street Paving Mr. Troyan reported that Mayor Brown walked down Montgomery St. last Thursday, accompanied by DPW officials. He has ordered it paved as soon as possible, each block begun and finished within 24 hours, coordinated to guarantee no utility work will be done within the moratorium period. We will contact all potential excavators that we know of to confirm clearance. The paving contract has been awarded, and a start date is being determined. Note the contract also includes parts of Post and Sutter Streets. Please examine the map included with these minutes and tell us immediately if you expect to do any work in or near the affected area.

THE PROJECT AREA WILL BE ASSUMED CLEAR UNLESS WE ARE TOLD OTHERWISE. ALL UTILITY WORK MUST BE COMPLETED BEFORE THE PAVING START DATE.

Please note that the coordination is mandatory not only in the project blocks themselves but also in the surrounding area. Traffic control will be a major concern, and ANY street opening near enough to affect it, on any day of the week and at any time, must be scheduled to avoid conflicts.

Mr. Troyan added that we will begin the work on some blocks at the north end of the Kearny Street project area as a rehearsal for the more critical area.

The next meeting will be at 10:00 am Thursday, February 11, 1998, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

1999 UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS Query

Event Name	Start Date	End Date	Type	Location	Status
Film Shoot SFO	1/31/99	2/2/99	Film	Leidesforff: Sac to Com	1/19/99
SF Half Marathon	1/31/99	1/31/99	Athletic	Various: Golden Gate Park area	11/12/98
Film Shoot SFO	2/2/99	2/3/99	Film	Waverly: Was to Sac	1/19/99
"Nash Bridges" Film Shoot	2/2/99	2/2/99	Film	N.Point: Baker to Broderick; Baker: Beach to Bay	
"Nash Bridges" Film Shoot	2/2/99	2/2/99	Film	Broderick: Sac to Cal	
"Nash Bridges" Film Shoot	2/2/99	2/2/99	Film	Jones: Pine to Bush	
Film Shoot SFO	2/3/99	2/4/99	Film	Maiden Ln: Sto to Gra	1/19/99
Shuttle Zones for NADA	2/6/99	2/6/99	Corp	Grove (parking lanes only): Lar to Pok	
Shuttle Zones for NADA	2/7/99	2/7/99	Corp.	Grove (parking lanes only): Lar to Pok	
Shuttle Zones for NADA	2/9/99	2/9/99	Corp.	Grove (parking lanes only). Lar to Pok	
Flower Market Fair	2/12/99	2/14/99	Fair	Gra: Was to Bwd, Pac.Col to Sto	9/24/98
Chinese New Year Carnival	2/13/99	3/1/99	Fair	Walter Lum Place	11/12/98
Parking for Chinese NY Cel	2/14/99	2/14/99	Private	9th Ave: Judah to Kirkham	Withdrawn
Vietnamese New Year's Cel	2/14/99	2/14/99	Fair	Ell:Hyd to Pok; Lar:Edy to Ofa	1/14/99
23rd Penny Pitch	2/15/99	2/15/99	Block	Powell: Filbert to Columbus	1/14/99
Corporate Event at Ghirad.	2/17/99	2/18/99	Corporat	Beach. Pok to Lar; Polk: NPT to Beach	1/14/99
Chinese NY Run	2/21/99	2/21/99	Athletic	Chinatown to Marina Green	1/14/99
Banana Republic Conferenc	2/24/99	2/24/99	Corporat	Sutter (N/S parking lane only): Van Ness to Polk	Hold

Event Name	Start Date	End Date	Type	Location	Status
Banana Republic Conferenc	2/24/99	2/24/99	Corporat	Van Ness: (E/S parking lane only): Sut to Fern	Hold
Banana Republic Conferenc	2/24/99	2/25/99	Corporat	Fern: Van Ness to Polk	Hold
Chinese Community Street	2/26/99	2/28/99	Fair	Gra:Cla to Bwd; Pac;Sto to Col, etc	9/24/98
TV for Chinese NY Parade	2/26/99	2/27/99	Parade	Post (parking lanes only): Pow to Sto; Stockton (w/s onl	1/28/99
Chinese New Year Parade	2/27/99	2/27/99	Parade	Mkt:2nd to Sto; etc	Permit by SFPD
St. Patrick's Day Parade	3/14/99	3/14/99	Parade	Market to Civic Center	Permit by SFPD
St. Patrick's Day Parade	3/14/99	3/14/99	Parade	Market: JH Plaza to Civic Center	Permit by SFPD
St. Patrick's Day Celebratio	3/17/99	3/17/99	Block	Front: California to Sacramento	1/28/99
O'Reilly's St. Patrick's Day	3/17/99	3/17/99	Celebrat	Green (N/S parking lane only): Columbus to Powell	1/28/99
Houlihan's to Houlihan's	3/28/99	3/28/99	Athletic	Marina Blvd (1 n/b lane only), etc	9/24/99
Parking for Easter Services	4/4/99	4/4/99	Private	Anza: 9th to 10th Avenues	
Sisters of P.I. Birthday Bas	4/4/99	4/4/99	Celebrat	Castro: Mkt to 18th	Disapproved
Cherry Blossom Festival	4/17/99	4/18/99	Fair	Pos:Lag to Flm; Web: Gea to Sut	
SF Inter. Triathlon	4/18/99	4/18/99	Athletic	Various (NW portion of SF)	10/22/98
Cherry Blossom Festival	4/24/99	4/25/99	Fair	Pos:Lag to Flm;	
California Mille	4/25/99	4/26/99		Mason: Ca to Sac	12/17/98
Cherry Blossom Parade	4/25/99	4/25/99	Parade	Civic Center to Polk to Post	permitted by PD
Asian Art Museum Ground	5/8/99	5/8/99	Civic	Fulton: Larkin to Hyde	
Bay to Breakers	5/16/99	5/16/99	Athletic	Various Locations	1/28/99
Carnaval	5/29/99	5/30/99	Fair	Har: 16th to 22nd, etc	

Event Name	Start Date	End Date	Type	Location	Status
Carnaval Parade	5/30/99	5/30/99	Parade	24th: Bry to Mis; Mission: 24th to 14th; 14th: Mis to Har	permitted by PD
Union Street Arts Festival	6/5/99	6/6/99	Fair	Union: Gou to Stn, etc	12/17/98
Escape From Alcatraz	6/5/99	6/5/99	Athletic	Marina Blvd (1 lane only): Scott to Lyon	7/23/98
Escape From Alcatraz	6/5/99	6/5/99	Athletic	NW portion of SF, Various Locations	7/23/98
Black & White Ball	6/5/99	6/6/99	Civic		
SPCA Animal WingDing	6/5/99	6/6/99	Fair	Alabama:15 to 16; Florida:16 to Tre; Treat:Har to 15th	12/17/98
CA Aids Ride	6/6/99	6/6/99	Athletic	Various, no street closures involved	No permit required
SPCA Animal WingDing	6/6/99	6/6/99	Fair	Alabama:16 to 17; Florida:16 to 17	12/17/98
North Beach Festival	6/12/99	6/13/99	Fair	Grant:Col to Fil;Green: Col to Gra; Vallejo:Col to Gra	
Haight Street Fair	6/13/99	6/13/99	Fair	Haight:Masonic to Stanyan, etc	11/13/98
Extreme Games	6/23/99	7/3/99	Athletic	Pier 30-32	permit by Port
Gay Pride Celebration	6/25/99	6/28/99	Fair	Civic Center Area	1/28/99
Pink Saturday	6/26/99	6/27/99	Civic	Castro: 19th to Mkt; 18th: Cwd to Hfd	
Gay Pride Parade	6/27/99	6/27/99	Parade	Market: 2nd to Civic Center	permit by PD
Tall Ships	7/2/99	7/5/99		Wharf Area	
Fillmore Street Fair	7/3/99	7/4/99	Fair	Fillmore: Jackson to Post, etc	
New Fillmore Street Fair	7/3/99	7/4/99	Fair	Fillmore: Geary to McAllister etc.	
Chronicle's 4th of July	7/3/99	7/5/99	Fair	Jefferson: Hyde to Terminus	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Embarcadero: Pow to Tay	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Jefferson: Hyde to Taylor	12/17/98

Event Name	Start Date	End Date	Type	Location	Status
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Wharf Area	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	N/B Embarcadero: Bwd to Bay	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Van Ness: North Pt To Muni Pier	12/17/98
SF Chronicle Marathon	7/11/99	7/11/99	Athletic	Various City Wide	
Third Street Fair	7/17/99	7/18/99	Fair	3rd St.:Cargo to Evans	1/14/99
Blues & Art on the Bay	9/4/99	9/6/99	Fair	Treasure Island	permit by T. Island
Fest. Of Culinary Arts	9/11/99	9/12/99	Fair	Polk: Eddy to MCA; Turk: Van to Lar	
Chinatown Moon Festival	9/17/99	9/19/99	Fair	Grant: Cal to Pac	
Alcatraz Triathlon XIX	9/18/99	9/18/99	Athletic	Marina Blvd (1 lane only): Lag to Buc	10/22/98
Bridge to Bridge	10/3/99	10/3/99	Athletic	Various: Ferry Bldg to Presidio	1/28/99
West Portal Fair	10/23/99	10/24/99	Fair	West Portal. Ulloa to 15th Sts.	

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, AIA, Director and City Architect

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

UNDERGROUND PLANNING MEETING

MEETING DATE: January 5, 1999

PRESENT:

Tom Trimbur	-	DPW/BSM	(554-6167)
Louis Victorio	-	TCI	(863-8500)
Carlos DeAnda	-	PG&E	(330-2138)
Cindy Vowell	-	PacBell	(542-9095)
José Saldaña	-	PG&E	(330-2249)
Don Hendricks	-	PG&E	(695-3394)
John Giusti	-	Dolores Hts. Improv. Club	(863-7500)
Brian Gatter	-	BOE Landscape	(554-8292)
Naoki Kaku	-	BOE Streets & Hwys.	(554-8246)

DISCUSSION:

A. PROJECT STATUS

1. UGD 318 - DOLORES HEIGHTS DISTRICT

Dorland/Dolores Terrace – PacBell to install conduit for 36 Dorland and then perform final conversion on that property and 32 Dorland. Work should be done by the end of 2nd week of January. Following that work, poles to be removed.

PHASE 2 – Project to bid in January, award in February, and begin construction in March. Only 20-25 properties need internal conversion work. Project to start with gas work at 18th and Dolores, work up 18th to Church, then up to 20th in order to facilitate installation of TCI trunk line.

2. UGD 310 - PRESIDIO HEIGHTS

PHASE 2 – Substructure to be completed by end of 3rd week of January. Following that, utilities can begin pulling wire. Next month PG&E to provide list of properties that need work (at this point 10-15).

California St. – Project to bid in January, award in February, and begin construction in March.

3. UGD 320 - BREWSTER/JOY

122 Brewster is being handled as new business and is expected to be completed in January. Although some work has been done on 124 Brewster, more work is required. The latter is of some concern due to a leaning pole which cannot be removed prior to cutover.

4. UGD 321 - INDIANA STREET/ISLAIS CREEK & UGD 323 - CESAR CHAVEZ

Questions remain as to Caltrans permits, CALTRIAN work, and estimates for final property. PG&E to report on status of first two, and City to contact owner regarding completion of latter.

5. UGD 324 - DUBOCE AVENUE

Utility work completed. Poles with streetlights to remain until new lights are installed. Mr. Trimbur to inquire as to MUNI schedule for their work. Results from PG&E tests on water finding its way into their facilities have not been reported.

6. UGD 311 - CORBETT AVENUE - PEMBERTON STAIRWAY

Mr. Gatter reported that the project is still on hold.

7. UGD 335 - UPPER FOLSOM

PG&E work continuing. Substructure work should be finished by June. PG&E reported that the number of property conversions have picked up, although a number remain to be done. Mr. DeAnda reiterated that contractors may be less willing to give estimates and perform work in this areas as it is not perceived as wealthy because their profits would not be as high; he will provide the City with additional list of contractors who have been successfully performing conversions.

B. OTHER BUSINESS

1. Mr. Kaku and Mr. Gatter reported that work was progressing on the Banks/Chapman area, a portion of UGD 339, Bernal South Slope. Mr. Trimbur reported that a meeting was set up with the project manager to discuss the scheduling of that project. The results of that meeting will be reported next month.

2. Mr. Victorio reported that TCI intended to install above ground, standby power supply facilities for the TCI system in future underground districts. Mr. Trimbur requested information on size of typical systems, reasons these facilities could not be placed underground (given that PG&E facilities could be placed underground), and why these facilities could not be placed out of the public right-of-way. Mr. Trimbur indicated that the City wants to minimize above ground facilities in underground districts.

THE NEXT MEETING WILL BE HELD ON TUESDAY, 2 February 1999, AT 9:00 A.M. AT 875 STEVENSON STREET, ROOM 460, BSM CONFERENCE ROOM.

cc: All Attendees
CULCOP - through Joe Norris
Ray Gigliati - BSM
Hin Lok Kung - BOE
Jack Donohoe - DTIS
Barbara Moy - BSM
Manfred Wong - CWP
Lynn Bunim - PacTel
Norman Chan - BOE
Dee Lemmon - BLHP
Lesley Wong - BOE/S&H
Patricia Healy - PG&E
Dave Bradley - PG&E
Amy Chow - PDS
Charles Yu - BOE/S&H
Amy Powell- DHIC
Brian Christiansen - Duboce
Carlos DeAnda - PG&E
Lynn Nakasato - BOE/S&H
Cynthia Chono - BSM
Ray Yamagishi - BLHP
Tom Flahavan - DET
Joe Ovadia - PMD
Kathy Devine - PG&E
Louis Victorio – TCI
John Katz - MUNI
Sam Lauter - PG&E
Carol Finucane - BOE
Don Stroh - DHIC
Brian Gatter - BOE/Landscape
Terry Bouey - TCI
Bob Striech - PG&E
Joe Marino - DHIC
Terry Elisaia - DET
Naoki Kaku - BOE
Richard Hong - PG&E
Ben Cruz – BOE

C:\My Documents\UD0199 DOC

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

UTILITY COORDINATION REPORT

for January 1, 1999 to January 30, 1999

Notice of Intent and Request for Information Issued (NOI):	**Date**
1631N — 4th/10 Ave/Anza/Cabrillo Streets Sewer Replacement	01/12/99
1645N — Third Street Sewer System Improvement Phase II (CW-220)	01/08/99
1732N — Eddy and Turk Streets Pavement Renovation	01/08/99
7458E — Clay Street Pavement Renovation	01/08/99

Final Preliminary Plans Issued (LOT):

State of California:

Other:

"IMPROVING THE QUALITY OFLIFE IN SAN FRANCISCO" We are dedicted individuals committed to teamwork, custormer service and continuous improvement in partnership with the community
Customer Service *Teamwork* *Continuous Improvement*

Projects in Progress (NOI)

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
----N	Greg Cruz	554-8268	Various Locations, Construction of Curb Ramps - STPL-5934(030)	Pav	09/04/1997
1034N	Ed Choy	554-8284	Chinatown Alleyway Improvements Phase 1 Commercial, Cordelia and Ross	STR	05/27/1998
1048N	Gene Handa	554-8341	Sunnydale Sewer Improvements	SW	07/03/1996
1076N	Arlen Ung	554-8263	West End Utilities	Pav	08/11/1997
1100N	Martha Ketterer	554-8296	Ecker Street, Mission Street to Elim Alley	Pav	01/08/1996
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements Locations #306 & 309	UG	02/15/1998
1145N	Naoki Kaku	554-8246	Bernal Heights Street Improvement, Banks/Chapman Area	Pav	12/02/1996
1202N	Linda Leong	648-6882	North Point Plant Improvement, Phase II	Pav	01/30/1996
1218N	Cliff Wong	554-8339	Market , Larkin and Harrison Streets Sewer Replacement	SW	03/29/1996
1243N	Ronald Cheng	558-4049	Marina Seawall and Roadway Improvement	Pav	04/12/1996
1277N(1)	Laarni Camerino	554-8256	Var Loc: As Needed Paving - McAllister, Polk, Grove & Van Ness Avenue	Pav	08/17/1998
1277N(2)	Pak Choi	554-8283	Various Locations: As Needed Paving - Stockton (Post to Market Street)	Pav	08/17/1998
1277N(3)	Greg Cruz	554-8268	Var Loc - As Needed Pav: Lake Merced from Skyline Blvd. To John Muir Drive	PAV	09/28/1998
1285N	Brian Gatter	554-8292	Pioneer Park Renovation -- Telegraph Hill Stairways	Pav	11/14/1997
1294N	Leon Louie	558-4070	Fourth Street Bridge Fender Repair Project	Str	12/18/1996
1330N	Wallis Lee	554-8344	2nd / 9th Streets Sewer Abandonment Project	SW	06/27/1997
1349N	Saed Toloui	558-4084	12th Avenue/Quintara Street, Stairway Construction	Str	02/07/1997
1362N	Edward Choy	554-8284	Various Locations SOMA Street District Track Removal & Pavement Renovation Phase 2	PAV	01/07/1999
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	12/02/1996
1381N	Patrick Riviera	558-4045	Martin Luther King Utilities	Pav	09/12/1997
1385N	Laarni Camerino	554-8256	Various Locations: Concrete Street Reconstruction - Stillings Ave from Teresita to Congo	PAV	07/10/1998
1389N	Pak Choi	554-8283	Mission Street Pavement Renovation	Pav	06/13/1997
1395N	Cliff Wong	554-8339	Sacramento/ Larkin/ Pine Streets Sewer Replacement	SW	04/10/1998
1407N	Narciso Paderanga Jr.	554-8258	California Street Pavement Renovation, STP-17	Pav	02/13/1997
1409N	Pak Choi	554-8283	Sutter Street Pavement Renovation STP-19	Pav	04/13/1998
1415N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	Str	07/31/1997
1421N	Clifford Wong	554-8339	Green Street Sewer Replacement - Columbus Avenue to Powell Street	SW	01/17/1997
1423N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	SR	07/31/1997
1432N	Gene Handa	554-8341	Post Street Sewer Replacement	SW	02/07/1997
1459N	Narciso Paderanga, Jr.	554-8258	Fillmore Street Pavement Renovation and Muni Underground Ductbank System	Pav	08/29/1997
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	11/10/1997
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SR	09/30/1997
1549N	Thomas Won	554-8275	Ocean/Victoria/Everglade Sewer Replacement	SW	09/23/1997
1573N	Wallis Lee	554-8344	5th Street & Harrison Sewer Replacement	SW	02/17/1998
1583N	Thomas Won	554-8275	Everglade/ Victoria/ Revere/ Bridge View Sewer Replacement	SW	03/23/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	04/13/1998
1587N	Jean To	554-8298	7th Avenue and Kirkham Street Sewer Replacement	SW	12/11/1998
1588N	Thomas Won	554-8275	Joost Ave/Alemany Blvd/Mt. Vernon Ave/Kensington Way Sewer Replacement	SW	12/22/1998
1590N	Thomas Won	554-8275	Ocean Avenue Sewer Replacement (Joint Venture with MUNI)	SW	07/13/1998
1605N	Bryan Dessaure	554-8299	Sacramento/Pierce/Wilmot Streets Sewer Replacement	SW	06/07/1998
1626N	Thomas Won	554-8275	4th/5th Ave/Stanyan St (easement) / Paris Street Sewer Replacement	SW	10/22/1998
1628N	Jean To	554-8298	Moraga Street Sewer Replacement: 17th to 18th Avenues	SW	09/16/1998
1629N	Peter Cheng	554-8348	Union/Kearny Streets Sewer Replacement	SW	10/28/1998
1630N	Birgit Chase	554-8336	Polk/Francisco/Quincy/Sacramento Streets Sewer Replacement	SW	11/09/1998
1632N	Bhula Patel	554-8324	Post, Grove and Potomac Streets Sewer Replacement	SW	12/10/1998
1653N	Uday Prasad	558-4061	Demolition of North Beach Garage at 763 Vallejo Street	Str	09/15/1997
1655N	Lesley Wong	554-8252	Cezar Chavez Improvements Phase 2		07/27/1998
1667N	Lesley Wong	554-8252	Fourth Street Sidewalk Widening Project - Phase 2	Pav	03/10/1998
1668N	Ken Chu	554-8388	Golden Gate Avenue Pavement Renovation	Pav	01/02/1998
1674N	Joe Haas	558-4539	1680 Mission Street Secondary Power Source	SDV	05/27/1998
1678N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Street Reconstruction No. 15	Pav	04/13/1998
1680N	Lesley Wong	554-8252	Great Highway and Point Lobos Pavement Renovation	Pav	05/13/1998
1701N	Laarni Camerino	554-8256	Seventh Street Pavement Renovation	Pav	08/24/1998
1724N	Laarni Camerino	554-8256	Various Locations: As Needed Paving - 2nd St. between Townsend & King Streets	Pav	07/10/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	10/28/1998

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
1729N	Narciso Paderanga, Jr.	558-8258	Brotherhood Way & Font Boulevard Pavement Renovation	Pav	09/08/1998
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	10/05/1998
1734N	Dimitrios Stavrakis	554-8271	Franklin/Greenwich and Union Streets Pavement Renovation	PAV	01/04/1999
1735N	Naoki Kaku	554-8246	Various Locations: Bayview District Pavement Renovation	PAV	10/13/1998
1748N	Carol Finucane	558-4581	Mid-Market Public Improvements		10/05/1998
1755N	David Pang	554-8278	Oak Street Pavement Renovation	PAV	02/02/1999
1759N	Pak Choi	554-8283	Mission Street Pavement Renovation Phase 2	PAV	12/30/1998
6618E	Leon L. Louie	558-4070	Seismic Retrofit of Third Street Bridge	Str	08/31/1997
6618N	Frank Piruzmand	558-4081	3rd Street Bridge Rehabilitation & Retrofit	Str	03/30/1998
7291E	Lynn Fong	554-8269	K-Line Rail Replacement & Ocean Avenue Improvements	Pav	11/03/1997
7381E	Fernando Cisneros	554-8278	Hunter's Point Naval Shipyard Infrastructure Backbone Phase I	Pav	11/25/1996
7416E	Deirdre Appel	558-4556	Golden Gate Park Reservoir and Pump Station		08/07/1998
N	Linda DeBolt	554-8265	Surface Streets Improvement Project	Pav	02/06/1998

Projects in Progress (NOI)

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
---N	09/04/1997		08/07/1997	11/09/1998	10/20/1997	08/20/1997			09/04/1997
1034N	05/27/1998		05/06/1998	06/02/1998	05/11/1998	05/12/1998	04/30/1998	05/06/1998	05/13/1998
1048N	07/03/1996	Mar-99	07/11/1996	06/17/1996		07/16/1996			07/14/1996
1076N	08/11/1997	Jul-98	07/17/1997			07/23/1997	07/18/1997	07/29/1997	08/26/1997
1100N	01/08/1996	May-98		05/14/1996		12/18/1995			02/16/1996
1109K	02/15/1998		12/30/1997	04/27/1998	01/21/1998	01/09/1998	12/30/1997	01/09/1998	01/13/1998
1145N	12/02/1996	Nov-98	11/08/1996			12/03/1996			12/07/1996
1202N	01/30/1996	18-Nov-97		01/29/1996				01/16/1996	
1218N	03/29/1996	On hold	03/22/1996			03/20/1996	03/01/1996		
1243N	04/12/1996		03/29/1996				03/25/1996	03/19/1996	04/23/1996
1277N(1)	08/17/1998			07/24/1998	08/19/1998	07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(2)	08/17/1998			07/24/1998		07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(3)	09/28/1998		09/08/1998	09/10/1998	11/02/1998	09/09/1998	09/04/1998	09/23/1998	09/17/1998
1285N	11/14/1997	Jul-98	10/21/1997	04/13/1998		10/24/1997	10/16/1997	10/20/1997	11/06/1997
1294N	12/18/1996	May-98	10/25/1996	03/19/1997		10/18/1996		10/09/1996	12/07/1996
1330N	06/27/1997	Apr-98	06/16/1997	06/17/1997		06/17/1997	06/16/1997		
1349N	02/07/1997	Apr-98	01/09/1997			03/27/1997	01/10/1997	01/24/1997	02/07/1997
1362N	01/07/1999		12/02/1998			12/02/1998	12/01/1998		12/14/1998
1374N	12/02/1996		11/08/1996	02/24/1997		12/03/1996			12/07/1996
1381N	09/12/1997		08/18/1997			08/22/1997	08/18/1997	10/29/1997	09/15/1997
1385N	07/10/1998		06/12/1998	07/10/1998		06/22/1998	06/18/1998	07/17/1998	06/23/1998
1389N	06/13/1997	May-98	05/28/1997	06/02/1997			06/05/1997	05/28/1997	06/03/1997
1395N	04/10/1998			04/27/1998	04/17/1998	06/02/1998	04/08/1998	04/13/1998	04/20/1998
1407N	02/13/1997	On hold	01/17/1997			01/21/1997	01/15/1997	01/27/1997	02/18/1997
1409N	04/13/1998			05/15/1998		06/02/1998	04/08/1998	04/13/1998	04/20/1998
1415N	07/31/1997	Sep-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997	07/22/1997	07/28/1997
1421N	01/17/1997	Jan-98	01/09/1997	01/06/1997		01/23/1997	01/02/1997		02/07/1997
1423N	07/31/1997	Nov-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997		07/28/1997
1432N	02/07/1997	Jun-98		02/20/1997		02/11/1997	01/23/1997		02/18/1997
1459N	08/29/1997	May-98	08/05/1997	12/22/1997	10/20/1997	08/07/1997	08/01/1997		09/05/1997
1474N	11/10/1997	Jul-98	10/21/1997	06/17/1998	10/16/1997	10/24/1997	10/16/1997		11/06/1997
1548N	09/30/1997		09/08/1997	04/13/1998	09/24/1997	09/19/1997	09/09/1997		09/30/1997
1549N	09/23/1997					09/19/1997	09/11/1997		09/30/1997
1573N	02/17/1998		01/23/1998	06/17/1998	01/23/1998	02/12/1998	01/23/1998		02/12/1998
1583N	03/23/1998		03/23/1998		03/09/1998	03/05/1998	03/09/1998	03/11/1998	03/24/1998
1585N	04/13/1998		04/29/1998	04/30/1998	04/15/1998	05/12/1998	04/09/1998	04/13/1998	04/23/1998
1587N	12/11/1998		11/09/1998		11/09/1998	11/09/1998	11/02/1998		11/16/1998
1588N	12/22/1998					12/02/1998	12/01/1998		12/09/1998
1590N	07/13/1998			07/13/1998		06/19/1998	06/18/1998	07/16/1998	06/23/1998
1605N	06/07/1998		05/11/1998	05/15/1998	05/11/1998	05/13/1998	05/11/1998		05/20/1998
1626N	10/22/1998		10/16/1998	11/12/1998			10/06/1998		10/15/1998
1628N	09/16/1998		09/14/1998	09/10/1998	09/10/1998	09/10/1998	09/10/1998	09/15/1998	09/17/1998
1629N	10/28/1998			11/12/1998		10/02/1998	10/01/1998	10/09/1998	10/13/1998
1630N	11/09/1998				11/09/1998	11/09/1998	10/16/1998	10/13/1998	10/21/1998
1632N	12/10/1998		11/09/1998		11/09/1998	11/09/1998	11/02/1998		11/06/1998
1653N	09/15/1997		09/02/1997	09/09/1997		09/02/1997		09/09/1997	09/10/1997
1655N	07/27/1998		07/01/1998		07/06/1998		06/29/1998		07/20/1998
1667N	03/10/1998		02/20/1998		02/20/1998		02/20/1998	03/13/1998	03/05/1998
1668N	01/02/1998	Sep-98	12/04/1997	04/27/1998	12/12/1997	01/13/1998	12/03/1997	12/04/1997	12/16/1997
1674N	05/27/1998		05/15/1998		05/26/1998	05/22/1998	05/19/1998	06/02/1998	06/09/1998
1678N	04/13/1998								
1680N	05/13/1998		04/27/1998	06/02/1998	05/11/1998	05/26/1998		04/22/1998	05/06/1998
1701N	08/24/1998		07/29/1998	09/02/1998		08/04/1998	07/24/1998	10/15/1998	08/13/1998
1724N	07/10/1998		06/22/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	06/22/1998	06/23/1998
1727N	10/28/1998		10/02/1998	11/06/1998		10/02/1998	10/01/1998	09/30/1998	10/13/1998

PRJ #	Due Date	NTP	ATT	*BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1729N	09/08/1998		08/12/1998	09/02/1998		08/12/1998	08/10/1998	09/15/1998	08/18/1998
1732N	10/05/1998		09/14/1998	11/06/1998	11/02/1998	09/22/1998	09/11/1998	10/15/1998	09/25/1998
1734N	01/04/1999		12/17/1998			12/31/1998			01/26/1999
1735N	10/13/1998		09/14/1998	11/06/1998		09/22/1998	09/15/1998	09/25/1998	09/25/1998
1748N	10/05/1998		09/14/1998	11/06/1998		09/22/1998	09/14/1998	10/13/1998	09/25/1998
1755N	02/02/1999					01/08/1999		01/14/1999	
1759N	12/30/1998		11/23/1998		12/27/1998	12/10/1998			12/09/1998
6618E	08/31/1997	Dec-98	07/16/1997		07/15/1997	07/18/1997	07/24/1997	07/28/1997	08/26/1997
6618N	03/30/1998		03/25/1998	03/23/1998		03/23/1998	03/24/1998	03/17/1998	03/30/1998
7291E	11/03/1997		10/21/1997	06/02/1998		10/24/1997	10/08/1997	10/09/1997	10/14/1997
7381E	11/25/1996		10/31/1996			11/13/1996	11/01/1996	10/30/1996	12/07/1996
7416E	08/07/1998		07/17/1998	07/10/1998		06/30/1998	07/13/1998	07/09/1998	07/29/1998
N	02/06/1998		01/08/1998		01/23/1998	05/13/1998	01/08/1998	03/09/1998	01/26/1998

Projects in Progress (NOI)

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
—N	09/04/1997	08/26/1997	11/24/1998		08/19/1997		09/30/1997	09/30/1997
1034N	05/27/1998	05/06/1998	05/06/1998		06/02/1998		06/25/1998	06/25/1998
1048N	07/03/1996	06/18/1996	06/25/1996	07/16/1996	07/01/1996	06/21/1996		
1076N	08/11/1997	07/28/1997			08/04/1997	07/28/1997	07/28/1997	07/28/1997
1100N	01/08/1996	12/11/1995	12/21/1995	12/11/1995	12/28/1995	12/08/1995		
1109K	02/15/1998		01/14/1998		01/15/1998		01/27/1998	01/27/1998
1145N	12/02/1996	12/07/1996	12/02/1996		11/25/1996	12/03/1996	12/03/1996	12/03/1996
1202N	01/30/1996			01/18/1996	02/02/1996	01/18/1996		
1218N	03/29/1996	03/14/1996		03/14/1996	03/18/1996	03/18/1996		
1243N	04/12/1996	03/27/1996		04/15/1996	03/25/1996	04/02/1996		
1277N(1)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998			
1277N(2)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998	07/31/1998	08/13/1998	08/13/1998
1277N(3)	09/28/1998	09/09/1998	09/04/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1285N	11/14/1997	11/07/1997		02/11/1998	10/24/1997	10/17/1997	11/25/1997	11/25/1997
1294N	12/18/1996	10/24/1996		11/07/1996	10/28/1996	11/19/1996		
1330N	06/27/1997	07/01/1997		07/09/1997	06/27/1997	06/12/1997	07/10/1997	07/10/1997
1349N	02/07/1997	01/17/1997	01/22/1997	03/17/1997		01/13/1997	02/05/1997	02/05/1997
1362N	01/07/1999	12/01/1998	01/05/1999		12/10/1998			01/12/1999
1374N	12/02/1996	11/07/1996			11/25/1996	11/07/1996	12/02/1996	12/02/1996
1381N	09/12/1997	08/26/1997			08/21/1997			09/24/1997
1385N	07/10/1998	06/15/1998	06/23/1998		06/25/1998	10/08/1998	07/29/1998	07/29/1998
1389N	06/13/1997	05/29/1997			05/23/1997	06/11/1997	05/23/1997	05/23/1997
1395N	04/10/1998	04/13/1998	01/05/1999		04/22/1998	04/13/1998		05/14/1998
1407N	02/13/1997	02/24/1997	04/17/1997	03/19/1997	01/23/1997	02/03/1997	02/05/1997	02/05/1997
1409N	04/13/1998	04/13/1998	04/15/1998		04/14/1998		06/25/1998	06/25/1998
1415N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1421N	01/17/1997	01/10/1997		01/29/1997	02/19/1997	12/30/1996	01/22/1997	01/22/1997
1423N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1432N	02/07/1997	02/24/1997	02/10/1997	03/18/1997	01/31/1997	01/22/1997	02/24/1997	02/24/1997
1459N	08/29/1997	08/05/1997			08/13/1997		09/24/1997	09/24/1997
1474N	11/10/1997	11/07/1997			10/23/1997	10/14/1997	11/25/1997	11/25/1997
1548N	09/30/1997	09/12/1997			09/15/1997	09/29/1997	10/09/1997	10/09/1997
1549N	09/23/1997	09/24/1997			09/17/1997	09/15/1997	10/09/1997	10/09/1997
1573N	02/17/1998	01/26/1998	03/30/1998			01/22/1998		02/12/1998
1583N	03/23/1998	03/11/1998	03/30/1998		03/18/1998	03/09/1998	03/17/1998	
1585N	04/13/1998	04/13/1998			04/30/1998	04/13/1998	06/25/1998	06/25/1998
1587N	12/11/1998	11/13/1998		12/18/1998	11/13/1998			01/12/1999
1588N	12/22/1998	12/01/1998			12/02/1998			01/12/1999
1590N	07/13/1998	06/17/1998	08/04/1998		06/29/1998	10/08/1998	07/29/1998	07/29/1998
1605N	06/07/1998	05/12/1998				05/15/1998	06/25/1998	06/25/1998
1626N	10/22/1998	10/06/1998		11/09/1998	10/13/1998			01/12/1999
1628N	09/16/1998	09/10/1998	09/08/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1629N	10/28/1998	10/06/1998		11/09/1998	10/08/1998		11/12/1998	11/12/1998
1630N	11/09/1998	10/15/1998			10/20/1998			01/12/1999
1632N	12/10/1998		01/05/1999		11/06/1998			01/12/1999
1653N	09/15/1997	09/12/1997			09/08/1997	09/04/1997	09/24/1997	09/24/1997
1655N	07/27/1998	07/01/1998			07/02/1998	07/01/1998	07/29/1998	07/29/1998
1667N	03/10/1998	02/20/1998			02/27/1998			
1668N	01/02/1998	12/04/1997			12/12/1997		01/27/1998	01/27/1998
1674N	05/27/1998	05/18/1998	05/19/1998		06/02/1998	05/14/1998	07/09/1998	07/09/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998	05/13/1998		04/30/1998		06/25/1998	06/25/1998
1701N	08/24/1998	07/24/1998	08/24/1998	11/09/1998			08/13/1998	08/13/1998
1724N	07/10/1998	06/15/1998	06/23/1998		06/23/1998	10/08/1998	07/09/1998	07/09/1998
1727N	10/28/1998	10/02/1998		11/09/1998	10/13/1998			01/12/1999

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1729N	09/08/1998	08/11/1998	08/12/1998	11/09/1998	08/18/1998	09/18/1998	09/01/1998	09/01/1998
1732N	10/05/1998	09/17/1998		11/09/1998	09/28/1998	09/11/1998		11/12/1998
1734N	01/04/1999	12/15/1998			12/29/1998			
1735N	10/13/1998	09/18/1998		11/09/1998	09/18/1998	09/09/1998		11/12/1998
1748N	10/05/1998	09/18/1998		11/09/1998	09/24/1998	09/11/1998		11/12/1998
1755N	02/02/1999	01/05/1999			12/30/1998			
1759N	12/30/1998	12/01/1998	11/23/1998		12/14/1998			12/01/1998
6618E	08/31/1997	07/16/1997		07/30/1997	07/24/1997	07/28/1997	08/21/1997	08/21/1997
6618N	03/30/1998	03/25/1998			04/01/1998		05/14/1998	
7291E	11/03/1997	10/29/1997			10/20/1997		11/10/1997	11/10/1997
7381E	11/25/1996	11/06/1996	11/05/1996	11/14/1996	11/08/1996	12/18/1996	12/02/1996	12/02/1996
7416E	08/07/1998	07/13/1998		11/09/1998	07/20/1998	07/01/1998		07/29/1998
N	02/06/1998	06/22/1998			01/26/1998	10/08/1998		02/12/1998

Projects in Progress (NOI)

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
---N	09/04/1997	08/12/1997		08/08/1997	08/13/1997	08/08/1997	08/08/1997	08/26/1997
1034N	05/27/1998	04/30/1998		05/19/1998	05/11/1998	05/20/1998		05/11/1998
1048N	07/03/1996		06/26/1996	07/01/1996		06/25/1996	07/03/1996	07/01/1996
1076N	08/11/1997	07/24/1997		07/24/1997	07/29/1997	08/08/1997	07/22/1997	08/15/1997
1100N	01/08/1996		12/20/1995	01/03/1996	12/14/1995	12/18/1995	12/27/1995	12/20/1995
1109K	02/15/1998	01/07/1998		01/14/1998	01/14/1998	05/20/1998	01/21/1998	01/21/1998
1145N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1202N	01/30/1996		01/16/1996	01/19/1996	01/31/1996	01/17/1996		02/06/1996
1218N	03/29/1996				03/12/1996	03/05/1996	03/27/1996	03/07/1996
1243N	04/12/1996		03/25/1996		03/27/1996	03/22/1996	03/27/1996	03/21/1996
1277N(1)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(2)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(3)	09/28/1998	09/03/1998		09/15/1998	09/17/1998		01/11/1999	09/17/1998
1285N	11/14/1997	10/20/1997	10/28/1997	10/27/1997	10/23/1997	11/18/1997	11/10/1997	11/13/1997
1294N	12/18/1996		10/25/1996	10/25/1996	10/31/1996		12/02/1996	10/24/1996
1330N	06/27/1997	06/16/1997	07/02/1997	06/23/1997	06/23/1997	07/11/1997	08/08/1997	07/02/1997
1349N	02/07/1997	01/13/1997	01/13/1997	01/21/1997	02/12/1997	02/27/1997		01/22/1997
1362N	01/07/1999	12/01/1998	12/02/1998	12/10/1998	12/10/1998		01/11/1999	12/14/1998
1374N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1381N	09/12/1997	08/15/1997		08/22/1997	08/22/1997	11/18/1997		08/26/1997
1385N	07/10/1998	06/15/1998		06/23/1998	06/19/1998			06/29/1998
1389N	06/13/1997	05/19/1997	05/29/1997	05/21/1997	05/23/1997	05/29/1997	06/26/1997	06/06/1997
1395N	04/10/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1407N	02/13/1997	01/17/1997	01/15/1997	01/24/1997	02/12/1997	02/27/1997	02/24/1997	01/22/1997
1409N	04/13/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1415N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1421N	01/17/1997	01/07/1997	01/06/1997		02/18/1997	02/27/1997		01/22/1997
1423N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1432N	02/07/1997	01/27/1997	01/27/1997	01/29/1997	02/12/1997	02/27/1997		01/30/1997
1459N	08/29/1997	08/05/1997		08/06/1997	08/12/1997	08/08/1997	11/10/1997	08/26/1997
1474N	11/10/1997	10/20/1997		10/21/1997	10/22/1997	11/18/1997	11/10/1997	11/13/1997
1548N	09/30/1997	09/19/1997		09/12/1997	09/12/1997	09/24/1997	09/11/1997	09/22/1997
1549N	09/23/1997	09/12/1997		09/18/1997	09/16/1997	09/24/1997	09/19/1997	09/22/1997
1573N	02/17/1998	01/26/1998		02/12/1998	02/12/1998			02/20/1998
1583N	03/23/1998		03/20/1998	03/24/1998	03/17/1998		04/08/1998	03/03/1998
1585N	04/13/1998	04/13/1998	04/28/1998	04/20/1998	04/28/1998	05/20/1998		04/28/1998
1587N	12/11/1998		11/12/1998	11/23/1998	11/19/1998			11/19/1998
1588N	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
1590N	07/13/1998	06/15/1998		07/08/1998	06/19/1998		01/11/1999	07/07/1998
1605N	06/07/1998	05/13/1998		05/19/1998	05/20/1998	05/20/1998		06/02/1998
1626N	10/22/1998	10/05/1998			10/15/1998		01/07/1999	10/15/1998
1628N	09/16/1998	09/08/1998	09/08/1998	09/15/1998	09/17/1998	09/16/1998	09/17/1998	09/17/1998
1629N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1630N	11/09/1998	10/09/1998			10/19/1998		01/07/1999	10/27/1998
1632N	12/10/1998	10/28/1998		11/23/1998	11/10/1998		01/07/1999	11/10/1998
1653N	09/15/1997	09/02/1997		09/08/1997	09/12/1997		09/15/1997	09/22/1997
1655N	07/27/1998	06/29/1998	07/20/1998	07/10/1998	07/15/1998	07/29/1998	01/11/1999	07/15/1998
1667N	03/10/1998	02/20/1998		02/20/1998	02/20/1998			02/20/1998
1668N	01/02/1998	12/03/1997		12/23/1997		02/12/1998	12/11/1997	12/12/1997
1674N	05/27/1998	05/19/1998			06/03/1998	05/20/1998		06/11/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998		05/06/1998	05/06/1998	06/02/1998		05/11/1998
1701N	08/24/1998	07/24/1998		08/04/1998	08/03/1998	07/24/1998	01/11/1999	
1724N	07/10/1998	06/22/1998		06/23/1998	06/19/1998			06/29/1998
1727N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1729N	09/08/1998	08/24/1998		09/01/1998	08/13/1998		01/11/1999	09/17/1998
1732N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/30/1998
1734N	01/04/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998		12/31/1998	12/18/1998
1735N	10/13/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/24/1998
1748N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/11/1999	09/30/1998
1755N	02/02/1999		12/28/1998	01/14/1999	01/05/1999		01/12/1999	01/07/1999
1759N	12/30/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/14/1998
6618E	08/31/1997	07/17/1997		07/21/1997	07/18/1997	03/24/1998	07/16/1997	07/18/1997
6618N	03/30/1998	03/26/1998	04/02/1998	04/02/1998		03/24/1998	04/01/1998	04/03/1998
7291E	11/03/1997	10/09/1997	10/16/1997	10/10/1997	10/15/1997	11/19/1997	11/10/1997	10/16/1997
7381E	11/25/1996	01/10/1997	11/13/1996	11/13/1996	11/07/1996		12/02/1996	11/19/1996
7416E	08/07/1998	07/21/1998		07/20/1998	07/20/1998		01/11/1999	07/31/1998
N	02/06/1998	02/10/1998	01/16/1998	01/14/1998	01/21/1997	02/10/1998	01/21/1998	01/21/1998

Projects in Progress (LOT)

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1001H	Paul Travis	557-4631	911/OES Emergency Communications Center		12/06/1996
1036N	Lesley Wong	554-8252	Fourth Street Pavement Renovation	Pav	05/28/1997
1077N	Steve Bui	554-8298	Bowling Green Drive Contract	SW	09/30/1997
1091N	Ed Choy	554-8284	Various Locations South of Market Removal & Pavement Renovation	Pav	04/30/1997
1106N	Steve Bui	554-8298	Western Presidio Drainage Improvements (NOI/LOT)	SW	05/16/1997
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements, Various Locations	UG	04/28/1997
1109N	Linda DeBolt	554-8265	Cesar Chavez (Army) Street Widening	Pav	12/27/1996
1133N	Ellaine Taraya	554-8245	Fulton Street Roadway Widening	Pav	10/27/1997
1155N	E. Ho/Bhula Patel	554-8324	Grant/Chestnut Street Sewer Replacements	SW	10/21/1998
1195N	Gyee Yang	558-4553	Market and Steuart Streets, AWSS Relocation	AWSS	07/20/1996
1208K	Joe Haas	558-4539	San Francisco General Hospital Underground Storage Tank Replacement	UG	03/09/1998
1223W	Lesley Wong	554-8252	Islais Creek, Street Improvements	Pav	04/30/1997
1245N	Wallis Lee	554-8344	Yosemite/Egbert Sewer Enlargment Project (formerly 3180W)	SW	11/27/1996
1253N	Iqbal Dhapa	554-8337	Twelfth Street (SR)	SW	05/16/1997
1254N	Cliff Wong	554-8339	Eleventh Street Sewer Replacement - Harrison St. to Folsom St.	SW	05/23/1997
1272N	Steve Bui	554-8298	Illinois-Cesar Chavez (Army) Streets Sewer Construction	SW	08/08/1997
1322N	Lesley Wong	554-8252	Cabrillo Street, 9th and 16th Avenues Pavement Renovation	Pav	03/11/1997
1373N	Ken Chu	554-8388	Lower Great Highway, 46th, and 48th Avenues, Pavement Renovation	Pav	09/15/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	05/28/1997
1392N	Birgit Chase	554-8336	Bayshore Blvd. - U.S. 101 Off-Ramp...Sewer Repl. (1108N)	Pav & SW	02/28/1997
1393N	Thomas Won	554-8275	Bush/Kearny/Post Streets Sewer Replacement	SW	10/24/1997
1396N	Peter Cheng	554-8348	Sutter/Fell/Broederick Streets Sewer Replacement	SW	05/12/1997
1397N	Bhula Patel	554-8324	Douglass/Dolores/Ord/23rd/28th Streets, Sewer Replacement	SW	10/17/1997
1408N	Naoki Kaku	554-8246	Geneva Avenue, Pavement Renovation	Pav	02/06/1998
1411N	Peter Cheng	554-8348	Harding Park SR	SW	11/14/1997
1413N	Iqbal Dhapa	554-8337	Davis/Kearny/Francisco Streets Sewer Replacement	SW	06/25/1997
1414N	Thomas Won	554-8275	Treat / 22nd Streets Sewer Replacement	SW	02/28/1997
1426N	Ting He	554-8338	Dore/Valencia/Clinton Park SR	SW	12/08/1997
1433N	Peter Cheng	554-8348	Shotwell Street Sewer Replacement - Army Street to 26th St	SW	11/07/1997
1440N	Pak Choi	554-8283	Various Locations Concrete Street Reconstruction No. 13	Pav	02/06/1998
1453N	Naoki Kaku	554-8246	Montgomery, Kearny, & Sacramento, Pavement Renovation	Pav	02/06/1998
1454N	Ed Choy	554-8284	Potrero Hill District Track Removal and Pavement Renovation, Phase 3	SW	04/27/1998
1460N	Birgit Chase	554-8336	Church / Folsom / Harper Streets Sewer Replacement	SW	10/22/1997
1461N	Iqbal Dhapa	554-8337	Mason / Pine / Leavenworth Streets and Meacham Place Sewer Replacement	SW	03/06/1998
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	06/22/1998
1475N	Birgit Chase	554-8336	Virginia / Fair Avenues/Godeus Street SR	SW	12/24/1997
1477N	Lynn Fong	554-8269	Various Locations Concrete Street Pavement Renovation No. 14	Pav	11/09/1998
1488N	Peter Cheng	554-8348	24th Ave/California Street Sewer Replacement (1452N)	SW	06/20/1997
1491N	Peter Cheng	554-8348	Pacific Ave. Sewer Replacement - Grant Ave. to Stockton St.	SW	09/25/1997
1519N	Pak Choi	554-8283	Bus Bulb Improvement Project Phase 1	Pav	01/23/1998
1528N	Iqbal Dhapa	554-8337	501 Laguna Honda Boulevard Easement Sewer Replacement	SW	08/25/1997
1547N	Peter Cheng	554-8348	33rd Ave/Lyon Street/Molimo Dr SR	SW	01/16/1998
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SW	01/09/1998
1550N	Bhula Patel	554-8324	Day/Congo/Marston/Cuvier SR	SW	01/30/1998
1562N	Birgit Chase	554-8336	Broadway/Bryant/22nd/Sonoma Streets Sewer Replacement	SW	06/26/1998
1563N	Iqbal Dhapa	554-8337	Balboa St. and 3rd/20th/42nd Avenues Sewer Replacement	SW	06/25/1998
1566N	Peter Cheng	554-8243	Fillmore Street SR	SW	12/19/1997
1569N	Peter Cheng	554-8348	Dolores Street/Block 7044 Easement Sewer Replacement	SW	06/12/1998
1578N	Jean To	554-8329	Golden Gate Ave. Sewer Replacement-Polk St/Van Ness & Pierce/Scott Sts	SW	03/10/1998
1579N	Jean To	554-8329	Illinois Street Sewer Replacement-20th to 19th Street		04/17/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	09/15/1998
1586N	Jean To	437-7012	Geary, Eddy, Elm and Turk Sewer Replacement	SW	10/20/1998
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	01/22/1999
1602N	Jean To	437-7012	Howard, Minna and 2nd Streets Sewer Replacement	SW	11/09/1998
1603N	Jean To	554-8270	Broad Street, Capitol to Plymouth Avenue Sewer Replacement	SW	07/10/1998

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1606N	Jean To	554-8348	Cayuga/Laurel/Rondel and Douglass Sewer Replacement	SW	10/29/1998
1631N	Jean To	554-8298	4th/10th Ave/Anza/Cabrillo Streets Sewer Replacement	SW	02/16/1999
1645N	Peter Cheng	554-8348	Third Street Sewer System Improvement Phase II	SW	02/24/1999
1687N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 15	Pav	08/31/1998
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	02/24/1999
6094Q	Deanna Calleros	554-8266	Mid Embarcadero Surface Rdwy and F-Line Extension	Pav	06/27/1997
7090E	Thinh Nguyen	558-4554	Various Locations Motorized Valves Contract #2	AWSS	03/19/1998
7437E	Laarni Camerino	554-8256	Howard, Folsom & Hawthorne Streets (SR)	SW	08/29/1997
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	02/24/1999
7474E	Peter Cheng	554-8348	Pine/California/Delancey Streets SR	SW	11/26/1997

Project in Progress (LOT)

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1001H	12/06/1996		12/03/1996	01/22/1997		12/05/1996		11/25/1996	12/16/1996
1036N	05/28/1997	Apr-98	05/15/1997	06/30/1997		05/09/1997	05/14/1997		
1077N	09/30/1997	Apr-98	09/08/1997	06/26/1998		09/24/1997	09/09/1997		09/05/1997
1091N	04/30/1997	15-Sep-97	04/04/1997	05/13/1997				04/11/1997	04/28/1997
1106N	05/16/1997	3-Nov-97	05/06/1997	05/13/1997		05/12/1997	05/06/1997		06/03/1997
1109K	04/28/1997		04/14/1997			04/16/1997		04/22/1997	05/08/1997
1109N	12/27/1996	Jun-98	12/05/1996				12/03/1996		02/07/1997
1133N	10/27/1997	May-98	10/21/1997		10/16/1997		10/10/1997		10/21/1997
1155N	10/21/1998		10/16/1998	11/09/1998		10/07/1998	10/06/1998		10/15/1998
1195N	07/20/1996						07/08/1996		
1208K	03/09/1998		03/24/1998	03/05/1998		03/18/1998	03/05/1998	03/12/1998	03/24/1998
1223W	04/30/1997	Jun-98	04/14/1997	05/13/1997		04/16/1997	04/21/1997		05/14/1997
1245N	11/27/1996		11/08/1996	02/24/1997					12/07/1996
1253N	05/16/1997	Apr-98	04/28/1997	05/13/1997		05/05/1997	04/29/1997		05/12/1997
1254N	05/23/1997	Jul-98	04/28/1997	05/13/1997		04/23/1997	04/22/1997		05/12/1997
1272N	08/08/1997	Jun-98	07/29/1997	06/15/1998		07/28/1997	07/28/1997		
1322N	03/11/1997	May-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997	02/14/1997	02/27/1997
1373N	09/15/1997	May-98	08/26/1997	04/22/1998			08/22/1997	08/28/1997	09/10/1997
1374N	05/28/1997	May-98	05/01/1997				04/30/1997	05/12/1997	05/14/1997
1392N	02/28/1997		02/20/1997				02/19/1997		02/27/1997
1393N	10/24/1997		10/21/1997			10/15/1997	10/08/1997		10/21/1997
1396N	05/12/1997	May-98	05/01/1997			05/28/1997			05/12/1997
1397N	10/17/1997		09/26/1997		10/20/1997	10/01/1997	09/26/1997		10/14/1997
1408N	02/06/1998	Jun-98	01/08/1998	04/22/1998	01/20/1998		01/08/1998	03/05/1998	01/21/1998
1411N	11/14/1997	Jul-98	10/23/1997			11/05/1997	10/24/1997		11/04/1997
1413N	06/25/1997	Jun-98	06/16/1997	06/17/1997		06/11/1997			07/11/1997
1414N	02/28/1997	Jul-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997		02/28/1997
1426N	12/08/1997	Sep-98	12/04/1997		12/03/1997	12/10/1997	12/03/1997		12/17/1997
1433N	11/07/1997	Jun-98	10/21/1997			10/24/1997	10/16/1997		11/13/1997
1440N	02/06/1998	Apr-98	01/08/1998	01/09/1998	01/20/1998	01/27/1998	01/08/1998		01/21/1998
1453N	02/06/1998	Jul-98	01/08/1998				01/08/1998	03/09/1998	01/26/1998
1454N	04/27/1998		04/27/1998			04/20/1998	04/16/1998	04/23/1998	07/09/1998
1460N	10/22/1997		10/21/1997			10/24/1997	10/10/1997		10/21/1997
1461N	03/06/1998	Jul-98	02/20/1998	04/02/1998			02/20/1998		
1474N	06/22/1998	Jul-98	06/03/1998	06/17/1998	06/02/1998	06/09/1998		06/02/1998	06/03/1998
1475N	12/24/1997		12/12/1997		01/20/1998	01/06/1998	12/15/1997		
1477N	11/09/1998	Jun-98	10/16/1998	11/12/1998	11/02/1998		10/16/1998	11/20/1998	10/20/1998
1488N	06/20/1997	Apr-98	06/09/1997			06/04/1997	06/03/1997		06/16/1997
1491N	09/25/1997	May-98	09/18/1997	06/30/1997		09/24/1997	09/16/1997		
1519N	01/23/1998	Jun-98	12/30/1997				12/30/1997	01/09/1998	01/26/1998
1528N	08/25/1997	Mar-98	08/20/1997		10/03/1997		08/21/1997		09/08/1997
1547N	01/16/1998		12/15/1997		01/20/1998	01/06/1998	12/17/1997		12/23/1997
1548N	01/09/1998		12/22/1997	04/13/1998	12/30/1997	01/09/1998	12/29/1997		01/06/1998
1550N	01/30/1998				01/20/1998	02/12/1998	01/14/1998		02/12/1998
1562N	06/26/1998		06/22/1998		06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1563N	06/25/1998		06/19/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1566N	12/19/1997		12/12/1997	12/19/1997	12/17/1997	12/17/1997	12/15/1997		
1569N	06/12/1998		05/15/1998	06/12/1998	06/17/1998	06/09/1998	05/19/1998	06/02/1998	06/09/1998
1578N	03/10/1998		03/24/1998	06/30/1998	03/09/1998		03/09/1998	03/11/1998	03/24/1998
1579N	04/17/1998			05/15/1998		04/14/1998	04/13/1998	04/13/1998	04/23/1998
1585N	09/15/1998		09/08/1998	09/02/1998	09/10/1998	09/17/1998	09/01/1998	09/21/1998	09/08/1998
1586N	10/20/1998		10/02/1998	11/06/1998	11/02/1998			10/09/1998	10/13/1998
1589N	01/22/1999		12/23/1998				12/29/1998	12/17/1998	01/26/1999
1602N	11/09/1998		10/16/1998				10/16/1998	10/13/1998	10/20/1998
1603N	07/10/1998		06/19/1998	07/10/1998		06/22/1998	06/18/1998	07/16/1998	06/23/1998

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1606N	10/29/1998		10/02/1998	11/09/1998	11/09/1998		10/06/1998	10/13/1998	10/13/1998
1631N	02/16/1999		01/19/1999					01/14/1999	
1645N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/19/1999	
1687N	08/31/1998		08/12/1998	11/06/1998	08/05/1998	08/12/1998	08/03/1998	08/03/1998	08/13/1998
1732N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/20/1999	
6094Q	06/27/1997	07/98							
7090E	03/19/1998		03/24/1998	04/22/1998				03/18/1998	
7437E	08/29/1997	Jul-98	08/05/1997	04/13/1998		08/08/1997	08/06/1997	09/23/1997	09/04/1997
7458E	02/24/1999		01/19/1999				01/13/1999	01/21/1999	
7474E	11/26/1997		11/19/1997			12/04/1997	11/20/1997		12/10/1997

Project in Progress (LOT)

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1001H	12/06/1996	12/30/1996	01/22/1997		12/05/1996	12/03/1996	12/06/1996	12/06/1996
1036N	05/28/1997	05/23/1997				06/04/1997	06/12/1997	
1077N	09/30/1997	09/24/1997			10/07/1997		11/10/1997	01/27/1998
1091N	04/30/1997					04/14/1997	05/23/1997	05/23/1997
1106N	05/16/1997	05/20/1997			05/19/1997	05/13/1997	05/19/1997	05/19/1997
1109K	04/28/1997					04/22/1997	09/24/1997	09/04/1998
1109N	12/27/1996	12/14/1996	01/29/1997	01/09/1997			06/23/1997	
1133N	10/27/1997	10/16/1997			10/20/1997	10/17/1997	11/10/1997	11/10/1997
1155N	10/21/1998	10/06/1998		11/09/1998	10/13/1998			
1195N	07/20/1996			08/02/1996		07/23/1996		
1208K	03/09/1998	03/05/1998	03/30/1998		03/10/1998		05/14/1998	
1223W	04/30/1997	04/18/1997	04/17/1997			04/25/1997	05/23/1997	03/06/1998
1245N	11/27/1996			12/02/1996	12/05/1996	11/08/1996	04/15/1997	04/15/1997
1253N	05/16/1997	05/20/1997		05/14/1997		04/29/1997	05/16/1997	05/16/1997
1254N	05/23/1997	04/28/1997				04/24/1997	06/12/1997	
1272N	08/08/1997	08/05/1997			10/07/1997	07/30/1997	09/24/1997	09/24/1997
1322N	03/11/1997	03/11/1997	04/21/1997	03/25/1997		03/03/1997	04/18/1997	04/18/1997
1373N	09/15/1997	09/12/1997		11/07/1997	10/07/1997		11/10/1997	12/22/1997
1374N	05/28/1997	05/20/1997				04/29/1997	09/24/1997	03/06/1998
1392N	02/28/1997	02/28/1997	04/21/1997	03/18/1997		02/24/1997		
1393N	10/24/1997		10/22/1997		10/14/1997	10/16/1997	11/10/1997	
1396N	05/12/1997			05/14/1997		04/30/1997	06/12/1997	
1397N	10/17/1997	09/30/1997			10/07/1997	09/29/1997	11/10/1997	11/10/1997
1408N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1411N	11/14/1997	11/07/1997			10/29/1997	10/29/1997	12/22/1997	12/22/1997
1413N	06/25/1997				10/07/1997	06/09/1997	06/23/1997	
1414N	02/28/1997		04/17/1997	03/18/1997		02/13/1997	04/15/1997	04/15/1997
1426N	12/08/1997				12/12/1997	12/04/1997		02/20/1998
1433N	11/07/1997	11/07/1997			10/21/1997	10/16/1997	11/25/1997	12/22/1997
1440N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1453N	02/06/1998	01/13/1998			01/14/1998		02/12/1998	
1454N	04/27/1998		04/20/1998		04/23/1998		07/09/1998	07/09/1998
1460N	10/22/1997	10/16/1997			10/20/1997	10/08/1997	11/25/1997	12/22/1997
1461N	03/06/1998	02/20/1998	03/30/1998		02/27/1998		05/14/1998	
1474N	06/22/1998	06/18/1998	06/05/1998		06/03/1998	10/08/1998	07/13/1998	
1475N	12/24/1997		01/14/1998		12/19/1997		01/27/1998	
1477N	11/09/1998	10/15/1998			10/13/1998			12/01/1998
1488N	06/20/1997	06/19/1997			06/09/1997	06/02/1997	08/08/1997	
1491N	09/25/1997	09/24/1997			10/07/1997	09/15/1997	11/10/1997	02/12/1998
1519N	01/23/1998				01/06/1998		02/12/1998	
1528N	08/25/1997	08/26/1997			10/07/1997	08/20/1997	09/26/1997	09/26/1997
1547N	01/16/1998		03/30/1998			12/15/1997	02/12/1998	
1548N	01/09/1998	12/29/1997	01/14/1998		12/29/1997	12/19/1997	02/12/1998	
1550N	01/30/1998		03/30/1998		01/21/1998	01/23/1998	04/07/1998	
1562N	06/26/1998	06/22/1998	06/23/1998		06/19/1998	06/19/1998	09/25/1998	
1563N	06/25/1998	06/22/1998	06/23/1998		06/19/1998	06/16/1998	10/27/1998	
1566N	12/19/1997		01/14/1998		12/19/1997	12/10/1997	02/20/1998	
1569N	06/12/1998	06/08/1998	05/19/1998		05/21/1998	05/15/1998	07/13/1998	
1578N	03/10/1998	03/11/1998				03/09/1998	05/14/1998	
1579N	04/17/1998	04/20/1998	04/20/1998		04/20/1998			
1585N	09/15/1998		08/28/1998	11/09/1998	08/31/1998	09/10/1998	10/27/1998	

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1586N	10/20/1998			11/09/1998	10/01/1998			
1589N	01/22/1999	12/21/1998			12/29/1998			
1602N	11/09/1998	10/15/1998	12/02/1998		10/13/1998			
1603N	07/10/1998	06/17/1998	08/04/1998		06/16/1998	10/08/1998	11/12/1998	
1606N	10/29/1998			11/09/1998	10/13/1998			
1631N	02/16/1999	01/20/1999			01/21/1999			
1645N	02/24/1999	01/25/1999				01/19/1999		
1687N	08/31/1998	08/07/1998	08/04/1998	11/09/1998	08/07/1998		10/06/1998	
1732N	02/24/1999	01/20/1999			01/20/1999	01/19/1999		
6094Q	06/27/1997	09/19/1998			10/07/1997	06/13/1997	09/24/1997	09/24/1997
7090E	03/19/1998		01/05/1999		04/08/1998			
7437E	08/29/1997	08/26/1997			10/07/1997	08/07/1997	09/24/1997	09/24/1997
7458E	02/24/1999	01/20/1999			01/20/1999	01/19/1999		
7474E	11/26/1997				11/25/1997	11/17/1997	02/12/1998	

Projects in Progress (LOT)

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1001H	12/06/1996	12/02/1996	12/02/1996		12/05/1996	12/23/1996	12/02/1996	12/05/1996
1036N	05/28/1997	05/19/1997	05/21/1997		05/23/1997	05/29/1997		05/28/1997
1077N	09/30/1997	09/19/1997			09/15/1997	09/24/1997	09/11/1997	10/02/1997
1091N	04/30/1997	04/09/1997			04/09/1997	04/14/1997	05/14/1997	04/10/1997
1106N	05/16/1997	05/06/1997		05/13/1997	05/13/1997	05/29/1997	05/14/1997	05/28/1997
1109K	04/28/1997	04/18/1997	04/24/1997	04/24/1997	04/16/1997	04/25/1997	05/14/1997	05/08/1997
1109N	12/27/1996	12/12/1996	01/06/1997		12/16/1996	12/23/1996	12/19/1996	12/10/1996
1133N	10/27/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1155N	10/21/1998	10/05/1998			10/15/1998		01/11/1999	10/15/1998
1195N	07/20/1996		07/17/1996		07/19/1996		07/30/1996	07/15/1996
1208K	03/09/1998	03/06/1998	03/20/1998		03/17/1998		04/08/1998	04/03/1998
1223W	04/30/1997	05/05/1997	04/24/1997		04/16/1997		05/14/1997	04/24/1997
1245N	11/27/1996		11/13/1996		11/20/1996		12/02/1996	11/19/1996
1253N	05/16/1997	05/01/1997			05/02/1997	05/29/1997	05/14/1997	06/03/1998
1254N	05/23/1997	04/29/1997			04/29/1997	05/29/1997	05/14/1997	05/08/1997
1272N	08/08/1997	08/12/1997			08/05/1997	08/08/1997	08/08/1997	08/15/1997
1322N	03/11/1997	02/18/1997			03/13/1997	02/27/1997	04/21/1997	02/20/1997
1373N	09/15/1997	08/27/1997			09/04/1997	09/24/1997	09/15/1997	09/22/1997
1374N	05/28/1997	05/01/1997			05/06/1997	05/29/1997	05/14/1997	05/08/1997
1392N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1393N	10/24/1997	10/14/1997			10/15/1997	11/18/1997	12/11/1997	10/16/1997
1396N	05/12/1997	05/05/1997			05/13/1997	05/29/1997	05/14/1997	05/28/1997
1397N	10/17/1997	09/26/1997			10/02/1997	11/19/1997		10/16/1997
1408N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1411N	11/14/1997	10/28/1997	11/13/1997		10/31/1997	11/19/1997	11/10/1997	11/13/1997
1413N	06/25/1997	06/11/1997			06/19/1997	06/10/1997	08/08/1997	06/20/1997
1414N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1426N	12/08/1997	12/03/1997	12/20/1997		12/17/1997	02/12/1998	12/08/1997	12/12/1997
1433N	11/07/1997	10/20/1997	10/28/1997		10/23/1997	11/19/1997	11/10/1997	11/13/1997
1440N	02/06/1998	01/12/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1453N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1454N	04/27/1998	04/20/1998			04/28/1998	05/20/1998		05/11/1998
1460N	10/22/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1461N	03/06/1998	02/20/1998			02/20/1998	05/20/1998	04/08/1998	02/20/1998
1474N	06/22/1998				06/09/1998			06/03/1998
1475N	12/24/1997	12/13/1997	12/19/1997		12/19/1997	02/10/1998	12/29/1997	11/29/1908
1477N	11/09/1998	10/08/1998			10/19/1998		01/12/1999	10/27/1998
1488N	06/20/1997	06/04/1997			06/11/1997	07/11/1997	08/08/1997	06/20/1997
1491N	09/25/1997	09/19/1997			09/25/1997	11/19/1997	09/19/1997	09/22/1997
1519N	01/23/1998	01/07/1998			01/14/1998	05/20/1998	01/21/1998	01/21/1998
1528N	08/25/1997	08/22/1997			08/26/1997	08/21/1997	09/15/1997	09/22/1997
1547N	01/16/1998	12/19/1997			12/19/1997		12/29/1997	01/12/1998
1548N	01/09/1998	01/07/1998			01/14/1998	02/12/1998	12/29/1997	01/12/1998
1550N	01/30/1998	01/16/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1562N	06/26/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1563N	06/25/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1566N	12/19/1997	12/13/1997	12/19/1997		12/17/1997	02/10/1998	12/29/1997	01/12/1998
1569N	06/12/1998	05/19/1998			06/03/1998	05/20/1998		06/08/1998
1578N	03/10/1998	03/10/1998			03/17/1998		04/08/1998	04/03/1998
1579N	04/17/1998	04/13/1998	04/28/1998			05/20/1998		04/16/1998
1585N	09/15/1998		08/31/1998		09/15/1998		01/07/1999	09/11/1998
1586N	10/20/1998	09/28/1998			10/06/1998		01/07/1999	10/15/1998
1589N	01/22/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998		01/12/1999	01/07/1999
1602N	11/09/1998	10/08/1998			10/19/1998		01/11/1999	10/27/1998
1603N	07/10/1998	06/15/1998			06/19/1998		01/11/1999	07/07/1998

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
		SEW=SEWER											MF=Mill & Fill		
		S&H=STREETS AND HIGHWAYS						?	= Exact year of construction not known				OL=Overlay		
		CON=CONFLICT							= New or revised project				RE=Reconstruction		
									= Under construction				JP=Joint Project		
	CLASS A EMERGENCY PROJECTS														
1615N		SEW	1998		Jackson	Montgomery	Columbus	1876	?	4 x 6	BRICK	Bad shape, out of round, crown sagging			100
1615N		SEW	1998		Columbus	Jackson	Pacific	1900	?	16"/18"	CP/BRICK				100
1615N		SEW	1998		Kearny	Jackson	Pacific	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1615N		SEW	1998		Kearny	Jackson	Washington	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1619N		SEW	1998		60 Scenic Way Easement Sewer (Assessor's Block 1303)					8"	VCP	Cracks and collpased sections			50
1621N		SEW	1998	1998	Anza	7th Ave	8th Ave	1908	?	2'6"x3'9	BRICK	Cracks and collpased sections			162
1622N		SEW	1998		3rd St	Jerrold	Kirkwood			18"	VCP	Many cracks, collapsing sections			250
1622N		SEW	1998		3rd St	Kirkwood	LaSalle			42"	CONC	Re-alignment			250
1622N		SEW	1998		3rd St	LaSalle	McKinnon			42"	CONC	Re-alignment			250
1622N		SEW	1998		3rd St	McKinnon	Newcomb			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		3rd St	Newcomb	Oakdale			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		3rd St	Oakdale	Palou			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		Donner	Jennings	Ingalls			15"	ISP	Hydraulically inadequate sewer			250
1622N		SEW	1998		Jennings	Egbert	Donner			N/A		Hydraulically inadequate sewer			250
1623N		SEW	1998		Green	Polk	Van Ness	1890	?	16"	VCP				150
1218N	BSSR	SEW	1998		Harrison	5th St	Morris	1935		12/18/21	VCP	Severe cracks, many dips/debris restrict flow	MF	3/98	230
			1998		Polk	Grove	McAlister	1877		3x5	BRICK	Bricks missing, sand infiltration	MF	1998	129
			1998		Van Ness	Golden Gate	McAlister	1877		3x5	BRICK	Bricks missing, crown starting to collapse			200
			1998		Polk	Bush	Sutter	1877		3x5	BRICK	Bricks missing, sand infiltration, walls collapsing			160
													CLASS A EMERGENCY =		$2,942
	ACCELERATED PROJECTS														
1433N		SEW	1998	Spl	Shotwell	26th St	Army St	1890	?	15"	VCP	Street Pavement & Sewer Collapsed			99
1433N	....N	SEW	1998		Moultrie	Eugenia	Cortland	1915	?	10"	VCP	Broken pipe, cracks, infiltration			111
1433N	....N	SEW	1998	136	26th St	Dolores	Church	1885		15"	VCP	Many medium & minor cracks, severe grout	MF		205
1432N	....N	SEW	1998		Post	Baker	Broderick	1900		18"	VCP	Joints open throughout, open ss, sand infiltration	MF	1/01	162
1432N	....N	SEW	1998		Post	Broderick	Divisadero	1900		18"	VCP	Collapsed @ 84-97' c-d, cracks @ 10-31'b-c	MF	1/01	162
1330N		SEW	1998		09th St	Harrison	McLea Ct MB	1900	?	24"	VCP	Crushed pipe @ 194-208, full of debris,dip			90
1547N	BSSR	SEW	1998		33rd Ave	Irving	Judah	1925	?	12"	ISP	Many St depressions, severe offsets, breaks @ ss's	MF	3/98	159
1547N		SEW	1998		Lyon	Hayes	Grove	1888		16"	ISP	Many St depressions, open joints, cracks, breaks; c-b			77
1547N		SEW	1998		Molimo	Bella Vista	Intersection	1946	?	12"/15"	VCP	Collapsed & crushed section @ 21'	MF		19
1569N		SEW	1998		Dolores	16th St	17th St	1889	?	18"	VCP	Egg shaped, Multiple cracks @ invert			168
1569N		SEW	1998		Dolores	17th St	18th St	1889	?	18"	VCP	Collapsing section, open joints			135
1569N		SEW	1998		York	21st St	22nd St	1888		10"	VCP	Collapsed sections			135
1625N	1385N	JP/S&H	1998		Lombard	Leavenworth	Jones	1900	?	18"	ISP	Cracks, open joints, fast flow	RE	Jul-98	100
1626N		SEW	1999		05th Ave	Irving	Lincoln	1900	?	12"	ISP	Many bad cracks; many street depressions			195

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1626N		SEW	1999		04th Ave	Lincoln	Hugo					Many cracks; crushed, street depressions			105
1626N		SEW	1999		Stanyan (west sic	Turk	Anza					Many bad cracks; many street depressions			185
1626N		SEW	1999		Paris	Brazil	Excelsior					Bad cracks; open joints, street depression			105
1362N	BSSR	JP/S&H	1999	188	Kate	End South	Bryant	1900	?	16"	VCP	Severe cracks 162-170' b-a; TV'd 13' b-c, offset	RE	Jul-99	100
1362N	BSSR	JP/S&H	1999	188	Gilbert	End South	Brannan	1900	?	12"	VCP	Cannot TV, flow is too high, sump area	RE	Jul-99	100
			1999		Chestnut	Fillmore	Steiner	1900		8"	VCP	Open joints, cracks, ss open, collapsed sections			100
			1999		21st Ave.	Ortega	Noreiga	1925		15"	VCP	Offsets, separated joints,holes, street depression.	MF	Jul-99	200
	. . . N		1999		Goettingen	Ward	Ordway	1915	?	8"	ISP	Open ss connections, sand infiltration, pavement sinkii	RE		100
	1668N		1999		Golden Gate	Lyon	Central	1887		16"	ISP	Crushed pipe, offsets, streetfailure	MF	Jul-99	100
	. . . N		1999		Gough	Post	Geary	1911		12"	VCP	Offset joints, cracks, street depressions	RE?		100
												ACCELERATED PROJECT TOTAL =			$3,012
	1ST PRIORITY PLANNED PROJECTS: Critical Replacements-Severely collapsed/crushed sewers recommended for immediate replacement														
1491N	BSSR	SEW	1998	W-014	Pacific	Stockton	Grant	1876		3'x5'	BRICK	Fairly bad shape, out of round, missing mortar	MF	1/98	134
1426N	BSSR	SEW	1998		Clinton Park	Guerrero	Valencia	1878		12"	ISP	Offsets, infiltration, many depressions	MF	7/98	139
1426N	....N	SEW	1998		Valencia	15th St	16th St	1890	?	3x5	BRICK	Bad shape, collapsed @ 447 Valencia			418
1426N		SEW	1998		Dore	Bryant	Harrison	1912	?	16"	VCP	Many cracks, offsets, dip, street depressions			140
1503N		SEW	1998		10th Ave	Kirkham	Judah MB	1902		12"	VCP	Cracked sections and many offsets b-c			75
1503N		SEW	1998		10th Ave	Pacheco	Ortega MB	1906	?	12"	ISP	Severe offsets, depressions, fast flow, worn invert			75
1461N	BSSR	SEW	1998		Mason	Ellis St.	Eddy St.	1880	?	3x5	BRICK	Severly deformed crown,missing bricks	OL		95
1461N	....N	SEW	1998		Pine	Hyde	Leavenworth	1880	?	3x5	BRICK	Fairly bad shape (oval), 3 broken s/s			280
1461N	1727N	SEW	1998		Leavenworth	O'Farrell	Geary	1900	?	3x5	BRICK	Bad shape	MF	7/99	221
1461N		SEW	1998		Meacham	Post	End: South		?	8"	VCP	Severe cracks and damaged ss connections			60
1488N		SEW	1998		California	10th Ave	11th Ave	1900	?	8"	VCP	St. depression; crushed / collapsed			65
1488N		SEW	1998		24th Ave	California	Clement MB	1907		8"	ISP	Cracks, breaks, dip, street depressions			100
1550N		SEW	1998		Day St	Dolores	San Jose	1888		18"	ISP	Collapsed pipe			70
1550N		SEW	1998		Congo	Monterey	Hearst	1910	?	12"	VCP	Multiple cracks, st dep @ 147-159' b-c, infiltration			72
1550N	BSSR	SEW	1998		Congo	Melrose	Mangels	1910		8"	VCP	Many cracks over the block	OL		60
1550N	BSSR	SEW	1998		Marston	Circular	Edna	1910		8"	ISP	Many severe cracks	MF		114
1550N	BSSR	SEW	1998		Cuvier	Bosworth MB (m	Mirando (mhE)	1902		15"	VCP	Multiple cracks & egg shape @ 64-140' d-e	MF		90
1550N		SEW	1998		28th St	Noe	East Xing	1900	?	15"	VCP	Bad open joints @20-50'			139
1562N	....N	SEW	1998		Broadway	Taylor	Himmelmann	1952		16"	VCP	Collapsed & Crushed	RE	1/99	56
1562N	....N	SEW	1998		Broadway	Florence	Taylor	1900	?	12"	VCP	Crushed invert, mult cracks	RE	1/99	63
1562N	....N	SEW	1998		Broadway(N Sid	Cyrus Pl	Hyde MB	1952		21"	VCP	Mult cracks, ready to collapse a-b	MF	1/99	54
1562N		SEW	1998		Bryant	18th St	19th St	1889		14"	VCP	Many cracks; pipe collapses			108
1562N		SEW	1998		Sonoma	Union	Green		?	12/15"	VCP	Crushed,broken pipe, ready to collapse			75
1606N	BSSR	SEW	1999	211	Douglass	23rd St	Elizabeth	1890	?	15"	VCP	Severe offsets, separated ss's, st depn	OL		111
1606N		SEW	1999	397	Cayuga	Seneca	Junior Terr	1939		8"	VCP	Many offsets, large street depressions, infiltration			50
1606N		SEW	1999	sp1001	Laurel	Washington	Jackson	1900	?	12"	CP	Multiple severe offsets, street depressions			86
1606N		SEW	1999	sp2001	Rondel Pl	End S(17th St)	16th St	1890	?	12"	ISP	Crushed, multi-cracked sections, severe offsets			138
			1999		Bertita	Seneca	end			8"	VCP	Street collapsing (field check) several bad sections			
1155N		SEW	1999		Chestnut	Culebra	Polk	1913		12"	ISP	Numerous Cracks, Collapsed Pipe			68
1155N		SEW	1999		Chestnut	Powell	Stockton	1890		16"	CEM	Cracks, invert erosion			140
1155N		SEW	1999		Grant	Chestnut	Francisco	1918	?	14"	VCP	Offsets, Crushed Pipe, Debris			99
1155N		SEW	1999		Grant	Greenwich	Lombard	1918	?	16"	VCP	Cracks, Dip, Cement Pipe			107

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1218N?		SEW	1999		Market S. Side	9th Street	10th Street	1878		3x5	BRICK	Ready to collapse			353
1218N?	....N	SEW	1999		Larkin	Golden Gate	McAllister	1874		18"	VCP	Collapsed, continuous cracks	MF		109
		SEW	1999	210	Eugenia	Prospect	Coleridge	1920	?	12"	ISP	Severe offsets, breaks, bad ss, rat, street depressions			
							NOTE: Projects with estimates rounded to 100k have not been finalized and will be revised after sizing.								
												PRIORITY 1 (Planned Projects) TOTAL =			**$3,964**
	2ND PRIORITY PLANNED PROJECTS: Severely cracked/crushed sewers to be replaced on a normal contract schedule.														
1254N	....N	SEW	1998		11th St	Folsom	Harrison	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			360
1603N		SEW	1998		Broad	Capitol	Plymouth	1910	?	8"	ISP	Many depressions, complaints, MUNI track replmt			215
7474E	BSSR	SEW	1998		Delancey (1st St)	Townsend	Brannan	?		12"/15"	VCP	Collapsed sections	MO		207
7474E		SEW	1998		Pine	Battery	Front	1907		18"	ISP	Collapsed, Cracks			86
7474E	1407N	SEW	1998		California	Webster	Buchanan	1880	?	15"	CEM	Offsets, hole @ 104',open joints st depressions	MF	1/1/01	142
7474E	1407N	SEW	1998		California	Laguna	Buchanan	1876	?	16"	CEM	TV'd 35', Collapsed	MF	1/1/01	323
1392N	1108N	JP/S&H	1998		Bayshore E	Oakdale MB	Jerrold	1928		15"/12"	VCP	Cracked (replace a-c), dip, debris	MF	1/98	75
1392N	1108N	JP/S&H	1998		Bayshore E	Oakdale	Jerrold MB	1928		15"/12"	VCP	Cracked (replace a-e), damaged @ 3' e-f	MF	1/98	178
1393N		SEW	1998		Bush	Kearny	Montgomery	1880	?	3x5	BRICK	Fairly bad shape,bricks, plastering			250
1393N	1453N	SEW	1998		Kearny	Sutter	Bush	1890	?	3x5	BRICK	Fairly bad shape, loose bricks	OL	10/98	208
1393N	BSSR	SEW	1998		Post	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, missing & loose bricks	MF		274
1393N	1453N	SEW	1998		Kearny	Sutter	Post	1875	?	3x5	BRICK	Bad shape, debris, crown sagging	MF	10/98	77
1393N	....N	SEW	1998		Sutter	Montgomery	Intersection	1876	?	3x5	BRICK	Intersection in bad shape	MF	1/1/01	50
1393N		SEW	1998		Bush	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, crown sagging			115
1397N	....N	SEW	1998		Ord	Corbett	Market	1900	?	15"	VCP	Cracks, cracked invert, severe offsets	MF		43
1397N	7317E	SEW	1998		Dolores	28th St	Valley	1885	?	18"	VCP	Crushed and multiple cracks	MF/JP		89
1397N	BSSR	SEW	1998		23rd St	Castro	Diamond	1888	?	15"	VCP	Severe cracks @ 25-70', heavy debris, dip	MF		180
1411N		SEW	1998		Harding Park	Skyline	Zoo					New Sewer			
1413N	6094Q	S&H	1998		Davis (Blk #200	Clay	Washington	1878	?	3x5	BRICK	Bad shape, debris, missing bricks & mortar	RE/JP		167
1413N	BSSR	SEW	1998		Francisco	Stockton	Powell	1876	?	3x5	BRICK	Bad shape 1/2, fairly bad shape 1/2	MF		290
1413N	1453N	SEW	1998		Kearny	Green	Union	1900	?	12/8"	VCP	Crushed & cracked sections	MF	10/98	99
1474N	BSSR	SEW	1998		43rd Ave	Anza St	Balboa MB	1917	?	15"	VCP	Many cracks @ mh b-c exfiltration @ 120' b-c	OL		95
1474N	....N	SEW	1998		08th Av	Fulton	Cabrillo	1907	?	8"	VCP	Numerous cracked sections, collapse			168
1474N	BSSR	SEW	1998		06th Ave	Cabrillo	Balboa	1902	?	12"	VCP	Many cracked sections; sev. open joints., bad ss & mh	MF		133
1474N	BSSR	SEW	1998		06th Ave	Fulton	Cabrillo	1907	?	8"	ISP	Many cracked sections, hole (repair done 1/12/96)	MF		168
1548N	....N	SEW	1998		O'Farrell	Anza Vista	Masonic	1947		15"	VCP	Numerous cracks			140
1548N	BSSR	SEW	1998		Deming	Clayton MB	Uranus	1920		12"	ISP	Ready to collapse	OL		105
1548N		SEW	1998		Iron Alley	Corbett	Clayton	1917	?	15"	VCP	Offsets, roots, Hole invert @ 140' b-c			129
1548N		SEW	1998		Farnsworth	Edgewood	Willard		?	12"	VCP	Severe cracks, stopped @ 83'; recommend lining			67
1579N	1454N	JP/S&H	1998		Illinois	20th St	19th St	1910	?	18"	VCP	Multi cracked, crushed sections b-c; TV'd 60' b-c	TR	5/98	132
1475N	1389N	JP/S&H	1998		Virginia	Coleridge	Mission St	1905	?	16"	VCP	BSSR RECOMMENDED REPLACEMENT			85
1475N	1389N	JP/S&H	1998		Fair St	Coleridge	Mission	1890		12"	VCP	Mult joint offsets,cracks, infiltration, st. depression		1/99	90
1475N	1389N	JP/S&H	1998		Godeus	Coleridge MB	Mission		?	15"	VCP	Cracks/crush @123'-145'; cracks; open joints b-c	MF	1/99	70
1563N	BSSR	SEW	1998		42nd Ave	Geary	Anza	1920	?	8"	VCP	Street depression, collapse; sev. open joints	MF		145
1563N	....N	SEW	1998		Balboa	Arguello	2nd Ave	1907	?	18"	ISP	Multiple cracks			107
1563N	BSSR	SEW	1998		03rd Ave	Balboa	Anza	1908	?	8"	VCP	Many street dep.; many cracks/holes ms/s	MF		158

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1563N		SEW	1998		20th Ave	Fulton	Cabrillo	1915		8"	ISP	Numerous street depressions			135
	98-99 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1477N		1999	201	Hamilton	Dwight	Woolsey	1952		12"	VCP	Cracks; crushed section (needs lining)	RE	1999	60
	1477N		1999	201	Dartmouth	Dwight	Woolsey	1952		12"	VCP	Invert cracks, Open joints (needs lining)	RE	1999	60
	7458E		1999	7	Clay	Jones MB	Taylor	1889	?	12"	?	Offsets, cracks, dip	RE	1999	90
1578N	1668N	JP/S&H	1999		Golden Gate	Polk St	Van Ness	1873		3'x5'	BRICK	Many St. depressions, Rec. by BSSR	MF	6/99	146
1578N	W-2240	JP/WD	1999		Golden Gate	Scott MB	Pierce	1875		14"	ISP/CP	Cement pipe sections, badly crackec	MF	6/99	80
1628N		S&H	1999		Moraga St	17th Ave	18th Ave								
1583N		SEW	1999		Everglade	Gellert	Lake Merced		?	21"	VCP	Easement;collapsed @ 30-40' a -b; exfiltration(line?			49
1583N	....N	SEW	1999		Victoria	Randolph	Brotherhood	1920	?	12"	ISP	Open break @112-115', cont. cracks, mh b-c			163
1583N	.......N	SEW	1999		Revere	Griffith	Hawes MB	1930		8"	VCP	Many severe cracks/crushed mh b-c	RE		70
1583N		SEW	1999		Bridgeview	Topeka	Thornton	1941		12"	VCP	Many cracks & ss problems, invert break			185
1395N		SEW	1999		Sacramento	Grant	Kearny	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			274
1395N		SEW	1999		Larkin	Pine	Bush	1875	?	3x5	BRICK	Bad shape, many loose bricks			208
1395N	1453N	SEW	1999		Sacramento	Sansome	Battery	1908		12"	ISP	Many cracks, crushed sections, debris	MF	10/98	80
1395N	....N	SEW	1999		Pine	Polk	Larkin	1880	?	3x5	BRICK	Fairly bad shape (230'), st. depression			280
START FY 99-00															
		SEW	1999		Cesar Chavez (A	Bryant	York		?	12"	VCP	Many cracks and collapsed sections			60
		SEW	1999		Folsom	Bessie	Precita	1890	?	16"	VCP	Collapsed sections, severe offsets,open ss, fast flow			39
	....N	SEW	1999		Larkin	Grove	Hayes	1915		18"	VCP	TV'd 190', collapsed, dip, debris			92
		SEW	1999		Winding Way	Prague	Xing	1915	?	8"	VCP	Collapsed & crushed pipe, exfiltration			30
1585N	BSSR	SEW	1999		05th Ave	Balboa	Anza	1908	?	16"	VCP	Severe cracks, depn @ 8-37 c-b, many separated ss	MF		166
1585N		SEW	1999		21st Ave	Clement	California	1902	?	8"	VCP	Severe offsets,Separated ss's, st. depressions			122
1585N	1407N	SEW	1999		California	Parker	Maple	1900	?	16"	VCP	Severe open joints, st. depression; Lining rec.	MF	1/1/00	30
1586N	.....N	SEW	1999		Geary Bl. S. Side	Lyon	Baker	1879		18"	VCP	Severe multi cracks, fast flow, begin to collapse	MF		151
1586N	.....N	SEW	1999		Geary Bl. S. Side	Baker	Broderick	1879	?	18"	VCP	Multi cracks, roots, fast flow	MF		138
1586N	1732N	SEW	1999		Turk	Broderick	Divisadero	1881		16"	ISP	Cracks, collapsed section	MF	7/99	152
	99-00 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
1586N	1732N	SEW	1999		Eddy	Pierce	Steiner	1875		3x5	BRICK	Bad shape (50'), rest needs plastering	MF		280
1586N	1732N	SEW	1999		Eddy	Steiner	Fillmore	1875		3'x5'	BRICK	Bad shape, missing bricks, mortar crown & walls; dirt	MF	7/99	153
1586N		SEW	2000		Elm	Scott MB	Pierce	1908	?	15"	ISP	Egg shape cracks & offsets			55
1587N		SEW	2000		07th Ave	Moraga	Lincoln	1890	?	3'x5'	Conc/Br	Fairly bad shape; Install spray-on mortar lining.			100
1587N	....N	SEW	2000		Kirkham	6th Ave MB	7th Ave	1906		18"	VCP	43 foot run with cracks throughout			107
1590N	7291E	SEW	2000		Ocean	San Leandro	San Fernando	1913		15"	VCP	Many severe cracks @ 1-90' a-b	MUNI	4/99	40
1590N	7291E	SEW	2000		Ocean	San Fernando	Junipero Serra	1913		18"	VCP	Severe Offsets & many cracked sections	MUNI	4/99	40
1590N	7291E	SEW	2000		Ocean	Pinehurst	Manor	1913		18"	VCP	Many cracked sections	MUNI	4/99	56
1589N		SEW	2000		Clipper	Douglass	Diamond MB	1962		15"	VCP	No TV Log; Many large cracks invert, exfiltration; fast flow			82
1589N	....N	SEW	2000		Noe	26th St.	Clipper MB	1888		18"	VCP	Cracks throughout, 33' run(debris)			101
1589N	BSSR	SEW	2000		Fair Oaks	22nd St	23rd St	1878		15"	ISP	Submerged, pipe coming apart. Rec by PUC	MF		144
1589N		SEW	2000		Kingston	Mission	San Jose	1910	?	12"	VCP	Many cracks , dip, size changed to 6"			40
1588N		SEW	2000		Joost	Acadia	Brompton	1926	?	12"	ISP	Many open joints, infiltration, street depresions			150
1588N	6680E	S&H	2000		Alemany	Prentiss	Putnam		?	12"	VCP	Badly crushed pipe	MF		110
START FY 00-01															
1588N	BSSR	SEW	2000		Mt Vernon	Delano	Cayuga	1927		12"	VCP	Crushed sections @ 88-103' a-b; st. depressior	MF		81

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1588N		SEW	2000		Kensington	Merced	Claremont	1915		12"	VCP	Replace mh a-b, otherwise fair condition			100
1602N	BSSR	SEW	2000		Minna	6th St	Russ	1908	?	18"	VCP	Cracked invert @ 76-78' c-d, st depressions	MF		112
1602N	....N	SEW	2000		02nd St	Brannan	Townsend	1890	?	18"	VCP	Many cracks / replace lower 1/2 block			160
1602N		SEW	2000		Howard	01st St	Fremont	1880	?	3'x5'	BRICK	Bad shape, needs cleaning, plaster and bricks	MF		100
1605N	BSSR	SEW	2000		Sacramento	Spruce	Maple	1890	?	8"	ISP	Many seaprated ss's; infiltration	MF		110
1605N	BSSR	SEW	2000		Pierce	Green MB	Union	1885		18"	VCP	May collapse @219'-238', 0-110' replaced	MF		96
1605N	....N	SEW	2000		Wilmot	Webster	Fillmore	1900	?	10"	ISP/CP	Multiple extensive cracks/ cement pipe			120
1629N	1734N	SEW	2000	398	Union	Hyde	Larkin	1900	?	12"/18"	ISP	Crushed invert; multiple cracks, exfiltration	MF	7/99	115
1629N	......N	SEW	2000		Union	Hyde	Leavenworth	1900	?	8"/15"	ISP	3pt cracks, errosion of cement pipe sections, hole	OL	1/99	51
		SEW	2000		Union	Divisadero	Broderick	1885	?	8"/12"	VCP	Cracks/collapse, offsets, open joints		done 4/95	125
	......N	SEW	2000		Union	Jones St	Taylor St	1900		16"	CEM	Many sections collapsed, fast flow, rat	MF	7/99	130
1629N		SEW	2000	208	Kearny	Filbert	Union	1900	?	15"	VCP	Severe offsets, crushed sections, exfiltration			78
1630N	....N	SEW	2000		Polk	Greenwich MB	Filbert	1890	?	10"/18"	VCP	Continuous cracks, offsets			109
1630N		SEW	2000	199	Francisco	Polk	Van Ness	1914		12"	VCP	Many offsets & cracks; fast flow; lining recommended			50
1630N		SEW	2000		Quincy	Pine	California	1900	?	15"	VCP	Many severe cracks, breaks			84
	00-01 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
1630N	....N	SEW	1999		Sacramento	Taylor	Mason	1875		16"	ISP	Many cracks, open joint			138
1631N		SEW	1999	383	04th Avenue	Cabrillo	Balboa	1908	?	8"	VCP	Street depressions, separated ss's, open breaks			166
1631N		SEW	1999	400	10th Ave	Clement MB	Geary	1912	?	8"	ISP	Separated ss's, st depressions, low spots, exfiltration			
1631N	......N	SEW	1999		Anza	9th Avenue	10th Avenue	1907		8"	VCP	Many separated side sewers, exfiltration	MF	1/00	55
1631N	......N	S &H	1999	366	Cabrillo St	6th Ave	7th Ave	1908	?	8"	VCP	Severe open breaks, street depressions	MF		63
1632N	......N	SEW	1999		Post	Lyon	Baker	1900		18"	VCP	ss separated ; hole invert 233-239' a-b, offses, fast flov	MF	1/01	146
1632N	BSSR	SEW	1999		Grove	Baker	Broderick	1890		16"	ISP	Severe offsets, cracks; crushed section	OL		119
1632N		SEW	1999		Potomac St	Waller St	End South	1930	?	8"	VCP	Mult cracks, separated ss, infiltrtion, st. depn			79
1633N		SEW	1999		Greenwich	Webster	Fillmore								
1633N		SEW	1999		Precita South	Coso	Emmet Pl								
		SEW	2001	210	Precita South	Treat	Harrison	1900	?	16"	ISP	Multi cracks, loosing shape, fast flow, rat			
		SEW	2001	210	Precita South	Harrison	Alabama	1900	?	16"/18"	ISP	Many cracks, ss open @ 79' & 148' a-b, rat, replace a-b			
		SEW	2001	211	Pacific	Walnut	Laurel	1900	?	15"/12"	VCP	Cracks and open joints, street depressions, fast flow			
	......N	SEW	2001	402	Clement	27th Ave	26th Ave	1908	?	15"	ISP	Offset joints, many cracked sections			
START FY 01-02															
		SEW	2001	402	3rd St	4th St MB	16th St	1911		12"	VCP	Many cracked sections, collapse @ 27' b-a			
		SEW	2001		Hayes	Larkin	Polk	1890	?	3x5	BRICK	Bad shape, severe sags, missing bricks,bulging			190
	BSSR	SEW	2001		Sterling	I-80 ramp	Bryant	1900	?	12"	CEM	Multi cracks; ready to collapse; Rec. lining	MO	10/98	56
	BSSR	SEW	2001		Jones	Bernard	Pacific	1906	?	12"	VCP	Multiple cracked & collapsed sections	MF	n/a	40
	....N	SEW	2001		Bryant	7th St	Gilbert	1876	?	3x5	BRICK	Bad shape, cracks on crown, ready to cave in	MF		119
	....N	SEW	2001		Townsend	7th St Mb	8th St Mb	1921		12"	VCP	Dips, Cracks, Crushed			167
		SEW	2001		Esmt blk #4315/1	Minnesota	3rd St	1949		12"	VCP	Several severe cracks & collapses			145
		SEW	2001		Esmt Blk #4317	Indiana	Minnesota	1949		12"	VCP	Severe multiple cracks			74
		SEW	2001		22nd Ave	Irving	Lincoln	1910	?	18"	VCP	Many active street depressions.			190
		SEW	2001		Folsom	18th St MB	17th St	1946		15"	VCP	Cont cracks 55-130', depression 157' b-c			145
	....N	SEW	2001		Rincon	Bay Bridge	Bryant	1917	?	12"	VCP	Collapsed			70
	....N	SEW	2001		Harrison	8th St	7th St	1880	?	3x5	BRICK	Missing mortar, loose bricks, out of rounc			550

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
	.....N	SEW	2001		Mission	13th St	14th St	1875	?	3'x5'	Brick	Bad shape, crown sagging, ready to collapse	MF		205
	....N	SEW	2001		08th St	Market	Intersection	?		15"	VCP	Cracked sects. replace (a-b) across Marke	RE		50
	01-02 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1727N	SEW	2002		Leavenworth	Washington	Jackson	1900	?	16"	VCP	Many cracks; invert break	MF	7/99	68
	....N	SEW	2002		Leavenworth	Greenwich	Lombard	1890	?	16"	VCP	Crushed Pipe, Numerous Cracks			110
	....N	SEW	2002		Geary	Mason	Powell	1880		3x5	BRICK	Bad shape, crown buckled, mortar, bricks missing	MF		115
	....N	SEW	2002		Jones	Filbert	Lombard	1919		12"	VCP	Numerous Cracks			213
	....N	SEW	2002		Buchanan	Greenwich	Lombard St	1887		18"	VCP	Cracks, offsets, open joints			120
			2002		Stonestown Trestle Removal							Trestle is an attractive nuisance			286
			2002		Chinatown Alleys(3)										150
	BSSR	SEW	2002		South Hill	Prague	Geneva	1915		8"	ISP	Broken sections, cracks	MF/OL		60
	....N	SEW	2002		Washburn	Howard	Mission	1900	?	3x5	BRICK	Fairly bad shape, bricks, broken s/s			350
	BSSR	SEW	2002		Bayshore(W Sid	Cortland	Oakdale	1928		12"	VCP	Many bad cracks & breaks	MF		93
START FY 02-03															
		SEW	2002		Esmt Block#113	End North	Anza	1935		8"	VCP	Many separated ss's from main, exfiltration			75
		SEW	2002		City View Way	Skyview	Knollview	1951		8"	VCP	Street depressions; crushed, open joints, exfiltration, fast flow			57
		SEW	2002		19th St	Collingwood	Castro	1887		18"	ISP	Open joints, bad cracks			90
		SEW	2002		O'Shaughnessy	Portola	Del Vale MB	1939		15"	VCP	Badly cracked, no tv log, sewer lining recommended		paved '96	70
		SEW	2002		Capp	21st St	20th St	1874	?	15"	CEM	Cement pipe, cracks			145
		SEW	2002		Liberty	Guerrero	Valencia	1875		15"	VCP/CP	SS discont'd @173', cracked sections			150
		SEW	2002		37th Ave	Balboa St	Cabrillo St	1920	?	18"	ISP	Offsets, several cracked sections, fast flow			207
		SEW	2002		Folsom	Precita	Army MB	1890	?	16"	VCP	Severe offsets, open invert, exfiltration, fast flow			49
		SEW	2002		Ashbury	Waller	Haight	1890		18"	VCP	Open joints, cracks; Replace Haig-Ash int.; fast flow			111
	BSSR	SEW	2002	208	Walter	Duboce	14th St	1890	?	8"	VCP	Many open breaks, separated ss, exfiltration	OL		148
		SEW	2002		Cole	Carl	Frederick	1888		3'x5'	BRICK	Bad shape			96
		SEW	2002	199	Pacific Ave	Presidio	Walnut	1900	?	12"	VCP	Crushed sections, bad side sewer, fast flow			112
		SEW	2002	398	26th Street	San Jose	Valencia	1889	?	15"	VCP	Open breaks, separated ss's, fast flow			64
	02-03 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1453N	SEW	2003		Kearny	Maiden Ln	Geary	1875	?	3'x5'	Brick	Bad shape, crown sagging, missing bricks	RE	7/98	77
	BSSR	SEW	2003		Moraga	23rd Ave	22nd Ave	1926		12"	ISP		MF		77
		SEW	2003		Lawton	21st Ave	23rd Ave	1925		15"/21"	VCP				177
		SEW	2003	382	11th Ave	Irving	Lincoln	1903	?	10"/12"	VCP	Many active street depressions, severe offsets,ss problems			
		SEW	2003		21st Ave	Moraga	Lawton	1925		15"	ISP				190
		SEW	2003		Russia	Madrid	Lisbon	1907	?	16"	VCP	Cracks, larghe street depression'			
1394N		SEW	hold		Kirkham	21st Ave	26th Ave					New Auxiliary Sewer 12"? VCP			216
				208	Morris	Harrison	Bryant	1935	?	12"	VCP	Cracks, offsets, dip	OL	1999	
												TOTAL PRIOTITY 2 PROJECTS=			**37,386**
												TOTAL EMERGENCY, ACCELERATED, & PRIOTITY 1 PROJECTS=			**$8,475**
												PRIORITY 3 PLANNED PROJECTS (not detailed)=			**$6,900**
												GRAND TOTAL=			**######**

3
79

DPW

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 408

February 11, 1999

DOCUMENTS DEPT.
MAR 10 1999
SAN FRANCISCO PUBLIC LIBRARY

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4004
Norman Chan	554-8355
Joe Ovadia	558-4004
Jean To	554-8298

Street Construction Coordination Center

Amy Chow	554-8249
Joe Norris	554-8274
Vitaly Troyan	554-5803

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Cynthia Chono	554-6196
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

Charles Kascal	554-1803

PUC Sewer R&R

(Representative not present)

San Francisco Port Authority

(Representative not present)

San Francisco Water Department

(Representative not present)

Redevelopment Agency

(Representative not present)

Caltrans

Don Manning	557-4021
Doug Sibley	510-286-5564

Caltrans Public Information

Veronica Faisant	495-5895

Pacific Bell

(Representative not present)

Pacific Gas & Electric

Gilbert Munoz	695-3550
Kathy Devine	695-3492

S F Thermal

Mike Eurkus	777-3415
Ben Stout	777-3415

Allstar / Metro Media

Nick Araujo	431-2510

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

Shaun Reid	510-782-0900

RCN

Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500

Underground Construction

Andrew McManus	882-1553

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 408

1. The members introduced themselves around the table.

2. The December 10, 1998 Minutes were approved.

3. **X-1104 Monthly Report**

Ms. Chono introduced the new monthly summary of outstanding X-1104 notices in BSM's records since July 1 of last year. Each agency will receive a detailed listing of its own notices and a summary of all forms. The summary will also be included in the monthly Minutes. BSM, on being notified by the public or observing the presence of a trench defect, determines the most likely owner, marks the defect, and notifies the owner. The recipient should either repair the defect or show that it has a different owner. When the owner notifies BSM the defect is repaired, or after 30 days, the inspector revisits the site and follows through as appropriate. This procedure is unchanged from the previous rules, under which a trench is the owner's responsibility until the street is repaved. The only new feature is the monthly summary and the more serious follow-through. The intent is to establish active communication towards achieving better street condition, given the recent decline in the City's average condition scores des[ite increased budgets and the increased volume of street work. The City's own trenches are included in this process. This is the first pass and we expect it to clear the records of things like repairs completed but not recorded, along with errors. We expect to issue a higher number of X-1104s after the wet season for rain-induced damage.

The X-1104 applies to trenches after completion. There is a separate but similar Notice of Violation for deficient trenching work in progress.

Joint trenches are the responsibility of the permittee, normally the lead agency for the site.

4. **Electronic Permitting**

Ms. Chono reported that the web site has been active since the last week of January. The Water Department has done 80% of their applications including the very first, for which we will present a certificate suitable for framing the next time a representative attends the meeting. PG&E has made 57% of their permit applications electronically, and TSC has done 100% of theirs.

So far, the system is set up for single block projects. Multiple blocks will be possible later. BSM will hold an assessment meeting in March to discuss how well the system is working and where next to develop it, including the multiple block feature. Members present agreed the system works well, and has prompted suggestions but no complaints.

Mr. Victorio would like to see an option for work in the sidewalks. Turnaround has been about two days because the handling is still in transition from manual to automated; we intend that it will eventually range from instantaneous to a few minutes.

5. **Engineer's Plan Signatures**

Mr. Troyan will discuss this issue next month.

6. **Montgomery Street Paving**

Mr. Troyan displayed a map of the project area delineating the limits of the paving and the utility work that must be done before it. In response to the Mayor's demand, the start of paving has been advanced to March 6. The Mayor has added a similar demand for paving the first three blocks of First Street by BSSR in mid-March when the paving operation starts. We are now sorting out scheduling issues with the utilities that have work in the project area. In the first block, from Market to Mission, there is a water main replacement and the Muni tracks are to be removed when the F-Line is completed in two years. The two projects together will entail complete reconstruction of that block when the tracks come out. The freeway on-ramp downstream will add to the challenges.

Kearny Street has been deferred until next year, due mainly to the number of major utility projects, particularly south of California St. The paving will probably be divided into two contracts at California St.

Mr. Troyan expressed appreciation for the cooperation we have received from the utility agencies in meeting the mandated schedule.

7. **Paving Program**

Mr. Ovadia distributed a bar chart showing the 1999 contract paving program, which notes the number of clearances we still need for each contract. We especially need to finish clearances for Mission St., which is due to begin on March 1. The scope and schedule for each project is real, not tentative.

Mr. Troyan noted that we need to clean the data of projects that are not likely to be done within the time horizon of interest. We have formed a project improvement team to discuss the clearance procedure, which will resume its meetings when we have more experience of the permit web site in operation. We have already met with PUC to remove over 500 sewer repair notations. Clearance has gained in importance because we are trying to reach a paving rate that will addresss the City's annual needs, based on total number of blocks divided by the average useful life. As part of this effort, we are revising the scheduling procedure for BSSR paving, which will now include the same 120 day notice we provide for contracts. Note also the existing "To Be Paved by BSSR" report included with the Status Report, which contains streets that BSSR has already been instructed to pave.

Ms. Chow added that many of the non-cleared blocks are so because of planned capital projects, whose project managers need to discuss scheduling with their pavement counterparts. Ms. Chono noted that permit applications in streets with approaching pavement dates will be flagged and questioned by the permit system.

Ms. Devine requested a chart similar to the 1999 projects, for 2000. Ms. Chono observed that a similar chart from PG&E would be very useful as well.

Mr. Burbank discussed non-clearances in the Status Report. Besides projects completed but not reported, there are many in the "maybe" category, that a utility thinks it might want to do sometime but has not assigned a definite schedule. This clogs the system and raises questions about distinguishing real projects from maybes. Mr. Munoz responded that in many cases, a maybe can unpredictably become an urgently real job. Its presence in the record should at least prompt an inquiry from another agency with plans for that block, to find out what the story is. Likewise, knowing of the other project allows the first utility to prod its customer, if the maybe involves a service installation that does not yet have a set date

Ms. Chono asked who should address a conflict when it appears. As the new requirements take effect, we can expect many cases in which the first appearance of a job in the Status Report will prompt others to announce their own. Mr. Ovadia and Mr. Troyan replied that the relevant project managers should negotiate the question.

8. **Caltrans**

Ms. Faisant and Mr. Sibley discussed the next six years' plans for the retrofitting work in San Francisco, involving the I-80 structures between 16th St. and the bridge. Most of the work will not affect the freeway traffic but will impact the surrounding areas. This will involve public outreach, including a web site (www.safersf.com) now under construction and expected to open in the next couple of months. The office at 833 Market St. should open in March. Ms. Faisant distributed fact sheets and other information about the projects, which are reproduced with these minutes. She will provide additional copies on request. Anyone interested in updates should ask to be on her mailing list.

There will be a community meeting about the I-80 work in March, date and time to be announced.

Mr. Troyan asked if the First St. paving would affect Caltrans. Ms. Faisant replied it would not, but that she had heard something about plans for the area by the Redevelopment Agency; it would be helpful if they were present to discuss that.

9. **Five Year Plans**

Ms. Chow reported that SCCC has hired Don Todd Associates (DTA) to develop a master schedule for FY 1999/2000. To get them started, we emailed members on January 28 asking for each agency's relevant construction start dates and duration. There has been confusion with different utilities interpreting "start date" to mean other things than the actual construction. The results, and their benefit to all, will be as good as the information. Ms. Chow distributed bar charts displaying the amount of coordination, joint trenching opportunities, and conflicts for FY 99-00. We have identified 232 blocks with utility work scheduled after paving, and 446 with joint project opportunities. The sample DTA bar chart illustrates the final product of a coordinated construction schedule for fiscal year 1999-2000.

Ms. Chow next distributed a report showing each utility's projected mitigation fees, assuming they are not waived for coordination, totaling $500,000. DPW is discussing which 20 blocks should be paved with available funds.

10. February 17 Teleconference

Mr. Troyan reminded members of the teleconference to be held at the training trailer at the DPW yard at 2323 Cesar Chavez Blvd. On February 17 from 8:30 to 12:30, at no charge to those attending.

11. New Meeting Location

Mr. Troyan deferred discussion until after we have worked out details about space at our new office location.

New Business

Mr. Munoz announced that a forthcoming meeting at PG&E will affect their representation at the CULCOP meetings. In case that function is passed to someone else, he expressed appreciation for his experiences with us during the past three years.

The next meeting will be at 10:00 am Thursday, March 11, 1998, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

SUM OF FEE TO BE PAID BY UTILITIES FOR PLANNED PROJECTS, BY FY

	AWSS	DPT	MUNI	PGE GAS	PGE ELEC	SEWER	SFWD	UGD	SUM
97-98		$6,503							**$6,503**
98-99		$38.822	$11.288	$281.947	$4.703	$55,961	$63.748	$47.266	**$503,735**
99-00	$12.435	$51,064	$13,467	$275,432	$32.063	$32,573	$56.231	$118.440	**$591,705**
2000-03	$53.663	$50,692	$178,203	$365.667	$1.380	$36,152	$253.154	$360.080	**$1,298,991**

Total amount estimated to be paid from FY 1997-2003: **$2,400,934**

*Based on utilities' five year plans, and does not account for fee waivers from coordination.

Activity ID	Activity Description	FROM	TO	Orig Dur
8702000PV	HYDE ST	FULTON ST	MC ALLISTE	5
8703000PV	HYDE ST	MC ALLISTER ST	GOLDEN GATE AV	5
8704000PV	HYDE ST	GOLDEN GATE AV	TURK ST	5
8705000PV	HYDE ST	TURK ST	EDDY ST	5
8706000PV	HYDE ST	EDDY ST	ELLIS ST	5
8707000PV	HYDE ST	ELLIS ST	O'FARRELL ST	5
8708000PV	HYDE ST	O'FARRELL ST	MABEL AL	5
8709000PV	HYDE ST	MABEL AL	GEARY ST	5
8710000PV	HYDE ST	GEARY ST	POST ST	5
8711000PV	HYDE ST	POST ST	SUTTER ST	5
8712000PV	HYDE ST	SUTTER ST	BUSH ST	5
8713000PV	HYDE ST	BUSH ST	PINE ST	5
8714000PV	HYDE ST	PINE ST	CALIFORNIA ST	5
13244000WD	PINE ST	DAVIS ST	FRONT ST	22
13245000WD	PINE ST	FRONT ST	BATTERY ST	22
13246000WD	PINE ST	BATTERY ST	SANSOME ST	22
13252000WD	PINE ST	MONTGOMERY ST	BELDEN ST	22
13253000WD	PINE ST	BELDEN ST	KEARNY ST	22
13268000WD	PINE ST	LEAVENWORTH ST	HYDE ST	22
13269000WD	PINE ST	HYDE ST	LARKIN ST	22
13270000WD	PINE ST	LARKIN ST	POLK ST	22
13271000WD	PINE ST	POLK ST	VAN NESS AV	22
13272000WD	PINE ST	VAN NESS AV	FRANKLIN ST	22
13273000WD	PINE ST	FRANKLIN ST	GOUGH ST	22
13282000WD	PINE ST	PIERCE ST	SCOTT ST	22
13283000WD	PINE ST	SCOTT ST	DIVISADERO ST	22
13284000WD	PINE ST	DIVISADERO ST	BRODERICK ST	22

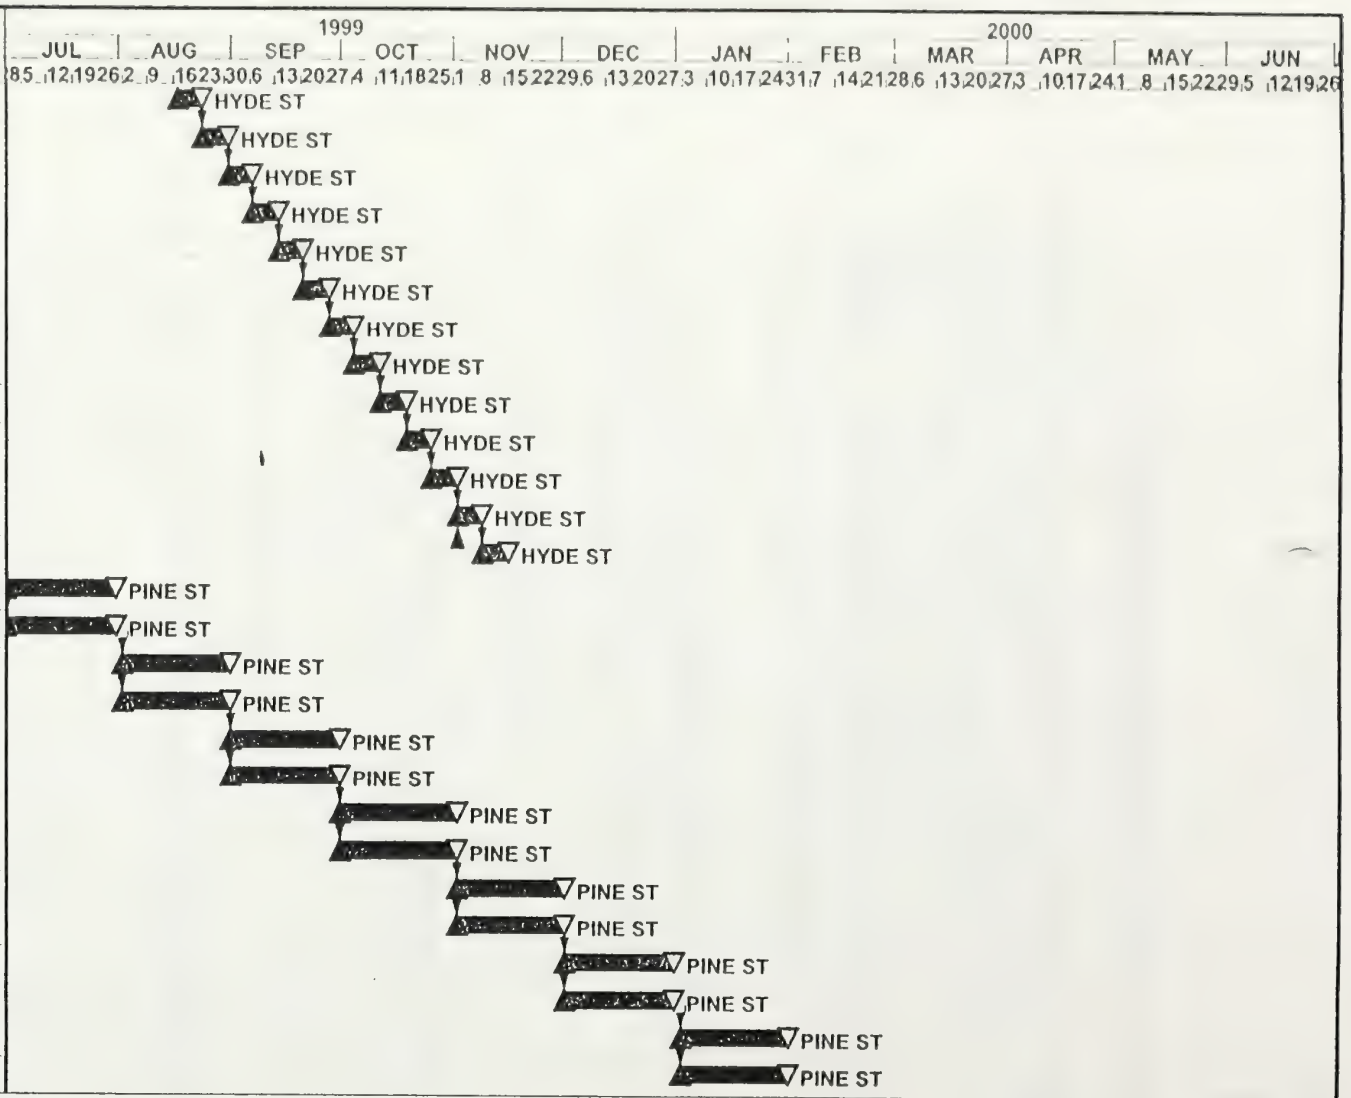

Project Start	01JUL99
Project Finish	01FEB00
Data Date	01JUL99
Run Date	15JAN99

△▽ Early Bar
▽ Float Bar
▲▼ Progress Bar
▲▼ Critical Activity

XWD7

Sheet 1 of 1

Sample 2
SFWD intersect with Pave
Hyde St and Pine St

Repaving Montgomery and Sacramento Streets to begin March 5, 1999. Get details inside and at the Open House.

DPW PUBLIC AFFAIRS
P.O. Box 429360
San Francisco, CA 94142-9360

PRESORTED
FIRST-CLASS MAIL
U.S. POSTAGE PAID
San Francisco, CA
Permit No. 4

OPEN HOUSE

WHAT?

At the Open House, you can view the plans and schedule for the Montgomery and Sacramento Streets Paving Project. Engineers will be available to answer questions.

WHEN and WHERE?

March 4 & 5, 11:30 AM – 1:30 PM
505 Sansome Street (lobby)

March 11 & 12, 11:30 AM – 1:30 PM
235 Montgomery Street (mezzanine)

QUESTIONS?

Frank W. Lee .... (415) 437-7018
e-mail: frank_w._lee@ci.sf.ca.us
DPW Public Affairs

Nancy Lynch .... (415) 554-5870
e-mail: nancy_lynch@ci.sf.ca.us
DPW Street Construction Coordination Center

TO RECEIVE PROJECT'S WEEKLY CONSTRUCTION UPDATES, PLEASE FAX YOUR NAME, COMPANY, AND FAX NUMBER TO (415) 437-7028.

PROJECT INFO

PROJECT AREA

Montgomery Street – Broadway to Market
Sacramento Street – Sansome to Kearny

CONSTRUCTION WORK SCHEDULE

10 Weekends; March 5 to May 9
Fridays 8:00 PM to Mondays 4:00 AM

For safety reasons, contractor has option to postpone any scheduled weekend work if raining.

CONTRACTORS:

M.H. Construction .... (415) 822-8828
Interstate Grading & Paving, Inc. .... (650) 952-7333

MUNI RE-ROUTING INFORMATION:

(415) 6SF-MUNI

☎ **24-HOUR PROJECT HOTLINE: (415) 437-7050**

WHAT'S GOING TO HAPPEN?

DPW will repave Montgomery and Sacramento Streets in 10 consecutive weekends, starting March 5. To minimize inconveniences, we have scheduled construction for weekends only. Work will occur continuously from Fridays 8:00 PM to Mondays 4:00 AM.

The project will involve two processes:

(1) **Base Repair**: Before replacing the asphalt surface, workers will use saw machines and jackhammers to remove any broken concrete base supporting the asphalt. Damaged spots will be replaced with new concrete.

(2) **Grinding and Paving**: Crews will use heavy equipment, including possibly jackhammers, to grind and strip away the old asphalt exposing the concrete base. Then, new asphalt will be paved over the base to give the roadway a new surface, followed by painting new road stripes and clean-up.

Base repair is scheduled for the first five weekends. Crews will grind and pave sections of street starting on the fifth weekend.

Work will not occur simultaneously on all 12 blocks. A plan has been developed to allow traffic to flow through the area with minimal disruptions. For detailed information, please visit us at our Open House.

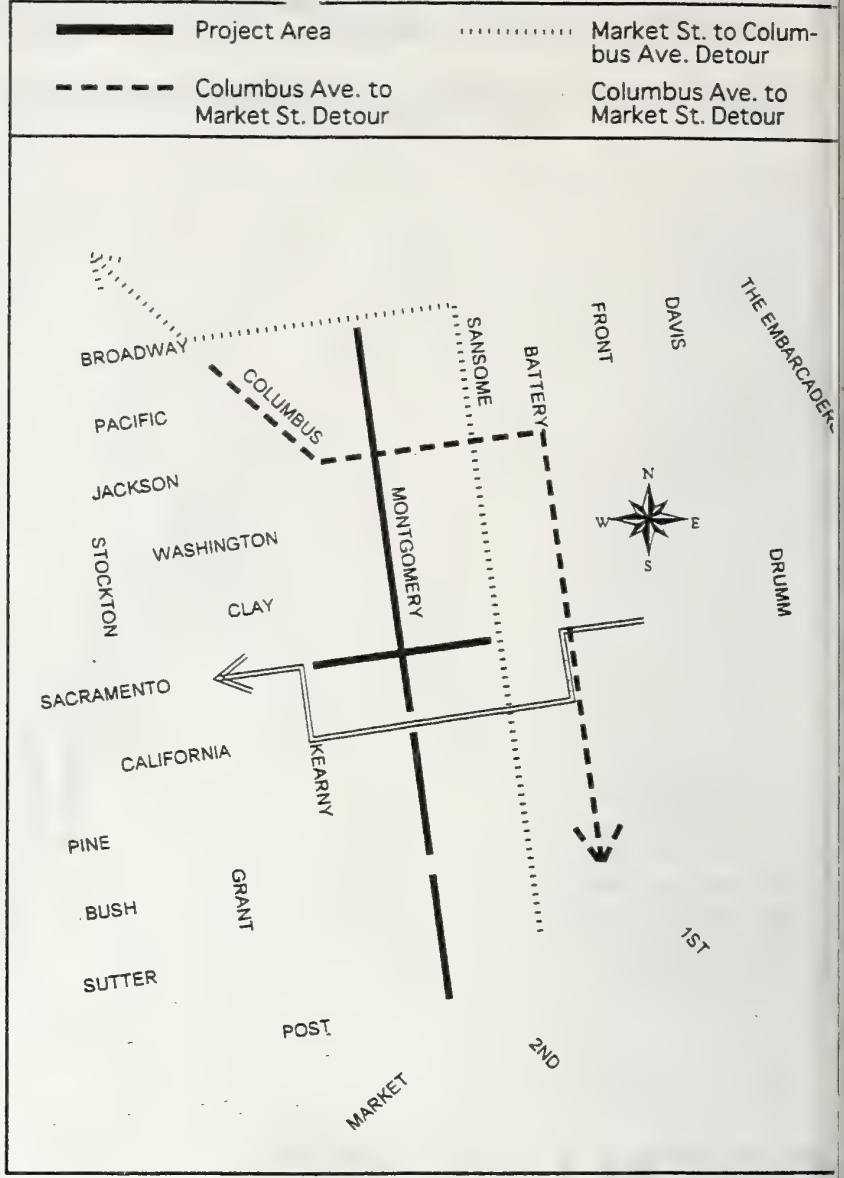
Project Area
Columbus Ave. to Market St. Detour
Market St. to Columbus Ave. Detour
Columbus Ave. to Market St. Detour
BROADWAY
PACIFIC
JACKSON
WASHINGTON
CLAY
SACRAMENTO
CALIFORNIA
PINE
BUSH
SUTTER
POST
MARKET
STOCKTON
GRANT
KEARNY
COLUMBUS
MONTGOMERY
SANSOME
BATTERY
FRONT
DAVIS
THE EMBARCADERO
DRUMM
1ST
2ND
N
S
E
W

HOW WILL THE RE-PAVING PROJECT AFFECT YOU?

Construction will create three primary impacts: NOISE, NO-PARKING, and TRAFFIC DETOURS.

NOISE

Base repair work and grinding will generate a degree of noise. However, we anticipate that both will be completed by Saturday evenings; thus, creating noise for Friday nights only.

Paving is much quieter and will be done on Saturdays during daylight.

NO-PARKING

Street parking along the project area will be prohibited for the weekend. The parking lanes will either become a construction area or a temporary lane for traffic.

In addition, parking on the south side of Jackson Street between Columbus and Sansome will be prohibited to accommodate MUNI articulated buses. On five weekends, MUNI #15 Third Street Line will be detoured from Columbus Ave. onto Jackson St.

Tow-away no-parking signs will be posted 72-hours in advance at affected locations.

DETOURS AND ALTERNATE ROUTES

We advise motorists to avoid Montgomery Street, if possible.

To reach Market Street from Columbus Avenue, motorists should use Battery Street via Jackson or Clay Street.

To reach Columbus Avenue from Market Street, motorists should use Sansome Street to Broadway to Columbus.

When work occurs on Sacramento Street, vehicles will be detoured onto California Street.

(Routes are shown on the map.)

MUNI

During construction, outbound MUNI #1 California and #15 Third Street Lines will be detoured around the work areas.

For more information and locations of temporary stops, call (415) 6SF-MUNI.

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

DOCUMENTS DEPT.

MAR 10 1999

SAN FRANCISCO
PUBLIC LIBRARY

SF
P85.93
#1
3/11/99

Location: 1680 Mission, 4th floor conference room
Date: Thursday, March 11, 1999 10am to 11:30am.
Subject: Committee Meeting 409- Coordination of Street Construction

1. Introduction	
2. Approval of Minutes for February 11th Meeting	
3. X1104 Monthly Report	Cynthia Chono
4. Signing of Permit Application Drawings by Civil Engineer	Vitaly Troyan
5. FY 1999-2000 Master Construction Schedule	Amy Chow / DTA
6. Mission Street Paving	Joe Ovadia
7. Ocean Avenue Project	Muni
8. Montgomery Street Construction Activity Update	Fernando Cisneros
9. Other New Business	All

Next Meeting: 2nd Thursday of Each Month
Thursday April 8, 1999 at 10:00 A. M.
Conference Room
1680 Mission Street, 4th Floor

City and County of San Francisco **Department of Public Works**

Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-8274, at leaStreet72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-8274.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 1680 Mission Street, the Fourth Floor Conference Room. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L on Mission Street; # 42 on Van Ness Avenue;
   #26 on Valencia Street; #71 on Noriega Street; #9 on Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 408

February 11, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4004
Norman Chan	554-8355
Joe Ovadia	558-4004
Jean To	554-8298

Street Construction Coordination Center

Amy Chow	554-8249
Joe Norris	554-8274
Vitaly Troyan	554-5803

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Cynthia Chono	554-6196
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

Charles Kascal	554-1803

PUC Sewer R&R

(Representative not present)

San Francisco Port Authority

(Representative not present)

San Francisco Water Department

(Representative not present)

Redevelopment Agency

(Representative not present)

Caltrans

Don Manning	557-4021
Doug Sibley	510-286-5564

Caltrans Public Information

Veronica Faisant	495-5895

Pacific Bell

(Representative not present)

Pacific Gas & Electric

Gilbert Munoz	695-3550
Kathy Devine	695-3492

S F Thermal

Mike Eurkus	777-3415
Ben Stout	777-3415

Allstar / Metro Media

Nick Araujo	431-2510

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

Shaun Reid	510-782-0900

RCN

Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500

Underground Construction

Andrew McManus	882-1553

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 408

1. The members introduced themselves around the table.

2. The December 10, 1998 Minutes were approved.

3. X-1104 Monthly Report

Ms. Chono introduced the new monthly summary of outstanding X-1104 notices in BSM's records since July 1 of last year. Each agency will receive a detailed listing of its own notices and a summary of all forms. The summary will also be included in the monthly Minutes. BSM, on being notified by the public or observing the presence of a trench defect, determines the most likely owner, marks the defect, and notifies the owner. The recipient should either repair the defect or show that it has a different owner. When the owner notifies BSM the defect is repaired, or after 30 days, the inspector revisits the site and follows through as appropriate. This procedure is unchanged from the previous rules, under which a trench is the owner's responsibility until the street is repaved. The only new feature is the monthly summary and the more serious follow-through. The intent is to establish active communication towards achieving better street condition, given the recent decline in the City's average condition scores des[ite increased budgets and the increased volume of street work. The City's own trenches are included in this process. This is the first pass and we expect it to clear the records of things like repairs completed but not recorded, along with errors. We expect to issue a higher number of X-1104s after the wet season for rain-induced damage.

The X-1104 applies to trenches after completion. There is a separate but similar Notice of Violation for deficient trenching work in progress.

Joint trenches are the responsibility of the permittee, normally the lead agency for the site.

4. Electronic Permitting

Ms. Chono reported that the web site has been active since the last week of January. The Water Department has done 80% of their applications including the very first, for which we will present a certificate suitable for framing the next time a representative attends the meeting. PG&E has made 57% of their permit applications electronically, and TSC has done 100% of theirs.

So far, the system is set up for single block projects. Multiple blocks will be possible later. BSM will hold an assessment meeting in March to discuss how well the system is working and where next to develop it, including the multiple block feature. Members present agreed the system works well, and has prompted suggestions but no complaints.

Mr. Victorio would like to see an option for work in the sidewalks. Turnaround has been about two days because the handling is still in transition from manual to automated; we intend that it will eventually range from instantaneous to a few minutes.

5. Engineer's Plan Signatures

Mr. Troyan will discuss this issue next month.

6. Montgomery Street Paving

Mr. Troyan displayed a map of the project area delineating the limits of the paving and the utility work that must be done before it. In response to the Mayor's demand, the start of paving has been advanced to March 6. The Mayor has added a similar demand for paving the first three blocks of First Street by BSSR in mid-March when the paving operation starts. We are now sorting out scheduling issues with the utilities that have work in the project area. In the first block, from Market to Mission, there is a water main replacement and the Muni tracks are to be removed when the F-Line is completed in two years. The two projects together will entail complete reconstruction of that block when the tracks come out. The freeway on-ramp downstream will add to the challenges.

Kearny Street has been deferred until next year, due mainly to the number of major utility projects, particularly south of California St. The paving will probably be divided into two contracts at California St.

Mr. Troyan expressed appreciation for the cooperation we have received from the utility agencies in meeting the mandated schedule.

7. Paving Program

Mr. Ovadia distributed a bar chart showing the 1999 contract paving program, which notes the number of clearances we still need for each contract. We especially need to finish clearances for Mission St., which is due to begin on March 1. The scope and schedule for each project is real, not tentative.

Mr. Troyan noted that we need to clean the data of projects that are not likely to be done within the time horizon of interest. We have formed a project improvement team to discuss the clearance procedure, which will resume its meetings when we have more experience of the permit web site in operation. We have already met with PUC to remove over 500 sewer repair notations. Clearance has gained in importance because we are trying to reach a paving rate that will addresss the City's annual needs, based on total number of blocks divided by the average useful life. As part of this effort, we are revising the scheduling procedure for BSSR paving, which will now include the same 120 day notice we provide for contracts. Note also the existing "To Be Paved by BSSR" report included with the Status Report, which contains streets that BSSR has already been instructed to pave.

Ms. Chow added that many of the non-cleared blocks are so because of planned capital projects, whose project managers need to discuss scheduling with their pavement counterparts. Ms. Chono noted that permit applications in streets with approaching pavement dates will be flagged and questioned by the permit system.

Ms. Devine requested a chart similar to the 1999 projects, for 2000. Ms. Chono observed that a similar chart from PG&E would be very useful as well.

Mr. Burbank discussed non-clearances in the Status Report. Besides projects completed but not reported, there are many in the "maybe" category, that a utility thinks it might want to do sometime but has not assigned a definite schedule. This clogs the system and raises questions about distinguishing real projects from maybes. Mr. Munoz responded that in many cases, a maybe can unpredictably become an urgently real job. Its presence in the record should at least prompt an inquiry from another agency with plans for that block, to find out what the story is. Likewise, knowing of the other project allows the first utility to prod its customer, if the maybe involves a service installation that does not yet have a set date

Ms. Chono asked who should address a conflict when it appears. As the new requirements take effect, we can expect many cases in which the first appearance of a job in the Status Report will prompt others to announce their own. Mr. Ovadia and Mr. Troyan replied that the relevant project managers should negotiate the question.

8. **Caltrans**

Ms. Faisant and Mr. Sibley discussed the next six years' plans for the retrofitting work in San Francisco, involving the I-80 structures between 16th St. and the bridge. Most of the work will not affect the freeway traffic but will impact the surrounding areas. This will involve public outreach, including a web site (www.safersf.com) now under construction and expected to open in the next couple of months. The office at 833 Market St. should open in March. Ms. Faisant distributed fact sheets and other information about the projects, which are reproduced with these minutes. She will provide additional copies on request. Anyone interested in updates should ask to be on her mailing list.

There will be a community meeting about the I-80 work in March, date and time to be announced.

Mr. Troyan asked if the First St. paving would affect Caltrans. Ms. Faisant replied it would not, but that she had heard something about plans for the area by the Redevelopment Agency; it would be helpful if they were present to discuss that.

9. **Five Year Plans**

Ms. Chow reported that SCCC has hired Don Todd Associates (DTA) to develop a master schedule for FY 1999/2000. To get them started, we emailed members on January 28 asking for each agency's relevant construction start dates and duration. There has been confusion with different utilities interpreting "start date" to mean other things than the actual construction. The results, and their benefit to all, will be as good as the information. Ms. Chow distributed bar charts displaying the amount of coordination, joint trenching opportunities, and conflicts for FY 99-00. We have identified 232 blocks with utility work scheduled after paving, and 446 with joint project opportunities. The sample DTA bar chart illustrates the final product of a coordinated construction schedule for fiscal year 1999-2000.

Ms. Chow next distributed a report showing each utility's projected mitigation fees, assuming they are not waived for coordination, totaling $500,000. DPW is discussing which 20 blocks should be paved with available funds.

10. February 17 Teleconference

Mr. Troyan reminded members of the teleconference to be held at the training trailer at the DPW yard at 2323 Cesar Chavez Blvd. On February 17 from 8:30 to 12:30, at no charge to those attending.

11. New Meeting Location

Mr. Troyan deferred discussion until after we have worked out details about space at our new office location.

New Business

Mr. Munoz announced that a forthcoming meeting at PG&E will affect their representation at the CULCOP meetings. In case that function is passed to someone else, he expressed appreciation for his experiences with us during the past three years.

The next meeting will be at 10:00 am Thursday, March 11, 1998, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

SUM OF FEE TO BE PAID BY UTILITIES FOR PLANNED PROJECTS, BY FY

	AWSS	DPT	MUNI	PGE GAS	PGE ELEC	SEWER	SFWD	UGD	SUM
97-98		$6,503							**$6,503**
98-99		$38.822	$11.288	$281.947	$4.703	$55,961	$63.748	$47.266	**$503,735**
99-00	$12.435	$51,064	$13.467	$275,432	$32.063	$32,573	$56.231	$118.440	**$591,705**
2000-03	$53.663	$50,692	$178,203	$365.667	$1.380	$36,152	$253.154	$360.080	**$1,298,991**

Total amount estimated to be paid from FY 1997-2003: **$2,400,934**

*Based on utilities' five year plans, and does not account for fee waivers from coordination.

Activity ID	Activity Description	FROM	TO	Orig Dur
8702000PV	HYDE ST	FULTON ST	MC ALLISTE	5
8703000PV	HYDE ST	MC ALLISTER ST	GOLDEN GATE AV	5
8704000PV	HYDE ST	GOLDEN GATE AV	TURK ST	5
8705000PV	HYDE ST	TURK ST	EDDY ST	5
8706000PV	HYDE ST	EDDY ST	ELLIS ST	5
8707000PV	HYDE ST	ELLIS ST	O'FARRELL ST	5
8708000PV	HYDE ST	O'FARRELL ST	MABEL AL	5
8709000PV	HYDE ST	MABEL AL	GEARY ST	5
8710000PV	HYDE ST	GEARY ST	POST ST	5
8711000PV	HYDE ST	POST ST	SUTTER ST	5
8712000PV	HYDE ST	SUTTER ST	BUSH ST	5
8713000PV	HYDE ST	BUSH ST	PINE ST	5
8714000PV	HYDE ST	PINE ST	CALIFORNIA ST	5
13244000WD	PINE ST	DAVIS ST	FRONT ST	22
13245000WD	PINE ST	FRONT ST	BATTERY ST	22
13246000WD	PINE ST	BATTERY ST	SANSOME ST	22
13252000WD	PINE ST	MONTGOMERY ST	BELDEN ST	22
13253000WD	PINE ST	BELDEN ST	KEARNY ST	22
13268000WD	PINE ST	LEAVENWORTH ST	HYDE ST	22
13269000WD	PINE ST	HYDE ST	LARKIN ST	22
13270000WD	PINE ST	LARKIN ST	POLK ST	22
13271000WD	PINE ST	POLK ST	VAN NESS AV	22
13272000WD	PINE ST	VAN NESS AV	FRANKLIN ST	22
13273000WD	PINE ST	FRANKLIN ST	GOUGH ST	22
13282000WD	PINE ST	PIERCE ST	SCOTT ST	22
13283000WD	PINE ST	SCOTT ST	DIVISADERO ST	22
13284000WD	PINE ST	DIVISADERO ST	BRODERICK ST	22

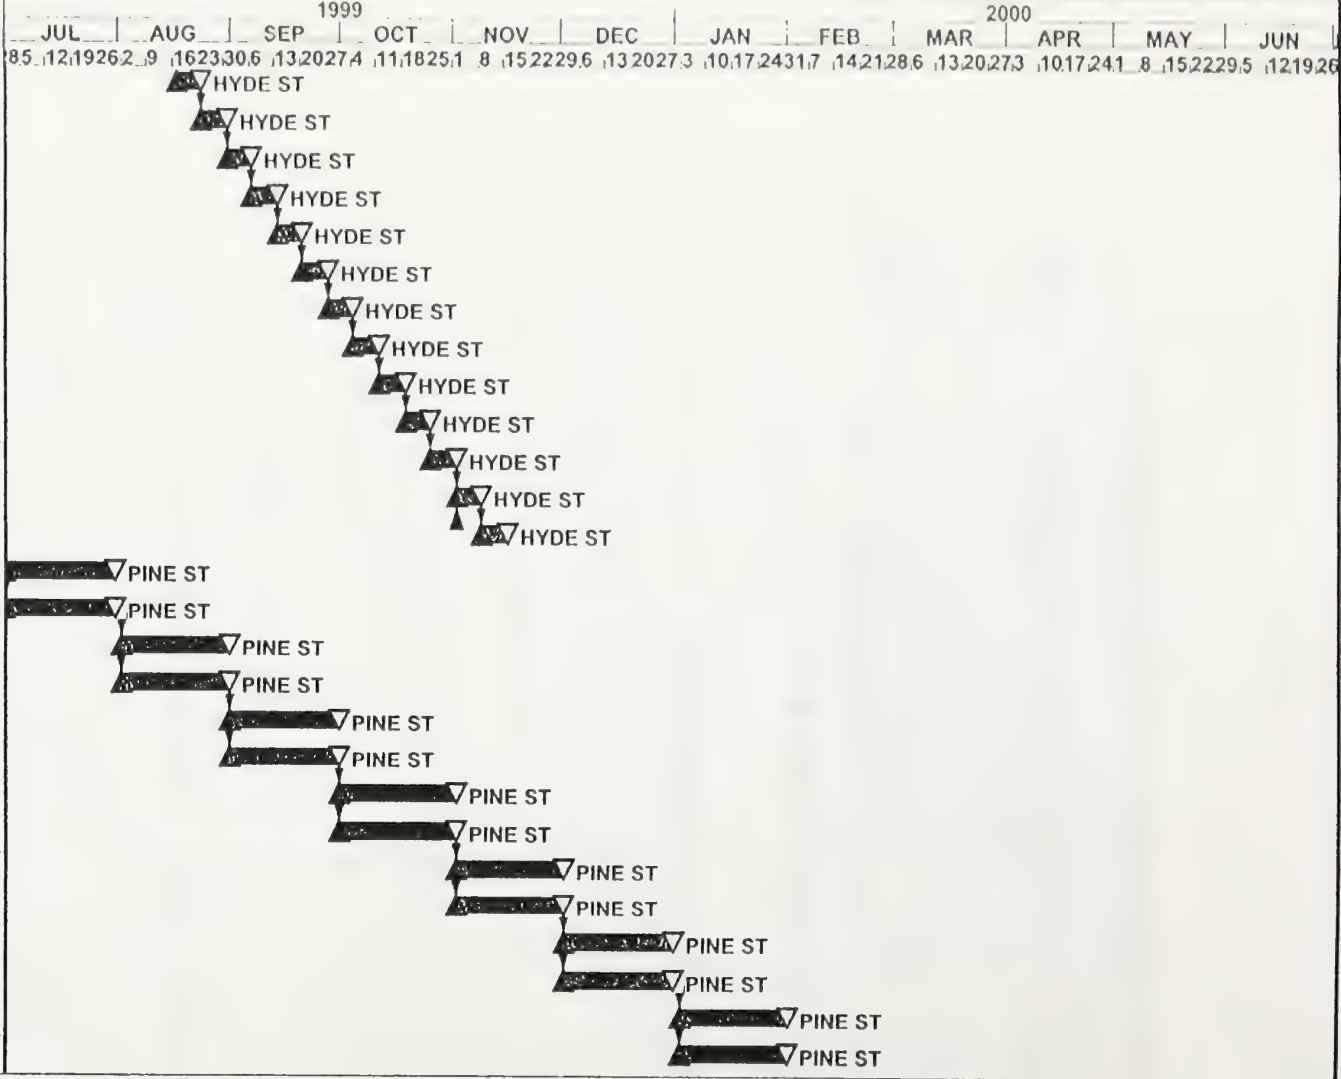

Project Start	01JUL99
Project Finish	01FEB00
Data Date	01JUL99
Run Date	[illegible]99

© Primavera System

Early Bar
Float Bar
Progress Bar
Critical Activity

XW07

Sheet 1 of 1

Sample 2

SFWD intersect with Pave

H[illegible] St and Pine St

Repaving Montgomery and Sacramento Streets to begin March 5, 1999. Get details inside and at the Open House.

DPW PUBLIC AFFAIRS
P.O. Box 429360
San Francisco, CA 94142-9360

PRESORTED
FIRST-CLASS MAIL
U.S. POSTAGE PAID
San Francisco, CA
Permit No. 4

OPEN HOUSE

WHAT?

At the Open House, you can view the plans and schedule for the Montgomery and Sacramento Streets Paving Project. Engineers will be available to answer questions.

WHEN and WHERE?

March 4 & 5, 11:30 AM – 1:30 PM
505 Sansome Street (lobby)

March 11 & 12, 11:30 AM – 1:30 PM
235 Montgomery Street (mezzanine)

QUESTIONS?

Frank W. Lee .... (415) 437-7018
e-mail: frank_w._lee@ci.sf.ca.us
DPW Public Affairs

Nancy Lynch .... (415) 554-5870
e-mail: nancy_lynch@ci.sf.ca.us
DPW Street Construction Coordination Center

TO RECEIVE PROJECT'S WEEKLY CONSTRUCTION UPDATES, PLEASE FAX YOUR NAME, COMPANY, AND FAX NUMBER TO (415) 437-7028.

PROJECT INFO

PROJECT AREA

Montgomery Street – Broadway to Market
Sacramento Street – Sansome to Kearny

CONSTRUCTION WORK SCHEDULE

10 Weekends; March 5 to May 9
Fridays 8:00 PM to Mondays 4:00 AM

For safety reasons, contractor has option to postpone any scheduled weekend work if raining.

CONTRACTORS:

M.H. Construction .... (415) 822-8828
Interstate Grading & Paving, Inc. .... (650) 952-7333

MUNI RE-ROUTING INFORMATION:

(415) 6SF-MUNI

☎ **24-HOUR PROJECT HOTLINE: (415) 437-7050**

WHAT'S GOING TO HAPPEN?

DPW will repave Montgomery and Sacramento Streets in 10 consecutive weekends, starting March 5. To minimize inconveniences, we have scheduled construction for weekends only. Work will occur continuously from Fridays 8:00 PM to Mondays 4:00 AM.

The project will involve two processes:

(1) **Base Repair**: Before replacing the asphalt surface, workers will use saw machines and jackhammers to remove any broken concrete base supporting the asphalt. Damaged spots will be replaced with new concrete.

(2) **Grinding and Paving**: Crews will use heavy equipment, including possibly jackhammers, to grind and strip away the old asphalt exposing the concrete base. Then, new asphalt will be paved over the base to give the roadway a new surface, followed by painting new road stripes and clean-up.

Base repair is scheduled for the first five weekends. Crews will grind and pave sections of street starting on the fifth weekend.

Work will not occur simultaneously on all 12 blocks. A plan has been developed to allow traffic to flow through the area with minimal disruptions. For detailed information, please visit us at our Open House.

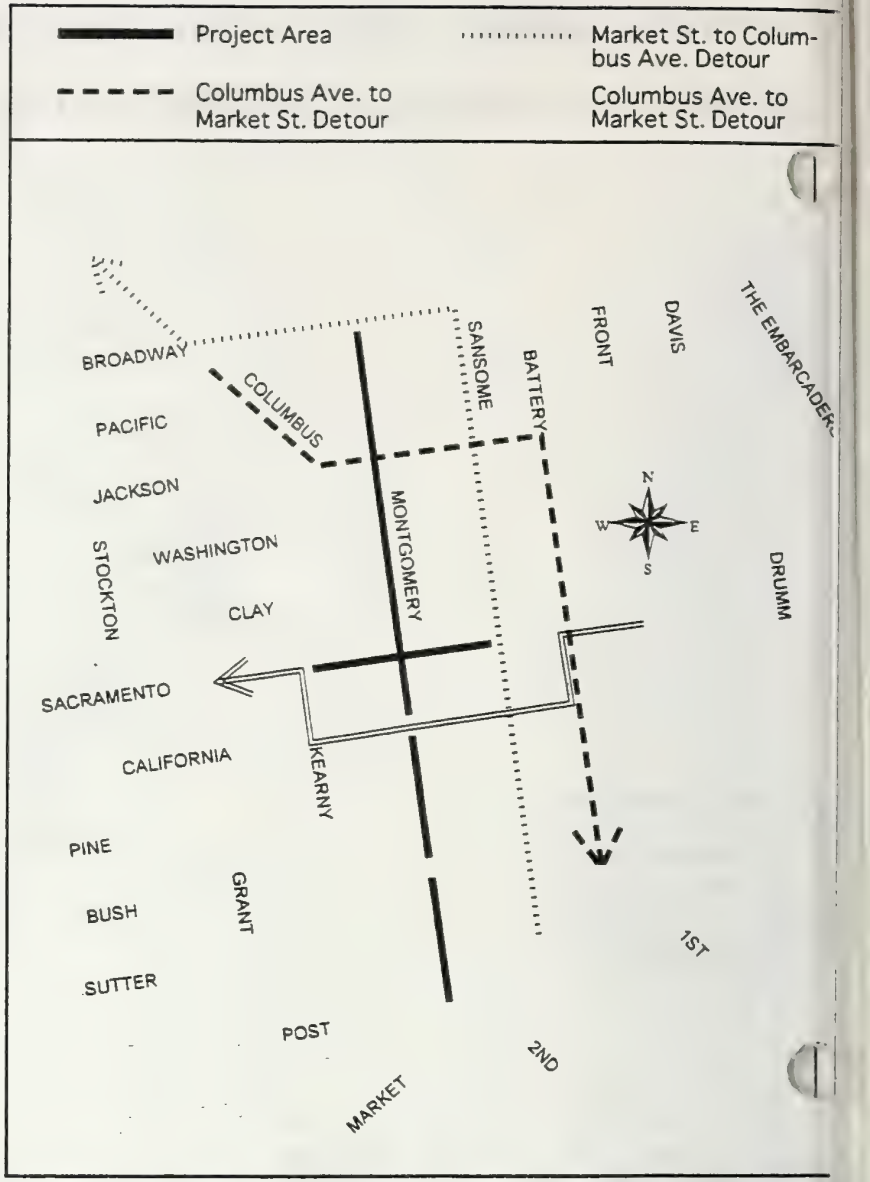
Project Area
Market St. to Columbus Ave. Detour
Columbus Ave. to Market St. Detour
Columbus Ave. to Market St. Detour
BROADWAY
COLUMBUS
PACIFIC
JACKSON
WASHINGTON
CLAY
STOCKTON
SACRAMENTO
CALIFORNIA
KEARNY
PINE
BUSH
GRANT
SUTTER
POST
MARKET
MONTGOMERY
SANSOME
BATTERY
FRONT
DAVIS
THE EMBARCADERO
DRUMM
N
E
S
W
1ST
2ND

HOW WILL THE RE-PAVING PROJECT AFFECT YOU?

Construction will create three primary impacts: NOISE, NO-PARKING, and TRAFFIC DETOURS.

NOISE

Base repair work and grinding will generate a degree of noise. However, we anticipate that both will be completed by Saturday evenings; thus, creating noise for Friday nights only.

Paving is much quieter and will be done on Saturdays during daylight.

NO-PARKING

Street parking along the project area will be prohibited for the weekend. The parking lanes will either become a construction area or a temporary lane for traffic.

In addition, parking on the south side of Jackson Street between Columbus and Sansome will be prohibited to accommodate MUNI articulated buses. On five weekends, MUNI #15 Third Street Line will be detoured from Columbus Ave. onto Jackson St.

Tow-away no-parking signs will be posted 72-hours in advance at affected locations.

DETOURS AND ALTERNATE ROUTES

We advise motorists to avoid Montgomery Street, if possible.

To reach Market Street from Columbus Avenue, motorists should use Battery Street via Jackson or Clay Street.

To reach Columbus Avenue from Market Street, motorists should use Sansome Street to Broadway to Columbus.

When work occurs on Sacramento Street, vehicles will be detoured onto California Street.

(Routes are shown on the map.)

MUNI

During construction, outbound MUNI #1 California and #15 Third Street Lines will be detoured around the work areas.

For more information and locations of temporary stops, call (415) 6SF-MUNI.

SAN FRANCISCO
DPT
DEPARTMENT OF PARKING & TRAFFIC
Traffic Engineering Division
City and County of San Francisco

FAX DISTRIBUTION LIST FOR UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS CALENDAR

WILLIE LEWIS BROWN, JR., MAYOR
STUART R. SUNSHINE, EXECUTIVE DIRECTOR

JOHN BANNER, CITY TOW
JOHN BUSHER, DPW, BUREAU OF ENVIRONMENTAL SERVICES
AMY CHOW, DPW, PROJECT DEVELOPMENT SECTION
ADRIENNE FRAZIER, DPT, OPERATIONS
PETE HOWES, SFFD, EMS
WALTER HOO, DPW/BSM
CAPTAIN LI, SFFD, BUREAU OF FIRE PREVENTION AND INSPECTION
RICHARD SKAFF, DPW, DISABILITY ACCESS COORDINATOR
ANNA WONG, DPW, PUBLIC RELATIONS
ALISON HOOD, GGNRA, SPECIAL EVENTS OFFICE
MARIA TRAPALIS-BAIRD, MAYOR'S OFFICE OF RECYCLING
VIRGINIA RICHARDSON, PARK & REC
LEO PIERINI, STATE PAROLE DIVISION
JEFF BAUER, PORT OF SAN FRANCISCO
LT. JACK BALLENTINE, SFPD, FILM COORDINATOR
BILL WEBB, DPW, BCM
MARY ELLEN O'BRIEN, PRESS OFFICER, DPT
SHEILAH TUCKER, TRAVINFO
LAMONT DEBARBIE, FLYING DUTCHMAN

This list is a summary of the various street closures for special events which have been approved by the Interdepartmental Staff Committee on Traffic and Transportation (ISCOTT). I have also included other events which may impact traffic on City streets when I know of them. If you would like more details about any of the events, please give me a call at 415-554-2341. This list may not include events which have been permitted by the Port of San Francisco, Golden Gate National Recreational Area, or the Recreation & Park Department. If you know of other events which should be listed, please let me know. I have added a Temporary Street Closures for Special Events database on DPT's web page. Closures may be searched by date, event name and street name. You may find more detailed information about the events through this database. Our web site address is www.ci.sf.ca.us/dpt.

Cindy Shamban
Management Assistant

c:\myfiles\faxisctt.199

1999 UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS Query

Event Name	Start Date	End Date	Type	Location	Status
Peugeot Commercial Film	3/11/99	3/11/99	Film	Taylor: Gre to Pac; Broadway: Mason to Taylor	
SF Inter. Asian Amer. Film	3/11/99	3/18/99		Post (partial southside parking lane only): Fillmore to W	2/25/99
Lion Dance Performance	3/14/99	3/14/99	Block	Waverly: Washington to Clay	2/25/99
St. Patrick's Day Parade	3/14/99	3/14/99	Parade	Market to Civic Center	Permit by SFPD
St. Patrick's Day Celebratio	3/14/99	3/14/99	Fair	Larkin: Hayes to McAllister	2/11/99
St. Patrick's Day Celebratio	3/14/99	3/14/99	Fair	Fulton: Larkin to Hyde Streets	2/11/99
St. Patrick's Day Celebratio	3/17/99	3/17/99	Block	Front: California to Sacramento	1/28/99
Fiddler' Green St. Patrick's	3/17/99	3/17/99	Celebrat	Columbus (3 parking spaces only): N.Point to Beach	
O'Reilly's St. Patrick's Day	3/17/99	3/17/99	Celebrat	Green (N/S parking lane only): Columbus to Powell	1/28/99
Greek Independence Day P	3/21/99	3/21/99	Parade	Valencia & 14th to Civic Center	Permit issued by
Houlihan's to Houlihan's	3/28/99	3/28/99	Athletic	Marina Blvd (1 n/b lane only), etc	9/24/99
Sisters of P.I. Birthday Bas	4/4/99	4/4/99	Celebrat	Castro: Mkt to 18th	Disapproved
Union Street Easter Celebra	4/4/99	4/4/99	Fair	Union: Gough to Fillmore; Webster: Green to Filbert	2/11/99
Union Street Easter Parade	4/4/99	4/4/99	Parade	Union: Franklin to Fillmore	Permit issued by
Parking for Easter Services	4/4/99	4/4/99	Private	Anza: 9th to 10th Avenues	2/11/99
CCAC Grand Opening	4/15/99	4/16/99	private	8th St: Irwin to Hooper	2/25/99
CCAC Grand Opening	4/16/99	4/17/99	private	8th St: Irwin to Hooper	2/25/99
Cherry Blossom Festival	4/17/99	4/18/99	Fair	Pos:Lag to Flm; Web: Gea to Sut	

Event Name	Start Date	End Date	Type	Location	Status
YMCA Community Cup Eve	4/17/99	4/17/99	Athletic	Steuart (west side parking lane and 1 lane of traffic only	2/25/99
SF Inter. Triathlon	4/18/99	4/18/99	Athletic	Various (NW portion of SF)	canceled
Cherry Blossom Festival	4/24/99	4/25/99	Fair	Pos:Lag to Flm;	
Cherry Blossom Parade	4/25/99	4/25/99	Parade	Civic Center to Polk to Post	permitted by PD
Neighborhood Block Party	4/26/99	4/25/99	Block	Filbert: Divisadero to Broderick	
California Mile	4/25/99	4/26/99		Mason: Ca to Sac	12/17/98
Cameron Carnival	5/1/99	5/1/99	Fair	Joice: Sacramento to Clay	2/25/99
Asian Art Museum Ground	5/8/99	5/8/99	Civic	Fulton: Larkin to Hyde	2/25/99
Neighborhood Block Party	5/15/99	5/15/99	Block	Mars: 17th to Corbett	
Bay to Breakers	5/16/99	5/16/99	Athletic	Various Locations	1/28/99
Young President's Organiza	5/21/99	5/21/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/22/99	5/22/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/23/99	5/23/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/24/99	5/24/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/25/99	5/25/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/26/99	5/26/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/27/99	5/27/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Young President's Organiza	5/28/99	5/28/99	Shuttle	Stockton: Pine to CA; Parking lane closures on Pine &	
Carnaval	5/29/99	5/30/99	Fair	Har: 16th to 22nd, etc	2/25/99
Carnaval Parade	5/30/99	5/30/99	Parade	24th: Bry to Mis; Mission: 24th to 14th; 14th: Mis to Har	permitted by PD

Event Name	Start Date	End Date	Type	Location	Status
Black & White Ball	6/3/99	6/7/99	civic	Fulton: Larkin to Hyde	2/25/99
Black & White Ball	6/3/99	6/3/99	Civic	Various Parking Lanes in Civic Center area	2/25/99
Black & White Ball	6/4/99	6/4/99	civic	Various Parking Lanes In Civic Center Area	2/25/99
Union Street Arts Festival	6/5/99	6/6/99	Fair	Union: Gou to Stn, etc	12/17/98
Black & White Ball	6/5/99	6/7/99	civic	Grove: Van Ness to Franklin	2/25/99
Black & White Ball	6/5/99	6/6/99	civic	Various Streets in Civic Center Area	2/25/99
Escape From Alcatraz	6/5/99	6/5/99	Athletic	Marina Blvd (1 lane only): Scott to Lyon	7/23/98
Escape From Alcatraz	6/5/99	6/5/99	Athletic	NW portion of SF, Various Locations	7/23/98
SPCA Animal WingDing	6/5/99	6/6/99	Fair	Alabama:15 to 16; Florida:16 to Tre; Treat:Har to 15th	12/17/98
SPCA Animal WingDing	6/6/99	6/6/99	Fair	Alabama:16 to 17; Florida:16 to 17	12/17/98
CA Aids Ride	6/6/99	6/6/99	Athletic	Various, no street closures involved	No permit required
North Beach Festival	6/12/99	6/13/99	Fair	Grant:Col to Fil;Green: Col to Gra; Vallejo:Col to Gra	2/11/99
Haight Street Fair	6/13/99	6/13/99	Fair	Haight:Masonic to Stanyan, etc	11/13/98
Extreme Games	6/23/99	7/3/99	Athletic	Pier 30-32	permit by Port
NASCAR Rally	6/24/99	6/24/99		Leavenworth: Chestnut to Greenwich; Lombard: Hyde t	
Gay Pride Celebration	6/25/99	6/28/99	Fair	Civic Center Area	1/28/99
Pink Saturday	6/26/99	6/27/99	Civic	Castro: 19th to Mkt; 18th: Cwd to Hfd	
Gay Pride Parade	6/27/99	6/27/99	Parade	Market: 2nd to Civic Center	permit by PD
Tall Ships	7/2/99	7/5/99		Wharf Area	
Fillmore Street Jazz Festiva	7/3/99	7/4/99	Fair	Fillmore: Jackson to Post, etc	2/11/99

Event Name	Start Date	End Date	Type	Location	Status
Jazz & All That Art on Fillm	7/3/99	7/4/99	Fair	Fillmore: Geary to McAllister etc.	Hold
Chronicle's 4th of July	7/3/99	7/5/99	Fair	Jefferson: Hyde to Terminus	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Van Ness: North Pt. To Muni Pier	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Embarcadero: Pow to Tay	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Jefferson: Hyde to Taylor	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Wharf Area	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	N/B Embarcadero: Bwd to Bay	12/17/98
SF Chronicle Marathon	7/11/99	7/11/99	Athletic	Various City Wide	2/25/99
Third Street Fair	7/17/99	7/18/99	Fair	3rd St.:Cargo to Evans	1/14/99
Blues & Art on the Bay	9/4/99	9/6/99	Fair	Treasure Island	permit by T. Island
Fest. Of Culinary Arts	9/11/99	9/12/99	Fair	Polk: Eddy to MCA; Turk: Van to Lar	
Chinatown Moon Festival	9/17/99	9/19/99	Fair	Grant: Cal to Pac	
Alcatraz Triathlon XIX	9/18/99	9/18/99	Athletic	Marina Blvd (1 lane only): Lag to Buc	10/22/98
Bridge to Bridge	10/3/99	10/3/99	Athletic	Various: Ferry Bldg to Presidio	1/28/99
West Portal Fair	10/23/99	10/24/99	Fair	West Portal: Ulloa to 15th Sts.	
Champion Run for Children	10/24/99	10/24/99	Athletic	Sanchez: Duboce to Market	
Champion Run for Children	10/24/99	10/24/99	Athletic	Dr. Carleton Goodlett Place	
Champion Run for Children	10/24/99	10/24/99	Athletic	Various Lane Closures	
Champion Run for Children	10/24/99	10/24/99	Athletic	McAllister: Polk to Larkin	
Champion Run for Children	10/24/99	10/24/99	Athletic	Larkin: McA to Gro; Hyde: McA to Grove; Grove: Hyd to	

Event Name	Start Date	End Date	Type	Location	Status
Run to the Far Side XV	11/28/99	11/28/99	Athletic	Oak: Stanyan to Broderick; Fell: Stanyan to Broderick,	

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, Architect, AIA, Director

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

UNDERGROUND PLANNING MEETING

MEETING DATE: February 2, 1999

PRESENT:

Tom Trimbur	-DPW/BSM	(554-6167)
Louis Victorio	-TCI	(863-8500)
Carlos DeAnda	-PG&E	(330-2138)
Cindy Vowell	-PacBell	(542-9095)
José Saldaña	-PG&E	(330-2249)
Patty Healy	-PG&E	(695-3394)
John Giusti	-DHIC	(863-7500)
Scot Burbank	-BOE/PMD	(558-4046)
Naoki Kaku	-BOE/S&H.	(554-8246)

DISCUSSION:

A. PROJECT STATUS

1. UGD 318 - DOLORES HEIGHTS DISTRICT

Dorland/Dolores Terrace – Poles removed. Patch paving should be completed by the 15th. This is the final report on this area.

PHASE 2 – PG&E needs to pull permit for work since previous permit expired. No significant change in number of property conversions. Construction to begin in March.

2. UGD 310 - PRESIDIO HEIGHTS

PHASE 2 – Substructure completed. PG&E pulling primary; system should be energized by the end of February and property cutovers should begin in March. PG&E needs street light tags. PG&E reported that they have not received streetlight submittal information from their contractor.

City to send letters to unconverted property owners.

California St. – Project to advertise in two weeks and construction to begin in March.

3. UGD 320 - BREWSTER/JOY

124 Brewster has been cutover. PG&E reported that there has been no progress on the construction at 122 Brewster for some time. One alternative to waiting for all the work to be completed is to have contractor/property owner pull permit for underground temporary service. An additional active phone service has been discovered leading to a service on the walkway over the freeway. Caltrans is attempting to ascertain if they are using the service or if it can be discontinued.

4. UGD 321 - INDIANA STREET/ISLAIS CREEK & UGD 323 - CESAR CHAVEZ

Y. C. Yang, owner of 1601 Indiana, has talked several times to contractor regarding conversion work but has not agreed to price. City to contact and then proceed with abatement procedure. CALTRIAN work back at square one; DPW to contact City's representative on Joint Powers Board to see about expediting process for approvals. Caltrans provided a verbal approval for removal of wires over the freeway. PacBell reported that the boxes along Chavez may need to be adjusted by 3 inches and, given that the City provided elevations, the utilities feel that the City should be responsible for the costs.

5. UGD 324 - DUBOCE AVENUE

Mr. Trimbur reported that he had contacted MUNI and that they had some contracting difficulties but that their work was to be advertised soon. Results from PG&E tests on water finding its way into their facilities have not been reported.

6. UGD 311 - CORBETT AVENUE - PEMBERTON STAIRWAY

Project is still on hold.

7. UGD 335 - UPPER FOLSOM

PG&E work continuing. Approximately 48% of substructure work completed; should be finished by June. PG&E reported that the number of property conversions have picked up; about 50% completed.

8. UGD 322 - Alpine Terrace/Museum Way

Community meeting to discuss construction and owner responsibilities scheduled for Thursday the 18th at the McKinley School, 1025-14th Street.

9. UGD 327 - INNER SUNSET

Community meeting to discuss construction and owner responsibilities scheduled for Wednesday the 24th at the Jefferson School, 1725 Irving.

10. UGD 338 - Ocean Avenue

Community meeting to discuss construction phasing scheduled for Wednesday the 17th at the Sloat School.

11. UGD 339 – Bernal South Slope (Banks/Chapman)

Ms. Healy distributed a tentative schedule for the Banks/Chapman portion of Bernal South Slope.

B. OTHER BUSINESS

1. Mr. Burbank requested a CULCOP undergrounding and gas main replacement update for California Street.

2. Ms. Healy suggested that each project have a schedule similar to the one she distributed for Banks/Chapman. General consensus was in agreement.

THE NEXT MEETING WILL BE HELD ON TUESDAY, 2 March 1999, AT 9:00 A.M. AT 875 STEVENSON STREET, ROOM 460, BSM CONFERENCE ROOM.

cc: All Attendees
CULCOP - through Joe Norris
Ray Gigliati - BSM
Hin Lok Kung - BOE
Jack Donohoe - DTIS
Barbara Moy - BSM
Manfred Wong - CWP
Lynn Bunim - PacTel
Norman Chan - BOE
Dee Lemmon - BLHP
Lesley Wong - BOE/S&H
Patricia Healy - PG&E
Dave Bradley - PG&E

Amy Chow - PDS
Charles Yu - BOE/S&H
Amy Powell- DHIC
Brian Christiansen - Duboce
Carlos DeAnda - PG&E
Lynn Nakasato - BOE/S&H
Cynthia Chono - BSM
Ray Yamagishi - BLHP
Tom Flahavan - DET
Joe Ovadia - PMD
Kathy Devine - PG&E
Louis Victorio – TCI

John Katz - MUNI
Sam Lauter - PG&E
Carol Finucane - BOE
Don Stroh - DHIC
Brian Gatter - BOE/Landscape
Terry Bouey - TCI
Bob Striech - PG&E
Joe Marino - DHIC
Terry Elisaia - DET
Naoki Kaku - BOE
Richard Hong - PG&E
Ben Cruz – BOE

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

UTILITY COORDINATION REPORT

for February 1, 1999 to February 28, 1999

Notice of Intent and Request for Information Issued (NOI):	**Date**
1984N - Van Ness Pedestrian Safety Improvements	2/2/99

Final Preliminary Plans Issued (LOT):	
1729N - Brotherhood Way & Font Boulevard Pavement Renovation	2/10/99
1632N - Post, Grove and Potomac Streets Sewer Replacement	2/23/99

State of California:

Other:

"IMPROVING THE QUALITY OFLIFE IN SAN FRANCISCO" We are dedicted individuals committed to teamwork, customer service and continuous improvement in partnership with the community

Customer Service *Teamwork* *Continuous Improvement*

S:\PD\UTILITYL\RPTS\CULCOP\UT0299.doc

Projects in Progress (NOI)

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
----N	Greg Cruz	554-8268	Various Locations, Construction of Curb Ramps - STPL-5934(030)	Pav	09/04/1997
1034N	Ed Choy	554-8284	Chinatown Alleyway Improvements Phase 1 Commercial, Cordelia and Ross	STR	05/27/1998
1048N	Gene Handa	554-8341	Sunnydale Sewer Improvements	SW	07/03/1996
1076N	Arlen Ung	554-8263	West End Utilities	Pav	08/11/1997
1100N	Martha Ketterer	554-8296	Ecker Street, Mission Street to Elim Alley	Pav	01/08/1996
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements Locations #306 & 309	UG	02/15/1998
1145N	Naoki Kaku	554-8246	Bernal Heights Street Improvement, Banks/Chapman Area	Pav	12/02/1996
1202N	Linda Leong	648-6882	North Point Plant Improvement, Phase II	Pav	01/30/1996
1218N	Cliff Wong	554-8339	Market , Larkin and Harrison Streets Sewer Replacement	SW	03/29/1996
1243N	Ronald Cheng	558-4049	Marina Seawall and Roadway Improvement	Pav	04/12/1996
1277N(1)	Laarni Camerino	554-8256	Var Loc: As Needed Paving - McAllister, Polk, Grove & Van Ness Avenue	Pav	08/17/1998
1277N(2)	Pak Choi	554-8283	Various Locations: As Needed Paving - Stockton (Post to Market Street)	Pav	08/17/1998
1277N(3)	Greg Cruz	554-8268	Var Loc - As Needed Pav: Lake Merced from Skyline Blvd. To John Muir Drive	PAV	09/28/1998
1285N	Brian Gatter	554-8292	Pioneer Park Renovation – Telegraph Hill Stairways	Pav	11/14/1997
1294N	Leon Louie	558-4070	Fourth Street Bridge Fender Repair Project	Str	12/18/1996
1330N	Wallis Lee	554-8344	2nd / 9th Streets Sewer Abandonment Project	SW	06/27/1997
1349N	Saed Toloui	558-4084	12th Avenue/Quintara Street, Stairway Construction	Str	02/07/1997
1362N	Edward Choy	554-8284	Various Locations SOMA Street District Track Removal & Pavement Renovation Phase 2	PAV	01/07/1999
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	12/02/1996
1381N	Patrick Riviera	558-4045	Martin Luther King Utilities	Pav	09/12/1997
1385N	Laarni Camerino	554-8256	Various Locations: Concrete Street Reconstruction - Stillings Ave from Teresita to Congo	PAV	07/10/1998
1389N	Pak Choi	554-8283	Mission Street Pavement Renovation	Pav	06/13/1997
1395N	Cliff Wong	554-8339	Sacramento/ Larkin/ Pine Streets Sewer Replacement	SW	04/10/1998
1407N	Narciso Paderanga Jr.	554-8258	California Street Pavement Renovation, STP-17	Pav	02/13/1997
1415N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	Str	07/31/1997
1421N	Clifford Wong	554-8339	Green Street Sewer Replacement - Columbus Avenue to Powell Street	SW	01/17/1997
1423N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	SR	07/31/1997
1432N	Gene Handa	554-8341	Post Street Sewer Replacement	SW	02/07/1997
1459N	Narciso Paderanga, Jr.	554-8258	Fillmore Street Pavement Renovation and Muni Underground Ductbank System	Pav	08/29/1997
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	11/10/1997
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SR	09/30/1997
1549N	Thomas Won	554-8275	Ocean/Victoria/Everglade Sewer Replacement	SW	09/23/1997
1573N	Wallis Lee	554-8344	5th Street & Harrison Sewer Replacement	SW	02/17/1998
1583N	Thomas Won	554-8275	Everglade/ Victoria/ Revere/ Bridge View Sewer Replacement	SW	03/23/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	04/13/1998
1587N	Jean To	554-8298	7th Avenue and Kirkham Street Sewer Replacement	SW	12/11/1998
1588N	Thomas Won	554-8275	Joost Ave/Alemany Blvd/Mt. Vernon Ave/Kensington Way Sewer Replacement	SW	12/22/1998
1590N	Thomas Won	554-8275	Ocean Avenue Sewer Replacement (Joint Venture with MUNI)	SW	07/13/1998
1605N	Bryan Dessaure	554-8299	Sacramento/Pierce/Wilmot Streets Sewer Replacement	SW	06/07/1998
1626N	Thomas Won	554-8275	4th/5th Ave/Stanyan St (easement) / Paris Street Sewer Replacement	SW	10/22/1998
1628N	Jean To	554-8298	Moraga Street Sewer Replacement: 17th to 18th Avenues	SW	09/16/1998
1629N	Peter Cheng	554-8348	Union/Kearny Streets Sewer Replacement	SW	10/28/1998
1630N	Birgit Chase	554-8336	Polk/Francisco/Quincy/Sacramento Streets Sewer Replacement	SW	11/09/1998
1653N	Uday Prasad	558-4061	Demolition of North Beach Garage at 763 Vallejo Street	Str	09/15/1997
1655N	Lesley Wong	554-8252	Cezar Chavez Improvements Phase 2		07/27/1998
1667N	Lesley Wong	554-8252	Fourth Street Sidewalk Widening Project - Phase 2	Pav	03/10/1998
1668N	Ken Chu	554-8388	Golden Gate Avenue Pavement Renovation	Pav	01/02/1998
1674N	Joe Haas	558-4539	1680 Mission Street Secondary Power Source	SDV	05/27/1998
1678N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Street Reconstruction No. 15	Pav	04/13/1998
1680N	Lesley Wong	554-8252	Great Highway and Point Lobos Pavement Renovation	Pav	05/13/1998
1701N	Laarni Camerino	554-8256	Seventh Street Pavement Renovation	Pav	08/24/1998
1724N	Laarni Camerino	554-8256	Various Locations: As Needed Paving - 2nd St. between Townsend & King Streets	Pav	07/10/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	10/28/1998
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	10/05/1998
1734N	Dimitrios Stavrakis	554-8271	Franklin/Greenwich and Union Streets Pavement Renovation	PAV	01/04/1999

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
1735N	Naoki Kaku	554-8246	Various Locations: Bayview District Pavement Renovation	PAV	10/13/1998
1748N	Carol Finucane	558-4581	Mid-Market Public Improvements		10/05/1998
1755N	David Pang	554-8278	Oak Street Pavement Renovation	PAV	02/02/1999
1759N	Pak Choi	554-8283	Mission Street Pavement Renovation Phase 2	PAV	12/30/1998
1984N	Naoki Kaku	554-8246	Van Ness Pedestrian Safety Improvements	PAV	03/17/1999
6618E	Leon L. Louie	558-4070	Seismic Retrofit of Third Street Bridge	Str	08/31/1997
6618N	Frank Piruzmand	558-4081	3rd Street Bridge Rehabilitation & Retrofit	Str	03/30/1998
7291E	Lynn Fong	554-8269	K-Line Rail Replacement & Ocean Avenue Improvements	Pav	11/03/1997
7381E	Fernando Cisneros	554-8278	Hunter's Point Naval Shipyard Infrastructure Backbone Phase I	Pav	11/25/1996
7416E	Deirdre Appel	558-4556	Golden Gate Park Reservoir and Pump Station		08/07/1998
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	12/22/1998
N	Linda DeBolt	554-8265	Surface Streets Improvement Project	Pav	02/06/1998

Projects in Progress (NOI)

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
----N	09/04/1997		08/07/1997	11/09/1998	10/20/1997	08/20/1997			09/04/1997
1034N	05/27/1998		05/06/1998	06/02/1998	05/11/1998	05/12/1998	04/30/1998	05/06/1998	05/13/1998
1048N	07/03/1996	Mar-99	07/11/1996	06/17/1996		07/16/1996			07/14/1996
1076N	08/11/1997	Jul-98	07/17/1997			07/23/1997	07/18/1997	07/29/1997	08/26/1997
1100N	01/08/1996	May-98		05/14/1996		12/18/1995			02/16/1996
1109K	02/15/1998		12/30/1997	04/27/1998	01/21/1998	01/09/1998	12/30/1997	01/09/1998	01/13/1998
1145N	12/02/1996	Nov-98	11/08/1996			12/03/1996			12/07/1996
1202N	01/30/1996	18-Nov-97		01/29/1996				01/16/1996	
1218N	03/29/1996	On hold	03/22/1996			03/20/1996	03/01/1996		
1243N	04/12/1996		03/29/1996				03/25/1996	03/19/1996	04/23/1996
1277N(1)	08/17/1998			07/24/1998	08/19/1998	07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(2)	08/17/1998			07/24/1998		07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(3)	09/28/1998		09/08/1998	09/10/1998	11/02/1998	09/09/1998	09/04/1998	09/23/1998	09/17/1998
1285N	11/14/1997	Jul-98	10/21/1997	04/13/1998		10/24/1997	10/16/1997	10/20/1997	11/06/1997
1294N	12/18/1996	May-98	10/25/1996	03/19/1997		10/18/1996		10/09/1996	12/07/1996
1330N	06/27/1997	Apr-98	06/16/1997	06/17/1997		06/17/1997	06/16/1997		
1349N	02/07/1997	Apr-98	01/09/1997			03/27/1997	01/10/1997	01/24/1997	02/07/1997
1362N	01/07/1999		12/02/1998			12/02/1998	12/01/1998		12/14/1998
1374N	12/02/1996		11/08/1996	02/24/1997		12/03/1996			12/07/1996
1381N	09/12/1997		08/18/1997			08/22/1997	08/18/1997	10/29/1997	09/15/1997
1385N	07/10/1998		06/12/1998	07/10/1998		06/22/1998	06/18/1998	07/17/1998	06/23/1998
1389N	06/13/1997	May-98	05/28/1997	06/02/1997			06/05/1997	05/28/1997	06/03/1997
1395N	04/10/1998			04/27/1998	04/17/1998	06/02/1998	04/08/1998	04/13/1998	04/20/1998
1407N	02/13/1997	On hold	01/17/1997			01/21/1997	01/15/1997	01/27/1997	02/18/1997
1415N	07/31/1997	Sep-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997	07/22/1997	07/28/1997
1421N	01/17/1997	Jan-98	01/09/1997	01/06/1997		01/23/1997	01/02/1997		02/07/1997
1423N	07/31/1997	Nov-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997		07/28/1997
1432N	02/07/1997	Jun-98		02/20/1997		02/11/1997	01/23/1997		02/18/1997
1459N	08/29/1997	May-98	08/05/1997	12/22/1997	10/20/1997	08/07/1997	08/01/1997		09/05/1997
1474N	11/10/1997	Jul-98	10/21/1997	06/17/1998	10/16/1997	10/24/1997	10/16/1997		11/06/1997
1548N	09/30/1997		09/08/1997	04/13/1998	09/24/1997	09/19/1997	09/09/1997		09/30/1997
1549N	09/23/1997					09/19/1997	09/11/1997		09/30/1997
1573N	02/17/1998		01/23/1998	06/17/1998	01/23/1998	02/12/1998	01/23/1998		02/12/1998
1583N	03/23/1998		03/23/1998		03/09/1998	03/05/1998	03/09/1998	03/11/1998	03/24/1998
1585N	04/13/1998		04/29/1998	04/30/1998	04/15/1998	05/12/1998	04/09/1998	04/13/1998	04/23/1998
1587N	12/11/1998		11/09/1998	02/22/1999	11/09/1998	11/09/1998	11/02/1998		11/16/1998
1588N	12/22/1998			02/22/1999		12/02/1998	12/01/1998		12/09/1998
1590N	07/13/1998			07/13/1998		06/19/1998	06/18/1998	07/16/1998	06/23/1998
1605N	06/07/1998		05/11/1998	05/15/1998	05/11/1998	05/13/1998	05/11/1998		05/20/1998
1626N	10/22/1998		10/16/1998	11/12/1998			10/06/1998		10/15/1998
1628N	09/16/1998		09/14/1998	09/10/1998	09/10/1998	09/10/1998	09/10/1998	09/15/1998	09/17/1998
1629N	10/28/1998			11/12/1998		10/02/1998	10/01/1998	10/09/1998	10/13/1998
1630N	11/09/1998			02/22/1999	11/09/1998	11/09/1998	10/16/1998	10/13/1998	10/21/1998
1653N	09/15/1997		09/02/1997	09/09/1997		09/02/1997		09/09/1997	09/10/1997
1655N	07/27/1998		07/01/1998		07/06/1998		06/29/1998		07/20/1998
1667N	03/10/1998		02/20/1998		02/20/1998		02/20/1998	03/13/1998	03/05/1998
1668N	01/02/1998	Sep-98	12/04/1997	04/27/1998	12/12/1997	01/13/1998	12/03/1997	12/04/1997	12/16/1997
1674N	05/27/1998		05/15/1998		05/26/1998	05/22/1998	05/19/1998	06/02/1998	06/09/1998
1678N	04/13/1998								
1680N	05/13/1998		04/27/1998	06/02/1998	05/11/1998	05/26/1998		04/22/1998	05/06/1998
1701N	08/24/1998		07/29/1998	09/02/1998		08/04/1998	07/24/1998	10/15/1998	08/13/1998
1724N	07/10/1998		06/22/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	06/22/1998	06/23/1998
1727N	10/28/1998		10/02/1998	11/06/1998		10/02/1998	10/01/1998	09/30/1998	10/13/1998
1732N	10/05/1998		09/14/1998	11/06/1998	11/02/1998	09/22/1998	09/11/1998	10/15/1998	09/25/1998
1734N	01/04/1999		12/17/1998	02/22/1999		12/31/1998			01/26/1999

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1735N	10/13/1998		09/14/1998	11/06/1998		09/22/1998	09/15/1998	09/25/1998	09/25/1998
1748N	10/05/1998		09/14/1998	11/06/1998		09/22/1998	09/14/1998	10/13/1998	09/25/1998
1755N	02/02/1999			02/22/1999		01/08/1999		01/14/1999	02/05/1999
1759N	12/30/1998		11/23/1998		12/27/1998	12/10/1998			12/09/1998
1984N	03/17/1999		02/08/1999			02/18/1999	02/03/1999	02/12/1999	02/05/1999
6618E	08/31/1997	Dec-98	07/16/1997		07/15/1997	07/18/1997	07/24/1997	07/28/1997	08/26/1997
6618N	03/30/1998		03/25/1998	03/23/1998		03/23/1998	03/24/1998	03/17/1998	03/30/1998
7291E	11/03/1997		10/21/1997	06/02/1998		10/24/1997	10/08/1997	10/09/1997	10/14/1997
7381E	11/25/1996		10/31/1996			11/13/1996	11/01/1996	10/30/1996	12/07/1996
7416E	08/07/1998		07/17/1998	07/10/1998		06/30/1998	07/13/1998	07/09/1998	07/29/1998
7458E	12/22/1998		11/25/1998	02/22/1999		12/10/1998	12/01/1998		12/10/1998
N	02/06/1998		01/08/1998		01/23/1998	05/13/1998	01/08/1998	03/09/1998	01/26/1998

Projects in Progress (NOI)

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
---N	09/04/1997	08/26/1997	11/24/1998		08/19/1997		09/30/1997	09/30/1997
1034N	05/27/1998	05/06/1998	05/06/1998		06/02/1998		06/25/1998	06/25/1998
1048N	07/03/1996	06/18/1996	06/25/1996	07/16/1996	07/01/1996	06/21/1996		
1076N	08/11/1997	07/28/1997			08/04/1997	07/28/1997	07/28/1997	07/28/1997
1100N	01/08/1996	12/11/1995	12/21/1995	12/11/1995	12/28/1995	12/08/1995		
1109K	02/15/1998		01/14/1998		01/15/1998		01/27/1998	01/27/1998
1145N	12/02/1996	12/07/1996	12/02/1996		11/25/1996	12/03/1996	12/03/1996	12/03/1996
1202N	01/30/1996			01/18/1996	02/02/1996	01/18/1996		
1218N	03/29/1996	03/14/1996		03/14/1996	03/18/1996	03/18/1996		
1243N	04/12/1996	03/27/1996		04/15/1996	03/25/1996	04/02/1996		
1277N(1)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998			
1277N(2)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998	07/31/1998	08/13/1998	08/13/1998
1277N(3)	09/28/1998	09/09/1998	09/04/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1285N	11/14/1997	11/07/1997		02/11/1998	10/24/1997	10/17/1997	11/25/1997	11/25/1997
1294N	12/18/1996	10/24/1996		11/07/1996	10/28/1996	11/19/1996		
1330N	06/27/1997	07/01/1997		07/09/1997	06/27/1997	06/12/1997	07/10/1997	07/10/1997
1349N	02/07/1997	01/17/1997	01/22/1997	03/17/1997		01/13/1997	02/05/1997	02/05/1997
1362N	01/07/1999	12/01/1998	01/05/1999		12/10/1998			01/12/1999
1374N	12/02/1996	11/07/1996			11/25/1996	11/07/1996	12/02/1996	12/02/1996
1381N	09/12/1997	08/26/1997			08/21/1997			09/24/1997
1385N	07/10/1998	06/15/1998	06/23/1998		06/25/1998	10/08/1998	07/29/1998	07/29/1998
1389N	06/13/1997	05/29/1997			05/23/1997	06/11/1997	05/23/1997	05/23/1997
1395N	04/10/1998	04/13/1998	01/05/1999		04/22/1998	04/13/1998		05/14/1998
1407N	02/13/1997	02/24/1997	04/17/1997	03/19/1997	01/23/1997	02/03/1997	02/05/1997	02/05/1997
1415N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1421N	01/17/1997	01/10/1997		01/29/1997	02/19/1997	12/30/1996	01/22/1997	01/22/1997
1423N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1432N	02/07/1997	02/24/1997	02/10/1997	03/18/1997	01/31/1997	01/22/1997	02/24/1997	02/24/1997
1459N	08/29/1997	08/05/1997			08/13/1997		09/24/1997	09/24/1997
1474N	11/10/1997	11/07/1997			10/23/1997	10/14/1997	11/25/1997	11/25/1997
1548N	09/30/1997	09/12/1997			09/15/1997	09/29/1997	10/09/1997	10/09/1997
1549N	09/23/1997	09/24/1997			09/17/1997	09/15/1997	10/09/1997	10/09/1997
1573N	02/17/1998	01/26/1998	03/30/1998			01/22/1998		02/12/1998
1583N	03/23/1998	03/11/1998	03/30/1998		03/18/1998	03/09/1998	03/17/1998	
1585N	04/13/1998	04/13/1998			04/30/1998	04/13/1998	06/25/1998	06/25/1998
1587N	12/11/1998	11/13/1998		12/18/1998	11/13/1998			01/12/1999
1588N	12/22/1998	12/01/1998			12/02/1998			01/12/1999
1590N	07/13/1998	06/17/1998	08/04/1998		06/29/1998	10/08/1998	07/29/1998	07/29/1998
1605N	06/07/1998	05/12/1998				05/15/1998	06/25/1998	06/25/1998
1626N	10/22/1998	10/06/1998		11/09/1998	10/13/1998			01/12/1999
1628N	09/16/1998	09/10/1998	09/08/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1629N	10/28/1998	10/06/1998		11/09/1998	10/08/1998		11/12/1998	11/12/1998
1630N	11/09/1998	10/15/1998			10/20/1998			01/12/1999
1653N	09/15/1997	09/12/1997			09/08/1997	09/04/1997	09/24/1997	09/24/1997
1655N	07/27/1998	07/01/1998			07/02/1998	07/01/1998	07/29/1998	07/29/1998
1667N	03/10/1998	02/20/1998			02/27/1998			
1668N	01/02/1998	12/04/1997			12/12/1997		01/27/1998	01/27/1998
1674N	05/27/1998	05/18/1998	05/19/1998		06/02/1998	05/14/1998	07/09/1998	07/09/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998	05/13/1998		04/30/1998		06/25/1998	06/25/1998
1701N	08/24/1998	07/24/1998	08/24/1998	11/09/1998			08/13/1998	08/13/1998
1724N	07/10/1998	06/15/1998	06/23/1998		06/23/1998	10/08/1998	07/09/1998	07/09/1998
1727N	10/28/1998	10/02/1998		11/09/1998	10/13/1998			01/12/1999
1732N	10/05/1998	09/17/1998		11/09/1998	09/28/1998	09/11/1998		11/12/1998
1734N	01/04/1999	12/15/1998			12/29/1998			

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1735N	10/13/1998	09/18/1998		11/09/1998	09/18/1998	09/09/1998		11/12/1998
1748N	10/05/1998	09/18/1998		11/09/1998	09/24/1998	09/11/1998		11/12/1998
1755N	02/02/1999	01/05/1999			12/30/1998			
1759N	12/30/1998	12/01/1998	11/23/1998		12/14/1998			12/01/1998
1984N	03/17/1999	02/08/1999			02/09/1999			
6618E	08/31/1997	07/16/1997		07/30/1997	07/24/1997	07/28/1997	08/21/1997	08/21/1997
6618N	03/30/1998	03/25/1998			04/01/1998		05/14/1998	
7291E	11/03/1997	10/29/1997			10/20/1997		11/10/1997	11/10/1997
7381E	11/25/1996	11/06/1996	11/05/1996	11/14/1996	11/08/1996	12/18/1996	12/02/1996	12/02/1996
7416E	08/07/1998	07/13/1998		11/09/1998	07/20/1998	07/01/1998		07/29/1998
7458E	12/22/1998	11/25/1998	12/14/1998		12/15/1998			12/01/1998
N	02/06/1998	06/22/1998			01/26/1998	10/08/1998		02/12/1998

Projects in Progress (NOI)

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
----N	09/04/1997	08/12/1997		08/08/1997	08/13/1997	08/08/1997	08/08/1997	08/26/1997
1034N	05/27/1998	04/30/1998		05/19/1998	05/11/1998	05/20/1998		05/11/1998
1048N	07/03/1996		06/26/1996	07/01/1996		06/25/1996	07/03/1996	07/01/1996
1076N	08/11/1997	07/24/1997		07/24/1997	07/29/1997	08/08/1997	07/22/1997	08/15/1997
1100N	01/08/1996		12/20/1995	01/03/1996	12/14/1995	12/18/1995	12/27/1995	12/20/1995
1109K	02/15/1998	01/07/1998		01/14/1998	01/14/1998	05/20/1998	01/21/1998	01/21/1998
1145N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1202N	01/30/1996		01/16/1996	01/19/1996	01/31/1996	01/17/1996		02/06/1996
1218N	03/29/1996				03/12/1996	03/05/1996	03/27/1996	03/07/1996
1243N	04/12/1996		03/25/1996		03/27/1996	03/22/1996	03/27/1996	03/21/1996
1277N(1)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(2)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(3)	09/28/1998	09/03/1998		09/15/1998	09/17/1998		01/11/1999	09/17/1998
1285N	11/14/1997	10/20/1997	10/28/1997	10/27/1997	10/23/1997	11/18/1997	11/10/1997	11/13/1997
1294N	12/18/1996		10/25/1996	10/25/1996	10/31/1996		12/02/1996	10/24/1996
1330N	06/27/1997	06/16/1997	07/02/1997	06/23/1997	06/23/1997	07/11/1997	08/08/1997	07/02/1997
1349N	02/07/1997	01/13/1997	01/13/1997	01/21/1997	02/12/1997	02/27/1997		01/22/1997
1362N	01/07/1999	12/01/1998	12/02/1998	12/10/1998	12/10/1998		01/11/1999	12/14/1998
1374N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1381N	09/12/1997	08/15/1997		08/22/1997	08/22/1997	11/18/1997		08/26/1997
1385N	07/10/1998	06/15/1998		06/23/1998	06/19/1998			06/29/1998
1389N	06/13/1997	05/19/1997	05/29/1997	05/21/1997	05/23/1997	05/29/1997	06/26/1997	06/06/1997
1395N	04/10/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1407N	02/13/1997	01/17/1997	01/15/1997	01/24/1997	02/12/1997	02/27/1997	02/24/1997	01/22/1997
1415N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1421N	01/17/1997	01/07/1997	01/06/1997		02/18/1997	02/27/1997		01/22/1997
1423N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1432N	02/07/1997	01/27/1997	01/27/1997	01/29/1997	02/12/1997	02/27/1997		01/30/1997
1459N	08/29/1997	08/05/1997		08/06/1997	08/12/1997	08/08/1997	11/10/1997	08/26/1997
1474N	11/10/1997	10/20/1997		10/21/1997	10/22/1997	11/18/1997	11/10/1997	11/13/1997
1548N	09/30/1997	09/19/1997		09/12/1997	09/12/1997	09/24/1997	09/11/1997	09/22/1997
1549N	09/23/1997	09/12/1997		09/18/1997	09/16/1997	09/24/1997	09/19/1997	09/22/1997
1573N	02/17/1998	01/26/1998		02/12/1998	02/12/1998			02/20/1998
1583N	03/23/1998		03/20/1998	03/24/1998	03/17/1998		04/08/1998	03/03/1998
1585N	04/13/1998	04/13/1998	04/28/1998	04/20/1998	04/28/1998	05/20/1998		04/28/1998
1587N	12/11/1998		11/12/1998	11/23/1998	11/19/1998			11/19/1998
1588N	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
1590N	07/13/1998	06/15/1998		07/08/1998	06/19/1998		01/11/1999	07/07/1998
1605N	06/07/1998	05/13/1998		05/19/1998	05/20/1998	05/20/1998		06/02/1998
1626N	10/22/1998	10/05/1998			10/15/1998		01/07/1999	10/15/1998
1628N	09/16/1998	09/08/1998	09/08/1998	09/15/1998	09/17/1998	09/16/1998	09/17/1998	09/17/1998
1629N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1630N	11/09/1998	10/09/1998			10/19/1998		01/07/1999	10/27/1998
1653N	09/15/1997	09/02/1997		09/08/1997	09/12/1997		09/15/1997	09/22/1997
1655N	07/27/1998	06/29/1998	07/20/1998	07/10/1998	07/15/1998	07/29/1998	01/11/1999	07/15/1998
1667N	03/10/1998	02/20/1998		02/20/1998	02/20/1998			02/20/1998
1668N	01/02/1998	12/03/1997		12/23/1997		02/12/1998	12/11/1997	12/12/1997
1674N	05/27/1998	05/19/1998			06/03/1998	05/20/1998		06/11/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998		05/06/1998	05/06/1998	06/02/1998		05/11/1998
1701N	08/24/1998	07/24/1998		08/04/1998	08/03/1998	07/24/1998	01/11/1999	
1724N	07/10/1998	06/22/1998		06/23/1998	06/19/1998			06/29/1998
1727N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1732N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/30/1998
1734N	01/04/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998		12/31/1998	12/18/1998

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1735N	10/13/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/24/1998
1748N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/11/1999	09/30/1998
1755N	02/02/1999		12/28/1998	01/14/1999	01/05/1999		01/12/1999	01/07/1999
1759N	12/30/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/14/1998
1984N	03/17/1999	02/04/1999	02/05/1999	02/10/1999	02/17/1999			02/10/1999
6618E	08/31/1997	07/17/1997		07/21/1997	07/18/1997	03/24/1998	07/16/1997	07/18/1997
6618N	03/30/1998	03/26/1998	04/02/1998	04/02/1998		03/24/1998	04/01/1998	04/03/1998
7291E	11/03/1997	10/09/1997	10/16/1997	10/10/1997	10/15/1997	11/19/1997	11/10/1997	10/16/1997
7381E	11/25/1996	01/10/1997	11/13/1996	11/13/1996	11/07/1996		12/02/1996	11/19/1996
7416E	08/07/1998	07/21/1998		07/20/1998	07/20/1998		01/11/1999	07/31/1998
7458E	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
N	02/06/1998	02/10/1998	01/16/1998	01/14/1998	01/21/1997	02/10/1998	01/21/1998	01/21/1998

Projects in Progress (LOT)

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1001H	Paul Travis	557-4631	911/OES Emergency Communications Center		12/06/1996
1036N	Lesley Wong	554-8252	Fourth Street Pavement Renovation	Pav	05/28/1997
1077N	Steve Bui	554-8298	Bowling Green Drive Contract	SW	09/30/1997
1091N	Ed Choy	554-8284	Various Locations South of Market Removal & Pavement Renovation	Pav	04/30/1997
1106N	Steve Bui	554-8298	Western Presidio Drainage Improvements (NOI/LOT)	SW	05/16/1997
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements, Various Locations	UG	04/28/1997
1109N	Linda DeBolt	554-8265	Cesar Chavez (Army) Street Widening	Pav	12/27/1996
1133N	Ellaine Taraya	554-8245	Fulton Street Roadway Widening	Pav	10/27/1997
1155N	E. Ho/Bhula Patel	554-8324	Grant/Chestnut Street Sewer Replacements	SW	10/21/1998
1195N	Gyee Yang	558-4553	Market and Steuart Streets, AWSS Relocation	AWSS	07/20/1996
1208K	Joe Haas	558-4539	San Francisco General Hospital Underground Storage Tank Replacement	UG	03/09/1998
1223W	Lesley Wong	554-8252	Islais Creek, Street Improvements	Pav	04/30/1997
1245N	Wallis Lee	554-8344	Yosemite/Egbert Sewer Enlargment Project (formerly 3180W)	SW	11/27/1996
1253N	Iqbal Dhapa	554-8337	Twelfth Street (SR)	SW	05/16/1997
1254N	Cliff Wong	554-8339	Eleventh Street Sewer Replacement - Harrison St. to Folsom St.	SW	05/23/1997
1272N	Steve Bui	554-8298	Illinois-Cesar Chavez (Army) Streets Sewer Construction	SW	08/08/1997
1322N	Lesley Wong	554-8252	Cabrillo Street, 9th and 16th Avenues Pavement Renovation	Pav	03/11/1997
1373N	Ken Chu	554-8388	Lower Great Highway, 46th, and 48th Avenues, Pavement Renovation	Pav	09/15/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	05/28/1997
1392N	Birgit Chase	554-8336	Bayshore Blvd. - U.S. 101 Off-Ramp...Sewer Repl. (1108N)	Pav & SW	02/28/1997
1393N	Thomas Won	554-8275	Bush/Kearny/Post Streets Sewer Replacement	SW	10/24/1997
1396N	Peter Cheng	554-8348	Sutter/Fell/Broederick Streets Sewer Replacement	SW	05/12/1997
1397N	Bhula Patel	554-8324	Douglass/Dolores/Ord/23rd/28th Streets, Sewer Replacement	SW	10/17/1997
1408N	Naoki Kaku	554-8246	Geneva Avenue, Pavement Renovation	Pav	02/06/1998
1409N	Pak Choi	554-8283	Sutter Street Pavement Renovation STP-19	Pav	
1411N	Peter Cheng	554-8348	Harding Park SR	SW	11/14/1997
1413N	Iqbal Dhapa	554-8337	Davis/Kearny/Francisco Streets Sewer Replacement	SW	06/25/1997
1414N	Thomas Won	554-8275	Treat / 22nd Streets Sewer Replacement	SW	02/28/1997
1426N	Ting He	554-8338	Dore/Valencia/Clinton Park SR	SW	12/08/1997
1433N	Peter Cheng	554-8348	Shotwell Street Sewer Replacement - Army Street to 26th St	SW	11/07/1997
1440N	Pak Choi	554-8283	Various Locations Concrete Street Reconstruction No. 13	Pav	02/06/1998
1453N	Naoki Kaku	554-8246	Montgomery, Kearny, & Sacramento, Pavement Renovation	Pav	02/06/1998
1454N	Ed Choy	554-8284	Potrero Hill District Track Removal and Pavement Renovation, Phase 3	SW	04/27/1998
1460N	Birgit Chase	554-8336	Church / Folsom / Harper Streets Sewer Replacement	SW	10/22/1997
1461N	Iqbal Dhapa	554-8337	Mason / Pine / Leavenworth Streets and Meacham Place Sewer Replacement	SW	03/06/1998
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	06/22/1998
1475N	Birgit Chase	554-8336	Virginia / Fair Avenues/Godeus Street SR	SW	12/24/1997
1477N	Lynn Fong	554-8269	Various Locations Concrete Street Pavement Renovation No. 14	Pav	11/09/1998
1488N	Peter Cheng	554-8348	24th Ave/California Street Sewer Replacement (1452N)	SW	06/20/1997
1491N	Peter Cheng	554-8348	Pacific Ave. Sewer Replacement - Grant Ave. to Stockton St.	SW	09/25/1997
1519N	Pak Choi	554-8283	Bus Bulb Improvement Project Phase 1	Pav	01/23/1998
1528N	Iqbal Dhapa	554-8337	501 Laguna Honda Boulevard Easement Sewer Replacement	SW	08/25/1997
1547N	Peter Cheng	554-8348	33rd Ave/Lyon Street/Molimo Dr SR	SW	01/16/1998
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SW	01/09/1998
1550N	Bhula Patel	554-8324	Day/Congo/Marston/Cuvier SR	SW	01/30/1998
1562N	Birgit Chase	554-8336	Broadway/Bryant/22nd/Sonoma Streets Sewer Replacement	SW	06/26/1998
1563N	Iqbal Dhapa	554-8337	Balboa St. and 3rd/20th/42nd Avenues Sewer Replacement	SW	06/25/1998
1566N	Peter Cheng	554-8243	Fillmore Street SR	SW	12/19/1997
1569N	Peter Cheng	554-8348	Dolores Street/Block 7044 Easement Sewer Replacement	SW	06/12/1998
1578N	Jean To	554-8329	Golden Gate Ave. Sewer Replacement-Polk St/Van Ness & Pierce/Scott Sts	SW	03/10/1998
1579N	Jean To	554-8329	Illinois Street Sewer Replacement-20th to 19th Street		04/17/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	09/15/1998
1586N	Jean To	437-7012	Geary, Eddy, Elm and Turk Sewer Replacement	SW	10/20/1998
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	01/22/1999
1602N	Jean To	437-7012	Howard, Minna and 2nd Streets Sewer Replacement	SW	11/09/1998

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1603N	Jean To	554-8270	Broad Street, Capitol to Plymouth Avenue Sewer Replacement	SW	07/10/1998
1606N	Jean To	554-8348	Cayuga/Laurel/Rondel and Douglass Sewer Replacement	SW	10/29/1998
1631N	Jean To	554-8298	4th/10th Ave/Anza/Cabrillo Streets Sewer Replacement	SW	02/16/1999
1632N	Bhula Patel	554-8324	Post, Grove and Potomac Streets Sewer Replacement	SW	04/06/1999
1645N	Peter Cheng	554-8348	Third Street Sewer System Improvement Phase II	SW	02/24/1999
1687N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 15	Pav	08/31/1998
1729N	Narciso Paderanga, Jr.	558-8258	Brotherhood Way & Font Boulevard Pavement Renovation	Pav	03/25/1999
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	02/24/1999
6094Q	Deanna Calleros	554-8266	Mid Embarcadero Surface Rdwy and F-Line Extension	Pav	06/27/1997
7090E	Thinh Nguyen	558-4554	Various Locations Motorized Valves Contract #2	AWSS	03/19/1998
7437E	Laarni Camerino	554-8256	Howard, Folsom & Hawthorne Streets (SR)	SW	08/29/1997
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	02/24/1999
7474E	Peter Cheng	554-8348	Pine/California/Delancey Streets SR	SW	11/26/1997

Project in Progress (LOT)

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1001H	12/06/1996		12/03/1996	01/22/1997		12/05/1996		11/25/1996	12/16/1996
1036N	05/28/1997	Apr-98	05/15/1997	06/30/1997		05/09/1997	05/14/1997		
1077N	09/30/1997	Apr-98	09/08/1997	06/26/1998		09/24/1997	09/09/1997		09/05/1997
1091N	04/30/1997	15-Sep-97	04/04/1997	05/13/1997				04/11/1997	04/28/1997
1106N	05/16/1997	3-Nov-97	05/06/1997	05/13/1997		05/12/1997	05/06/1997		06/03/1997
1109K	04/28/1997		04/14/1997			04/16/1997		04/22/1997	05/08/1997
1109N	12/27/1996	Jun-98	12/05/1996				12/03/1996		02/07/1997
1133N	10/27/1997	May-98	10/21/1997		10/16/1997		10/10/1997		10/21/1997
1155N	10/21/1998		10/16/1998	11/09/1998		10/07/1998	10/06/1998		10/15/1998
1195N	07/20/1996						07/08/1996		
1208K	03/09/1998		03/24/1998	03/05/1998		03/18/1998	03/05/1998	03/12/1998	03/24/1998
1223W	04/30/1997	Jun-98	04/14/1997	05/13/1997		04/16/1997	04/21/1997		05/14/1997
1245N	11/27/1996		11/08/1996	02/24/1997					12/07/1996
1253N	05/16/1997	Apr-98	04/28/1997	05/13/1997		05/05/1997	04/29/1997		05/12/1997
1254N	05/23/1997	Jul-98	04/28/1997	05/13/1997		04/23/1997	04/22/1997		05/12/1997
1272N	08/08/1997	Jun-98	07/29/1997	06/15/1998		07/28/1997	07/28/1997		
1322N	03/11/1997	May-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997	02/14/1997	02/27/1997
1373N	09/15/1997	May-98	08/26/1997	04/22/1998			08/22/1997	08/28/1997	09/10/1997
1374N	05/28/1997	May-98	05/01/1997				04/30/1997	05/12/1997	05/14/1997
1392N	02/28/1997		02/20/1997				02/19/1997		02/27/1997
1393N	10/24/1997		10/21/1997			10/15/1997	10/08/1997		10/21/1997
1396N	05/12/1997	May-98	05/01/1997			05/28/1997			05/12/1997
1397N	10/17/1997		09/26/1997		10/20/1997	10/01/1997	09/26/1997		10/14/1997
1408N	02/06/1998	Jun-98	01/08/1998	04/22/1998	01/20/1998		01/08/1998	03/05/1998	01/21/1998
1409N							02/16/1999		
1411N	11/14/1997	Jul-98	10/23/1997			11/05/1997	10/24/1997		11/04/1997
1413N	06/25/1997	Jun-98	06/16/1997	06/17/1997		06/11/1997			07/11/1997
1414N	02/28/1997	Jul-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997		02/28/1997
1426N	12/08/1997	Sep-98	12/04/1997		12/03/1997	12/10/1997	12/03/1997		12/17/1997
1433N	11/07/1997	Jun-98	10/21/1997			10/24/1997	10/16/1997		11/13/1997
1440N	02/06/1998	Apr-98	01/08/1998	01/09/1998	01/20/1998	01/27/1998	01/08/1998		01/21/1998
1453N	02/06/1998	Jul-98	01/08/1998				01/08/1998	03/09/1998	01/26/1998
1454N	04/27/1998		04/27/1998			04/20/1998	04/16/1998	04/23/1998	07/09/1998
1460N	10/22/1997		10/21/1997			10/24/1997	10/10/1997		10/21/1997
1461N	03/06/1998	Jul-98	02/20/1998	04/02/1998			02/20/1998		
1474N	06/22/1998	Jul-98	06/03/1998	06/17/1998	06/02/1998	06/09/1998		06/02/1998	06/03/1998
1475N	12/24/1997		12/12/1997		01/20/1998	01/06/1998	12/15/1997		
1477N	11/09/1998	Jun-98	10/16/1998	11/12/1998	11/02/1998		10/16/1998	11/20/1998	10/20/1998
1488N	06/20/1997	Apr-98	06/09/1997			06/04/1997	06/03/1997		06/16/1997
1491N	09/25/1997	May-98	09/18/1997	06/30/1997		09/24/1997	09/16/1997		
1519N	01/23/1998	Jun-98	12/30/1997				12/30/1997	01/09/1998	01/26/1998
1528N	08/25/1997	Mar-98	08/20/1997		10/03/1997		08/21/1997		09/08/1997
1547N	01/16/1998		12/15/1997		01/20/1998	01/06/1998	12/17/1997		12/23/1997
1548N	01/09/1998		12/22/1997	04/13/1998	12/30/1997	01/09/1998	12/29/1997		01/06/1998
1550N	01/30/1998				01/20/1998	02/12/1998	01/14/1998		02/12/1998
1562N	06/26/1998		06/22/1998		06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1563N	06/25/1998		06/19/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1566N	12/19/1997		12/12/1997	12/19/1997	12/17/1997	12/17/1997	12/15/1997		
1569N	06/12/1998		05/15/1998	06/12/1998	06/17/1998	06/09/1998	05/19/1998	06/02/1998	06/09/1998
1578N	03/10/1998		03/24/1998	06/30/1998	03/09/1998		03/09/1998	03/11/1998	03/24/1998
1579N	04/17/1998			05/15/1998		04/14/1998	04/13/1998	04/13/1998	04/23/1998
1585N	09/15/1998		09/08/1998	09/02/1998	09/10/1998	09/17/1998	09/01/1998	09/21/1998	09/08/1998
1586N	10/20/1998		10/02/1998	11/06/1998	11/02/1998			10/09/1998	10/13/1998
1589N	01/22/1999		12/23/1998	02/22/1999			12/29/1998	12/17/1998	01/26/1999
1602N	11/09/1998		10/16/1998				10/16/1998	10/13/1998	10/20/1998

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1603N	07/10/1998		06/19/1998	07/10/1998		06/22/1998	06/18/1998	07/16/1998	06/23/1998
1606N	10/29/1998		10/02/1998	11/09/1998	11/09/1998		10/06/1998	10/13/1998	10/13/1998
1631N	02/16/1999		01/19/1999					01/14/1999	02/05/1999
1632N	04/06/1999						03/02/1999		
1645N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/19/1999	02/24/1999
1687N	08/31/1998		08/12/1998	11/06/1998	08/05/1998	08/12/1998	08/03/1998	08/03/1998	08/13/1998
1729N	03/25/1999			03/02/1999			02/16/1999	02/24/1999	
1732N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/20/1999	02/05/1999
6094Q	06/27/1997	07/98							
7090E	03/19/1998		03/24/1998	04/22/1998				03/18/1998	
7437E	08/29/1997	Jul-98	08/05/1997	04/13/1998		08/08/1997	08/06/1997	09/23/1997	09/04/1997
7458E	02/24/1999		01/19/1999				01/13/1999	01/21/1999	
7474E	11/26/1997		11/19/1997			12/04/1997	11/20/1997		12/10/1997

Project in Progress (LOT)

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1001H	12/06/1996	12/30/1996	01/22/1997		12/05/1996	12/03/1996	12/06/1996	12/06/1996
1036N	05/28/1997	05/23/1997				06/04/1997	06/12/1997	
1077N	09/30/1997	09/24/1997			10/07/1997		11/10/1997	01/27/1998
1091N	04/30/1997					04/14/1997	05/23/1997	05/23/1997
1106N	05/16/1997	05/20/1997			05/19/1997	05/13/1997	05/19/1997	05/19/1997
1109K	04/28/1997					04/22/1997	09/24/1997	09/04/1998
1109N	12/27/1996	12/14/1996	01/29/1997	01/09/1997			06/23/1997	
1133N	10/27/1997	10/16/1997			10/20/1997	10/17/1997	11/10/1997	11/10/1997
1155N	10/21/1998	10/06/1998		11/09/1998	10/13/1998			
1195N	07/20/1996			08/02/1996		07/23/1996		
1208K	03/09/1998	03/05/1998	03/30/1998		03/10/1998		05/14/1998	
1223W	04/30/1997	04/18/1997	04/17/1997			04/25/1997	05/23/1997	03/06/1998
1245N	11/27/1996			12/02/1996	12/05/1996	11/08/1996	04/15/1997	04/15/1997
1253N	05/16/1997	05/20/1997		05/14/1997		04/29/1997	05/16/1997	05/16/1997
1254N	05/23/1997	04/28/1997				04/24/1997	06/12/1997	
1272N	08/08/1997	08/05/1997			10/07/1997	07/30/1997	09/24/1997	09/24/1997
1322N	03/11/1997	03/11/1997	04/21/1997	03/25/1997		03/03/1997	04/18/1997	04/18/1997
1373N	09/15/1997	09/12/1997		11/07/1997	10/07/1997		11/10/1997	12/22/1997
1374N	05/28/1997	05/20/1997				04/29/1997	09/24/1997	03/06/1998
1392N	02/28/1997	02/28/1997	04/21/1997	03/18/1997		02/24/1997		
1393N	10/24/1997		10/22/1997		10/14/1997	10/16/1997	11/10/1997	
1396N	05/12/1997			05/14/1997		04/30/1997	06/12/1997	
1397N	10/17/1997	09/30/1997			10/07/1997	09/29/1997	11/10/1997	11/10/1997
1408N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1409N		02/22/1999			02/22/1999			
1411N	11/14/1997	11/07/1997			10/29/1997	10/29/1997	12/22/1997	12/22/1997
1413N	06/25/1997				10/07/1997	06/09/1997	06/23/1997	
1414N	02/28/1997		04/17/1997	03/18/1997		02/13/1997	04/15/1997	04/15/1997
1426N	12/08/1997				12/12/1997	12/04/1997		02/20/1998
1433N	11/07/1997	11/07/1997			10/21/1997	10/16/1997	11/25/1997	12/22/1997
1440N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1453N	02/06/1998	01/13/1998			01/14/1998		02/12/1998	
1454N	04/27/1998		04/20/1998		04/23/1998		07/09/1998	07/09/1998
1460N	10/22/1997	10/16/1997			10/20/1997	10/08/1997	11/25/1997	12/22/1997
1461N	03/06/1998	02/20/1998	03/30/1998		02/27/1998		05/14/1998	
1474N	06/22/1998	06/18/1998	06/05/1998		06/03/1998	10/08/1998	07/13/1998	
1475N	12/24/1997		01/14/1998		12/19/1997		01/27/1998	
1477N	11/09/1998	10/15/1998			10/13/1998			12/01/1998
1488N	06/20/1997	06/19/1997			06/09/1997	06/02/1997	08/08/1997	
1491N	09/25/1997	09/24/1997			10/07/1997	09/15/1997	11/10/1997	02/12/1998
1519N	01/23/1998				01/06/1998		02/12/1998	
1528N	08/25/1997	08/26/1997			10/07/1997	08/20/1997	09/26/1997	09/26/1997
1547N	01/16/1998		03/30/1998			12/15/1997	02/12/1998	
1548N	01/09/1998	12/29/1997	01/14/1998		12/29/1997	12/19/1997	02/12/1998	
1550N	01/30/1998		03/30/1998		01/21/1998	01/23/1998	04/07/1998	
1562N	06/26/1998	06/22/1998	06/23/1998		06/19/1998	06/19/1998	09/25/1998	
1563N	06/25/1998	06/22/1998	06/23/1998		06/19/1998	06/16/1998	10/27/1998	
1566N	12/19/1997		01/14/1998		12/19/1997	12/10/1997	02/20/1998	
1569N	06/12/1998	06/08/1998	05/19/1998		05/21/1998	05/15/1998	07/13/1998	
1578N	03/10/1998	03/11/1998				03/09/1998	05/14/1998	
1579N	04/17/1998	04/20/1998	04/20/1998		04/20/1998			

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1585N	09/15/1998		08/28/1998	11/09/1998	08/31/1998	09/10/1998	10/27/1998	
1586N	10/20/1998			11/09/1998	10/01/1998			
1589N	01/22/1999	12/21/1998			12/29/1998			
1602N	11/09/1998	10/15/1998	12/02/1998		10/13/1998			
1603N	07/10/1998	06/17/1998	08/04/1998		06/16/1998	10/08/1998	11/12/1998	
1606N	10/29/1998			11/09/1998	10/13/1998			
1631N	02/16/1999	01/20/1999			01/21/1999			
1632N	04/06/1999	03/02/1999			03/02/1999			
1645N	02/24/1999	01/25/1999				01/19/1999		
1687N	08/31/1998	08/07/1998	08/04/1998	11/09/1998	08/07/1998		10/06/1998	
1729N	03/25/1999	02/22/1999			02/22/1999			
1732N	02/24/1999	01/20/1999			01/20/1999	01/19/1999	02/01/1999	
6094Q	06/27/1997	09/19/1998			10/07/1997	06/13/1997	09/24/1997	09/24/1997
7090E	03/19/1998		01/05/1999		04/08/1998			
7437E	08/29/1997	08/26/1997			10/07/1997	08/07/1997	09/24/1997	09/24/1997
7458E	02/24/1999	01/20/1999			01/20/1999	01/19/1999		02/01/1999
7474E	11/26/1997				11/25/1997	11/17/1997	02/12/1998	

Projects in Progress (LOT)

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1001H	12/06/1996	12/02/1996	12/02/1996		12/05/1996	12/23/1996	12/02/1996	12/05/1996
1036N	05/28/1997	05/19/1997	05/21/1997		05/23/1997	05/29/1997		05/28/1997
1077N	09/30/1997	09/19/1997			09/15/1997	09/24/1997	09/11/1997	10/02/1997
1091N	04/30/1997	04/09/1997			04/09/1997	04/14/1997	05/14/1997	04/10/1997
1106N	05/16/1997	05/06/1997		05/13/1997	05/13/1997	05/29/1997	05/14/1997	05/28/1997
1109K	04/28/1997	04/18/1997	04/24/1997	04/24/1997	04/16/1997	04/25/1997	05/14/1997	05/08/1997
1109N	12/27/1996	12/12/1996	01/06/1997		12/16/1996	12/23/1996	12/19/1996	12/10/1996
1133N	10/27/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1155N	10/21/1998	10/05/1998			10/15/1998		01/11/1999	10/15/1998
1195N	07/20/1996		07/17/1996		07/19/1996		07/30/1996	07/15/1996
1208K	03/09/1998	03/06/1998	03/20/1998		03/17/1998		04/08/1998	04/03/1998
1223W	04/30/1997	05/05/1997	04/24/1997		04/16/1997		05/14/1997	04/24/1997
1245N	11/27/1996		11/13/1996		11/20/1996		12/02/1996	11/19/1996
1253N	05/16/1997	05/01/1997			05/02/1997	05/29/1997	05/14/1997	06/03/1998
1254N	05/23/1997	04/29/1997			04/29/1997	05/29/1997	05/14/1997	05/08/1997
1272N	08/08/1997	08/12/1997			08/05/1997	08/08/1997	08/08/1997	08/15/1997
1322N	03/11/1997	02/18/1997			03/13/1997	02/27/1997	04/21/1997	02/20/1997
1373N	09/15/1997	08/27/1997			09/04/1997	09/24/1997	09/15/1997	09/22/1997
1374N	05/28/1997	05/01/1997			05/06/1997	05/29/1997	05/14/1997	05/08/1997
1392N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1393N	10/24/1997	10/14/1997			10/15/1997	11/18/1997	12/11/1997	10/16/1997
1396N	05/12/1997	05/05/1997			05/13/1997	05/29/1997	05/14/1997	05/28/1997
1397N	10/17/1997	09/26/1997			10/02/1997	11/19/1997		10/16/1997
1408N	02/06/1998	0[illegible]2/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1409N		02/19/1999	02/22/1999		02/23/1999			03/02/1999
1411N	11/14/1997	10/28/1997	11/13/1997		10/31/1997	11/19/1997	11/10/1997	11/13/1997
1413N	06/25/1997	06/11/1997			06/19/1997	06/10/1997	08/08/1997	06/20/1997
1414N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1426N	12/08/1997	12/03/1997	12/20/1997		12/17/1997	02/12/1998	12/08/1997	12/12/1997
1433N	11/07/1997	10/20/1997	10/28/1997		10/23/1997	11/19/1997	11/10/1997	11/13/1997
1440N	02/06/1998	01/12/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1453N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1454N	04/27/1998	04/20/1998			04/28/1998	05/20/1998		05/11/1998
1460N	10/22/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1461N	03/06/1998	02/20/1998			02/20/1998	05/20/1998	04/08/1998	02/20/1998
1474N	06/22/1998				06/09/1998			06/03/1998
1475N	12/24/1997	12/13/1997	12/19/1997		12/19/1997	02/10/1998	12/29/1997	11/29/1908
1477N	11/09/1998	10/08/1998			10/19/1998		01/12/1999	10/27/1998
1488N	06/20/1997	06/04/1997			06/11/1997	07/11/1997	08/08/1997	06/20/1997
1491N	09/25/1997	09/19/1997			09/25/1997	11/19/1997	09/19/1997	09/22/1997
1519N	01/23/1998	01/07/1998			01/14/1998	05/20/1998	01/21/1998	01/21/1998
1528N	08/25/1997	08/22/1997			08/26/1997	08/21/1997	09/15/1997	09/22/1997
1547N	01/16/1998	12/19/1997			12/19/1997		12/29/1997	01/12/1998
1548N	01/09/1998	01/07/1998			01/14/1998	02/12/1998	12/29/1997	01/12/1998
1550N	01/30/1998	01/16/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1562N	06/26/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1563N	06/25/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1566N	12/19/1997	12/13/1997	12/19/1997		12/17/1997	02/10/1998	12/29/1997	01/12/1998
1569N	06/12/1998	05/19/1998			06/03/1998	05/20/1998		06/08/1998
1578N	03/10/1998	03/10/1998			03/17/1998		04/08/1998	04/03/1998
1579N	04/17/1998	04/13/1998	04/28/1998			05/20/1998		04/16/1998
1585N	09/15/1998		08/31/1998		09/15/1998		01/07/1999	09/11/1998
1586N	10/20/1998	09/28/1998			10/06/1998		01/07/1999	10/15/1998
1589N	01/22/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998		01/12/1999	01/07/1999
1602N	11/09/1998	10/08/1998			10/19/1998		01/11/1999	10/27/1998

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1603N	07/10/1998	06/15/1998			06/19/1998		01/11/1999	07/07/1998
1606N	10/29/1998	10/05/1998			10/06/1998		01/07/1999	10/15/1998
1631N	02/16/1999	01/14/1999			01/26/1999			02/03/1999
1632N	04/06/1999	10/28/1998	03/02/1999	11/23/1998	03/02/1999			11/10/1998
1645N	02/24/1999	01/11/1999	01/13/1999		01/19/1999			01/20/1999
1687N	08/31/1998	08/24/1998			08/13/1998		01/11/1999	08/25/1998
1729N	03/25/1999	02/19/1999	02/22/1999		02/23/1999			03/02/1999
1732N	02/24/1999	01/11/1999	01/13/1999		01/19/1999			01/20/1999
6094Q	06/27/1997	06/27/1997			06/12/1997			
7090E	03/19/1998				03/24/1998		04/08/1998	04/03/1998
7437E	08/29/1997	08/06/1997			08/12/1997	08/08/1997	08/08/1997	08/26/1997
7458E	02/24/1999	01/12/1999			01/20/1999			01/20/1999
7474E	11/26/1997	11/25/1997	12/03/1997		12/01/1997	02/12/1998	12/12/1997	12/12/1997

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	OP'D PAVE DATE	PROJ. COST (000)
	*	SEW=SEWER											MF=Mill & Fill		
		S&H=STREETS AND HIGHWAYS						?	= Exact year of construction not known				OL=Overlay		
		CON=CONFLICT							= New or revised project				RE=Reconstruction		
									= Under construction				JP=Joint Project		
	CLASS A EMERGENCY PROJECTS														
1615N		SEW	1998		Jackson	Montgomery	Columbus	1876	?	4 x 6	BRICK	Bad shape, out of round, crown sagging			100
1615N		SEW	1998		Columbus	Jackson	Pacific	1900	?	16"/18"	CP/BRICK				100
1615N		SEW	1998		Kearny	Jackson	Pacific	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1615N		SEW	1998		Kearny	Jackson	Washington	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1619N		SEW	1998		60 Scenic Way Easement Sewer (Assessor's Block 1303)					8"	VCP	Cracks and collpased sections			50
1621N		SEW	1998	1998	Anza	7th Ave	8th Ave	1908	?	2'6"x3'9	BRICK	Cracks and collpased sections			162
1622N		SEW	1998		3rd St	Jerrold	Kirkwood			18"	VCP	Many cracks, collapsing sections			250
1622N		SEW	1998		3rd St	Kirkwood	LaSalle			42"	CONC	Re-alignment			250
1622N		SEW	1998		3rd St	LaSalle	McKinnon			42"	CONC	Re-alignment			250
1622N		SEW	1998		3rd St	McKinnon	Newcomb			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		3rd St	Newcomb	Oakdale			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		3rd St	Oakdale	Palou			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		Donner	Jennings	Ingalls			15"	ISP	Hydraulically inadequate sewer			250
1622N		SEW	1998		Jennings	Egbert	Donner			N/A		Hydraulically inadequate sewer			250
1623N		SEW	1998		Green	Polk	Van Ness	1890	?	16"	VCP				150
1218N	BSSR	SEW	1998		Harrison	5th St	Morris	1935		12/18/21	VCP	Severe cracks, many dips/debris restrict flow	MF	3/98	230
			1998		Polk	Grove	McAlister	1877		3x5	BRICK	Bricks missing, sand infiltration	MF	1998	129
			1998		Van Ness	Golden Gate	McAlister	1877		3x5	BRICK	Bricks missing, crown starting to collapse			200
			1998		Polk	Bush	Sutter	1877		3x5	BRICK	Bricks missing, sand infiltration, walls collapsing			160
														CLASS A EMERGENCY =	$2,942
	ACCELERATED PROJECTS														
1433N		SEW	1998	Spl	Shotwell	26th St	Army St	1890	?	15"	VCP	Street Pavement & Sewer Collapsed			99
1433N	....N	SEW	1998		Moultrie	Eugenia	Cortland	1915	?	10"	VCP	Broken pipe, cracks, infiltration			111
1433N	....N	SEW	1998	136	26th St	Dolores	Church	1885		15"	VCP	Many medium & minor cracks, severe grout	MF		205
1432N	....N	SEW	1998		Post	Baker	Broderick	1900		18"	VCP	Joints open throughout, open ss, sand infiltration	MF	1/01	162
1432N	....N	SEW	1998		Post	Broderick	Divisadero	1900		18"	VCP	Collapsed @ 84-97' c-d, cracks @ 10-31'b-c	MF	1/01	162
1330N		SEW	1998		09th St	Harrison	McLea Ct MB	1900	?	24"	VCP	Crushed pipe @ 194-208, full of debris,dip			90
1547N	BSSR	SEW	1998		33rd Ave	Irving	Judah	1925	?	12"	ISP	Many St depressions, severe offsets, breaks @ ss's	MF	3/98	159
1547N		SEW	1998		Lyon	Hayes	Grove	1888		16"	ISP	Many St depressions, open joints, cracks, breaks; c-b			77
1547N		SEW	1998		Molimo	Bella Vista	Intersection	1946	?	12"/15"	VCP	Collapsed & crushed section @ 21'	MF		19
1569N		SEW	1998		Dolores	16th St	17th St	1889	?	18"	VCP	Egg shaped, Multiple cracks @ invert			168
1569N		SEW	1998		Dolores	17th St	18th St	1889	?	18"	VCP	Collapsing section, open joints			135
1569N		SEW	1998		York	21st St	22nd St	1888		10"	VCP	Collapsed sections			135
1625N	1385N	JP/S&H	1998		Lombard	Leavenworth	Jones	1900	?	18"	ISP	Cracks, open joints, fast flow	RE	Jul-98	100
1626N		SEW	1999		05th Ave	Irving	Lincoln	1900	?	12"	ISP	Many bad cracks; many street depressions			195

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1626N		SEW	1999		04th Ave	Lincoln	Hugo					Many cracks; crushed, street depressions			105
1626N		SEW	1999		Stanyan (west sic	Turk	Anza					Many bad cracks; many street depressions			185
1626N		SEW	1999		Paris	Brazil	Excelsior					Bad cracks; open joints, street depression			105
1362N	BSSR	JP/S&H	1999	188	Kate	End South	Bryant	1900	?	16"	VCP	Severe cracks 162-170' b-a; TV'd 13' b-c, offset	RE	Jul-99	100
1362N	BSSR	JP/S&H	1999	188	Gilbert	End South	Brannan	1900	?	12"	VCP	Cannot TV, flow is too high, sump area	RE	Jul-99	100
			1999		Chestnut	Fillmore	Steiner	1900		8"	VCP	Open joints, cracks, ss open, collapsed sections			100
			1999		21st Ave.	Ortega	Noreiga	1925		15"	VCP	Offsets, separated joints,holes, street depression.	MF	Jul-99	200
	. . . N		1999		Goettingen	Ward	Ordway	1915	?	8"	ISP	Open ss connections, sand infiltration, pavement sinki	RE		100
	1668N		1999		Golden Gate	Lyon	Central	1887		16"	ISP	Crushed pipe, offsets, streetfailure	MF	Jul-99	100
	. . . N		1999		Gough	Post	Geary	1911		12"	VCP	Offset joints, cracks, street depressions	RE?		100
												ACCELERATED PROJECT TOTAL =			$3,012
	1ST PRIORITY PLANNED PROJECTS: Critical Replacements-Severely collapsed/crushed sewers recommended for immediate replacement														
1491N	BSSR	SEW	1998	W-014	Pacific	Stockton	Grant	1876		3'x5'	BRICK	Fairly bad shape, out of round, missing mortar	MF	1/98	134
1426N	BSSR	SEW	1998		Clinton Park	Guerrero	Valencia	1878		12"	ISP	Offsets, infiltration, many depressions	MF	7/98	139
1426N	....N	SEW	1998		Valencia	15th St	16th St	1890	?	3x5	BRICK	Bad shape, collapsed @ 447 Valencia			418
1426N		SEW	1998		Dore	Bryant	Harrison	1912	?	16"	VCP	Many cracks, offsets, dip, street depressions			140
1503N		SEW	1998		10th Ave	Kirkham	Judah MB	1902		12"	VCP	Cracked sections and many offsets b-c			75
1503N		SEW	1998		10th Ave	Pacheco	Ortega MB	1906	?	12"	ISP	Severe offsets, depressions, fast flow, worn invert			75
1461N	BSSR	SEW	1998		Mason	Ellis St.	Eddy St.	1880	?	3x5	BRICK	Severly deformed crown,missing bricks	OL		95
1461N	....N	SEW	1998		Pine	Hyde	Leavenworth	1880	?	3x5	BRICK	Fairly bad shape (oval), 3 broken s/s			280
1461N	1727N	SEW	1998		Leavenworth	O'Farrell	Geary	1900	?	3x5	BRICK	Bad shape	MF	7/99	221
1461N		SEW	1998		Meacham	Post	End: South		?	8"	VCP	Severe cracks and damaged ss connections			60
1488N		SEW	1998		California	10th Ave	11th Ave	1900	?	8"	VCP	St. depression; crushed / collapsed			65
1488N		SEW	1998		24th Ave	California	Clement MB	1907		8"	ISP	Cracks, breaks, dip, street depressions			100
1550N		SEW	1998		Day St	Dolores	San Jose	1888		18"	ISP	Collapsed pipe			70
1550N		SEW	1998		Congo	Monterey	Hearst	1910	?	12"	VCP	Multiple cracks, st dep @ 147-159' b-c, infiltration			72
1550N	BSSR	SEW	1998		Congo	Melrose	Mangels	1910		8"	VCP	Many cracks over the block	OL		60
1550N	BSSR	SEW	1998		Marston	Circular	Edna	1910		8"	ISP	Many severe cracks	MF		114
1550N	BSSR	SEW	1998		Cuvier	Bosworth MB (m	Mirando (mhE)	1902		15"	VCP	Multiple cracks & egg shape @ 64-140' d-c	MF		90
1550N		SEW	1998		28th St	Noe	East Xing	1900	?	15"	VCP	Bad open joints @20-50'			139
1562N	....N	SEW	1998		Broadway	Taylor	Himmelmann	1952		16"	VCP	Collapsed & Crushed	RE	1/99	56
1562N	....N	SEW	1998		Broadway	Florence	Taylor	1900	?	12"	VCP	Crushed invert, mult cracks	RE	1/99	63
1562N	....N	SEW	1998		Broadway(N Sid	Cyrus Pl	Hyde MB	1952		21"	VCP	Mult cracks, ready to collapse a-b	MF	1/99	54
1562N		SEW	1998		Bryant	18th St	19th St	1889		14"	VCP	Many cracks; pipe collapses			108
1562N		SEW	1998		Sonoma	Union	Green		?	12/15"	VCP	Crushed,broken pipe, ready to collapse			75
1606N	BSSR	SEW	1999	211	Douglass	23rd St	Elizabeth	1890	?	15"	VCP	Severe offsets, separated ss's, st depn	OL		111
1606N		SEW	1999	397	Cayuga	Seneca	Junior Terr	1939		8"	VCP	Many offsets, large street depressions, infiltration			50
1606N		SEW	1999	sp1001	Laurel	Washington	Jackson	1900	?	12"	CP	Multiple severe offsets, street depressions			86
1606N		SEW	1999	sp2001	Rondel Pl	End S(17th St)	16th St	1890	?	12"	ISP	Crushed, multi-cracked sections, severe offsets			138
			1999		Bertita	Seneca	end			8"	VCP	Street collapsing (field check) several bad sections			
1155N		SEW	1999		Chestnut	Culebra	Polk	1913		12"	ISP	Numerous Cracks, Collapsed Pipe			68
1155N		SEW	1999		Chestnut	Powell	Stockton	1890		16"	CEM	Cracks, invert erosion			140
1155N		SEW	1999		Grant	Chestnut	Francisco	1918	?	14"	VCP	Offsets, Crushed Pipe, Debris			99
										16"	VCP	Cracks, Dip, Cement Pipe			107

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	OP'D PAVE DATE	PROJ. COST (000)
1218N?		SEW	1999		Market S. Side	9th Street	10th Street	1878		3x5	BRICK	Ready to collapse			353
1218N?	....N	SEW	1999		Larkin	Golden Gate	McAllister	1874		18"	VCP	Collapsed, continuous cracks	MF		109
		SEW	1999	210	Eugenia	Prospect	Coleridge	1920	?	12"	ISP	Severe offsets, breaks, bad ss, rat, street depressions			
							NOTE: Projects with estimates rounded to 100k have not been finalized and will be revised after sizing.								
												PRIORITY 1 (Planned Projects) TOTAL =			$3,964
	2ND PRIORITY PLANNED PROJECTS: Severely cracked/crushed sewers to be replaced on a normal contract schedule.														
1254N	....N	SEW	1998		11th St	Folsom	Harrison	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			360
1603N		SEW	1998		Broad	Capitol	Plymouth	1910	?	8"	ISP	Many depressions, complaints, MUNI track replmt			215
7474E	BSSR	SEW	1998		Delancey (1st St)	Townsend	Brannan	?		12"/15"	VCP	Collapsed sections	MO		207
7474E		SEW	1998		Pine	Battery	Front	1907		18"	ISP	Collapsed, Cracks			86
7474E	1407N	SEW	1998		California	Webster	Buchanan	1880	?	15"	CEM	Offsets, hole @ 104',open joints st depressions	MF	1/1/01	142
7474E	1407N	SEW	1998		California	Laguna	Buchanan	1876	?	16"	CEM	TV'd 35', Collapsed	MF	1/1/01	323
1392N	1108N	JP/S&H	1998		Bayshore E	Oakdale MB	Jerrold	1928		15"/12"	VCP	Cracked (replace a-c), dip, debris	MF	1/98	75
1392N	1108N	JP/S&H	1998		Bayshore E	Oakdale	Jerrold MB	1928		15"/12"	VCP	Cracked (replace a-e), damaged @ 3' e-f	MF	1/98	178
1393N		SEW	1998		Bush	Kearny	Montgomery	1880	?	3x5	BRICK	Fairly bad shape,bricks, plastering			250
1393N	1453N	SEW	1998		Kearny	Sutter	Bush	1890	?	3x5	BRICK	Fairly bad shape, loose bricks	OL	10/98	208
1393N	BSSR	SEW	1998		Post	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, missing & loose bricks	MF		274
1393N	1453N	SEW	1998		Kearny	Sutter	Post	1875	?	3x5	BRICK	Bad shape, debris, crown sagging	MF	10/98	77
1393N	....N	SEW	1998		Sutter	Montgomery	Intersection	1876	?	3x5	BRICK	Intersection in bad shape	MF	1/1/01	50
1393N		SEW	1998		Bush	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, crown sagging			115
1397N	....N	SEW	1998		Ord	Corbett	Market	1900	?	15"	VCP	Cracks, cracked invert, severe offsets	MF		43
1397N	7317E	SEW	1998		Dolores	28th St	Valley	1885	?	18"	VCP	Crushed and multiple cracks	MF/JP		89
1397N	BSSR	SEW	1998		23rd St	Castro	Diamond	1888	?	15"	VCP	Severe cracks @ 25-70', heavy debris, dip	MF		180
1411N		SEW	1998		Harding Park	Skyline	Zoo					New Sewer			
1413N	6094Q	S&H	1998		Davis (Blk #200'	Clay	Washington	1878	?	3x5	BRICK	Bad shape, debris, missing bricks & mortar	RE/JP		167
1413N	BSSR	SEW	1998		Francisco	Stockton	Powell	1876	?	3x5	BRICK	Bad shape 1/2, fairly bad shape 1/2	MF		290
1413N	1453N	SEW	1998		Kearny	Green	Union	1900	?	12/8"	VCP	Crushed & cracked sections	MF	10/98	99
1474N	BSSR	SEW	1998		43rd Ave	Anza St	Balboa MB	1917	?	15"	VCP	Many cracks @ mh b-c exfiltration @ 120' b-c	OL		95
1474N	....N	SEW	1998		08th Av	Fulton	Cabrillo	1907	?	8"	VCP	Numerous cracked sections, collapse			168
1474N	BSSR	SEW	1998		06th Ave	Cabrillo	Balboa	1902	?	12"	VCP	Many cracked sections; sev. open joints., bad ss & ml	MF		133
1474N	BSSR	SEW	1998		06th Ave	Fulton	Cabrillo	1907	?	8"	ISP	Many cracked sections, hole (repair done 1/12/96)	MF		168
1548N	....N	SEW	1998		O'Farrell	Anza Vista	Masonic	1947		15"	VCP	Numerous cracks			140
1548N	BSSR	SEW	1998		Deming	Clayton MB	Uranus	1920		12"	ISP	Ready to collapse	OL		105
1548N		SEW	1998		Iron Alley	Corbett	Clayton	1917	?	15"	VCP	Offsets, roots, Hole invert @ 140' b-c			129
1548N		SEW	1998		Farnsworth	Edgewood	Willard		?	12"	VCP	Severe cracks, stopped @ 83'; recommend lining			67
1579N	1454N	JP/S&H	1998		Illinois	20th St	19th St	1910	?	18"	VCP	Multi cracked, crushed sections b-c; TV'd 60' b-c	TR	5/98	132
1475N	1389N	JP/S&H	1998		Virginia	Coleridge	Mission St	1905	?	16"	VCP	BSSR RECOMMENDED REPLACEMENT			85
1475N	1389N	JP/S&H	1998		Fair St	Coleridge	Mission	1890		12"	VCP	Mult joint offsets,cracks, infiltration, st. depression		1/99	90
1475N	1389N	JP/S&H	1998		Godeus	Coleridge MB	Mission		?	15"	VCP	Cracks/crush @123'-145'; cracks; open joints b-c	MF	1/99	70
1563N	BSSR	SEW	1998		42nd Ave	Geary	Anza	1920	?	8"	VCP	Street depression, collapse; sev. open joints	MF		145
1563N	....N	SEW	1998		Balboa	Arguello	2nd Ave	1907	?	18"	ISP	Multiple cracks			107
1563N	BSSR	SEW	1998		03rd Ave	Balboa	Anza	1908	?	8"	VCP	Many street dep.; many cracks/holes ms/s:	MF		158

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1563N		SEW	1998		20th Ave	Fulton	Cabrillo	1915		8"	ISP	Numerous street depressions			135
98-99 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)															4,000
	1477N		1999	201	Hamilton	Dwight	Woolsey	1952		12"	VCP	Cracks; crushed section (needs lining)	RE	1999	60
	1477N		1999	201	Dartmouth	Dwight	Woolsey	1952		12"	VCP	Invert cracks, Open joints (needs lining)	RE	1999	60
	7458E		1999	7	Clay	Jones MB	Taylor	1889	?	12"	?	Offsets, cracks, dip	RE	1999	90
1578N	1668N	JP/S&H	1999		Golden Gate	Polk St	Van Ness	1873		3'x5'	BRICK	Many St. depressions, Rec. by BSSR	MF	6/99	146
1578N	W-2240	JP/WD	1999		Golden Gate	Scott MB	Pierce	1875		14"	ISP/CP	Cement pipe sections, badly crackec	MF	6/99	80
1628N		S&H	1999		Moraga St	17th Ave	18th Ave								
1583N		SEW	1999		Everglade	Gellert	Lake Merced		?	21"	VCP	Easement;collapsed @ 30-40' a -b; exfiltration(line?			49
1583N	....N	SEW	1999		Victoria	Randolph	Brotherhood	1920	?	12"	ISP	Open break @112-115', cont. cracks, mh b-c			163
1583N	.......N	SEW	1999		Revere	Griffith	Hawes MB	1930		8"	VCP	Many severe cracks/crushed mh b-c	RE		70
1583N		SEW	1999		Bridgeview	Topeka	Thornton	1941		12"	VCP	Many cracks & ss problems, invert break			185
1395N		SEW	1999		Sacramento	Grant	Kearny	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			274
1395N		SEW	1999		Larkin	Pine	Bush	1875	?	3x5	BRICK	Bad shape, many loose bricks			208
1395N	1453N	SEW	1999		Sacramento	Sansome	Battery	1908		12"	ISP	Many cracks, crushed sections, debris	MF	10/98	80
1395N	....N	SEW	1999		Pine	Polk	Larkin	1880	?	3x5	BRICK	Fairly bad shape (230'), st. depression			280
START FY 99-00															
		SEW	1999		Cesar Chavez (A	Bryant	York		?	12"	VCP	Many cracks and collapsed sections			60
		SEW	1999		Folsom	Bessie	Precita	1890	?	16"	VCP	Collapsed sections, severe offsets,open ss, fast flow			39
	....N	SEW	1999		Larkin	Grove	Hayes	1915		18"	VCP	TV'd 190', collapsed, dip, debris			92
		SEW	1999		Winding Way	Prague	Xing	1915	?	8"	VCP	Collapsed & crushed pipe, exfiltration			30
1585N	BSSR	SEW	1999		05th Ave	Balboa	Anza	1908	?	16"	VCP	Severe cracks, depn @ 8-37 c-b, many separated ss	MF		166
1585N		SEW	1999		21st Ave	Clement	California	1902	?	8"	VCP	Severe offsets,Separated ss's, st. depressions			122
1585N	1407N	SEW	1999		California	Parker	Maple	1900	?	16"	VCP	Severe open joints, st. depression; Lining rec.	MF	1/1/00	30
1586N	.....N	SEW	1999		Geary Bl. S. Side	Lyon	Baker	1879		18"	VCP	Severe multi cracks, fast flow, begin to collapse	MF		151
1586N	.....N	SEW	1999		Geary Bl. S. Side	Baker	Broderick	1879	?	18"	VCP	Multi cracks, roots, fast flow	MF		138
1586N	1732N	SEW	1999		Turk	Broderick	Divisadero	1881		16"	ISP	Cracks, collapsed section	MF	7/99	152
99-00 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)															4,000
1586N	1732N	SEW	1999		Eddy	Pierce	Steiner	1875		3x5	BRICK	Bad shape (50'), rest needs plastering	MF		280
1586N	1732N	SEW	1999		Eddy	Steiner	Fillmore	1875		3'x5'	BRICK	Bad shape, missing bricks, mortar crown & walls; dirt	MF	7/99	153
1586N		SEW	2000		Elm	Scott MB	Pierce	1908	?	15"	ISP	Egg shape cracks & offsets			55
1587N		SEW	2000		07th Ave	Moraga	Lincoln	1890	?	3'x5'	Conc/Br	Fairly bad shape; Install spray-on mortar lining.			100
1587N	....N	SEW	2000		Kirkham	6th Ave MB	7th Ave	1906		18"	VCP	43 foot run with cracks throughout			107
1590N	7291E	SEW	2000		Ocean	San Leandro	San Fernando	1913		15"	VCP	Many severe cracks @ 1-90' a-b	MUNI	4/99	40
1590N	7291E	SEW	2000		Ocean	San Fernando	Junipero Serra	1913		18"	VCP	Severe Offsets & many cracked sections	MUNI	4/99	40
1590N	7291E	SEW	2000		Ocean	Pinehurst	Manor	1913		18"	VCP	Many cracked sections	MUNI	4/99	56
1589N		SEW	2000		Clipper	Douglass	Diamond MB	1962		15"	VCP	No TV Log; Many large cracks invert, exfiltration; fast flow			82
1589N	....N	SEW	2000		Noe	26th St.	Clipper MB	1888		18"	VCP	Cracks throughout, 33' run(debris)			101
1589N	BSSR	SEW	2000		Fair Oaks	22nd St	23rd St	1878		15"	ISP	Submerged, pipe coming apart. Rec by PUC	MF		144
1589N		SEW	2000		Kingston	Mission	San Jose	1910	?	12"	VCP	Many cracks , dip, size changed to 6"			40
1588N		SEW	2000		Joost	Acadia	Brompton	1926	?	12"	ISP	Many open joints, infiltration, street depresions			150
1588N	6680E	S&H	2000		Alemany	Prentiss	Putnam		?	12"	VCP	Badly crushed pipe	MF		110
START FY 00-01															

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	OP'D PAVE DATE	PROJ. COST (000)
1588N		SEW	2000		Kensington	Merced	Claremont	1915		12"	VCP	Replace mh a-b, otherwise fair condition			100
1602N	BSSR	SEW	2000		Minna	6th St	Russ	1908	?	18"	VCP	Cracked invert @ 76-78' c-d, st depressions	MF		112
1602N	....N	SEW	2000		02nd St	Brannan	Townsend	1890	?	18"	VCP	Many cracks / replace lower 1/2 block			160
1602N		SEW	2000		Howard	01st St	Fremont	1880	?	3'x5'	BRICK	Bad shape, needs cleaning, plaster and bricks	MF		100
1605N	BSSR	SEW	2000		Sacramento	Spruce	Maple	1890	?	8"	ISP	Many seaprated ss's; infiltration	MF		110
1605N	BSSR	SEW	2000		Pierce	Green MB	Union	1885		18"	VCP	May collapse @219'-238', 0-110' replaced	MF		96
1605N	....N	SEW	2000		Wilmot	Webster	Fillmore	1900	?	10"	ISP/CP	Multiple extensive cracks/ cement pipe			120
1629N	1734N	SEW	2000	398	Union	Hyde	Larkin	1900	?	12"/18"	ISP	Crushed invert; multiple cracks, exfiltration	MF	7/99	115
1629N	......N	SEW	2000		Union	Hyde	Leavenworth	1900	?	8"/15"	ISP	3pt cracks, errosion of cement pipe sections, hole	OL	1/99	51
		SEW	2000		Union	Divisadero	Broderick	1885	?	8"/12"	VCP	Cracks/collapse, offsets, open joints		done 4/95	125
	......N	SEW	2000		Union	Jones St	Taylor St	1900		16"	CEM	Many sections collapsed, fast flow, rat	MF	7/99	130
1629N		SEW	2000	208	Kearny	Filbert	Union	1900	?	15"	VCP	Severe offsets, crushed sections, exfiltration			78
1630N	....N	SEW	2000		Polk	Greenwich MB	Filbert	1890	?	10"/18"	VCP	Continuous cracks, offsets			109
1630N		SEW	2000	199	Francisco	Polk	Van Ness	1914		12"	VCP	Many offsets & cracks; fast flow; lining recommended			50
1630N		SEW	2000		Quincy	Pine	California	1900	?	15"	VCP	Many severe cracks, breaks			84
	00-01 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
1630N	....N	SEW	1999		Sacramento	Taylor	Mason	1875		16"	ISP	Many cracks, open joint			138
1631N		SEW	1999	383	04th Avenue	Cabrillo	Balboa	1908	?	8"	VCP	Street depressions, separated ss's, open breaks			166
1631N		SEW	1999	400	10th Ave	Clement MB	Geary	1912	?	8"	ISP	Separated ss's, st depressions, low spots, exfiltration			
1631N	......N	SEW	1999		Anza	9th Avenue	10th Avenue	1907		8"	VCP	Many separated side sewers, exfiltration	MF	1/00	55
1631N	......N	S &H	1999	366	Cabrillo St	6th Ave	7th Ave	1908	?	8"	VCP	Severe open breaks, street depressions	MF		63
1632N	......N	SEW	1999		Post	Lyon	Baker	1900		18"	VCP	ss separated ; hole invert 233-239' a-b, offses, fast flo	MF	1/01	146
1632N	BSSR	SEW	1999		Grove	Baker	Broderick	1890		16"	ISP	Severe offsets, cracks; crushed section	OL		119
1632N		SEW	1999		Potomac St	Waller St	End South	1930	?	8"	VCP	Mult cracks, separated ss, infiltrtion, st. depn			79
1633N		SEW	1999		Greenwich	Webster	Fillmore								
1633N		SEW	1999		Precita South	Coso	Emmet Pl								
		SEW	2001	210	Precita South	Treat	Harrison	1900	?	16"	ISP	Multi cracks, loosing shape, fast flow, rat			
		SEW	2001	210	Precita South	Harrison	Alabama	1900	?	16"/18"	ISP	Many cracks, ss open @ 79' & 148' a-b, rat, replace a-b			
		SEW	2001	211	Pacific	Walnut	Laurel	1900	?	15"/12"	VCP	Cracks and open joints, street depressions, fast flow			
	......N	SEW	2001	402	Clement	27th Ave	26th Ave	1908	?	15"	ISP	Offset joints, many cracked sections			
START FY 01-02															
		SEW	2001	402	3rd St	4th St MB	16th St	1911		12"	VCP	Many cracked sections, collapse @ 27' b-a			
		SEW	2001		Hayes	Larkin	Polk	1890	?	3x5	BRICK	Bad shape, severe sags, missing bricks,bulging			190
	BSSR	SEW	2001		Sterling	1-80 ramp	Bryant	1900	?	12"	CEM	Multi cracks; ready to collapse; Rec. lining	MO	10/98	56
	BSSR	SEW	2001		Jones	Bernard	Pacific	1906	?	12"	VCP	Multiple cracked & collapsed sections	MF	n/a	40
	....N	SEW	2001		Bryant	7th St	Gilbert	1876	?	3x5	BRICK	Bad shape, cracks on crown, ready to cave in	MF		119
	....N	SEW	2001		Townsend	7th St Mb	8th St Mb	1921		12"	VCP	Dips, Cracks, Crushed			167
		SEW	2001		Esmt blk #4315/	Minnesota	3rd St	1949		12"	VCP	Several severe cracks & collapses			145
		SEW	2001		Esmt Blk #4317	Indiana	Minnesota	1949		12"	VCP	Severe multiple cracks			74
		SEW	2001		22nd Ave	Irving	Lincoln	1910	?	18"	VCP	Many active street depressions.			190
		SEW	2001		Folsom	18th St MB	17th St	1946		15"	VCP	Cont cracks 55-130', depression 157' b-c			145
	....N	SEW	2001		Rincon	Bay Bridge	Bryant	1917	?	12"	VCP	Collapsed			70
	....N	SEW	2001		Harrison	8th St	7th St	1880	?	3x5	BRICK	Missing mortar, loose bricks, out of rounc			550

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
	.....N	SEW	2001		Mission	13th St	14th St	1875	?	3'x5'	Brick	Bad shape, crown sagging, ready to collapse	MF		205
	....N	SEW	2001		08th St	Market	Intersection	?		15"	VCP	Cracked sects. replace (a-b) across Marke	RE		50
	01-02 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1727N	SEW	2002		Leavenworth	Washington	Jackson	1900	?	16"	VCP	Many cracks; invert break	MF	7/99	68
	....N	SEW	2002		Leavenworth	Greenwich	Lombard	1890	?	16"	VCP	Crushed Pipe, Numerous Cracks			110
	....N	SEW	2002		Geary	Mason	Powell	1880		3x5	BRICK	Bad shape, crown buckled, mortar, bricks missing	MF		115
	....N	SEW	2002		Jones	Filbert	Lombard	1919		12"	VCP	Numerous Cracks			213
	....N	SEW	2002		Buchanan	Greenwich	Lombard St	1887		18"	VCP	Cracks, offsets, open joints			120
			2002		Stonestown Trestle Removal							Trestle is an attractive nuisance			286
			2002		Chinatown Alleys(3)										150
	BSSR	SEW	2002		South Hill	Prague	Geneva	1915		8"	ISP	Broken sections, cracks	MF/OL		60
	....N	SEW	2002		Washburn	Howard	Mission	1900	?	3x5	BRICK	Fairly bad shape, bricks, broken s/s			350
	BSSR	SEW	2002		Bayshore(W Sid	Cortland	Oakdale	1928		12"	VCP	Many bad cracks & breaks	MF		93
START FY 02-03															
		SEW	2002		Esmt Block#113	End North	Anza	1935		8"	VCP	Many separated ss's from main, exfiltration			75
		SEW	2002		City View Way	Skyview	Knollview	1951		8"	VCP	Street depressions; crushed, open joints, exfiltration, fast flow			57
		SEW	2002		19th St	Collingwood	Castro	1887		18"	ISP	Open joints, bad cracks			90
		SEW	2002		O'Shaughnessy	Portola	Del Vale MB	1939		15"	VCP	Badly cracked, no tv log, sewer lining recommended		paved '96	70
		SEW	2002		Capp	21st St	20th St	1874	?	15"	CEM	Cement pipe, cracks			145
		SEW	2002		Liberty	Guerrero	Valencia	1875		15"	VCP/CP	SS discont'd @173', cracked sections			150
		SEW	2002		37th Ave	Balboa St	Cabrillo St	1920	?	18"	ISP	Offsets, several cracked sections, fast flow			207
		SEW	2002		Folsom	Precita	Army MB	1890	?	16"	VCP	Severe offsets, open invert, exfiltration, fast flow			49
		SEW	2002		Ashbury	Waller	Haight	1890		18"	VCP	Open joints, cracks; Replace Haig-Ash int.; fast flow			111
	BSSR	SEW	2002	208	Walter	Duboce	14th St	1890	?	8"	VCP	Many open breaks, separated ss, exfiltration	OL		148
		SEW	2002		Cole	Carl	Frederick	1888		3'x5'	BRICK	Bad shape			96
		SEW	2002	199	Pacific Ave	Presidio	Walnut	1900	?	12"	VCP	Crushed sections, bad side sewer, fast flow			112
		SEW	2002	398	26th Street	San Jose	Valencia	1889	?	15"	VCP	Open breaks, separated ss's, fast flow			64
	02-03 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1453N	SEW	2003		Kearny	Maiden Ln	Geary	1875	?	3'x5'	Brick	Bad shape, crown sagging, missing bricks	RE	7/98	77
	BSSR	SEW	2003		Moraga	23rd Ave	22nd Ave	1926		12"	ISP		MF		77
		SEW	2003		Lawton	21st Ave	23rd Ave	1925		15"/21"	VCP				177
		SEW	2003	382	11th Ave	Irving	Lincoln	1903	?	10"/12"	VCP	Many active street depressions, severe offsets,ss problems			
		SEW	2003		21st Ave	Moraga	Lawton	1925		15"	ISP				190
		SEW	2003		Russia	Madrid	Lisbon	1907	?	16"	VCP	Cracks, larghe street depression'			
1394N		SEW	hold		Kirkham	21st Ave	26th Ave					New Auxiliary Sewer 12"? VCP			216
				208	Morris	Harrison	Bryant	1935	?	12"	VCP	Cracks, offsets, dip	OL	1999	
												TOTAL PRIOTITY 2 PROJECTS=			**37,386**
												TOTAL EMERGENCY, ACCELERATED, & PRIOTITY 1 PROJECTS=			**$8,475**
												PRIORITY 3 PLANNED PROJECTS (not detailed)=			**$6,900**
												GRAND TOTAL=			**######**

5.93
1/99

DPW

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

DOCUMENTS DEPT.
APR 12 1999
SAN FRANCISCO
PUBLIC LIBRARY

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 409
March 11, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4004
Joe Ovadia	558-4004
Jean To	554-8298
James Walsh	554-8272

Street Construction Coordination Center

Amy Chow	554-8249
Joe Norris	554-8274
Vitaly Troyan	554-5803

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Cynthia Chono	554-6196
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Albert Wong	554-2331

MUNI Engineering/DDC

Charles Kascal	554-1803
Roger Nguyen	554-1742

PUC UEB

Luke Cheng	554-1834
Mohammad Rohgadai	554-1852

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

Bob Rief	920-4010

Redevelopment Agency

(Representative not present)

Caltrans

Karen Ashe	557-7052
Don Manning	557-4021

Caltrans Public Information

(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric

Kathy Devine	695-3492

S F Thermal

(Representative not present)

Allstar / Metro Media

Nick Araujo	431-2510

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

Shaun Reid	510-782-0900

RCN

Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 409

1. The members introduced themselves around the table.

2. The February 11, 1998 Minutes were approved.

3. X-1104 Monthly Report

Ms. Chono brought this month's X-1104 summaries and distributed copies of the new X-1104 form. The "72 hours" is from the inspection by BSM, and the forms will be faxed in order to expedite. BSM needs the current contact person to receive them for each agency to minimize routing time after it arrives.

Summaries for Notices of Violation will be issued next month.

Mr. Zeller noted that the Excavation Code rules apply only to streets under DPW maintenance jurisdiction, and do not apply to other jurisdictions such as Port, Caltrans, or Park & Rec.

4. Engineer's Plan Signatures

Mr. Troyan distributed a draft memo clarifying the requirement: Any drawing of work done that affects a municipal facility must be signed and stamped by a civil engineer. **See Attachment A.** The requirement does not apply where no municipal facility is involved. For non-City agencies, the only frequent application will be for undergrounding projects.

5. FY 1999/2000 Master Schedule

Ms. Chow displayed a map of the roughly 1000 projects sites in the schedule. Of these, about 200 need coordination. The information is en route to the consultant for preparation of summaries. Ms. Chow added that a Web page is in preparation for electronic clearance updates. **See Attachment B**.

Mr. Troyan noted that the next 5 Year Plan updates are due on March 31. The information, so far as it is knowable, must be accurate so the system can work. We advise a formal hard-copy transmittal signed by a suitable agency official. As before, the schedule should be in three tiers: first year, second year, and last three years.

6. Mayor's Action Plan for Restoring the Condition of City Streets

Mr. Troyan distributed copies of a draft of the action plan. The procedure for potholes will be that a street inspector will mark defects attributable to utility trenches and prepare the X-1104 forms. The inspector will be followed by a BSSR cold patch crew who will repair minor non-marked defects and note more serious ones for repair by the BSSR hot patch crew the next day. There will be five cold patch crews and three hot patch crews, each assigned to sections of the City. The objective is to eliminate potholes as nearly as possible. **See Attachment C**.

Meetings are in progress with the major players about excavation control. The new Code rules go into effect for all sites on March 15. Requests for exceptions will be received and answered only in writing.

The increased paving rate will be from blocks already in the Status Report for clearance.

Public information sign rules will be strictly enforced, both for advance notice to the neighborhood and to alert traffic of the site far enough upstream to select an alternate route. SCCC's new public service number, at which to reach Nancy Lynch, will be 554-SCCC beginning on March 22.

7. Mission Street Paving

Mr. Ovadia reported that the contract has been awarded to Interstate Construction, to begin in three or four weeks and continue for about six months. The duration is governed by the need to permit traffic and buses to pass, and by rush hour street use. Clearances are in place except for some Gas Main notations that need to be updated, and two sewer repair notations that should be confirmed; if work is needed, it could be done by BSSR or by change order. Ms. To will investigate.

8. Ocean Avenue Project

Mr. Nguyen discussed the current status of the K-Line and street renovation project, and distributed a fact sheet. **See Attachment D.** The schedules and sequencing are now being arranged, to do the work in ten segments of about four blocks each. At the request of the Mayor's Office, bus bulbs have been added. The project should take about 18 months to complete. A project bar chart is in preparation. Three blocks require sewer work, but there is no anticipated water main work. The undergrounding will precede the rest of the project by installing electrical conduit in preparation for street lighting, with the wires to be pulled later. Public outreach is in progress, including flyers and neighborhood meetings, and will continue. Ms. Devine suggested that it could be covered in the newsletter enclosed with the PG&E bill. The project will be discussed at the Quality of Life meeting at City College on March 23 (see New Business) and at a neighborhood site on April 12, location to be determined.

9. Montgomery Street Paving

Mr. Cisneros reported that work began last weekend on Montgomery and on First Street. The schedule will be adjusted to accommodate the St. Patrick's Day parade.

10. New Business

Mr. Troyan asked that RCN present their current project plans at next month's meeting. Mr. Weber said they would.

Mr. Walsh reported three blocks in Leavenworth have been found to require urgent sewer repairs. These blocks have been dropped from the paving project and will be resurfaced as part of the sewer work. The rest of the sewer program will have to be adjusted accordingly.

The Neighborhood Quality of Life meeting for the West of Twin Peaks area will be at City College, 50 Phelan Avenue, Room E101 of Conlan Hall, from 6:30 pm to 8:30 pm.

A contact list for SCCC-related matters was distributed. **See Attachment F**.

The next meeting will be at 10:00 am Thursday, April 8, 1999, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

Attachment A

Signing of Plans by Civil Engineer

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, AIA, Director and City Architect

(415) 554-5803
FAX (415) 554-6944
http://www.sfdpw.com

Department of Public Works
Office of the Director
#1 Dr. Carlton B. Goodlett Place, Ste. 348
San Francisco, CA 94102-4645
Vitaly B. Troyan, P.E., Special Assistant to the Director

DRAFT MARCH 11,1999

INTER-OFFICE MEMO

TO: Cynthia Chono **DATE:**

FROM: Vitaly B. Troyan, PE

SUBJECT: Signing of Trench Plans by Civil Engineer

Based on discussions with the State Board of Registration for Professional Engineers and Surveyors and with the City Attorney, the following policy shall be adopted for the signing of plans submitted with excavation permit applications:

"Any plan showing the location or cross section of trenches in City streets for municipal facilities such as water mains, sewer mains or undergrounding of City owned facilities shall be signed and stamped by a licensed Civil Engineer."

Attachment B

CULCOP Email Clearance Form

City & County of San Francisco

Deparment of Public Works

BOE

CULCOP - CLEARANCE FORM

-Clear within 2 weeks- ***APRIL***

NAME_:

AGENCY_:

JP	JP Notes	ST	From	TO	Job Order	Clearance date
		MARKET ST	**MISSION ST**	**ASHBY AV**		
		CHESTNUT ST	**CASTRO ST**	**VALENCIA ST**		
		AMY ST	**CHAW ST**	**VALENCIA ST**		
		MARKET ST	**MISSION ST**	**ASHBY AV**		
*		**CHESTNUT ST**	**CASTRO ST**	**VALENCIA ST**		
		AMY ST	**CHAW ST**	**VALENCIA ST**		

		VALENCIA ST	**VALENCIA ST**	**VALENCIA ST**		
		BEMIS ST	**DIGBY ST**	**DIGBY ST**		

*Note: For Streets with * in JP column, please confirm clearance status.*

TEXT:

Please complete form and return

POST CLEAR

THANKS

If you need information about CULCOP data

Attachment C

Mayor's Action Plan

DRAFT 3/7/99

ACTION PLAN

RESTORING THE CONDITION OF CITY STREETS

The condition of City streets has worsened by 25% during the last decade. The Pavement Condition Score of the average City block has deteriorated from 74.1 in FY 1988-89 to 55.1 in FY 1998-99.

During the last five years, the amount of utility excavation has increased by over 1/3 (from 534,677 in FY 92-93 to over 720,000 square feet in FY 97-98). This trend is increasing - plans for future work submitted by the utilities show that over half of all city blocks will be excavated in the next five years.

This excavation, combined with unusually large amounts of rainfall, has resulted in a large number of potholes, failed trenches, and other street defects. Transit riders, the motoring public, bicyclists and pedestrians are suffering from the deteriorated condition of City streets.

Effective immediately, the Department of Public Works (DPW) is initiating the following actions to restore City streets to an acceptable condition:

1. **Fix the potholes**.
    - DPW will form five extra "pothole patrols" and one extra "hot patch" crew to identify and repair street defects. On March 15th, these pothole patrols will begin driving along streets in one area after another repairing every pothole they encounter. [Resp: Rich]
    - For street defects beyond the "pothole patrols" ability to repair, streets inspectors working in the same areas will issue Notices to Repair which will be sent to the Bureau of Street and Sewer Repair. BSSR will dispatch "hot patch" crews to fix these defects. [Resp: Rich/Cynthia]
    - Street defects which are the responsibility of utilities will be repaired and billed to the utility. [Resp: Rich]

2. **Control utility excavation**.
    - A new Excavation Code went into effect on January 1, 1999. Utilities with existing permits or contracts were allowed to continue to operate under the "old" rules. This grace period will expire on March 31st. After that, all excavators must operate under the new rules, which require improved coordination, housekeeping and trench restoration. [Resp: Vit]
    - Each utility is required to post a bond guaranteeing the quality of its work by March 31st. [Resp: Cynthia]
    - A complete review of all utility construction has been initiated with the intent of limiting the total amount of construction in City streets at any time. [Resp: Amy/Vit/Cynthia]

3. **Pave the streets**.
    - DPW plans to pave 478 blocks this year, the largest amount of paving in the last decade. Over $14M will be spent, primarily from the City's ½ cent sales tax for transportation projects. [Resp: Joe]
    - The first paving project will involve paving of Montgomery Street, which will be done at night and on weekends. Construction will begin March 6th. [Resp: Fernando] Paving of Mission Street, from Cesar Chavez to Santa Marina (near Cortland), will begin shortly thereafter. [Resp: Joe]
    - Additional funds from the Street Damage Restoration Fee, a fee paid by those who excavate in City streets after January 1st, will also be used for paving. [Resp: Vit]
    - The City's popular slurry sealing program, a low cost method of extending pavement life, will resume once dry weather returns. Over 100 blocks will be sealed this year. [Resp: Rich]

4. **Keep the public informed.**
    - Fliers describing paving and major utility projects will be distributed to affected residents. [Resp: Alex/Frank/Nancy?]
    - Project signs containing project hotline numbers will be posted at each major project. [Joe/Cynthia]
    - Signs will be posted diverting traffic away from major construction projects. [Resp: Joe/Cynthia]

- The City's new Street Construction Coordination Center has been formed. For answers to paving or excavation questions, call **554-SCCC** after March 22nd. [Resp: Nancy]

COMMENTS? PLEASE EMAIL OR CALL ME ASAP AT 554-5803. VIT

DISTRIBUTION (POTHOLE TEAM):
Harlan Kelly, Jr.
Cynthia Chono
Amy Chow
Rich Cunningham
Fernando Cisneros
Nancy Lynch
Alex Mamak
Barbara Moy
Joe Ovadia
Vitaly Troyan

c: Mark Primeau
Marcia de Vaughn
Robert Carlson
Kathy How
Don Eng
Don Munakata

Attachment D

K-Line Rail and Ocean Ave. Improvements

Public Transportation Department
Rail Replacement Program

K-LINE RAIL REPLACEMENT & OCEAN AVENUE IMPROVEMENTS PROJECT
CULCOP 3-11-99

LIMITS OF WORK:

- Ocean Avenue, between Junipero Serra and the K-Line pull-in at the Metro Green Light Rail Maintenance Center (near San Jose Avenue).
  Including: the curve at Junipero Serra and the track leading into and out of the Metro Green Facility

SCOPE OF WORK:

Municipal Railway:
- Trackway Reconstruction: including replacing the Metro Green pull-in and pull-out track and replacing/relocating in-street crossover near J. Serra to ROW near platform.
- Overhead Electrical Power System Reconstruction
- Construct new inbound and outbound fully accessible platforms at: Ocean & Lee (Phelan Loop)
- Reconstruction of existing boarding islands

Department of Public Works:
- Repave Ocean Ave. between Junipero Serra Blvd. and San Jose Ave.
- Repair sewers and catch basins (various locations)
- Utility Undergrounding (in conjunction with PG&E): Coordinate this work which is to be constructed under a separate contract

Department of Parking and Traffic:
- Replace traffic signals and traffic controllers between Junipero Serra and Howth Avenue

Bureau of Light, Heat and Power:
- Upgrade and replace streetlights along Ocean Avenue

Construction Sequencing:
- Community meetings
- Coordination meetings with PG & E, DPT and City College

New Issues:
- Sidewalk Bulb Outs – DPW and DPT are leading this effort

PROJECT SCHEDULE:

Final Design	July 1998 - June 1999
Bid and Award Contract	July 1999 – October 1999
Construction Notice-to-Proceed	November 1999
Complete Construction	July 2001

PROJECT COST:

- Approximate Construction Cost = $15.0M

Attachment E

SFWD Clarendon Pump Station and Pipelines to Stanford Heights and Summit Reservoirs

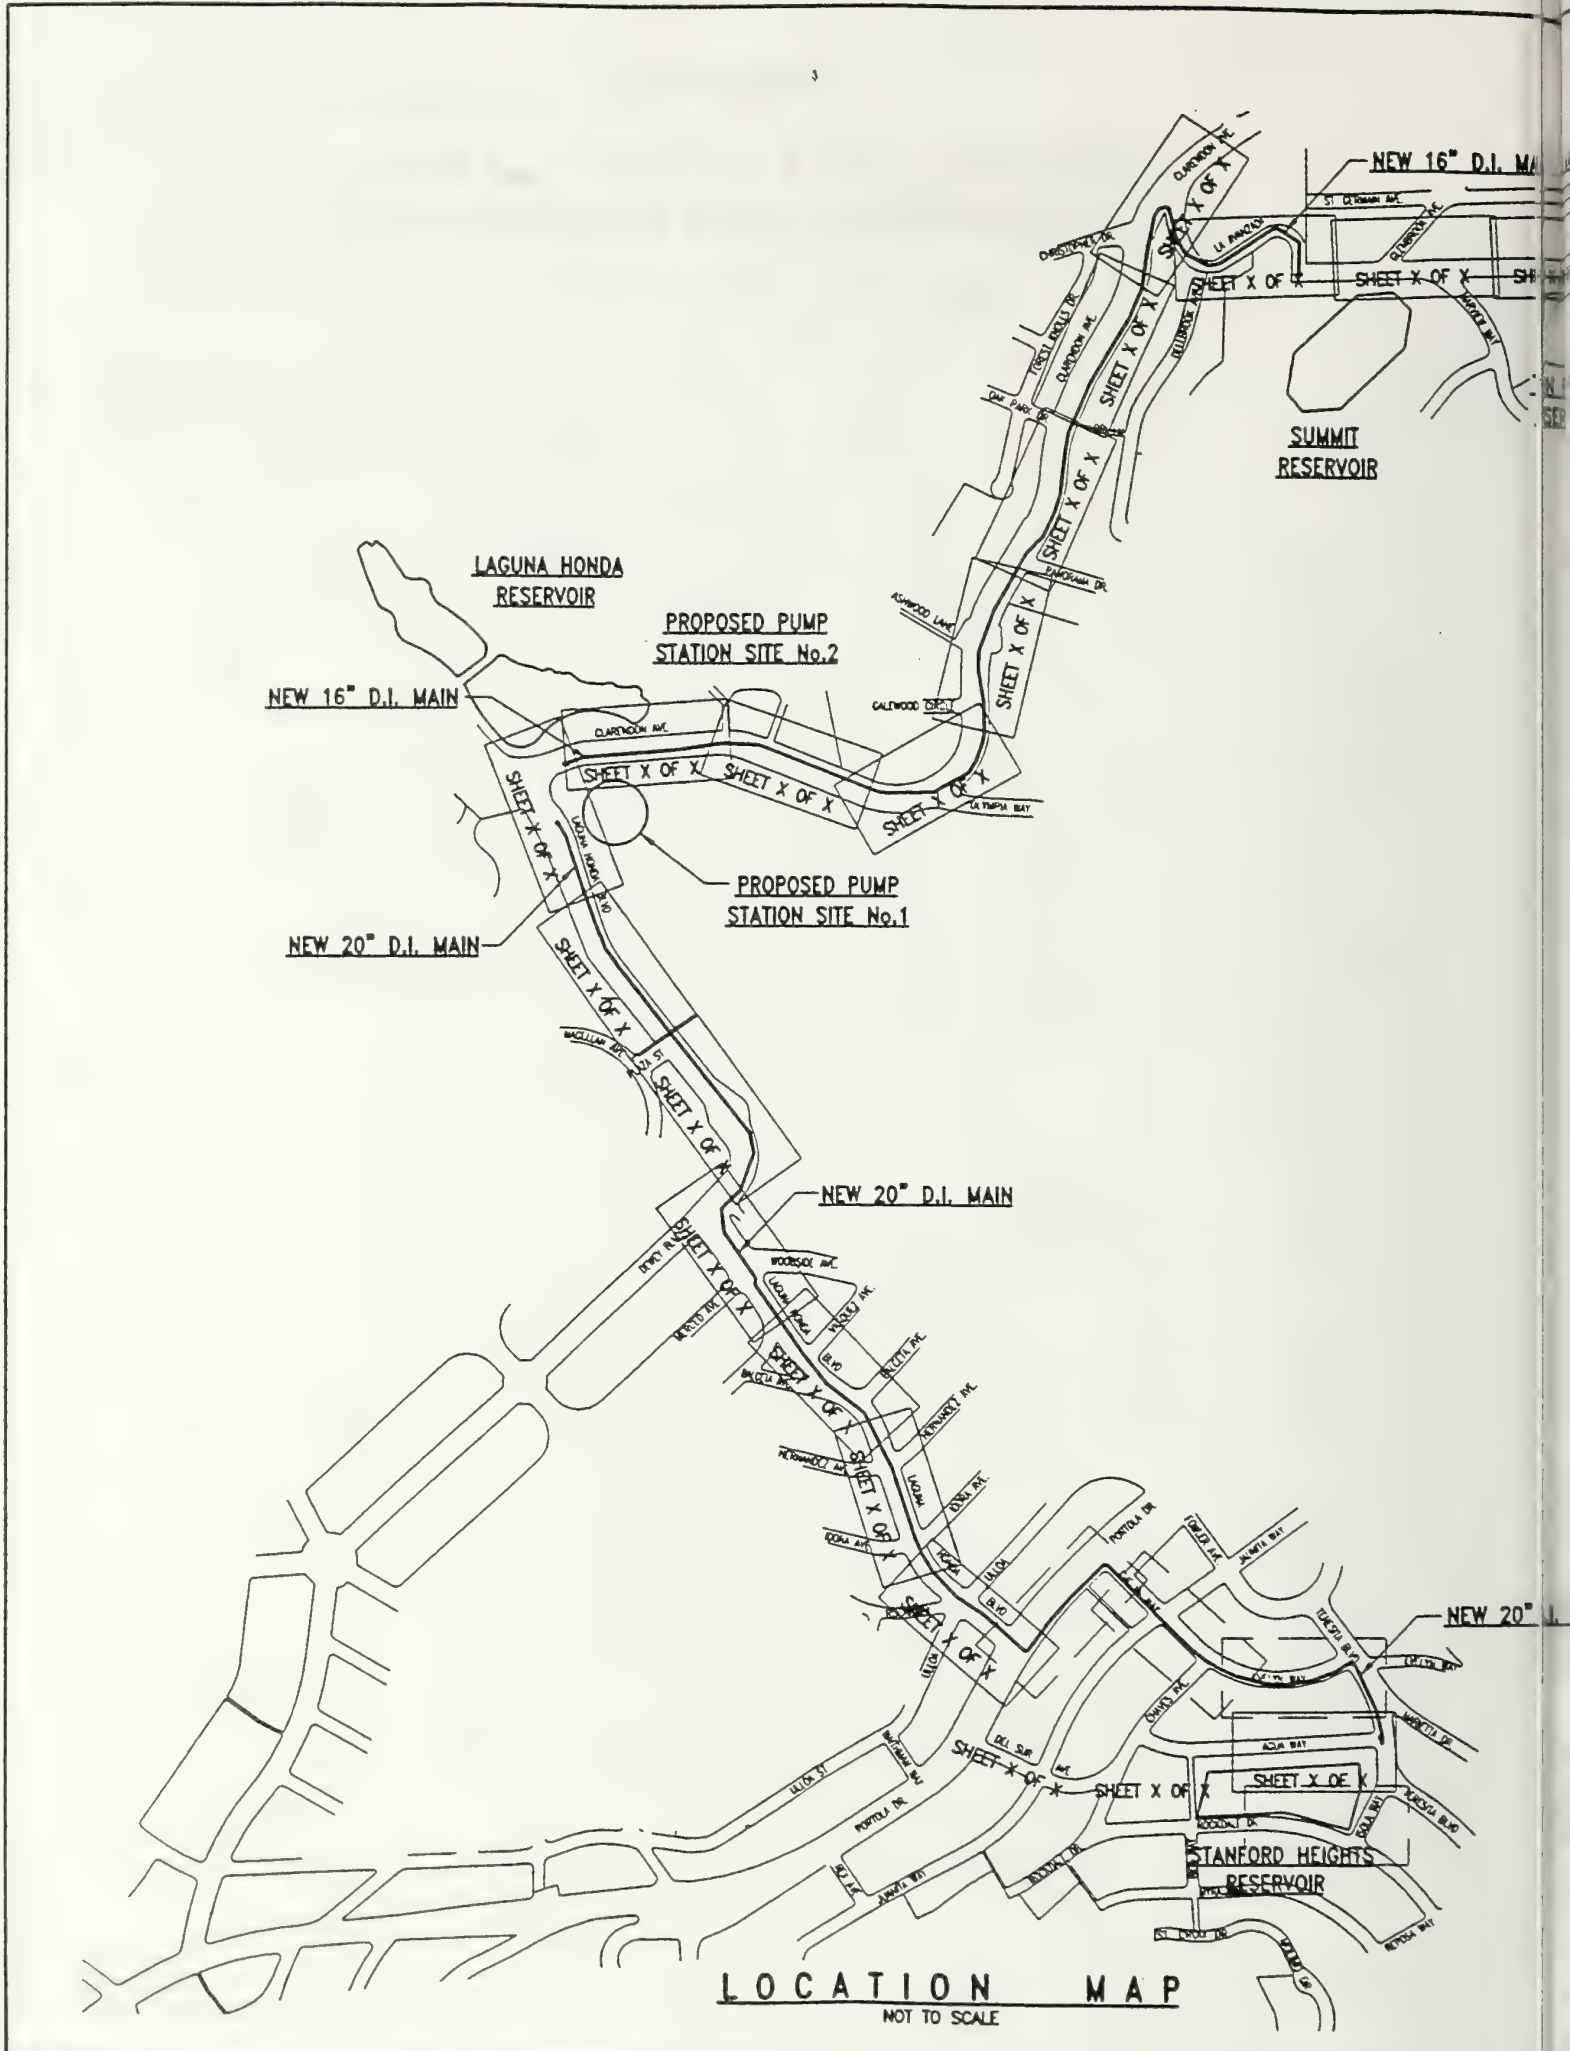
NEW 16" D.I. MA
SUMMIT RESERVOIR
LAGUNA HONDA RESERVOIR
PROPOSED PUMP STATION SITE No.2
NEW 16" D.I. MAIN
PROPOSED PUMP STATION SITE No.1
NEW 20" D.I. MAIN
NEW 20" D.I. MAIN
NEW 20"
STANFORD HEIGHTS RESERVOIR
SHEET X OF X
CLARENDON AVE
ST GERMAIN AVE
CHRISTOPHER DR
FOREST KNOLLS DR
OAK PARK DR
PANORAMA DR
ASHWOOD LANE
OLYMPIA WAY
LAGUNA HONDA BLVD
WOODSIDE AVE
ULLOA ST
PORTOLA DR
DEL SUR AVE
ST CROIX DR

L O C A T I O N   M A P

NOT TO SCALE

1/360XP
PLOT.
SCALE:
PAPER SIZE
36.24

COLOR	No
RED	028
YELLOW	008
GREEN	008
CYAN	016
BLUE	016
MAGENTA	012
WHITE	016
8	006
9	006
10	006
11	006
12	006
13	006
14	008
15	008

FILE: J:\#6321\SHT300\V21

FOR REDUCED PLANS
ORIGINAL SCALE IS IN INCHES

MAIN
SHEET X OF X
PALO ALTO AVE.
TWIN PEAKS
RESERVOIR
N
20" D.I. MAIN
0
1
2
3
4
ES

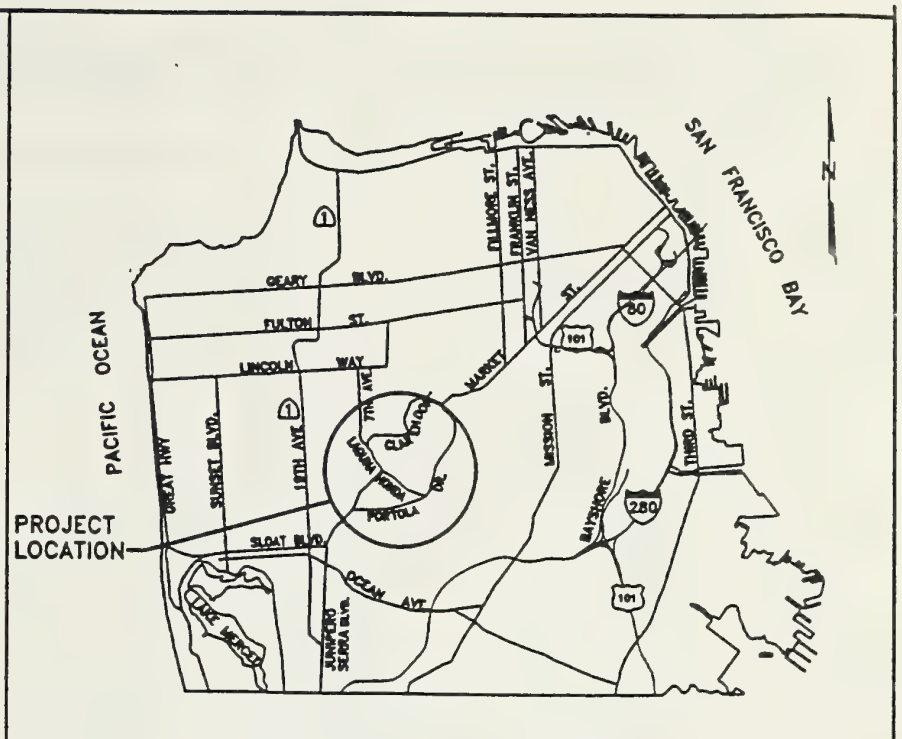
SAN FRANCISCO BAY
N
PACIFIC OCEAN
GEARY BLVD.
FULTON ST.
LINCOLN WAY
FILLMORE ST.
FRANKLIN ST.
VAN NESS AVE.
MARKET ST.
MISSION ST.
THIRD ST.
GREAT HWY
SUNSET BLVD.
19TH AVE.
7TH AVE.
CLARENDON
LAGUNA HONDA
PORTOLA DR.
SLOAT BLVD.
OCEAN AVE.
JUNIPERO SERRA BLVD.
LAKE MERCED
BAYSHORE BLVD.
PROJECT LOCATION
1
1
80
101
101
280

VICINITY MAP

NOT TO SCALE

3/8/99

PRELIMINARY PRINT
MAR/01/99

CONTRACT NO. WD-

NO	DATE	DESCRIPTION	BY	APP'D

REVISIONS

CITY AND COUNTY OF SAN FRANCISCO
PUBLIC UTILITIES COMMISSION
SAN FRANCISCO WATER DEPARTMENT

CLARENDON PUMP STATION AND PIPELINES
TO STANFORD HEIGHT & SUMMIT RESERVOIRS

LOCATION MAP AND VICINITY MAP

REFERENCES
GATE BOOK PAGES, PLANS, SURVEY NOTES, ETC. USED

GATE BOOK PAGES NO.
77, 83, 84, 87, 88
A-654 A-1168
A-1113 A-1175
A-1146

JF
SCALE N.T.S.
DATE 00-00-00

GENERAL MANAGER
SAN FRANCISCO WATER DEPARTMENT

SHEET 0 OF 0
DRAWING NO. WD-
0
0

Attachment F

SCCC Contact List

Street Construction Coordination Center Contact People List *3/5/99*

TO REPORT A PROBLEM: Call (415) 554-SCCC

NAME			PHONE NUMBER	FAX NUMBER
		STREET CONSTRUCTION COORDINATION CENTER		
Cynthia	Chono	Inspection Services Division Manager	554-6196	554-5843
Amy	Chow	Planning Manager	554-8249	554-8243
Mario	Escalona	Utility Inspector	554-5814	554-5843
Berhame	Gaime	Excavation Permit Coordinator	554-6201	554-5843
Walter	Hoo	Inspection Supervisor	554-5863	554-5843
Anthony	Lee	Utility Inspector	554-5861	554-5843
Rene	Lopez	Utility Inspector	554-5817	554-5843
Nancy	Lynch	Service Representative	554-5870	554-5843
Cora	Mingaracal	Utility Liaison	554-8270	554-8243
Joe	Norris	CULCOP Secretary	554-8274	554-8243
Robert	Sanford	Utility Inspector	554-5849	554-5843
		AUXILIARY WATER SUPPLY SYSTEM		
Patrick	Rivera	Project Manager	558-4045	558-4515
		FIRE DEPARTMENT		
Bill	Gunn	Supervisor of Engineering & Water	558-3557	647-8505
		MUNI		
Phil	Chin	Director of System Safety & Security	292-2048	292-2053
Robert	Mason	Assistant to the Director	923-6219	923-6218
Len	Olson	Chief Inspector	554-9286	554-9902
		PARKING & TRAFFIC		
James	Howard	PCO Enforcement	553-1325	553-1573
Joern	Kroll	Assistant Transportation Engineer	554-2347	554-2352
Tony	Novello	PCO Enforcement	553-7993	553-1575
Harvey	Quan	Senior Traffic Engineer	554-2319	554-2352
Stuart	Sunshine	Executive Director	554-9835	554-9814
Peter	Woo	Assistant Transportation Engineer	554-2320	554-2352
		POLICE		
Lt. Jack	Ballentine	Law Enforcement Service	553-9764	553-4946
Sgt. George	Carrington	Law Enforcement Service	553-9764	553-4946
		PUBLIC WORKS		
Scot	Burbank	Assistant Manager, Paving	558-4046	558-4519
Norman	Chan	Hydraulic Engineering Manager	554-8355	554-8308
Fernando	Cisneros	Assistant to the Director of DPW	554-6935	554-6944
Rich	Cunningham	Supt. Street & Sewer Repair	695-2101	695-2097
Don	Eng	Chief, Bureau of Construction	554-8216	554-8218
Harlan	Kelly, Jr.	City Engineer	558-4522	558-5950
Frank	Lee	Public Affairs Officer	437-7018	554-8218
Barbara	Moy	Chief, Street Use & Mapping	554-5801	554-5843
Don	Munakata	Chief, Engineering	558-4517	558-4519
Morris	Olson	Assistant Superintendent, Street & Sewer Repair	695-2086	697-2097
Joe	Ovadia	Project Manager, Paving	558-4004	558-4519

Street Construction Coordination Center Contact People List *3/5/99*

TO REPORT A PROBLEM: Call (415) 554-SCCC

NAME			PHONE NUMBER	FAX NUMBER
		STREET CONSTRUCTION COORDINATION CENTER		
Cynthia	Chono	Inspection Services Division Manager	554-6196	554-5843
Amy	Chow	Planning Manager	554-8249	554-8243
Mario	Escalona	Utility Inspector	554-5814	554-5843
Berhame	Gaime	Excavation Permit Coordinator	554-6201	554-5843
Walter	Hoo	Inspection Supervisor	554-5863	554-5843
Anthony	Lee	Utility Inspector	554-5861	554-5843
Rene	Lopez	Utility Inspector	554-5817	554-5843
Nancy	Lynch	Service Representative	554-5870	554-5843
Cora	Mingaracal	Utility Liaison	554-8270	554-8243
Joe	Norris	CULCOP Secretary	554-8274	554-8243
Robert	Sanford	Utility Inspector	554-5849	554-5843
		AUXILIARY WATER SUPPLY SYSTEM		
Patrick	Rivera	Project Manager	558-4045	558-4515
		FIRE DEPARTMENT		
Bill	Gunn	Supervisor of Engineering & Water	558-3557	647-8505
		MUNI		
Phil	Chin	Director of System Safety & Security	292-2048	292-2053
Robert	Mason	Assistant to the Director	923-6219	923-6218
Len	Olson	Chief Inspector	554-9286	554-9902
		PARKING & TRAFFIC		
James	Howard	PCO Enforcement	553-1325	553-1573
Joern	Kroll	Assistant Transportation Engineer	554-2347	554-2352
Tony	Novello	PCO Enforcement	553-7993	553-1575
Harvey	Quan	Senior Traffic Engineer	554-2319	554-2352
Stuart	Sunshine	Executive Director	554-9835	554-9814
Peter	Woo	Assistant Transportation Engineer	554-2320	554-2352
		POLICE		
Lt. Jack	Ballentine	Law Enforcement Service	553-9764	553-4946
Sgt. George	Carrington	Law Enforcement Service	553-9764	553-4946
		PUBLIC WORKS		
Scot	Burbank	Assistant Manager, Paving	558-4046	558-4519
Norman	Chan	Hydraulic Engineering Manager	554-8355	554-8308
Fernando	Cisneros	Assistant to the Director of DPW	554-6935	554-6944
Rich	Cunningham	Supt. Street & Sewer Repair	695-2101	695-2097
Don	Eng	Chief, Bureau of Construction	554-8216	554-8218
Harlan	Kelly, Jr.	City Engineer	558-4522	558-5950
Frank	Lee	Public Affairs Officer	437-7018	554-8218
Barbara	Moy	Chief, Street Use & Mapping	554-5801	554-5843
Don	Munakata	Chief, Engineering	558-4517	558-4519
Morris	Olson	Assistant Superintendent, Street & Sewer Repair	695-2086	697-2097
Joe	Ovadia	Project Manager, Paving	558-4004	558-4519

City and County of San Francisco **Department of Public Works**
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Agenda

.93

/99

Location: 1680 Mission, 4th floor conference room

Date: Thursday, April 8, 1999 10am to 11:30am.

Subject: Committee Meeting 410- Coordination of Street Construction

DOCUMENTS DEPT.
APR 12 1999
SAN FRANCISCO
PUBLIC LIBRARY

1.	Introduction	
2.	Approval of Minutes for March 11th Meeting	
3.	X1104 Monthly Report	Cynthia Chono
4.	City Distribution Division's Reservoir Inlet Piping (Attachment E)	Karen Kubick
5.	Project Montgomery Street Construction Activity Update	Fernando Cisneros
6.	Other New Business	All

Next Meeting: 2nd Thursday of Each Month
Thursday May 13, 1999 at 10:00 A. M.
Conference Room
1680 Mission Street, 4th Floor

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-8274, at leaStreet72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-8274.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 1680 Mission Street, the Fourth Floor Conference Room. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L on Mission Street; # 42 on Van Ness Avenue;
   #26 on Valencia Street; #71 on Noriega Street; #9 on Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 409
March 11, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4004
Joe Ovadia	558-4004
Jean To	554-8298
James Walsh	554-8272

Street Construction Coordination Center

Amy Chow	554-8249
Joe Norris	554-8274
Vitaly Troyan	554-5803

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Cynthia Chono	554-6196
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Albert Wong	554-2331

MUNI Engineering/DDC

Charles Kascal	554-1803
Roger Nguyen	554-1742

PUC UEB

Luke Cheng	554-1834
Mohammad Rohgadai	554-1852

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

Bob Rief	920-4010

Redevelopment Agency

(Representative not present)

Caltrans

Karen Ashe	557-7052
Don Manning	557-4021

Caltrans Public Information

(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric

Kathy Devine	695-3492

S F Thermal

(Representative not present)

Allstar / Metro Media

Nick Araujo	431-2510

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

Shaun Reid	510-782-0900

RCN

Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 409

1. The members introduced themselves around the table.

2. The February 11, 1998 Minutes were approved.

3. X-1104 Monthly Report

Ms. Chono brought this month's X-1104 summaries and distributed copies of the new X-1104 form. The "72 hours" is from the inspection by BSM, and the forms will be faxed in order to expedite. BSM needs the current contact person to receive them for each agency to minimize routing time after it arrives.

Summaries for Notices of Violation will be issued next month.

Mr. Zeller noted that the Excavation Code rules apply only to streets under DPW maintenance jurisdiction, and do not apply to other jurisdictions such as Port, Caltrans, or Park & Rec.

4. Engineer's Plan Signatures

Mr. Troyan distributed a draft memo clarifying the requirement: Any drawing of work done that affects a municipal facility must be signed and stamped by a civil engineer. **See Attachment A.** The requirement does not apply where no municipal facility is involved. For non-City agencies, the only frequent application will be for undergrounding projects.

5. FY 1999/2000 Master Schedule

Ms. Chow displayed a map of the roughly 1000 projects sites in the schedule. Of these, about 200 need coordination. The information is en route to the consultant for preparation of summaries. Ms. Chow added that a Web page is in preparation for electronic clearance updates. **See Attachment B**.

Mr. Troyan noted that the next 5 Year Plan updates are due on March 31. The information, so far as it is knowable, must be accurate so the system can work. We advise a formal hard-copy transmittal signed by a suitable agency official. As before, the schedule should be in three tiers: first year, second year, and last three years.

6. Mayor's Action Plan for Restoring the Condition of City Streets

Mr. Troyan distributed copies of a draft of the action plan. The procedure for potholes will be that a street inspector will mark defects attributable to utility trenches and prepare the X-1104 forms. The inspector will be followed by a BSSR cold patch crew who will repair minor non-marked defects and note more serious ones for repair by the BSSR hot patch crew the next day. There will be five cold patch crews and three hot patch crews, each assigned to sections of the City. The objective is to eliminate potholes as nearly as possible. **See Attachment C**.

Meetings are in progress with the major players about excavation control. The new Code rules go into effect for all sites on March 15. Requests for exceptions will be received and answered only in writing.

The increased paving rate will be from blocks already in the Status Report for clearance.

Public information sign rules will be strictly enforced, both for advance notice to the neighborhood and to alert traffic of the site far enough upstream to select an alternate route. SCCC's new public service number, at which to reach Nancy Lynch, will be 554-SCCC beginning on March 22.

7. Mission Street Paving

Mr. Ovadia reported that the contract has been awarded to Interstate Construction, to begin in three or four weeks and continue for about six months. The duration is governed by the need to permit traffic and buses to pass, and by rush hour street use. Clearances are in place except for some Gas Main notations that need to be updated, and two sewer repair notations that should be confirmed; if work is needed, it could be done by BSSR or by change order. Ms. To will investigate.

8. Ocean Avenue Project

Mr. Nguyen discussed the current status of the K-Line and street renovation project, and distributed a fact sheet. **See Attachment D.** The schedules and sequencing are now being arranged, to do the work in ten segments of about four blocks each. At the request of the Mayor's Office, bus bulbs have been added. The project should take about 18 months to complete. A project bar chart is in preparation. Three blocks require sewer work, but there is no anticipated water main work. The undergrounding will precede the rest of the project by installing electrical conduit in preparation for street lighting, with the wires to be pulled later. Public outreach is in progress, including flyers and neighborhood meetings, and will continue. Ms. Devine suggested that it could be covered in the newsletter enclosed with the PG&E bill. The project will be discussed at the Quality of Life meeting at City College on March 23 (see New Business) and at a neighborhood site on April 12, location to be determined.

9. Montgomery Street Paving

Mr. Cisneros reported that work began last weekend on Montgomery and on First Street. The schedule will be adjusted to accommodate the St. Patrick's Day parade.

10. New Business

Mr. Troyan asked that RCN present their current project plans at next month's meeting. Mr. Weber said they would.

Mr. Walsh reported three blocks in Leavenworth have been found to require urgent sewer repairs. These blocks have been dropped from the paving project and will be resurfaced as part of the sewer work. The rest of the sewer program will have to be adjusted accordingly.

The Neighborhood Quality of Life meeting for the West of Twin Peaks area will be at City College, 50 Phelan Avenue, Room E101 of Conlan Hall, from 6:30 pm to 8:30 pm.

A contact list for SCCC-related matters was distributed. **See Attachment F**.

The next meeting will be at 10:00 am Thursday, April 8, 1999, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

Attachment A

Signing of Plans by Civil Engineer

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, AIA, Director and City Architect

(415) 554-5803
FAX (415) 554-6944
http://www.sfdpw.com

Department of Public Works
Office of the Director
#1 Dr. Carlton B. Goodlett Place, Ste. 348
San Francisco, CA 94102-4645
Vitaly B. Troyan, P.E., Special Assistant to the Director

DRAFT MARCH 11,1999

INTER-OFFICE MEMO

TO: Cynthia Chono **DATE:**

FROM: Vitaly B. Troyan, PE

SUBJECT: Signing of Trench Plans by Civil Engineer

Based on discussions with the State Board of Registration for Professional Engineers and Surveyors and with the City Attorney, the following policy shall be adopted for the signing of plans submitted with excavation permit applications:

"Any plan showing the location or cross section of trenches in City streets for municipal facilities such as water mains, sewer mains or undergrounding of City owned facilities shall be signed and stamped by a licensed Civil Engineer."

Attachment B

CULCOP Email Clearance Form

City & County of San Francisco

Deparment of Public Works

BOE

CULCOP - CLEARANCE FORM

-Clear within 2 weeks- *APRIL*

NAME_:

AGENCY_:

JP	JP Notes	ST	From	TO	Job Order	Clearance date
		MARKET ST	MISSION ST	ASHBY AV		
		CHESTNUT ST	CASTRO ST	VALENCIA ST		
		AMY ST	CHAW ST	VALENCIA ST		
		MARKET ST	MISSION ST	ASHBY AV		
*		CHESTNUT ST	CASTRO ST	VALENCIA ST		
		AMY ST	CHAW ST	VALENCIA ST		

		VALENCIA ST	**VALENCIA ST**	**VALENCIA ST**		
		BEMIS ST	**DIGBY ST**	**DIGBY ST**		

*Note: For Streets with * in JP column, please confirm clearance status.*

TEXT:

Please complete form and return

POST CLEAR

THANKS

If you need information about *CULCOP data*

Attachment C

Mayor's Action Plan

DRAFT 3/7/99

ACTION PLAN

RESTORING THE CONDITION OF CITY STREETS

The condition of City streets has worsened by 25% during the last decade. The Pavement Condition Score of the average City block has deteriorated from 74.1 in FY 1988-89 to 55.1 in FY 1998-99.

During the last five years, the amount of utility excavation has increased by over 1/3 (from 534,677 in FY 92-93 to over 720,000 square feet in FY 97-98). This trend is increasing - plans for future work submitted by the utilities show that over half of all city blocks will be excavated in the next five years.

This excavation, combined with unusually large amounts of rainfall, has resulted in a large number of potholes, failed trenches, and other street defects. Transit riders, the motoring public, bicyclists and pedestrians are suffering from the deteriorated condition of City streets.

Effective immediately, the Department of Public Works (DPW) is initiating the following actions to restore City streets to an acceptable condition:

1. **Fix the potholes**.
    - DPW will form five extra "pothole patrols" and one extra "hot patch" crew to identify and repair street defects. On March 15th, these pothole patrols will begin driving along streets in one area after another repairing every pothole they encounter. [Resp: Rich]
    - For street defects beyond the "pothole patrols" ability to repair, streets inspectors working in the same areas will issue Notices to Repair which will be sent to the Bureau of Street and Sewer Repair. BSSR will dispatch "hot patch" crews to fix these defects. [Resp: Rich/Cynthia]
    - Street defects which are the responsibility of utilities will be repaired and billed to the utility. [Resp: Rich]

2. **Control utility excavation**.
   - A new Excavation Code went into effect on January 1, 1999. Utilities with existing permits or contracts were allowed to continue to operate under the "old" rules. This grace period will expire on March 31st. After that, all excavators must operate under the new rules, which require improved coordination, housekeeping and trench restoration. [Resp: Vit]
   - Each utility is required to post a bond guaranteeing the quality of its work by March 31st. [Resp: Cynthia]
   - A complete review of all utility construction has been initiated with the intent of limiting the total amount of construction in City streets at any time. [Resp: Amy/Vit/Cynthia]

3. **Pave the streets**.
   - DPW plans to pave 478 blocks this year, the largest amount of paving in the last decade. Over $14M will be spent, primarily from the City's ½ cent sales tax for transportation projects. [Resp: Joe]
   - The first paving project will involve paving of Montgomery Street, which will be done at night and on weekends. Construction will begin March 6th. [Resp: Fernando] Paving of Mission Street, from Cesar Chavez to Santa Marina (near Cortland), will begin shortly thereafter. [Resp: Joe]
   - Additional funds from the Street Damage Restoration Fee, a fee paid by those who excavate in City streets after January 1st, will also be used for paving. [Resp: Vit]
   - The City's popular slurry sealing program, a low cost method of extending pavement life, will resume once dry weather returns. Over 100 blocks will be sealed this year. [Resp: Rich]

4. **Keep the public informed.**
   - Fliers describing paving and major utility projects will be distributed to affected residents. [Resp: Alex/Frank/Nancy?]
   - Project signs containing project hotline numbers will be posted at each major project. [Joe/Cynthia]
   - Signs will be posted diverting traffic away from major construction projects. [Resp: Joe/Cynthia]

- The City's new Street Construction Coordination Center has been formed. For answers to paving or excavation questions, call **554-SCCC** after March 22nd. [Resp: Nancy]

COMMENTS? PLEASE EMAIL OR CALL ME ASAP AT 554-5803. VIT

DISTRIBUTION (POTHOLE TEAM):
Harlan Kelly, Jr.
Cynthia Chono
Amy Chow
Rich Cunningham
Fernando Cisneros
Nancy Lynch
Alex Mamak
Barbara Moy
Joe Ovadia
Vitaly Troyan

c: Mark Primeau
Marcia de Vaughn
Robert Carlson
Kathy How
Don Eng
Don Munakata

Attachment D

K-Line Rail and Ocean Ave. Improvements

Public Transportation Department
Rail Replacement Program

K-LINE RAIL REPLACEMENT & OCEAN AVENUE IMPROVEMENTS PROJECT
CULCOP 3-11-99

LIMITS OF WORK:

- Ocean Avenue, between Junipero Serra and the K-Line pull-in at the Metro Green Light Rail Maintenance Center (near San Jose Avenue).
  Including: the curve at Junipero Serra and the track leading into and out of the Metro Green Facility

SCOPE OF WORK:

Municipal Railway:
- Trackway Reconstruction: including replacing the Metro Green pull-in and pull-out track and replacing/relocating in-street crossover near J. Serra to ROW near platform.
- Overhead Electrical Power System Reconstruction
- Construct new inbound and outbound fully accessible platforms at: Ocean & Lee (Phelan Loop)
- Reconstruction of existing boarding islands

Department of Public Works:
- Repave Ocean Ave. between Junipero Serra Blvd. and San Jose Ave.
- Repair sewers and catch basins (various locations)
- Utility Undergrounding (in conjunction with PG&E): Coordinate this work which is to be constructed under a separate contract

Department of Parking and Traffic:
- Replace traffic signals and traffic controllers between Junipero Serra and Howth Avenue

Bureau of Light, Heat and Power:
- Upgrade and replace streetlights along Ocean Avenue

Construction Sequencing:
- Community meetings
- Coordination meetings with PG & E, DPT and City College

New Issues:
- Sidewalk Bulb Outs – DPW and DPT are leading this effort

PROJECT SCHEDULE:

• Final Design	July 1998 - June 1999
• Bid and Award Contract	July 1999 – October 1999
• Construction Notice-to-Proceed	November 1999
• Complete Construction	July 2001

PROJECT COST:

- Approximate Construction Cost = $15.0M

Attachment E

SFWD Clarendon Pump Station and Pipelines to Stanford Heights and Summit Reservoirs

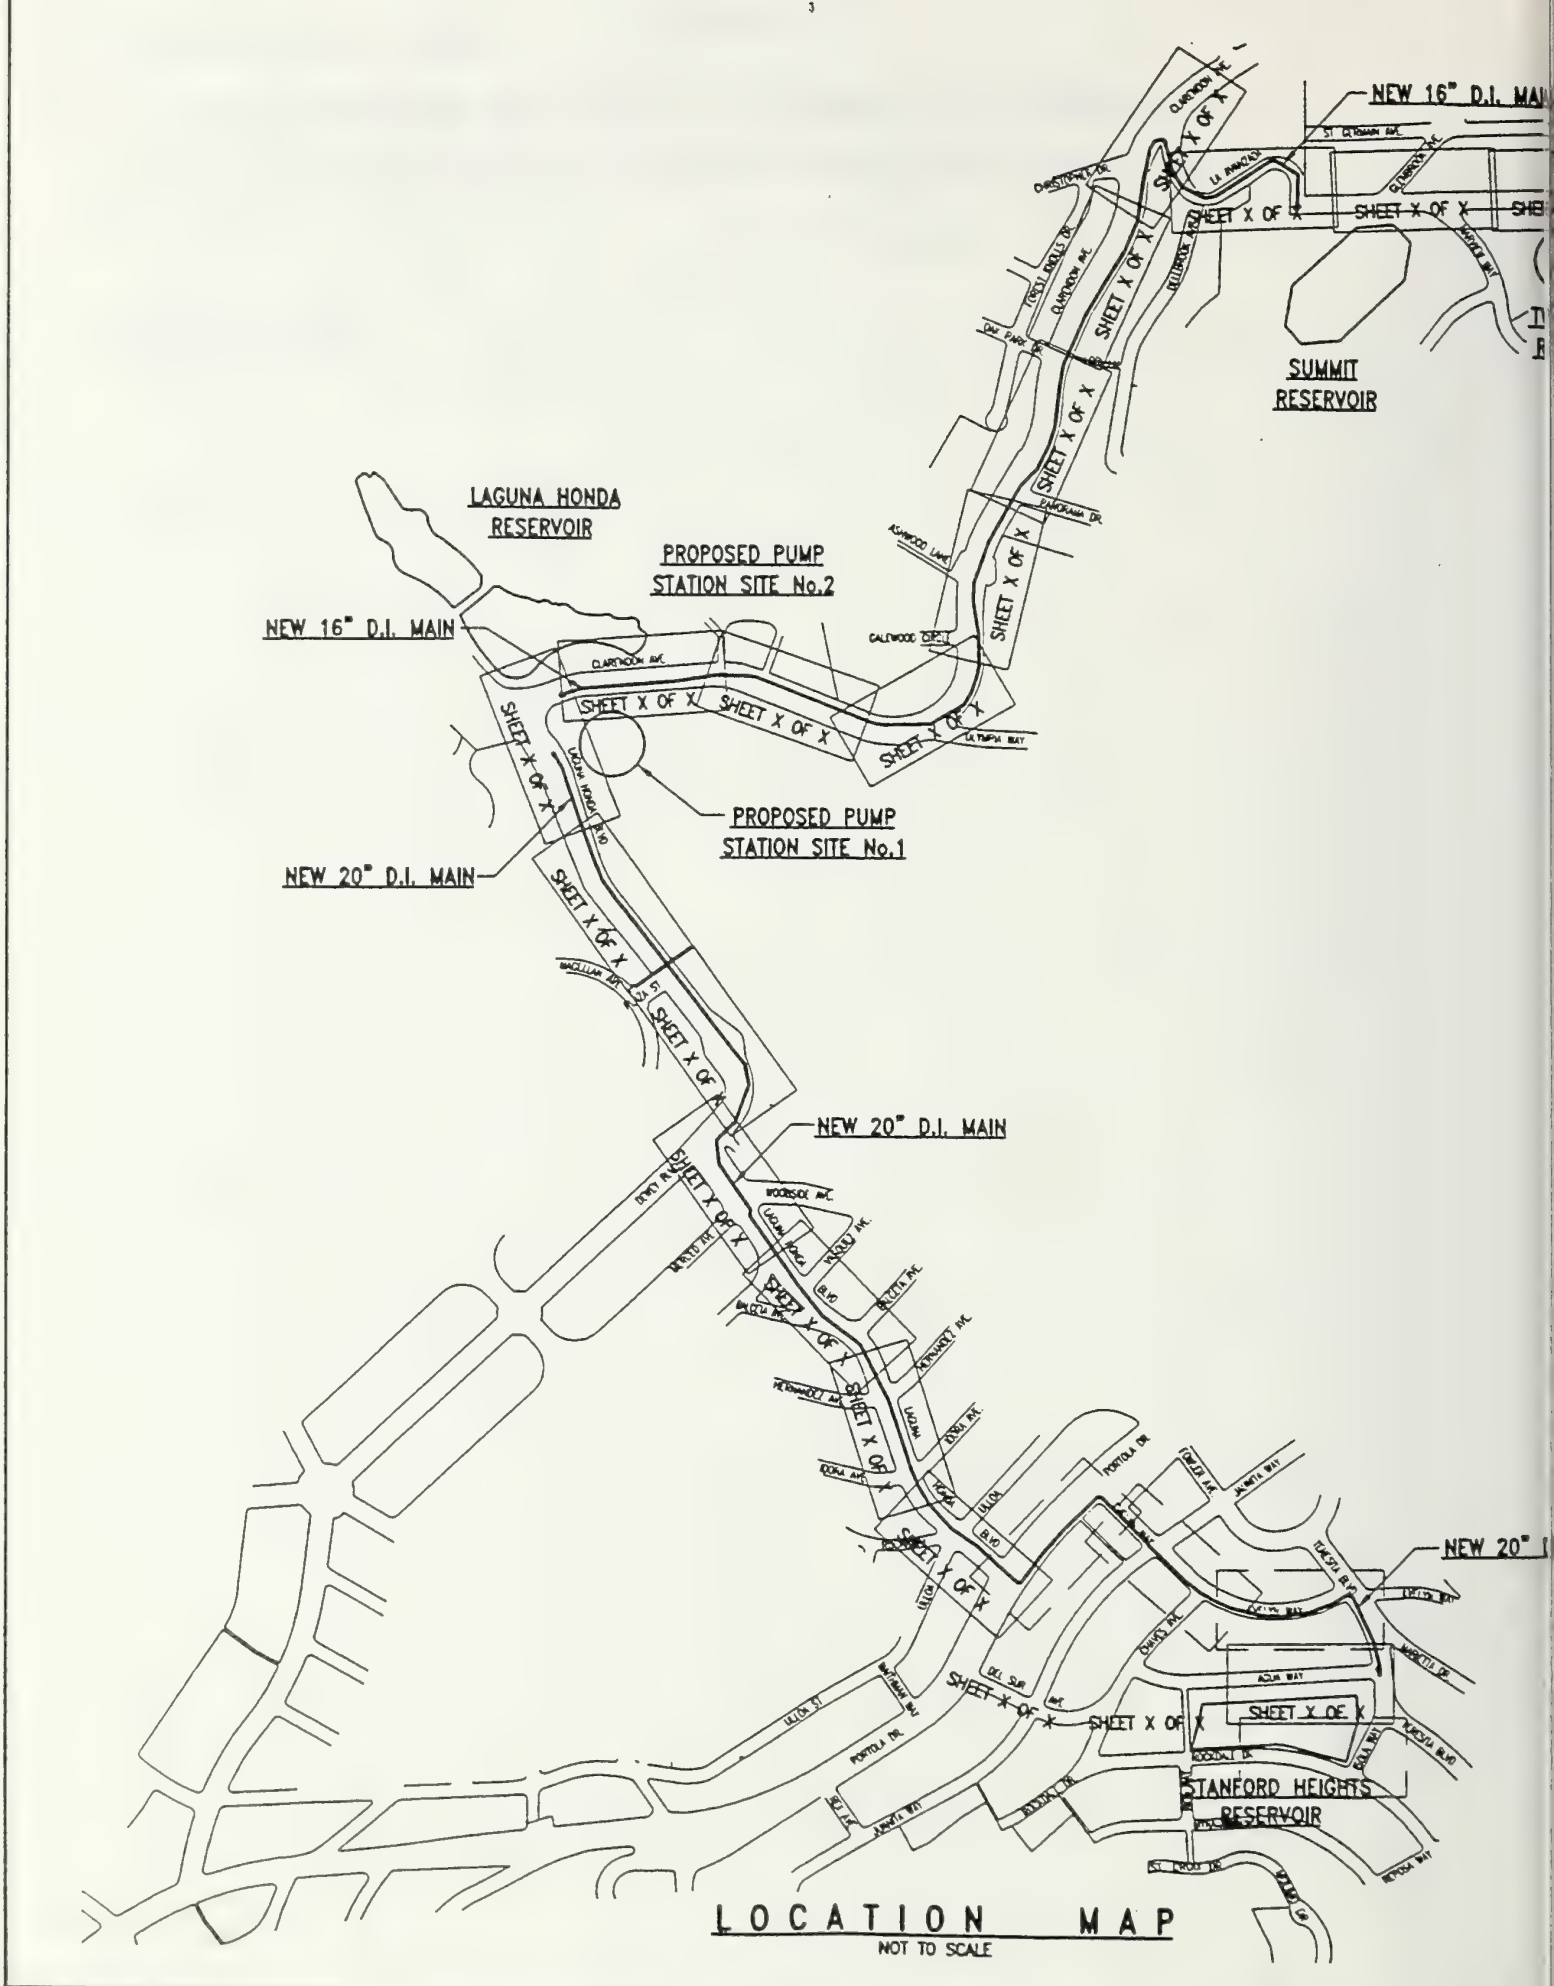
NEW 16" D.I. MAI
SUMMIT RESERVOIR
LAGUNA HONDA RESERVOIR
PROPOSED PUMP STATION SITE No.2
NEW 16" D.I. MAIN
PROPOSED PUMP STATION SITE No.1
NEW 20" D.I. MAIN
NEW 20" D.I. MAIN
NEW 20"
STANFORD HEIGHTS RESERVOIR
SHEET X OF X
CLARENDON AVE
ST GERMAIN AVE
CHRISTOPHER DR
FOREST KNOLLS DR
OAK PARK DR
PANORAMA DR
ASHWOOD LANE
GALEWOOD CIR
OLYMPIA WAY
LAGUNA HONDA BLVD
WOODSIDE AVE
PORTOLA DR
ULLOA ST
DEL SUR AVE
ASHWOOD LANE
DEWEY BLVD
ST CROIX DR

LOCATION MAP

NOT TO SCALE

FILE: J:\W6321\SHT300\V21

FOR REDUCED PLANS
ORIGINAL SCALE IS IN INCHES

1/360XP
PLOT.
SCALE
PAPER SIZE
36.24

COLOR	No
RED	028
YELLOW	008
GREEN	008
CYAN	016
BLUE	016
MAGENTA	012
WHITE	016
8	006
9	006
10	006
11	006
12	006
13	006
14	006
15	006

MAIN
SHEET X OF X
PALO ALTO AVE.
TWIN PEAKS RESERVOIR
N
20" D.I. MAIN

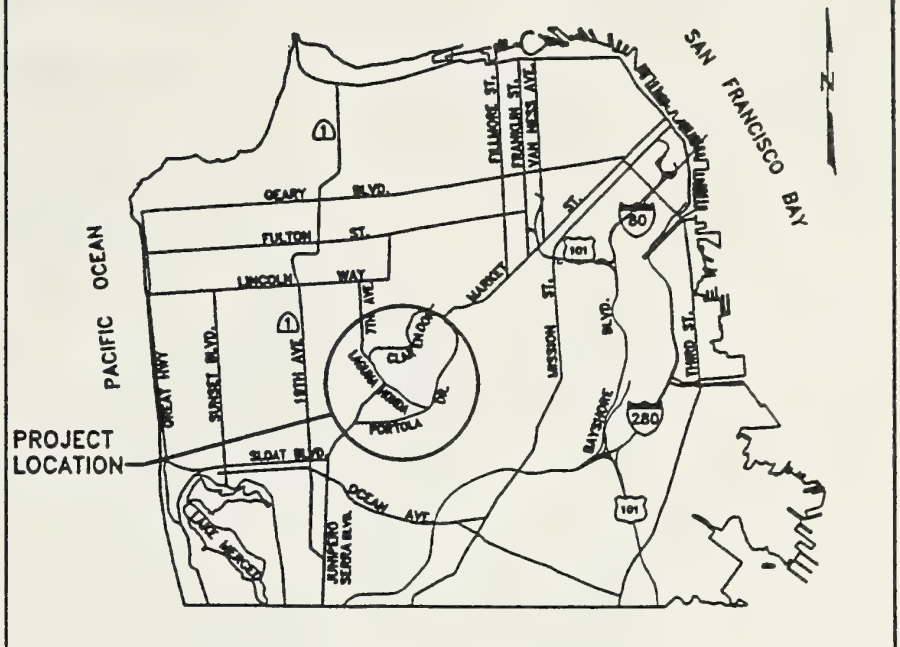
SAN FRANCISCO BAY
PACIFIC OCEAN
N
FILLMORE ST.
FRANKLIN ST.
VAN NESS AVE.
GEARY BLVD.
FULTON ST.
LINCOLN WAY
1
80
101
MARKET ST.
MISSION ST.
BLVD.
THIRD ST.
7TH AVE.
CLARENDON
LAGUNA HONDA
DR.
PORTOLA
19TH AVE.
SUNSET BLVD.
GREAT HWY
PROJECT LOCATION
SLOAT BLVD.
OCEAN AVE.
LAKE MERCED
JUNIPERO SERRA BLVD.
BAYSHORE
280
101

VICINITY MAP

NOT TO SCALE

3/8/99

PRELIMINARY PRINT
MAR/01/99

CONTRACT NO. WD-

NO.	DATE	DESCRIPTION	BY	APP'D

REVISIONS

CITY AND COUNTY OF SAN FRANCISCO
PUBLIC UTILITIES COMMISSION
SAN FRANCISCO WATER DEPARTMENT

CLARENDON PUMP STATION AND PIPELINES
TO STANFORD HEIGHT & SUMMIT RESERVOIRS

LOCATION MAP AND VICINITY MAP

REFERENCES
GATE BOOK PAGES, PLANS, SURVEY NOTES, ETC. USED

GATE BOOK PAGES NO.
77, 83, 84, 87, 88
A-654 A-1168
A-1113 A-1175
A-1146

JF
N.T.S.
00-00-00

GENERAL MANAGER
SAN FRANCISCO WATER DEPARTMENT

SHEET 0 OF 0
WD-
0
0



Attachment F

SCCC Contact List

Street Construction Coordination Center Contact People List *3/5/99*

TO REPORT A PROBLEM: Call (415) 554-SCCC

NAME			PHONE NUMBER	FAX NUMBER
		STREET CONSTRUCTION COORDINATION CENTER		
Cynthia	Chono	Inspection Services Division Manager	554-6196	554-5843
Amy	Chow	Planning Manager	554-8249	554-8243
Mario	Escalona	Utility Inspector	554-5814	554-5843
Berhame	Gaime	Excavation Permit Coordinator	554-6201	554-5843
Walter	Hoo	Inspection Supervisor	554-5863	554-5843
Anthony	Lee	Utility Inspector	554-5861	554-5843
Rene	Lopez	Utility Inspector	554-5817	554-5843
Nancy	Lynch	Service Representative	554-5870	554-5843
Cora	Mingaracal	Utility Liaison	554-8270	554-8243
Joe	Norris	CULCOP Secretary	554-8274	554-8243
Robert	Sanford	Utility Inspector	554-5849	554-5843
		AUXILIARY WATER SUPPLY SYSTEM		
Patrick	Rivera	Project Manager	558-4045	558-4515
		FIRE DEPARTMENT		
Bill	Gunn	Supervisor of Engineering & Water	558-3557	647-8505
		MUNI		
Phil	Chin	Director of System Safety & Security	292-2048	292-2053
Robert	Mason	Assistant to the Director	923-6219	923-6218
Len	Olson	Chief Inspector	554-9286	554-9902
		PARKING & TRAFFIC		
James	Howard	PCO Enforcement	553-1325	553-1573
Joern	Kroll	Assistant Transportation Engineer	554-2347	554-2352
Tony	Novello	PCO Enforcement	553-7993	553-1575
Harvey	Quan	Senior Traffic Engineer	554-2319	554-2352
Stuart	Sunshine	Executive Director	554-9835	554-9814
Peter	Woo	Assistant Transportation Engineer	554-2320	554-2352
		POLICE		
Lt. Jack	Ballentine	Law Enforcement Service	553-9764	553-4946
Sgt. George	Carrington	Law Enforcement Service	553-9764	553-4946
		PUBLIC WORKS		
Scot	Burbank	Assistant Manager, Paving	558-4046	558-4519
Norman	Chan	Hydraulic Engineering Manager	554-8355	554-8308
Fernando	Cisneros	Assistant to the Director of DPW	554-6935	554-6944
Rich	Cunningham	Supt. Street & Sewer Repair	695-2101	695-2097
Don	Eng	Chief, Bureau of Construction	554-8216	554-8218
Harlan	Kelly, Jr.	City Engineer	558-4522	558-5950
Frank	Lee	Public Affairs Officer	437-7018	554-8218
Barbara	Moy	Chief, Street Use & Mapping	554-5801	554-5843
Don	Munakata	Chief, Engineering	558-4517	558-4519
Morris	Olson	Assistant Superintendent, Street & Sewer Repair	695-2086	697-2097
Joe	Ovadia	Project Manager, Paving	558-4004	558-4519

Street Construction Coordination Center Contact People List *3/5/99*

TO REPORT A PROBLEM: Call (415) 554-SCCC

NAME			PHONE NUMBER	FAX NUMBER
		STREET CONSTRUCTION COORDINATION CENTER		
Cynthia	Chono	Inspection Services Division Manager	554-6196	554-5843
Amy	Chow	Planning Manager	554-8249	554-8243
Mario	Escalona	Utility Inspector	554-5814	554-5843
Berhame	Gaime	Excavation Permit Coordinator	554-6201	554-5843
Walter	Hoo	Inspection Supervisor	554-5863	554-5843
Anthony	Lee	Utility Inspector	554-5861	554-5843
Rene	Lopez	Utility Inspector	554-5817	554-5843
Nancy	Lynch	Service Representative	554-5870	554-5843
Cora	Mingaracal	Utility Liaison	554-8270	554-8243
Joe	Norris	CULCOP Secretary	554-8274	554-8243
Robert	Sanford	Utility Inspector	554-5849	554-5843
		AUXILIARY WATER SUPPLY SYSTEM		
Patrick	Rivera	Project Manager	558-4045	558-4515
		FIRE DEPARTMENT		
Bill	Gunn	Supervisor of Engineering & Water	558-3557	647-8505
		MUNI		
Phil	Chin	Director of System Safety & Security	292-2048	292-2053
Robert	Mason	Assistant to the Director	923-6219	923-6218
Len	Olson	Chief Inspector	554-9286	554-9902
		PARKING & TRAFFIC		
James	Howard	PCO Enforcement	553-1325	553-1573
Joern	Kroll	Assistant Transportation Engineer	554-2347	554-2352
Tony	Novello	PCO Enforcement	553-7993	553-1575
Harvey	Quan	Senior Traffic Engineer	554-2319	554-2352
Stuart	Sunshine	Executive Director	554-9835	554-9814
Peter	Woo	Assistant Transportation Engineer	554-2320	554-2352
		POLICE		
Lt. Jack	Ballentine	Law Enforcement Service	553-9764	553-4946
Sgt. George	Carrington	Law Enforcement Service	553-9764	553-4946
		PUBLIC WORKS		
Scot	Burbank	Assistant Manager, Paving	558-4046	558-4519
Norman	Chan	Hydraulic Engineering Manager	554-8355	554-8308
Fernando	Cisneros	Assistant to the Director of DPW	554-6935	554-6944
Rich	Cunningham	Supt. Street & Sewer Repair	695-2101	695-2097
Don	Eng	Chief, Bureau of Construction	554-8216	554-8218
Harlan	Kelly, Jr.	City Engineer	558-4522	558-5950
Frank	Lee	Public Affairs Officer	437-7018	554-8218
Barbara	Moy	Chief, Street Use & Mapping	554-5801	554-5843
Don	Munakata	Chief, Engineering	558-4517	558-4519
Morris	Olson	Assistant Superintendent, Street & Sewer Repair	695-2086	697-2097
Joe	Ovadia	Project Manager, Paving	558-4004	558-4519

SAN FRANCISCO
DPT
DEPARTMENT OF PARKING & TRAFFIC
Traffic Engineering Division
City and County of San Francisco

WILLIE LEWIS BROWN, JR., MAYOR
STUART R. SUNSHINE, EXECUTIVE DIRECTOR

FAX DISTRIBUTION LIST FOR UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS CALENDAR

JOHN BANNER, CITY TOW
JOHN BUSHER, DPW, BUREAU OF ENVIRONMENTAL SERVICES
AMY CHOW, DPW, PROJECT DEVELOPMENT SECTION
ADRIENNE FRAZIER, DPT, OPERATIONS
PETE HOWES, SFFD, EMS
WALTER HOO, DPW/BSM
CAPTAIN LI, SFFD, BUREAU OF FIRE PREVENTION AND INSPECTION
RICHARD SKAFF, DPW, DISABILITY ACCESS COORDINATOR
ANNA WONG, DPW, PUBLIC RELATIONS
ALISON HOOD, GGNRA, SPECIAL EVENTS OFFICE
MARIA TRAPALIS-BAIRD, MAYOR'S OFFICE OF RECYCLING
VIRGINIA RICHARDSON, PARK & REC
LEO PIERINI, STATE PAROLE DIVISION
JEFF BAUER, PORT OF SAN FRANCISCO
LT. JACK BALLENTINE, SFPD, FILM COORDINATOR
BILL WEBB, DPW, BCM
MARY ELLEN O'BRIEN, PRESS OFFICER, DPT
SHEILAH TUCKER, TRAVINFO
LAMONT DEBARBIE, FLYING DUTCHMAN

This list is a summary of the various street closures for special events which have been approved by the Interdepartmental Staff Committee on Traffic and Transportation (ISCOTT). I have also included other events which may impact traffic on City streets when I know of them. If you would like more details about any of the events, please give me a call at 415-554-2341. This list may not include events which have been permitted by the Port of San Francisco, Golden Gate National Recreational Area, or the Recreation & Park Department. If you know of other events which should be listed, please let me know. I have added a Temporary Street Closures for Special Events database on DPT's web page. Closures may be searched by date, event name and street name. You may find more detailed information about the events through this database. Our web site address is www.ci.sf.ca.us/dpt.

Cindy Shamban
Management Assistant

c:\myfiles\faxdscit.199

1999 UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS Query

Event Name	Start Date	End Date	Type	Location	Status
Bench Dedication	3/27/99	3/27/99	Block	Sanchez: 21st to Hill	3/11/99
Houlihan's to Houlihan's	3/28/99	3/28/99	Athletic	Marine Blvd (1 n/b lane only), etc	9/24/98
Sisters of P.I. Birthday Bas	4/4/99	4/4/99	Celebrat	Castro: Mkt to 18th	3/1/99, B of Supes
Union Street Easter Parade	4/4/99	4/4/99	Parade	Union: Franklin to Fillmore	Permit issued by
Union Street Easter Celebra	4/4/99	4/4/99	Fair	Union: Gough to Fillmore; Webster: Green to Filbert	2/11/99
Parking for Easter Services	4/4/99	4/4/99	Private	Anza: 9th to 10th Avenues	2/11/99
Metallica Walk of Fame Ind	4/7/99	4/7/99		Grove: Larkin to Polk	
Annual Health Fair	4/10/99	4/10/99	Block	Shotwell: 16th to 17th	3/25/99
CCAC Grand Opening	4/15/99	4/16/99	private	8th St: Irwin to Hooper	2/25/99
CCAC Grand Opening	4/16/99	4/17/99	private	8th St: Irwin to Hooper	2/25/99
SF YMCA Community Cup	4/17/99	4/17/99	Athletic	Steuart: west side parking & traffic lane only	2/25/99
YMCA Community Cup Eve	4/17/99	4/17/99	Athletic	Steuart (west side parking lane and 1 lane of traffic only	2/25/99
Cherry Blossom Festival	4/17/99	4/18/99	Fair	Pos:Lag to Flm; Web: Gea to Sut	3/26/99
SF Inter. Triathlon	4/18/99	4/18/99	Athletic	Various (NW portion of SF)	canceled
SF Inter. Film Fest.	4/19/99	5/9/99	Film	Post: Flm to Web. 3 parking meters only	3/11/99
SF Inter. Film Fest.	4/22/99	4/28/99	Film	Castro: 17th to 18th Sts., 2 parking meters only	3/11/99
Cherry Blossom Festival	4/24/99	4/25/99	Fair	Pos:Lag to Flm;	3/25/99
Cherry Blossom Parade	4/25/99	4/25/99	Parade	Civic Center to Polk to Post	permitted by PD

Event Name	Start Date	End Date	Type	Location	Status
California Mile	4/25/99	4/26/99		Mason: Ca to Sac	12/17/98
Neighborhood Block Party	4/25/99	4/25/99	Block	Filbert: Divisadero to Broderick	3/11/99
Cameron Carnival	5/1/99	5/1/99	Fair	Joice. Sacramento to Clay	2/25/99
Neighborhood Block Party	5/1/99	5/1/99	Block	Brentwood: Hazelwood to Valdez	3/25/99
Southern Exposure Fund R	5/1/99	5/2/99	Block	Alabama: 17th and Mariposa	
SF Inter. Film Fest.	5/6/99	5/6/99	Film	Castro: 17th to 18th Sts., 2 parking meters only	3/11/99
Asian Art Museum Ground	5/8/99	5/8/99	Civic	Fulton: Larkin to Hyde	2/25/99
School May Fair	5/8/99	5/8/99	Block	North Point: Scott to Divisadero	3/25/99
First Baptist Church Block	5/8/99	5/8/99	Block	Waller: Octavia to Laguna	3/25/99
Mission Library Gran Reope	5/8/99	5/8/99	Block	Bartlett: 24th to 25th	3/25/99
Neighborhood Block Party	5/15/99	5/15/99	Block	Mars: 17th to Corbett	3/11/99
AIDS Candlelight Vigil & Ma	5/16/99	5/16/99	Parade	Mkt & Castro to Market to City Hall	permit by PD
Bay to Breakers	5/16/99	5/16/99	Athletic	Various Locations	1/28/99
Young President's Organiza	5/21/99	5/21/99	Shuttle	Stockton(parking lanes): Pine to CA; Parking lane closu	3/25/99
Young President's Organiza	5/22/99	5/22/99	Shuttle	Stockton(parking lanes): Pine to CA; Parking lane closu	3/25/99
Neighborhood Block Party	5/22/99	5/22/99	Block	Ulloa: Sydney Way to Laguna Honda Blvd.	3/11/99
KFOG Kaboom	5/22/99	5/22/99	Celebrat	Embarcadero: Harrison to Townsend	
Young President's Organiza	5/23/99	5/23/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/24/99	5/24/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/25/99	5/25/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99

Event Name	Start Date	End Date	Type	Location	Status
Young President's Organiza	5/26/99	5/26/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/27/99	5/27/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/28/99	5/28/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Carnaval	5/29/99	5/30/99	Fair	Har: 16th to 22nd, etc	2/25/99
Carnaval Parade	5/30/99	5/30/99	Parade	24th: Bry to Mis; Mission: 24th to 14th; 14th: Mis to Har	permitted by PD
Black & White Ball	6/3/99	6/7/99	civic	Fulton: Larkin to Hyde	2/25/99
Black & White Ball	6/3/99	6/3/99	Civic	Various Parking Lanes in Civic Center area	2/25/99
Black & White Ball	6/4/99	6/4/99	civic	Various Parking Lanes in Civic Center Area	2/25/99
Cyberbuss	6/5/99	6/6/99	Block	Griffith: Revere to Quesada	
Union Street Arts Festival	6/5/99	6/6/99	Fair	Union: Gou to Stn, etc	12/17/98
Escape From Alcatraz	6/5/99	6/5/99	Athletic	Marina Blvd (1 lane only): Scott to Lyon	7/23/98
Escape From Alcatraz	6/5/99	6/5/99	Athletic	NW portion of SF, Various Locations	7/23/98
Black & White Ball	6/5/99	6/6/99	civic	Various Streets in Civic Center Area	2/25/99
Black & White Ball	6/5/99	6/6/99	civic	Grove: Van Ness to Franklin	2/25/99
SPCA Animal WingDing	6/5/99	6/6/99	Fair	Alabama:15 to 16; Florida:16 to Tre; Treat:Har to 15th	12/17/98
PBS Broadcasting Display	6/5/99	6/9/99	Display	Ellis (most most northerly parking lane & traffic lane onl	
SPCA Animal WingDing	6/6/99	6/6/99	Fair	Alabama:16 to 17; Florida:16 to 17	12/17/98
CA Aids Ride	6/6/99	6/6/99	Athletic	Various, no street closures involved	No permit required
North Beach Festival	6/12/99	6/13/99	Fair	Grant:Col to Fil;Green: Col to Gra; Vallejo:Col to Gra	2/11/99
Haight Street Fair	6/13/99	6/13/99	Fair	Haight:Masonic to Stanyan, etc	11/13/98

Event Name	Start Date	End Date	Type	Location	Status
Gay & Lesbian Film Festivi	6/15/99	6/28/99	Festival	Eureka Valley Lot #1 behind the Castro Theater	
Extreme Games	6/23/99	7/3/99	Athletic	Pier 30-32	permit by Port
NASCAR Rally	6/24/99	6/24/99		Leavenworth: Chestnut to Greenwich; Lombard: Hyde t	Disapproved
Gay Pride Celebration	6/25/99	6/28/99	Fair	Civic Center Area	1/28/99
Pink Saturday	6/26/99	6/27/99	Civic	Castro: 19th to Mkt; 18th: Cwd to Hfd	
Gay Pride Parade	6/27/99	6/27/99	Parade	Market: 2nd to Civic Center	permit by PD
Tall Ships	7/2/99	7/5/99		Wharf Area	
Jazz & All That Art on Fillm	7/3/99	7/4/99	Fair	Fillmore: Geary to McAllister etc.	Hold
Fillmore Street Jazz Festiva	7/3/99	7/4/99	Fair	Fillmore: Jackson to Post, etc	2/11/99
Chronicle's 4th of July	7/3/99	7/5/99	Fair	Jefferson: Hyde to Terminus	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Van Ness: North Pt. To Muni Pier	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Embarcadero: Pow to Tay	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Jefferson: Hyde to Taylor	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	N/B Embarcadero: Bwd to Bay	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Wharf Area	12/17/98
SF Chronicle Marathon	7/11/99	7/11/99	Athletic	Various City Wide	2/25/99
Third Street Fair	7/17/99	7/18/99	Fair	3rd St.:Cargo to Evans	1/14/99
Blues & Art on the Bay	9/4/99	9/6/99	Fair	Treasure Island	permit by T. Island
Opera Gala	9/11/99	9/11/99	Civic		
Fest. Of Culinary Arts	9/11/99	9/12/99	Fair	Polk: Eddy to MCA; Turk: Van to Lar	

Event Name	Start Date	End Date	Type	Location	Status
Chinatown Moon Festival	9/17/99	9/19/99	Fair	Grant: Cal to Pac	
Alcatraz Triathlon XIX	9/18/99	9/18/99	Athletic	Marina Blvd (1 lane only): Lag to Buc	10/22/98
Annual March of Witness	9/26/99	9/26/99	March	Powell: Broadway to Vallejo	3/25/99
Bridge to Bridge	10/3/99	10/3/99	Athletic	Various: Ferry Bldg to Presidio	1/28/99
Page Street Fair	10/9/99	10/9/99	Fair	Page: Franklin to Gough	3/25/99
Page Street Fair	10/10/99	10/10/99	Fair	Page: Franklin to Gough	3/25/99
West Portal Fair	10/23/99	10/24/99	Fair	West Portal: Ulloa to 15th Sts.	
Champion Run for Children	10/24/99	10/24/99	Athletic	Various Lane Closures	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	McAllister: Polk to Larkin	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Sanchez: Duboce to Market	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Dr. Carleton Goodlett Place	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Larkin: McA to Gro; Hyde: McA to Grove; Grove: Hyd to	3/11/99
Run to the Far Side XV	11/28/99	11/28/99	Athletic	Oak: Stanyan to Broderick; Fell: Stanyan to Broderick,	3/11/99
Corporate Event	12/3/99	12/4/99	Corporat	Fern: Van Ness to Polk	

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, Architect, AIA, Director

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

UNDERGROUND PLANNING MEETING

MEETING DATE: March 2, 1999
PRESENT:

Tom Trimbur	-DPW/BSM	(554-6167)	Patty Healy	-PG&E	(695-3394)
Louis Victorio	-TCI	(863-8500)	Cindy Vowell	-PacBell	(542-9095)
Carlos DeAnda	-PG&E	(330-2138)	John Fadeff	DPW/BSM	(554-5830)

DISCUSSION:

A. PROJECT STATUS

1. UGD 318 - DOLORES HEIGHTS DISTRICT

PHASE 2 – PG&E needs to pull permit for work since previous permit expired. Ms. Healy to contact permitting to set up a meeting. Construction to begin in May.

2. UGD 310 - PRESIDIO HEIGHTS

PHASE 2 – PG&E needs street light tags. PG&E delivered streetlight submittal information from their contractor. PacBell to begin placing cable at the end of this month with completion of cutovers to take approximately six months. Pole out expected by end of year.

California St. – Project out to bid. RCN included in the joint trench.

3. UGD 320 - BREWSTER/JOY

Mr. Trimbur contacted the head of Electrical Inspection about the expired orange tag at 122 Brewster. Electrical inspection for green tag of underground service scheduled for Wednesday. PacBell needs Caltrans permit to service the phone line to the pedestrian bridge over the freeway; paperwork submitted about a month ago.

4. UGD 321 - INDIANA STREET/ISLAIS CREEK & UGD 323 - CESAR CHAVEZ

1601 Indiana work completed; PG&E to cut over this week. The City to contact CALTRAIN/Joint Powers Board regarding approvals for receiving utilities underground. Overhead facilities removed from over freeway. PG&E reported that the boxes along Chavez may need to be adjusted by more than 3 inches. When curbs are poured, utilities will know how much adjustment is required; if more than 3 inches, adjustment will take some time. PG&E is reviewing grading information provided by City. There is also a billboard which has overhead service and a communications line crossing Chavez which may be a City emergency line (PacBell says it's not theirs).

5. UGD 324 - DUBOCE AVENUE

MUNI in contact with PG&E regarding removal of their pole in front of MUNI trailer. This pole has light which and PG&E is waiting for Hetch Hetchy request to remove. Given the receipt of that request, PG&E will remove their facilities in sufficient time as to not be a problem for MUNI construction. Removal of another pole with light will need to wait until new streetlights are in place. Results from PG&E tests on water finding its way into their facilities have not been reported.

6. UGD 311 - CORBETT AVENUE - PEMBERTON STAIRWAY

Project is still on hold.

7. UGD 335 - UPPER FOLSOM

PG&E work continuing; should be finished by mid-April. PG&E reported that property conversions have moving along and they are seeing new contractors doing the work. This should help competition.

8. UGD 322 - Alpine Terrace/Museum Way

Community meeting to discuss construction and owner responsibilities held on 18th of February. Meeting went well and City close to choosing streetlight type.

9. UGD 327 - INNER SUNSET

Community meeting to discuss construction and owner responsibilities held on 24th of February. Meeting went well and City close to choosing streetlight type. Ms. Healy distributed a schedule.

10. UGD 338 - Ocean Avenue

Community meeting to discuss construction phasing held on 17th of February. A community member presented proposal for widening sidewalks at intersections. Mayor's office has indicated that City staff should investigate proposal. This may delay project by 4 to 6 months. Utilities indicated that some of their facilities in the street such as manholes may be affected. Mr. Trimbur to transmit this caution to City staff investigating the proposal.

11. UGD 339 – Bernal South Slope (Banks/Chapman)

Mr. Trimbur indicated that Mr. Burbank requested that Ms. Healy re-examine schedule per his e-mail.

B. OTHER BUSINESS

1. Mr. Trimbur noted that the information on PG&E specifications that Mr. DeAnda had provided at the Inner Sunset community meeting seemed very popular. Often the affected owners are looking for just these specs. He suggested that all the utilities provide something and that perhaps we could re-examine the information that Palo Alto sent and we could develop a similar package.

THE NEXT MEETING WILL BE HELD ON TUESDAY, 6 APRIL 1999, AT 9:00 A.M. AT 875 STEVENSON STREET, ROOM 460, BSM CONFERENCE ROOM.

cc: All Attendees
CULCOP - through Joe Norris
Kris Kilgore - BSM
Hin Lok Kung - BOE
Jack Donohoe - DTIS
Barbara Moy - BSM
Manfred Wong - CWP
Lynn Bunim - PacTel
Norman Chan - BOE
Dee Lemmon - BLHP
Lesley Wong - BOE/S&H
Patricia Healy - PG&E
Naoki Kaku - BOE S&H
José Saldaña – PG&E
Amy Chow - PDS
Charles Yu - BOE/S&H
Amy Powell- DHIC
Brian Christiansen - Duboce
Carlos DeAnda - PG&E
Lynn Nakasato - BOE/S&H
Cynthia Chono - BSM
Ray Yamagishi - BLHP
Tom Flahavan - DET
Joe Ovadia - PMD
Kathy Devine - PG&E
Louis Victorio – TCI
Scot Burbank - BOE/PMD
Sieg Weber - RCN
John Katz - MUNI
Sam Lauter - PG&E
Carol Finucane - BOE
Don Stroh - DHIC
Brian Gatter - BOE/Landscape
Terry Bouey - TCI
Dave Bradley - PG&E
Joe Marino - DHIC
Terry Elisaia - DET
Naoki Kaku - BOE
Richard Hong - PG&E
Ben Cruz – BOE
John Giusti – DHIC

C:\My Documents\MEET39~1.DOC

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

UTILITY COORDINATION REPORT

for March 1, 1999 to March 31, 1999

Notice of Intent and Request for Information Issued (NOI):	**Date**
1765N - Kearny/Vallejo to Green Streets AWSS Replacement	3/3/99
1978N - Upgrade Pressure Reducing Stations, Various Locations	3/4/99
1785N - Taber Place/Gough Street Sewer Replacement	3/11/99
1784N - Leavenworth Street Sewer Replacement	3/24/99
1791N - 3rd Street Sewer System Improvement Phase III	3/29/99

Final Preliminary Plans Issued (LOT):	
1362N - Various Locations SOMA Street District Track Removal and Resurfacing	3/8/99
1727N - Broadway/Leavenworth/Taylor Pavement Renovation	3/8/99
1765N - Kearny/Vallejo to Green Streets AWSS Replacement	3/9/99
1034N - Chinatown Alleyway Improvements Phase I Commercial, Cordelia and Ross	3/11/99
1734N - Franklin/Greenwich and Union Streets Pavement Renovation	3/23/99

State of California:

Other:

"IMPROVING THE QUALITY OFLIFE IN SAN FRANCISCO" We are dedicted individuals committed to teamwork, custormer service and continuous improvement in partnership with the community

Customer Service *Teamwork* *Continuous Improvement*

S:\PD\UTILITYL\RPTS\CULCOP\UT0399.doc

Projects in Progress (NOI)

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
---N	Greg Cruz	554-8268	Various Locations, Construction of Curb Ramps - STPL-5934(030)	Pav	09/04/1997
1048N	Gene Handa	554-8341	Sunnydale Sewer Improvements	SW	07/03/1996
1076N	Arlen Ung	554-8263	West End Utilities	Pav	08/11/1997
1100N	Martha Ketterer	554-8296	Ecker Street, Mission Street to Elim Alley	Pav	01/08/1996
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements Locations #306 & 309	UG	02/15/1998
1145N	Naoki Kaku	554-8246	Bernal Heights Street Improvement, Banks/Chapman Area	Pav	12/02/1996
1202N	Linda Leong	648-6882	North Point Plant Improvement, Phase II	Pav	01/30/1996
1218N	Cliff Wong	554-8339	Market , Larkin and Harrison Streets Sewer Replacement	SW	03/29/1996
1243N	Ronald Cheng	558-4049	Marina Seawall and Roadway Improvement	Pav	04/12/1996
1277N(1)	Laarni Camerino	554-8256	Var Loc: As Needed Paving - McAllister, Polk, Grove & Van Ness Avenue	Pav	08/17/1998
1277N(2)	Pak Choi	554-8283	Various Locations: As Needed Paving - Stockton (Post to Market Street)	Pav	08/17/1998
1277N(3)	Greg Cruz	554-8268	Var Loc - As Needed Pav: Lake Merced from Skyline Blvd. To John Muir Drive	PAV	09/28/1998
1285N	Brian Gatter	554-8292	Pioneer Park Renovation – Telegraph Hill Stairways	Pav	11/14/1997
1294N	Leon Louie	558-4070	Fourth Street Bridge Fender Repair Project	Str	12/18/1996
1330N	Wallis Lee	554-8344	2nd / 9th Streets Sewer Abandonment Project	SW	06/27/1997
1349N	Saed Toloui	558-4084	12th Avenue/Quintara Street, Stairway Construction	Str	02/07/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	12/02/1996
1381N	Patrick Riviera	558-4045	Martin Luther King Utilities	Pav	09/12/1997
1385N	Laarni Camerino	554-8256	Various Locations: Concrete Street Reconstruction - Stillings Ave from Teresita to Congo	PAV	07/10/1998
1389N	Pak Choi	554-8283	Mission Street Pavement Renovation	Pav	06/13/1997
1395N	Cliff Wong	554-8339	Sacramento/ Larkin/ Pine Streets Sewer Replacement	SW	04/10/1998
1407N	Narciso Paderanga Jr.	554-8258	California Street Pavement Renovation, STP-17	Pav	02/13/1997
1415N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	Str	07/31/1997
1421N	Clifford Wong	554-8339	Green Street Sewer Replacement - Columbus Avenue to Powell Street	SW	01/17/1997
1423N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	SR	07/31/1997
1432N	Gene Handa	554-8341	Post Street Sewer Replacement	SW	02/07/1997
1459N	Narciso Paderanga, Jr.	554-8258	Fillmore Street Pavement Renovation and Muni Underground Ductbank System	Pav	08/29/1997
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	11/10/1997
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SR	09/30/1997
1549N	Thomas Won	554-8275	Ocean/Victoria/Everglade Sewer Replacement	SW	09/23/1997
1573N	Wallis Lee	554-8344	5th Street & Harrison Sewer Replacement	SW	02/17/1998
1583N	Thomas Won	554-8275	Everglade/ Victoria/ Revere/ Bridge View Sewer Replacement	SW	03/23/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	04/13/1998
1587N	Jean To	554-8298	7th Avenue and Kirkham Street Sewer Replacement	SW	12/11/1998
1588N	Thomas Won	554-8275	Joost Ave/Alemany Blvd/Mt. Vernon Ave/Kensington Way Sewer Replacement	SW	12/22/1998
1590N	Thomas Won	554-8275	Ocean Avenue Sewer Replacement (Joint Venture with MUNI)	SW	07/13/1998
1605N	Bryan Dessaure	554-8299	Sacramento/Pierce/Wilmot Streets Sewer Replacement	SW	06/07/1998
1626N	Thomas Won	554-8275	4th/5th Ave/Stanyan St (easement) / Paris Street Sewer Replacement	SW	10/22/1998
1628N	Jean To	554-8298	Moraga Street Sewer Replacement: 17th to 18th Avenues	SW	09/16/1998
1629N	Peter Cheng	554-8348	Union/Kearny Streets Sewer Replacement	SW	10/28/1998
1630N	Birgit Chase	554-8336	Polk/Francisco/Quincy/Sacramento Streets Sewer Replacement	SW	11/09/1998
1653N	Uday Prasad	558-4061	Demolition of North Beach Garage at 763 Vallejo Street	Str	09/15/1997
1655N	Lesley Wong	554-8252	Cezar Chavez Improvements Phase 2		07/27/1998
1667N	Lesley Wong	554-8252	Fourth Street Sidewalk Widening Project - Phase 2	Pav	03/10/1998
1668N	Ken Chu	554-8388	Golden Gate Avenue Pavement Renovation	Pav	01/02/1998
1674N	Joe Haas	558-4539	1680 Mission Street Secondary Power Source	SDV	05/27/1998
1678N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Street Reconstruction No. 15	Pav	04/13/1998
1680N	Lesley Wong	554-8252	Great Highway and Point Lobos Pavement Renovation	Pav	05/13/1998
1701N	Laarni Camerino	554-8256	Seventh Street Pavement Renovation	Pav	08/24/1998
1724N	Laarni Camerino	554-8256	Various Locations: As Needed Paving - 2nd St. between Townsend & King Streets	Pav	07/10/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	10/28/1998
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	10/05/1998
1735N	Naoki Kaku	554-8246	Various Locations: Bayview District Pavement Renovation	PAV	10/13/1998
1748N	Carol Finucane	558-4581	Mid-Market Public Improvements		10/05/1998
1755N	David Pang	554-8278	Oak Street Pavement Renovation	PAV	02/02/1999

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
1759N	Pak Choi	554-8283	Mission Street Pavement Renovation Phase 2	PAV	12/30/1998
1765N	Thinh Nguyen	558-4554	Kearny/Vallejo to Green Streets AWSS Replacement		03/22/1999
1784N	Thomas Won	554-8275	Leavenworth Street Sewer Replacement (CW-231)	PAV	04/08/1999
1785N	Peter Cheng	554-8343	Taber Place/Gough Street Sewer Replacement	SW	04/12/1999
1791N	Peter Cheng	554-8348	3rd Street Sewer System Improvement Phase III	SW	03/29/1999
1978N	Gary Fleming	558-4539	Upgrade Pressure Reducing Stations, Various Locations		04/02/1999
1984N	Naoki Kaku	554-8246	Van Ness Pedestrian Safety Improvements	PAV	03/17/1999
6618E	Leon L. Louie	558-4070	Seismic Retrofit of Third Street Bridge	Str	08/31/1997
6618N	Frank Piruzmand	558-4081	3rd Street Bridge Rehabilitation & Retrofit	Str	03/30/1998
7291E	Lynn Fong	554-8269	K-Line Rail Replacement & Ocean Avenue Improvements	Pav	11/03/1997
7381E	Fernando Cisneros	554-8278	Hunter's Point Naval Shipyard Infrastructure Backbone Phase I	Pav	11/25/1996
7416E	Deirdre Appel	558-4556	Golden Gate Park Reservoir and Pump Station		08/07/1998
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	12/22/1998
N	Linda DeBolt	554-8265	Surface Streets Improvement Project	Pav	02/06/1998

Projects in Progress (NOI)

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
---N	09/04/1997		08/07/1997	11/09/1998	10/20/1997	08/20/1997			09/04/1997
1048N	07/03/1996	Mar-99	07/11/1996	06/17/1996		07/16/1996			07/14/1996
1076N	08/11/1997	Jul-98	07/17/1997			07/23/1997	07/18/1997	07/29/1997	08/26/1997
1100N	01/08/1996	May-98		05/14/1996		12/18/1995			02/16/1996
1109K	02/15/1998		12/30/1997	04/27/1998	01/21/1998	01/09/1998	12/30/1997	01/09/1998	01/13/1998
1145N	12/02/1996	Nov-98	11/08/1996			12/03/1996			12/07/1996
1202N	01/30/1996	18-Nov-97		01/29/1996				01/16/1996	
1218N	03/29/1996	On hold	03/22/1996			03/20/1996	03/01/1996		
1243N	04/12/1996		03/29/1996				03/25/1996	03/19/1996	04/23/1996
1277N(1)	08/17/1998			07/24/1998	08/19/1998	07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(2)	08/17/1998			07/24/1998		07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(3)	09/28/1998		09/08/1998	09/10/1998	11/02/1998	09/09/1998	09/04/1998	09/23/1998	09/17/1998
1285N	11/14/1997	Jul-98	10/21/1997	04/13/1998		10/24/1997	10/16/1997	10/20/1997	11/06/1997
1294N	12/18/1996	May-98	10/25/1996	03/19/1997		10/18/1996		10/09/1996	12/07/1996
1330N	06/27/1997	Apr-98	06/16/1997	06/17/1997		06/17/1997	06/16/1997		
1349N	02/07/1997	Apr-98	01/09/1997			03/27/1997	01/10/1997	01/24/1997	02/07/1997
1374N	12/02/1996		11/08/1996	02/24/1997		12/03/1996			12/07/1996
1381N	09/12/1997		08/18/1997			08/22/1997	08/18/1997	10/29/1997	09/15/1997
1385N	07/10/1998		06/12/1998	07/10/1998		06/22/1998	06/18/1998	07/17/1998	06/23/1998
1389N	06/13/1997	May-98	05/28/1997	06/02/1997			06/05/1997	05/28/1997	06/03/1997
1395N	04/10/1998			04/27/1998	04/17/1998	06/02/1998	04/08/1998	04/13/1998	04/20/1998
1407N	02/13/1997	On hold	01/17/1997			01/21/1997	01/15/1997	01/27/1997	02/18/1997
1415N	07/31/1997	Sep-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997	07/22/1997	07/28/1997
1421N	01/17/1997	Jan-98	01/09/1997	01/06/1997		01/23/1997	01/02/1997		02/07/1997
1423N	07/31/1997	Nov-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997		07/28/1997
1432N	02/07/1997	Jun-98		02/20/1997		02/11/1997	01/23/1997		02/18/1997
1459N	08/29/1997	May-98	08/05/1997	12/22/1997	10/20/1997	08/07/1997	08/01/1997		09/05/1997
1474N	11/10/1997	Jul-98	10/21/1997	06/17/1998	10/16/1997	10/24/1997	10/16/1997		11/06/1997
1548N	09/30/1997		09/08/1997	04/13/1998	09/24/1997	09/19/1997	09/09/1997		09/30/1997
1549N	09/23/1997					09/19/1997	09/11/1997		09/30/1997
1573N	02/17/1998		01/23/1998	06/17/1998	01/23/1998	02/12/1998	01/23/1998		02/12/1998
1583N	03/23/1998		03/23/1998		03/09/1998	03/05/1998	03/09/1998	03/11/1998	03/24/1998
1585N	04/13/1998		04/29/1998	04/30/1998	04/15/1998	05/12/1998	04/09/1998	04/13/1998	04/23/1998
1587N	12/11/1998		11/09/1998	02/22/1999	11/09/1998	11/09/1998	11/02/1998		11/16/1998
1588N	12/22/1998		03/17/1999	02/22/1999		12/02/1998	12/01/1998		12/09/1998
1590N	07/13/1998			07/13/1998		06/19/1998	06/18/1998	07/16/1998	06/23/1998
1605N	06/07/1998		05/11/1998	05/15/1998	05/11/1998	05/13/1998	05/11/1998		05/20/1998
1626N	10/22/1998		10/16/1998	11/12/1998			10/06/1998		10/15/1998
1628N	09/16/1998		09/14/1998	09/10/1998	09/10/1998	09/10/1998	09/10/1998	09/15/1998	09/17/1998
1629N	10/28/1998			11/12/1998		10/02/1998	10/01/1998	10/09/1998	10/13/1998
1630N	11/09/1998			02/22/1999	11/09/1998	11/09/1998	10/16/1998	10/13/1998	10/21/1998
1653N	09/15/1997		09/02/1997	09/09/1997		09/02/1997		09/09/1997	09/10/1997
1655N	07/27/1998		07/01/1998		07/06/1998		06/29/1998		07/20/1998
1667N	03/10/1998		02/20/1998		02/20/1998		02/20/1998	03/13/1998	03/05/1998
1668N	01/02/1998	Sep-98	12/04/1997	04/27/1998	12/12/1997	01/13/1998	12/03/1997	12/04/1997	12/16/1997
1674N	05/27/1998		05/15/1998		05/26/1998	05/22/1998	05/19/1998	06/02/1998	06/09/1998
1678N	04/13/1998								
1680N	05/13/1998		04/27/1998	06/02/1998	05/11/1998	05/26/1998		04/22/1998	05/06/1998
1701N	08/24/1998		07/29/1998	09/02/1998		08/04/1998	07/24/1998	10/15/1998	08/13/1998
1724N	07/10/1998		06/22/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	06/22/1998	06/23/1998
1727N	10/28/1998		10/02/1998	11/06/1998		10/02/1998	10/01/1998	09/30/1998	10/13/1998
1732N	10/05/1998		09/14/1998	11/06/1998	11/02/1998	09/22/1998	09/11/1998	10/15/1998	09/25/1998
1735N	10/13/1998		09/14/1998	11/06/1998		09/22/1998	09/15/1998	09/25/1998	09/25/1998
1748N	10/05/1998		09/14/1998	11/06/1998		09/22/1998	09/14/1998	10/13/1998	09/25/1998
1755N	02/02/1999			02/22/1999		01/08/1999		01/14/1999	02/05/1999

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1759N	12/30/1998		11/23/1998		12/27/1998	12/10/1998			12/09/1998
1765N	03/22/1999		03/12/1999	03/17/1999		03/23/1999	03/10/1999	03/11/1999	
1784N	04/08/1999		03/29/1999						
1785N	04/12/1999					03/23/1999		03/22/1999	
1791N	03/29/1999								
1978N	04/02/1999		03/12/1999			03/12/1999	03/12/1999	03/11/1999	
1984N	03/17/1999		02/08/1999			02/18/1999	02/03/1999	02/12/1999	02/05/1999
6618E	08/31/1997	Dec-98	07/16/1997		07/15/1997	07/18/1997	07/24/1997	07/28/1997	08/26/1997
6618N	03/30/1998		03/25/1998	03/23/1998		03/23/1998	03/24/1998	03/17/1998	03/30/1998
7291E	11/03/1997		10/21/1997	06/02/1998		10/24/1997	10/08/1997	10/09/1997	10/14/1997
7381E	11/25/1996		10/31/1996			11/13/1996	11/01/1996	10/30/1996	12/07/1996
7416E	08/07/1998		07/17/1998	07/10/1998		06/30/1998	07/13/1998	07/09/1998	07/29/1998
7458E	12/22/1998		11/25/1998	02/22/1999		12/10/1998	12/01/1998		12/10/1998
N	02/06/1998		01/08/1998		01/23/1998	05/13/1998	01/08/1998	03/09/1998	01/26/1998

Projects in Progress (NOI)

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
—N	09/04/1997	08/26/1997	11/24/1998		08/19/1997		09/30/1997	09/30/1997
1048N	07/03/1996	06/18/1996	06/25/1996	07/16/1996	07/01/1996	06/21/1996		
1076N	08/11/1997	07/28/1997			08/04/1997	07/28/1997	07/28/1997	07/28/1997
1100N	01/08/1996	12/11/1995	12/21/1995	12/11/1995	12/28/1995	12/08/1995		
1109K	02/15/1998		01/14/1998		01/15/1998		01/27/1998	01/27/1998
1145N	12/02/1996	12/07/1996	12/02/1996		11/25/1996	12/03/1996	12/03/1996	12/03/1996
1202N	01/30/1996			01/18/1996	02/02/1996	01/18/1996		
1218N	03/29/1996	03/14/1996		03/14/1996	03/18/1996	03/18/1996		
1243N	04/12/1996	03/27/1996		04/15/1996	03/25/1996	04/02/1996		
1277N(1)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998			
1277N(2)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998	07/31/1998	08/13/1998	08/13/1998
1277N(3)	09/28/1998	09/09/1998	09/04/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1285N	11/14/1997	11/07/1997		02/11/1998	10/24/1997	10/17/1997	11/25/1997	11/25/1997
1294N	12/18/1996	10/24/1996		11/07/1996	10/28/1996	11/19/1996		
1330N	06/27/1997	07/01/1997		07/09/1997	06/27/1997	06/12/1997	07/10/1997	07/10/1997
1349N	02/07/1997	01/17/1997	01/22/1997	03/17/1997		01/13/1997	02/05/1997	02/05/1997
1374N	12/02/1996	11/07/1996			11/25/1996	11/07/1996	12/02/1996	12/02/1996
1381N	09/12/1997	08/26/1997			08/21/1997			09/24/1997
1385N	07/10/1998	06/15/1998	06/23/1998		06/25/1998	10/08/1998	07/29/1998	07/29/1998
1389N	06/13/1997	05/29/1997			05/23/1997	06/11/1997	05/23/1997	05/23/1997
1395N	04/10/1998	04/13/1998	01/05/1999		04/22/1998	04/13/1998		05/14/1998
1407N	02/13/1997	02/24/1997	04/17/1997	03/19/1997	01/23/1997	02/03/1997	02/05/1997	02/05/1997
1415N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1421N	01/17/1997	01/10/1997		01/29/1997	02/19/1997	12/30/1996	01/22/1997	01/22/1997
1423N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1432N	02/07/1997	02/24/1997	02/10/1997	03/18/1997	01/31/1997	01/22/1997	02/24/1997	02/24/1997
1459N	08/29/1997	08/05/1997			08/13/1997		09/24/1997	09/24/1997
1474N	11/10/1997	11/07/1997			10/23/1997	10/14/1997	11/25/1997	11/25/1997
1548N	09/30/1997	09/12/1997			09/15/1997	09/29/1997	10/09/1997	10/09/1997
1549N	09/23/1997	09/24/1997			09/17/1997	09/15/1997	10/09/1997	10/09/1997
1573N	02/17/1998	01/26/1998	03/30/1998			01/22/1998		02/12/1998
1583N	03/23/1998	03/11/1998	03/30/1998		03/18/1998	03/09/1998	03/17/1998	
1585N	04/13/1998	04/13/1998			04/30/1998	04/13/1998	06/25/1998	06/25/1998
1587N	12/11/1998	11/13/1998		12/18/1998	11/13/1998			01/12/1999
1588N	12/22/1998	12/01/1998			12/02/1998			01/12/1999
1590N	07/13/1998	06/17/1998	08/04/1998		06/29/1998	10/08/1998	07/29/1998	07/29/1998
1605N	06/07/1998	05/12/1998				05/15/1998	06/25/1998	06/25/1998
1626N	10/22/1998	10/06/1998		11/09/1998	10/13/1998			01/12/1999
1628N	09/16/1998	09/10/1998	09/08/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1629N	10/28/1998	10/06/1998		11/09/1998	10/08/1998		11/12/1998	11/12/1998
1630N	11/09/1998	10/15/1998			10/20/1998			01/12/1999
1653N	09/15/1997	09/12/1997			09/08/1997	09/04/1997	09/24/1997	09/24/1997
1655N	07/27/1998	07/01/1998			07/02/1998	07/01/1998	07/29/1998	07/29/1998
1667N	03/10/1998	02/20/1998			02/27/1998			
1668N	01/02/1998	12/04/1997			12/12/1997		01/27/1998	01/27/1998
1674N	05/27/1998	05/18/1998	05/19/1998		06/02/1998	05/14/1998	07/09/1998	07/09/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998	05/13/1998		04/30/1998		06/25/1998	06/25/1998
1701N	08/24/1998	07/24/1998	08/24/1998	11/09/1998			08/13/1998	08/13/1998
1724N	07/10/1998	06/15/1998	06/23/1998		06/23/1998	10/08/1998	07/09/1998	07/09/1998
1727N	10/28/1998	10/02/1998		11/09/1998	10/13/1998			01/12/1999
1732N	10/05/1998	09/17/1998		11/09/1998	09/28/1998	09/11/1998		11/12/1998
1735N	10/13/1998	09/18/1998		11/09/1998	09/18/1998	09/09/1998		11/12/1998
1748N	10/05/1998	09/18/1998		11/09/1998	09/24/1998	09/11/1998		11/12/1998
1755N	02/02/1999	01/05/1999			12/30/1998			

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1759N	12/30/1998	12/01/1998	11/23/1998		12/14/1998			12/01/1998
1765N	03/22/1999		03/17/1999		03/16/1999			
1784N	04/08/1999	03/30/1999	03/31/1999					
1785N	04/12/1999	03/16/1999	03/26/1999		03/29/1999			
1791N	03/29/1999							
1978N	04/02/1999	03/16/1999	03/17/1999		03/16/1999			
1984N	03/17/1999	02/08/1999			02/09/1999			
6618E	08/31/1997	07/16/1997		07/30/1997	07/24/1997	07/28/1997	08/21/1997	08/21/1997
6618N	03/30/1998	03/25/1998			04/01/1998		05/14/1998	
7291E	11/03/1997	10/29/1997			10/20/1997		11/10/1997	11/10/1997
7381E	11/25/1996	11/06/1996	11/05/1996	11/14/1996	11/08/1996	12/18/1996	12/02/1996	12/02/1996
7416E	08/07/1998	07/13/1998		11/09/1998	07/20/1998	07/01/1998		07/29/1998
7458E	12/22/1998	11/25/1998	12/14/1998		12/15/1998			12/01/1998
N	02/06/1998	06/22/1998			01/26/1998	10/08/1998		02/12/1998

Projects in Progress (NOI)

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
---N	09/04/1997	08/12/1997		08/08/1997	08/13/1997	08/08/1997	08/08/1997	08/26/1997
1048N	07/03/1996		06/26/1996	07/01/1996		06/25/1996	07/03/1996	07/01/1996
1076N	08/11/1997	07/24/1997		07/24/1997	07/29/1997	08/08/1997	07/22/1997	08/15/1997
1100N	01/08/1996		12/20/1995	01/03/1996	12/14/1995	12/18/1995	12/27/1995	12/20/1995
1109K	02/15/1998	01/07/1998		01/14/1998	01/14/1998	05/20/1998	01/21/1998	01/21/1998
1145N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1202N	01/30/1996		01/16/1996	01/19/1996	01/31/1996	01/17/1996		02/06/1996
1218N	03/29/1996				03/12/1996	03/05/1996	03/27/1996	03/07/1996
1243N	04/12/1996		03/25/1996		03/27/1996	03/22/1996	03/27/1996	03/21/1996
1277N(1)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(2)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(3)	09/28/1998	09/03/1998		09/15/1998	09/17/1998		01/11/1999	09/17/1998
1285N	11/14/1997	10/20/1997	10/28/1997	10/27/1997	10/23/1997	11/18/1997	11/10/1997	11/13/1997
1294N	12/18/1996		10/25/1996	10/25/1996	10/31/1996		12/02/1996	10/24/1996
1330N	06/27/1997	06/16/1997	07/02/1997	06/23/1997	06/23/1997	07/11/1997	08/08/1997	07/02/1997
1349N	02/07/1997	01/13/1997	01/13/1997	01/21/1997	02/12/1997	02/27/1997		01/22/1997
1374N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1381N	09/12/1997	08/15/1997		08/22/1997	08/22/1997	11/18/1997		08/26/1997
1385N	07/10/1998	06/15/1998		06/23/1998	06/19/1998			06/29/1998
1389N	06/13/1997	05/19/1997	05/29/1997	05/21/1997	05/23/1997	05/29/1997	06/26/1997	06/06/1997
1395N	04/10/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1407N	02/13/1997	01/17/1997	01/15/1997	01/24/1997	02/12/1997	02/27/1997	02/24/1997	01/22/1997
1415N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1421N	01/17/1997	01/07/1997	01/06/1997		02/18/1997	02/27/1997		01/22/1997
1423N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1432N	02/07/1997	01/27/1997	01/27/1997	01/29/1997	02/12/1997	02/27/1997		01/30/1997
1459N	08/29/1997	08/05/1997		08/06/1997	08/12/1997	08/08/1997	11/10/1997	08/26/1997
1474N	11/10/1997	10/20/1997		10/21/1997	10/22/1997	11/18/1997	11/10/1997	11/13/1997
1548N	09/30/1997	09/19/1997		09/12/1997	09/12/1997	09/24/1997	09/11/1997	09/22/1997
1549N	09/23/1997	09/12/1997		09/18/1997	09/16/1997	09/24/1997	09/19/1997	09/22/1997
1573N	02/17/1998	01/26/1998		02/12/1998	02/12/1998			02/20/1998
1583N	03/23/1998		03/20/1998	03/24/1998	03/17/1998		04/08/1998	03/03/1998
1585N	04/13/1998	04/13/1998	04/28/1998	04/20/1998	04/28/1998	05/20/1998		04/28/1998
1587N	12/11/1998		11/12/1998	11/23/1998	11/19/1998			11/19/1998
1588N	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
1590N	07/13/1998	06/15/1998		07/08/1998	06/19/1998		01/11/1999	07/07/1998
1605N	06/07/1998	05/13/1998		05/19/1998	05/20/1998	05/20/1998		06/02/1998
1626N	10/22/1998	10/05/1998			10/15/1998		01/07/1999	10/15/1998
1628N	09/16/1998	09/08/1998	09/08/1998	09/15/1998	09/17/1998	09/16/1998	09/17/1998	09/17/1998
1629N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1630N	11/09/1998	10/09/1998			10/19/1998		01/07/1999	10/27/1998
1653N	09/15/1997	09/02/1997		09/08/1997	09/12/1997		09/15/1997	09/22/1997
1655N	07/27/1998	06/29/1998	07/20/1998	07/10/1998	07/15/1998	07/29/1998	01/11/1999	07/15/1998
1667N	03/10/1998	02/20/1998		02/20/1998	02/20/1998			02/20/1998
1668N	01/02/1998	12/03/1997		12/23/1997		02/12/1998	12/11/1997	12/12/1997
1674N	05/27/1998	05/19/1998			06/03/1998	05/20/1998		06/11/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998		05/06/1998	05/06/1998	06/02/1998		05/11/1998
1701N	08/24/1998	07/24/1998		08/04/1998	08/03/1998	07/24/1998	01/11/1999	
1724N	07/10/1998	06/22/1998		06/23/1998	06/19/1998			06/29/1998
1727N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1732N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/30/1998
1735N	10/13/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/24/1998
1748N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/11/1999	09/30/1998
1755N	02/02/1999		12/28/1998	01/14/1999	01/05/1999		01/12/1999	01/07/1999

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1759N	12/30/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/14/1998
1765N	03/22/1999	03/11/1999	03/23/1999	03/17/1999	03/12/1999		03/15/1999	03/23/1999
1784N	04/08/1999	03/31/1999	03/31/1999					
1785N	04/12/1999	03/15/1999	03/18/1999	03/23/1999	03/26/1999			03/26/1999
1791N	03/29/1999	03/31/1999						
1978N	04/02/1999	03/11/1999	03/23/1999	03/17/1999	03/12/1999		03/15/1999	03/26/1999
1984N	03/17/1999	02/04/1999	02/05/1999	02/10/1999	02/17/1999		03/15/1999	02/10/1999
6618E	08/31/1997	07/17/1997		07/21/1997	07/18/1997	03/24/1998	07/16/1997	07/18/1997
6618N	03/30/1998	03/26/1998	04/02/1998	04/02/1998		03/24/1998	04/01/1998	04/03/1998
7291E	11/03/1997	10/09/1997	10/16/1997	10/10/1997	10/15/1997	11/19/1997	11/10/1997	10/16/1997
7381E	11/25/1996	01/10/1997	11/13/1996	11/13/1996	11/07/1996		12/02/1996	11/19/1996
7416E	08/07/1998	07/21/1998		07/20/1998	07/20/1998		01/11/1999	07/31/1998
7458E	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
N	02/06/1998	02/10/1998	01/16/1998	01/14/1998	01/21/1997	02/10/1998	01/21/1998	01/21/1998

Projects in Progress (LOT)

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1001H	Paul Travis	557-4631	911/OES Emergency Communications Center		12/06/1996
1034N	Ed Choy	554-8284	Chinatown Alleyway Improvements Phase 1 Commercial, Cordelia and Ross	STR	03/26/1999
1036N	Lesley Wong	554-8252	Fourth Street Pavement Renovation	Pav	05/28/1997
1077N	Steve Bui	554-8298	Bowling Green Drive Contract	SW	09/30/1997
1091N	Ed Choy	554-8284	Various Locations South of Market Removal & Pavement Renovation	Pav	04/30/1997
1106N	Steve Bui	554-8298	Western Presidio Drainage Improvements (NOI/LOT)	SW	05/16/1997
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements, Various Locations	UG	04/28/1997
1109N	Linda DeBolt	554-8265	Cesar Chavez (Army) Street Widening	Pav	12/27/1996
1133N	Ellaine Taraya	554-8245	Fulton Street Roadway Widening	Pav	10/27/1997
1155N	E. Ho/Bhula Patel	554-8324	Grant/Chestnut Street Sewer Replacements	SW	10/21/1998
1195N	Gyee Yang	558-4553	Market and Steuart Streets, AWSS Relocation	AWSS	07/20/1996
1208K	Joe Haas	558-4539	San Francisco General Hospital Underground Storage Tank Replacement	UG	03/09/1998
1223W	Lesley Wong	554-8252	Islais Creek, Street Improvements	Pav	04/30/1997
1245N	Wallis Lee	554-8344	Yosemite/Egbert Sewer Enlargment Project (formerly 3180W)	SW	11/27/1996
1253N	Iqbal Dhapa	554-8337	Twelfth Street (SR)	SW	05/16/1997
1254N	Cliff Wong	554-8339	Eleventh Street Sewer Replacement - Harrison St. to Folsom St.	SW	05/23/1997
1272N	Steve Bui	554-8298	Illinois-Cesar Chavez (Army) Streets Sewer Construction	SW	08/08/1997
1322N	Lesley Wong	554-8252	Cabrillo Street, 9th and 16th Avenues Pavement Renovation	Pav	03/11/1997
1362N	Edward Choy	554-8284	Various Locations SOMA Street District Track Removal & Pavement Renovation Phase	PAV	03/22/1999
1373N	Ken Chu	554-8388	Lower Great Highway, 46th, and 48th Avenues, Pavement Renovation	Pav	09/15/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	05/28/1997
1392N	Birgit Chase	554-8336	Bayshore Blvd. - U.S. 101 Off-Ramp...Sewer Repl. (1108N)	Pav & SW	02/28/1997
1393N	Thomas Won	554-8275	Bush/Kearny/Post Streets Sewer Replacement	SW	10/24/1997
1396N	Peter Cheng	554-8348	Sutter/Fell/Broederick Streets Sewer Replacement	SW	05/12/1997
1397N	Bhula Patel	554-8324	Douglass/Dolores/Ord/23rd/28th Streets, Sewer Replacement	SW	10/17/1997
1408N	Naoki Kaku	554-8246	Geneva Avenue, Pavement Renovation	Pav	02/06/1998
1409N	Pak Choi	554-8283	Sutter Street Pavement Renovation STP-19	Pav	03/25/1999
1411N	Peter Cheng	554-8348	Harding Park SR	SW	11/14/1997
1413N	Iqbal Dhapa	554-8337	Davis/Kearny/Francisco Streets Sewer Replacement	SW	06/25/1997
1414N	Thomas Won	554-8275	Treat / 22nd Streets Sewer Replacement	SW	02/28/1997
1426N	Ting He	554-8338	Dore/Valencia/Clinton Park SR	SW	12/08/1997
1433N	Peter Cheng	554-8348	Shotwell Street Sewer Replacement - Army Street to 26th St	SW	11/07/1997
1440N	Pak Choi	554-8283	Various Locations Concrete Street Reconstruction No. 13	Pav	02/06/1998
1453N	Naoki Kaku	554-8246	Montgomery, Kearny, & Sacramento, Pavement Renovation	Pav	02/06/1998
1454N	Ed Choy	554-8284	Potrero Hill District Track Removal and Pavement Renovation, Phase 3	SW	04/27/1998
1460N	Birgit Chase	554-8336	Church / Folsom / Harper Streets Sewer Replacement	SW	10/22/1997
1461N	Iqbal Dhapa	554-8337	Mason / Pine / Leavenworth Streets and Meacham Place Sewer Replacement	SW	03/06/1998
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	06/22/1998
1475N	Birgit Chase	554-8336	Virginia / Fair Avenues/Godeus Street SR	SW	12/24/1997
1477N	Lynn Fong	554-8269	Various Locations Concrete Street Pavement Renovation No. 14	Pav	11/09/1998
1488N	Peter Cheng	554-8348	24th Ave/California Street Sewer Replacement (1452N)	SW	06/20/1997
1491N	Peter Cheng	554-8348	Pacific Ave. Sewer Replacement - Grant Ave. to Stockton St.	SW	09/25/1997
1519N	Pak Choi	554-8283	Bus Bulb Improvement Project Phase 1	Pav	01/23/1998
1528N	Iqbal Dhapa	554-8337	501 Laguna Honda Boulevard Easement Sewer Replacement	SW	08/25/1997
1547N	Peter Cheng	554-8348	33rd Ave/Lyon Street/Molimo Dr SR	SW	01/16/1998
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SW	01/09/1998
1550N	Bhula Patel	554-8324	Day/Congo/Marston/Cuvier SR	SW	01/30/1998
1562N	Birgit Chase	554-8336	Broadway/Bryant/22nd/Sonoma Streets Sewer Replacement	SW	06/26/1998
1563N	Iqbal Dhapa	554-8337	Balboa St. and 3rd/20th/42nd Avenues Sewer Replacement	SW	06/25/1998
1566N	Peter Cheng	554-8243	Fillmore Street SR	SW	12/19/1997
1569N	Peter Cheng	554-8348	Dolores Street/Block 7044 Easement Sewer Replacement	SW	06/12/1998
1578N	Jean To	554-8329	Golden Gate Ave. Sewer Replacement-Polk St/Van Ness & Pierce/Scott Sts	SW	03/10/1998
1579N	Jean To	554-8329	Illinois Street Sewer Replacement-20th to 19th Street		04/17/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	09/15/1998
1586N	Jean To	437-7012	Geary, Eddy, Elm and Turk Sewer Replacement	SW	10/20/1998

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	01/22/1999
1602N	Jean To	437-7012	Howard, Minna and 2nd Streets Sewer Replacement	SW	11/09/1998
1603N	Jean To	554-8270	Broad Street, Capitol to Plymouth Avenue Sewer Replacement	SW	07/10/1998
1606N	Jean To	554-8348	Cayuga/Laurel/Rondel and Douglass Sewer Replacement	SW	10/29/1998
1631N	Jean To	554-8298	4th/10th Ave/Anza/Cabrillo Streets Sewer Replacement	SW	02/16/1999
1632N	Bhula Patel	554-8324	Post, Grove and Potomac Streets Sewer Replacement	SW	04/06/1999
1645N	Peter Cheng	554-8348	Third Street Sewer System Improvement Phase II	SW	02/24/1999
1687N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 15	Pav	08/31/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	03/22/1999
1729N	Narciso Paderanga, Jr.	558-8258	Brotherhood Way & Font Boulevard Pavement Renovation	Pav	03/25/1999
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	02/24/1999
1734N	Dimitrios Stavrakis	554-8271	Franklin/Greenwich and Union Streets Pavement Renovation	PAV	04/08/1999
1765N	Thinh Nguyen	558-4554	Kearny/Vallejo to Green Streets AWSS Replacement		03/22/1999
6094Q	Deanna Calleros	554-8266	Mid Embarcadero Surface Rdwy and F-Line Extension	Pav	06/27/1997
7090E	Thinh Nguyen	558-4554	Various Locations Motorized Valves Contract #2	AWSS	03/19/1998
7437E	Laami Camerino	554-8256	Howard, Folsom & Hawthorne Streets (SR)	SW	08/29/1997
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	02/24/1999
7474E	Peter Cheng	554-8348	Pine/California/Delancey Streets SR	SW	11/26/1997

Project in Progress (LOT)

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1001H	12/06/1996		12/03/1996	01/22/1997		12/05/1996		11/25/1996	12/16/1996
1034N	03/26/1999		03/17/1999					03/18/1999	
1036N	05/28/1997	Apr-98	05/15/1997	06/30/1997		05/09/1997	05/14/1997		
1077N	09/30/1997	Apr-98	09/08/1997	06/26/1998		09/24/1997	09/09/1997		09/05/1997
1091N	04/30/1997	15-Sep-97	04/04/1997	05/13/1997				04/11/1997	04/28/1997
1106N	05/16/1997	3-Nov-97	05/06/1997	05/13/1997		05/12/1997	05/06/1997		06/03/1997
1109K	04/28/1997		04/14/1997			04/16/1997		04/22/1997	05/08/1997
1109N	12/27/1996	Jun-98	12/05/1996				12/03/1996		02/07/1997
1133N	10/27/1997	May-98	10/21/1997		10/16/1997		10/10/1997		10/21/1997
1155N	10/21/1998		10/16/1998	11/09/1998		10/07/1998	10/06/1998		10/15/1998
1195N	07/20/1996						07/08/1996		
1208K	03/09/1998		03/24/1998	03/05/1998		03/18/1998	03/05/1998	03/12/1998	03/24/1998
1223W	04/30/1997	Jun-98	04/14/1997	05/13/1997		04/16/1997	04/21/1997		05/14/1997
1245N	11/27/1996		11/08/1996	02/24/1997					12/07/1996
1253N	05/16/1997	Apr-98	04/28/1997	05/13/1997		05/05/1997	04/29/1997		05/12/1997
1254N	05/23/1997	Jul-98	04/28/1997	05/13/1997		04/23/1997	04/22/1997		05/12/1997
1272N	08/08/1997	Jun-98	07/29/1997	06/15/1998		07/28/1997	07/28/1997		
1322N	03/11/1997	May-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997	02/14/1997	02/27/1997
1362N	03/22/1999		03/12/1999	03/22/1999			03/12/1999	03/19/1999	03/16/1999
1373N	09/15/1997	May-98	08/26/1997	04/22/1998			08/22/1997	08/28/1997	09/10/1997
1374N	05/28/1997	May-98	05/01/1997				04/30/1997	05/12/1997	05/14/1997
1392N	02/28/1997		02/20/1997				02/19/1997		02/27/1997
1393N	10/24/1997		10/21/1997	05/19/1998		10/15/1997	10/08/1997		10/21/1997
1396N	05/12/1997	May-98	05/01/1997			05/28/1997			05/12/1997
1397N	10/17/1997		09/26/1997		10/20/1997	10/01/1997	09/26/1997		10/14/1997
1408N	02/06/1998	Jun-98	01/08/1998	04/22/1998	01/20/1998		01/08/1998	03/05/1998	01/21/1998
1409N	03/25/1999		03/09/1999			03/11/1999	02/16/1999	03/18/1999	03/11/1999
1411N	11/14/1997	Jul-98	10/23/1997			11/05/1997	10/24/1997		11/04/1997
1413N	06/25/1997	Jun-98	06/16/1997	06/17/1997		06/11/1997			07/11/1997
1414N	02/28/1997	Jul-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997		02/28/1997
1426N	12/08/1997	Sep-98	12/04/1997		12/03/1997	12/10/1997	12/03/1997		12/17/1997
1433N	11/07/1997	Jun-98	10/21/1997			10/24/1997	10/16/1997		11/13/1997
1440N	02/06/1998	Apr-98	01/08/1998	01/09/1998	01/20/1998	01/27/1998	01/08/1998		01/21/1998
1453N	02/06/1998	Jul-98	01/08/1998				01/08/1998	03/09/1998	01/26/1998
1454N	04/27/1998		04/27/1998			04/20/1998	04/16/1998	04/23/1998	07/09/1998
1460N	10/22/1997		10/21/1997			10/24/1997	10/10/1997		10/21/1997
1461N	03/06/1998	Jul-98	02/20/1998	04/02/1998			02/20/1998		
1474N	06/22/1998	Jul-98	06/03/1998	06/17/1998	06/02/1998	06/09/1998		06/02/1998	06/03/1998
1475N	12/24/1997		12/12/1997		01/20/1998	01/06/1998	12/15/1997		
1477N	11/09/1998	Jun-98	10/16/1998	11/12/1998	11/02/1998		10/16/1998	11/20/1998	10/20/1998
1488N	06/20/1997	Apr-98	06/09/1997			06/04/1997	06/03/1997		06/16/1997
1491N	09/25/1997	May-98	09/18/1997	06/30/1997		09/24/1997	09/16/1997		
1519N	01/23/1998	Jun-98	12/30/1997				12/30/1997	01/09/1998	01/26/1998
1528N	08/25/1997	Mar-98	08/20/1997		10/03/1997		08/21/1997		09/08/1997
1547N	01/16/1998		12/15/1997		01/20/1998	01/06/1998	12/17/1997		12/23/1997
1548N	01/09/1998		12/22/1997	04/13/1998	12/30/1997	01/09/1998	12/29/1997		01/06/1998
1550N	01/30/1998				01/20/1998	02/12/1998	01/14/1998		02/12/1998
1562N	06/26/1998		06/22/1998		06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1563N	06/25/1998		06/19/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1566N	12/19/1997		12/12/1997	12/19/1997	12/17/1997	12/17/1997	12/15/1997		
1569N	06/12/1998		05/15/1998	06/12/1998	06/17/1998	06/09/1998	05/19/1998	06/02/1998	06/09/1998
1578N	03/10/1998		03/24/1998	06/30/1998	03/09/1998		03/09/1998	03/11/1998	03/24/1998
1579N	04/17/1998			05/15/1998		04/14/1998	04/13/1998	04/13/1998	04/23/1998
1585N	09/15/1998		09/08/1998	09/02/1998	09/10/1998	09/17/1998	09/01/1998	09/21/1998	09/08/1998
1586N	10/20/1998		10/02/1998	11/06/1998	11/02/1998			10/09/1998	10/13/1998

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1589N	01/22/1999		12/23/1998	02/22/1999			12/29/1998	12/17/1998	01/26/1999
1602N	11/09/1998		10/16/1998				10/16/1998	10/13/1998	10/20/1998
1603N	07/10/1998		06/19/1998	07/10/1998		06/22/1998	06/18/1998	07/16/1998	06/23/1998
1606N	10/29/1998		10/02/1998	11/09/1998	11/09/1998		10/06/1998	10/13/1998	10/13/1998
1631N	02/16/1999		01/19/1999					01/14/1999	02/05/1999
1632N	04/06/1999		03/09/1999	03/17/1999	03/05/1999		03/02/1999		
1645N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/19/1999	02/24/1999
1687N	08/31/1998		08/12/1998	11/06/1998	08/05/1998	08/12/1998	08/03/1998	08/03/1998	08/13/1998
1727N	03/22/1999		03/12/1999				03/12/1999	03/17/1999	
1729N	03/25/1999		03/12/1999	03/02/1999			02/16/1999	02/24/1999	03/10/1999
1732N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/20/1999	02/05/1999
1734N	04/08/1999		03/29/1999				03/26/1999	03/26/1999	
1765N	03/22/1999			03/17/1999			03/11/1999		
6094Q	06/27/1997	07/98							
7090E	03/19/1998		03/24/1998	04/22/1998				03/18/1998	
7437E	08/29/1997	Jul-98	08/05/1997	04/13/1998		08/08/1997	08/06/1997	09/23/1997	09/04/1997
7458E	02/24/1999		01/19/1999				01/13/1999	01/21/1999	03/04/1999
7474E	11/26/1997		11/19/1997			12/04/1997	11/20/1997		12/10/1997

Project in Progress (LOT)

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1001H	12/06/1996	12/30/1996	01/22/1997		12/05/1996	12/03/1996	12/06/1996	12/06/1996
1034N	03/26/1999	03/16/1999	03/26/1999		03/26/1999			
1036N	05/28/1997	05/23/1997				06/04/1997	06/12/1997	
1077N	09/30/1997	09/24/1997			10/07/1997		11/10/1997	01/27/1998
1091N	04/30/1997					04/14/1997	05/23/1997	05/23/1997
1106N	05/16/1997	05/20/1997			05/19/1997	05/13/1997	05/19/1997	05/19/1997
1109K	04/28/1997					04/22/1997	09/24/1997	09/04/1998
1109N	12/27/1996	12/14/1996	01/29/1997	01/09/1997			06/23/1997	
1133N	10/27/1997	10/16/1997			10/20/1997	10/17/1997	11/10/1997	11/10/1997
1155N	10/21/1998	10/06/1998		11/09/1998	10/13/1998			
1195N	07/20/1996			08/02/1996		07/23/1996		
1208K	03/09/1998	03/05/1998	03/30/1998		03/10/1998		05/14/1998	
1223W	04/30/1997	04/18/1997	04/17/1997			04/25/1997	05/23/1997	03/06/1998
1245N	11/27/1996			12/02/1996	12/05/1996	11/08/1996	04/15/1997	04/15/1997
1253N	05/16/1997	05/20/1997		05/14/1997		04/29/1997	05/16/1997	05/16/1997
1254N	05/23/1997	04/28/1997				04/24/1997	06/12/1997	
1272N	08/08/1997	08/05/1997			10/07/1997	07/30/1997	09/24/1997	09/24/1997
1322N	03/11/1997	03/11/1997	04/21/1997	03/25/1997		03/03/1997	04/18/1997	04/18/1997
1362N	03/22/1999	03/17/1999	03/17/1999		03/16/1999			
1373N	09/15/1997	09/12/1997		11/07/1997	10/07/1997		11/10/1997	12/22/1997
1374N	05/28/1997	05/20/1997				04/29/1997	09/24/1997	03/06/1998
1392N	02/28/1997	02/28/1997	04/21/1997	03/18/1997		02/24/1997		
1393N	10/24/1997		10/22/1997		10/14/1997	10/16/1997	11/10/1997	
1396N	05/12/1997			05/14/1997		04/30/1997	06/12/1997	
1397N	10/17/1997	09/30/1997			10/07/1997	09/29/1997	11/10/1997	11/10/1997
1408N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1409N	03/25/1999	02/22/1999	03/08/1999		02/22/1999			
1411N	11/14/1997	11/07/1997			10/29/1997	10/29/1997	12/22/1997	12/22/1997
1413N	06/25/1997				10/07/1997	06/09/1997	06/23/1997	
1414N	02/28/1997		04/17/1997	03/18/1997		02/13/1997	04/15/1997	04/15/1997
1426N	12/08/1997				12/12/1997	12/04/1997		02/20/1998
1433N	11/07/1997	11/07/1997			10/21/1997	10/16/1997	11/25/1997	12/22/1997
1440N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1453N	02/06/1998	01/13/1998			01/14/1998		02/12/1998	
1454N	04/27/1998		04/20/1998		04/23/1998		07/09/1998	07/09/1998
1460N	10/22/1997	10/16/1997			10/20/1997	10/08/1997	11/25/1997	12/22/1997
1461N	03/06/1998	02/20/1998	03/30/1998		02/27/1998		05/14/1998	
1474N	06/22/1998	06/18/1998	06/05/1998		06/03/1998	10/08/1998	07/13/1998	
1475N	12/24/1997		01/14/1998		12/19/1997		01/27/1998	
1477N	11/09/1998	10/15/1998			10/13/1998			12/01/1998
1488N	06/20/1997	06/19/1997			06/09/1997	06/02/1997	08/08/1997	
1491N	09/25/1997	09/24/1997			10/07/1997	09/15/1997	11/10/1997	02/12/1998
1519N	01/23/1998				01/06/1998		02/12/1998	
1528N	08/25/1997	08/26/1997			10/07/1997	08/20/1997	09/26/1997	09/26/1997
1547N	01/16/1998		03/30/1998			12/15/1997	02/12/1998	
1548N	01/09/1998	12/29/1997	01/14/1998		12/29/1997	12/19/1997	02/12/1998	
1550N	01/30/1998		03/30/1998		01/21/1998	01/23/1998	04/07/1998	
1562N	06/26/1998	06/22/1998	06/23/1998		06/19/1998	06/19/1998	09/25/1998	
1563N	06/25/1998	06/22/1998	06/23/1998		06/19/1998	06/16/1998	10/27/1998	
1566N	12/19/1997		01/14/1998		12/19/1997	12/10/1997	02/20/1998	
1569N	06/12/1998	06/08/1998	05/19/1998		05/21/1998	05/15/1998	07/13/1998	

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1578N	03/10/1998	03/11/1998				03/09/1998	05/14/1998	
1579N	04/17/1998	04/20/1998	04/20/1998		04/20/1998			
1585N	09/15/1998		08/28/1998	11/09/1998	08/31/1998	09/10/1998	10/27/1998	
1586N	10/20/1998			11/09/1998	10/01/1998			
1589N	01/22/1999	12/21/1998			12/29/1998			
1602N	11/09/1998	10/15/1998	12/02/1998		10/13/1998			
1603N	07/10/1998	06/17/1998	08/04/1998		06/16/1998	10/08/1998	11/12/1998	
1606N	10/29/1998			11/09/1998	10/13/1998			
1631N	02/16/1999	01/20/1999			01/21/1999			
1632N	04/06/1999	03/02/1999	03/10/1999		03/02/1999			
1645N	02/24/1999	01/25/1999				01/19/1999		
1687N	08/31/1998	08/07/1998	08/04/1998	11/09/1998	08/07/1998		10/06/1998	
1727N	03/22/1999	03/16/1999	03/17/1999		03/16/1999			
1729N	03/25/1999	02/22/1999	03/08/1999		02/22/1999			
1732N	02/24/1999	01/20/1999			01/20/1999	01/19/1999	02/01/1999	
1734N	04/08/1999	03/30/1999	03/31/1999		03/29/1999			
1765N	03/22/1999				03/29/1999			
6094Q	06/27/1997	09/19/1998			10/07/1997	06/13/1997	09/24/1997	09/24/1997
7090E	03/19/1998		01/05/1999		04/08/1998			
7437E	08/29/1997	08/26/1997			10/07/1997	08/07/1997	09/24/1997	09/24/1997
7458E	02/24/1999	01/20/1999			01/20/1999	01/19/1999		02/01/1999
7474E	11/26/1997				11/25/1997	11/17/1997	02/12/1998	

Projects in Progress (LOT)

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1001H	12/06/1996	12/02/1996	12/02/1996		12/05/1996	12/23/1996	12/02/1996	12/05/1996
1034N	03/26/1999	03/15/1999	03/18/1999					03/26/1999
1036N	05/28/1997	05/19/1997	05/21/1997		05/23/1997	05/29/1997		05/28/1997
1077N	09/30/1997	09/19/1997			09/15/1997	09/24/1997	09/11/1997	10/02/1997
1091N	04/30/1997	04/09/1997			04/09/1997	04/14/1997	05/14/1997	04/10/1997
1106N	05/16/1997	05/06/1997		05/13/1997	05/13/1997	05/29/1997	05/14/1997	05/28/1997
1109K	04/28/1997	04/18/1997	04/24/1997	04/24/1997	04/16/1997	04/25/1997	05/14/1997	05/08/1997
1109N	12/27/1996	12/12/1996	01/06/1997		12/16/1996	12/23/1996	12/19/1996	12/10/1996
1133N	10/27/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1155N	10/21/1998	10/05/1998			10/15/1998		01/11/1999	10/15/1998
1195N	07/20/1996		07/17/1996		07/19/1996		07/30/1996	07/15/1996
1208K	03/09/1998	03/06/1998	03/20/1998		03/17/1998		04/08/1998	04/03/1998
1223W	04/30/1997	05/05/1997	04/24/1997		04/16/1997		05/14/1997	04/24/1997
1245N	11/27/1996		11/13/1996		11/20/1996		12/02/1996	11/19/1996
1253N	05/16/1997	05/01/1997			05/02/1997	05/29/1997	05/14/1997	06/03/1998
1254N	05/23/1997	04/29/1997			04/29/1997	05/29/1997	05/14/1997	05/08/1997
1272N	08/08/1997	08/12/1997			08/05/1997	08/08/1997	08/08/1997	08/15/1997
1322N	03/11/1997	02/18/1997			03/13/1997	02/27/1997	04/21/1997	02/20/1997
1362N	03/22/1999	03/11/1999	03/18/1999		03/26/1999		03/15/1999	03/24/1999
1373N	09/15/1997	08/27/1997			09/04/1997	09/24/1997	09/15/1997	09/22/1997
1374N	05/28/1997	05/01/1997			05/06/1997	05/29/1997	05/14/1997	05/08/1997
1392N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1393N	10/24/1997	10/14/1997			10/15/1997	11/18/1997	12/11/1997	10/16/1997
1396N	05/12/1997	05/05/1997			05/13/1997	05/29/1997	05/14/1997	05/28/1997
1397N	10/17/1997	09/26/1997			10/02/1997	11/19/1997		10/16/1997
1408N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1409N	03/25/1999	02/19/1999	02/22/1999		02/23/1999		03/09/1999	03/02/1999
1411N	11/14/1997	10/28/1997	11/13/1997		10/31/1997	11/19/1997	11/10/1997	11/13/1997
1413N	06/25/1997	06/11/1997			06/19/1997	06/10/1997	08/08/1997	06/20/1997
1414N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1426N	12/08/1997	12/03/1997	12/20/1997		12/17/1997	02/12/1998	12/08/1997	12/12/1997
1433N	11/07/1997	10/20/1997	10/28/1997		10/23/1997	11/19/1997	11/10/1997	11/13/1997
1440N	02/06/1998	01/12/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1453N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1454N	04/27/1998	04/20/1998			04/28/1998	05/20/1998		05/11/1998
1460N	10/22/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1461N	03/06/1998	02/20/1998			02/20/1998	05/20/1998	04/08/1998	02/20/1998
1474N	06/22/1998				06/09/1998			06/03/1998
1475N	12/24/1997	12/13/1997	12/19/1997		12/19/1997	02/10/1998	12/29/1997	11/29/1908
1477N	11/09/1998	10/08/1998			10/19/1998		01/12/1999	10/27/1998
1488N	06/20/1997	06/04/1997			06/11/1997	07/11/1997	08/08/1997	06/20/1997
1491N	09/25/1997	09/19/1997			09/25/1997	11/19/1997	09/19/1997	09/22/1997
1519N	01/23/1998	01/07/1998			01/14/1998	05/20/1998	01/21/1998	01/21/1998
1528N	08/25/1997	08/22/1997			08/26/1997	08/21/1997	09/15/1997	09/22/1997
1547N	01/16/1998	12/19/1997			12/19/1997		12/29/1997	01/12/1998
1548N	01/09/1998	01/07/1998			01/14/1998	02/12/1998	12/29/1997	01/12/1998
1550N	01/30/1998	01/16/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1562N	06/26/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1563N	06/25/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1566N	12/19/1997	12/13/1997	12/19/1997		12/17/1997	02/10/1998	12/29/1997	01/12/1998
1569N	06/12/1998	05/19/1998			06/03/1998	05/20/1998		06/08/1998
1578N	03/10/1998	03/10/1998			03/17/1998		04/08/1998	04/03/1998
1579N	04/17/1998	04/13/1998	04/28/1998			05/20/1998		04/16/1998
1585N	09/15/1998		08/31/1998		09/15/1998		01/07/1999	09/11/1998
1586N	10/20/1998	09/28/1998			10/06/1998		01/07/1999	10/15/1998

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1589N	01/22/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998		01/12/1999	01/07/1999
1602N	11/09/1998	10/08/1998			10/19/1998		01/11/1999	10/27/1998
1603N	07/10/1998	06/15/1998			06/19/1998		01/11/1999	07/07/1998
1606N	10/29/1998	10/05/1998			10/06/1998		01/07/1999	10/15/1998
1631N	02/16/1999	01/14/1999			01/26/1999		03/15/1999	02/03/1999
1632N	04/06/1999	10/28/1998	03/02/1999	11/23/1998	03/02/1999		03/09/1999	03/05/1999
1645N	02/24/1999	01/11/1999	01/13/1999		01/19/1999		03/09/1999	01/20/1999
1687N	08/31/1998	08/24/1998			08/13/1998		01/11/1999	08/25/1998
1727N	03/22/1999	03/11/1999	03/18/1999				03/15/1999	03/24/1999
1729N	03/25/1999	02/19/1999	02/22/1999		02/23/1999		03/09/1999	03/02/1999
1732N	02/24/1999	01/11/1999	01/13/1999		01/19/1999		03/09/1999	01/20/1999
1734N	04/08/1999	03/31/1999	03/31/1999					
1765N	03/22/1999	03/11/1999	03/23/1999					03/23/1999
6094Q	06/27/1997	06/27/1997			06/12/1997			
7090E	03/19/1998				03/24/1998		04/08/1998	04/03/1998
7437E	08/29/1997	08/06/1997			08/12/1997	08/08/1997	08/08/1997	08/26/1997
7458E	02/24/1999	01/12/1999			01/20/1999		03/09/1999	01/20/1999
7474E	11/26/1997	11/25/1997	12/03/1997		12/01/1997	02/12/1998	12/12/1997	12/12/1997

ME

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
		SEW=SEWER											MF=Mill & Fill		
		S&H=STREETS AND HIGHWAYS						?	= Exact year of construction not known				OL=Overlay		
		CON=CONFLICT							= New or revised project				RE=Reconstruction		
									= Under construction				JP=Joint Project		
	CLASS A EMERGENCY PROJECTS														
1615N		SEW	1998		Jackson	Montgomery	Columbus	1876	?	4 x 6	BRICK	Bad shape, out of round, crown sagging			100
1615N		SEW	1998		Columbus	Jackson	Pacific	1900	?	16"/18"	CP/BRICK				100
1615N		SEW	1998		Kearny	Jackson	Pacific	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1615N		SEW	1998		Kearny	Jackson	Washington	1890	?	3 x 5	BRICK	Bad shape, crown out of round			75
1619N		SEW	1998		60 Scenic Way Easement Sewer (Assessor's Block 1303)					8"	VCP	Cracks and collpased sections			50
1621N		SEW	1998	1998	Anza	7th Ave	8th Ave	1908	?	2'6"x3'9	BRICK	Cracks and collpased sections			162
1622N		SEW	1998		3rd St	Jerrold	Kirkwood			18"	VCP	Many cracks, collapsing sections			250
1622N		SEW	1998		3rd St	Kirkwood	LaSalle			42"	CONC	Re-alignment			250
1622N		SEW	1998		3rd St	LaSalle	McKinnon			42"	CONC	Re-alignment			250
1622N		SEW	1998		3rd St	McKinnon	Newcomb			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		3rd St	Newcomb	Oakdale			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		3rd St	Oakdale	Palou			18"	VCP	Hydraulically inadequate sewer			250
1622N		SEW	1998		Donner	Jennings	Ingalls			15"	ISP	Hydraulically inadequate sewer			250
1622N		SEW	1998		Jennings	Egbert	Donner			N/A		Hydraulically inadequate sewer			250
1623N		SEW	1998		Green	Polk	Van Ness	1890	?	16"	VCP				150
1218N	BSSR	SEW	1998		Harrison	5th St	Morris	1935		12/18/21	VCP	Severe cracks, many dips/debris restrict flow	MF	3/98	230
			1998		Polk	Grove	McAlister	1877		3x5	BRICK	Bricks missing, sand infiltration	MF	1998	129
			1998		Van Ness	Golden Gate	McAlister	1877		3x5	BRICK	Bricks missing, crown starting to collapse			200
			1998		Polk	Bush	Sutter	1877		3x5	BRICK	Bricks missing, sand infiltration, walls collapsing			160
												CLASS A EMERGENCY =			$2,942
	ACCELERATED PROJECTS														
1433N		SEW	1998	Spl	Shotwell	26th St	Army St	1890	?	15"	VCP	Street Pavement & Sewer Collapsed			99
1433N	....N	SEW	1998		Moultrie	Eugenia	Cortland	1915	?	10"	VCP	Broken pipe, cracks, infiltration			111
1433N	....N	SEW	1998	136	26th St	Dolores	Church	1885		15"	VCP	Many medium & minor cracks, severe grout	MF		205
1432N	....N	SEW	1998		Post	Baker	Broderick	1900		18"	VCP	Joints open throughout, open ss, sand infiltration	MF	1/01	162
1432N	....N	SEW	1998		Post	Broderick	Divisadero	1900		18"	VCP	Collapsed @ 84-97' c-d, cracks @ 10-31'b-c	MF	1/01	162
1330N		SEW	1998		09th St	Harrison	McLea Ct MB	1900	?	24"	VCP	Crushed pipe @ 194-208, full of debris,dip			90
1547N	BSSR	SEW	1998		33rd Ave	Irving	Judah	1925	?	12"	ISP	Many St depressions, severe offsets, breaks @ ss's	MF	3/98	159
1547N		SEW	1998		Lyon	Hayes	Grove	1888		16"	ISP	Many St depressions, open joints, cracks, breaks; c-b			77
1547N		SEW	1998		Molimo	Bella Vista	Intersection	1946	?	12"/15"	VCP	Collapsed & crushed section @ 21'	MF		19
1569N		SEW	1998		Dolores	16th St	17th St	1889	?	18"	VCP	Egg shaped, Multiple cracks @ invert			168
1569N		SEW	1998		Dolores	17th St	18th St	1889	?	18"	VCP	Collapsing section, open joints			135
1569N		SEW	1998		York	21st St	22nd St	1888		10"	VCP	Collapsed sections			135
1625N	1385N	JP/S&H	1998		Lombard	Leavenworth	Jones	1900	?	18"	ISP	Cracks, open joints, fast flow	RE	Jul-98	100
1626N		SEW	1999		05th Ave	Irving	Lincoln	1900	?	12"	ISP	Many bad cracks; many street depressions			195

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1626N		SEW	1999		04th Ave	Lincoln	Hugo					Many cracks; crushed, street depressions			105
1626N		SEW	1999		Stanyan (west sic	Turk	Anza					Many bad cracks; many street depressions			185
1626N		SEW	1999		Paris	Brazil	Excelsior					Bad cracks; open joints, street depression			105
1362N	BSSR	JP/S&H	1999	188	Kate	End South	Bryant	1900	?	16"	VCP	Severe cracks 162-170' b-a; TV'd 13' b-c, offset	RE	Jul-99	100
1362N	BSSR	JP/S&H	1999	188	Gilbert	End South	Brannan	1900	?	12"	VCP	Cannot TV, flow is too high, sump area	RE	Jul-99	100
			1999		Chestnut	Fillmore	Steiner	1900		8"	VCP	Open joints, cracks, ss open, collapsed sections			100
			1999		21st Ave.	Ortega	Noreiga	1925		15"	VCP	Offsets, separated joints,holes, street depression.	MF	Jul-99	200
	. . . N		1999		Goettingen	Ward	Ordway	1915	?	8"	ISP	Open ss connections, sand infiltration, pavement sinki	RE		100
	1668N		1999		Golden Gate	Lyon	Central	1887		16"	ISP	Crushed pipe, offsets, streetfailure	MF	Jul-99	100
	. . . N		1999		Gough	Post	Geary	1911		12"	VCP	Offset joints, cracks, street depressions	RE?		100
												ACCELERATED PROJECT TOTAL =			**$3,012**
	1ST PRIORITY PLANNED PROJECTS: Critical Replacements-Severely collapsed/crushed sewers recommended for immediate replacement														
1491N	BSSR	SEW	1998	W-014	Pacific	Stockton	Grant	1876		3'x5'	BRICK	Fairly bad shape, out of round, missing mortar	MF	1/98	134
1426N	BSSR	SEW	1998		Clinton Park	Guerrero	Valencia	1878		12"	ISP	Offsets, infiltration, many depressions	MF	7/98	139
1426N	....N	SEW	1998		Valencia	15th St	16th St	1890	?	3x5	BRICK	Bad shape, collapsed @ 447 Valencia			418
1426N		SEW	1998		Dore	Bryant	Harrison	1912	?	16"	VCP	Many cracks, offsets, dip, street depressions			140
1503N		SEW	1998		10th Ave	Kirkham	Judah MB	1902		12"	VCP	Cracked sections and many offsets b-c			75
1503N		SEW	1998		10th Ave	Pacheco	Ortega MB	1906	?	12"	ISP	Severe offsets, depressions, fast flow, worn invert			75
1461N	BSSR	SEW	1998		Mason	Ellis St.	Eddy St.	1880	?	3x5	BRICK	Severly deformed crown,missing bricks	OL		95
1461N	....N	SEW	1998		Pine	Hyde	Leavenworth	1880	?	3x5	BRICK	Fairly bad shape (oval), 3 broken s/s			280
1461N	1727N	SEW	1998		Leavenworth	O'Farrell	Geary	1900	?	3x5	BRICK	Bad shape	MF	7/99	221
1461N		SEW	1998		Meacham	Post	End: South		?	8"	VCP	Severe cracks and damaged ss connections			60
1488N		SEW	1998		California	10th Ave	11th Ave	1900	?	8"	VCP	St. depression; crushed / collapsed			65
1488N		SEW	1998		24th Ave	California	Clement MB	1907		8"	ISP	Cracks, breaks, dip, street depressions			100
1550N		SEW	1998		Day St	Dolores	San Jose	1888		18"	ISP	Collapsed pipe			70
1550N		SEW	1998		Congo	Monterey	Hearst	1910	?	12"	VCP	Multiple cracks, st dep @ 147-159' b-c, infiltration			72
1550N	BSSR	SEW	1998		Congo	Melrose	Mangels	1910		8"	VCP	Many cracks over the block	OL		60
1550N	BSSR	SEW	1998		Marston	Circular	Edna	1910		8"	ISP	Many severe cracks	MF		114
1550N	BSSR	SEW	1998		Cuvier	Bosworth MB (m	Mirando (mhE)	1902		15"	VCP	Multiple cracks & egg shape @ 64-140' d-e	MF		90
1550N		SEW	1998		28th St	Noe	East Xing	1900	?	15"	VCP	Bad open joints @20-50'			139
1562N	....N	SEW	1998		Broadway	Taylor	Himmelmann	1952		16"	VCP	Collapsed & Crushed	RE	1/99	56
1562N	....N	SEW	1998		Broadway	Florence	Taylor	1900	?	12"	VCP	Crushed invert, mult cracks	RE	1/99	63
1562N	....N	SEW	1998		Broadway(N Sid	Cyrus Pl	Hyde MB	1952		21"	VCP	Mult cracks, ready to collapse a-b	MF	1/99	54
1562N		SEW	1998		Bryant	18th St	19th St	1889		14"	VCP	Many cracks; pipe collapses			108
1562N		SEW	1998		Sonoma	Union	Green		?	12/15"	VCP	Crushed,broken pipe, ready to collapse			75
1606N	BSSR	SEW	1999	211	Douglass	23rd St	Elizabeth	1890	?	15"	VCP	Severe offsets, separated ss's, st depn	OL		111
1606N		SEW	1999	397	Cayuga	Seneca	Junior Terr	1939		8"	VCP	Many offsets, large street depressions, infiltration			50
1606N		SEW	1999	sp1001	Laurel	Washington	Jackson	1900	?	12"	CP	Multiple severe offsets, street depressions			86
1606N		SEW	1999	sp2001	Rondel Pl	End S(17th St)	16th St	1890	?	12"	ISP	Crushed, multi-cracked sections, severe offsets			138
			1999		Bertita	Seneca	end			8"	VCP	Street collapsing (field check) several bad sections			
1155N		SEW	1999		Chestnut	Culebra	Polk	1913		12"	ISP	Numerous Cracks, Collapsed Pipe			68
1155N		SEW	1999		Chestnut	Powell	Stockton	1890		16"	CEM	Cracks, invert erosion			140
1155N		SEW	1999		Grant	Chestnut	Francisco	1918	?	14"	VCP	Offsets, Crushed Pipe, Debris			99
1155N		SEW	1999		Grant	Greenwich	Lombard	1918	?	16"	VCP	Cracks, Dip, Cement Pipe			107

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1218N?		SEW	1999		Market S. Side	9th Street	10th Street	1878		3x5	BRICK	Ready to collapse			353
1218N?	....N	SEW	1999		Larkin	Golden Gate	McAllister	1874		18"	VCP	Collapsed, continuous cracks	MF		109
		SEW	1999	210	Eugenia	Prospect	Coleridge	1920	?	12"	ISP	Severe offsets, breaks, bad ss, rat, street depressions			
							NOTE: Projects with estimates rounded to 100k have not been finalized and will be revised after sizing								
												PRIORITY 1 (Planned Projects) TOTAL =			$3,964
	2ND PRIORITY PLANNED PROJECTS: Severely cracked/crushed sewers to be replaced on a normal contract schedule.														
1254N	....N	SEW	1998		11th St	Folsom	Harrison	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			360
1603N		SEW	1998		Broad	Capitol	Plymouth	1910	?	8"	ISP	Many depressions, complaints, MUNI track replmt			215
7474E	BSSR	SEW	1998		Delancey (1st St)	Townsend	Brannan	?		12"/15"	VCP	Collapsed sections	MO		207
7474E		SEW	1998		Pine	Battery	Front	1907		18"	ISP	Collapsed, Cracks			86
7474E	1407N	SEW	1998		California	Webster	Buchanan	1880	?	15"	CEM	Offsets, hole @ 104',open joints st depressions	MF	1/1/01	142
7474E	1407N	SEW	1998		California	Laguna	Buchanan	1876	?	16"	CEM	TV'd 35', Collapsed	MF	1/1/01	323
1392N	1108N	JP/S&H	1998		Bayshore E	Oakdale MB	Jerrold	1928		15"/12"	VCP	Cracked (replace a-c), dip, debris	MF	1/98	75
1392N	1108N	JP/S&H	1998		Bayshore E	Oakdale	Jerrold MB	1928		15"/12"	VCP	Cracked (replace a-e), damaged @ 3' e-f	MF	1/98	178
1393N		SEW	1998		Bush	Kearny	Montgomery	1880	?	3x5	BRICK	Fairly bad shape,bricks, plastering			250
1393N	1453N	SEW	1998		Kearny	Sutter	Bush	1890	?	3x5	BRICK	Fairly bad shape, loose bricks	OL	10/98	208
1393N	BSSR	SEW	1998		Post	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, missing & loose bricks	MF		274
1393N	1453N	SEW	1998		Kearny	Sutter	Post	1875	?	3x5	BRICK	Bad shape, debris, crown sagging	MF	10/98	77
1393N	....N	SEW	1998		Sutter	Montgomery	Intersection	1876	?	3x5	BRICK	Intersection in bad shape	MF	1/1/01	50
1393N		SEW	1998		Bush	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, crown sagging			115
1397N	....N	SEW	1998		Ord	Corbett	Market	1900	?	15"	VCP	Cracks, cracked invert, severe offsets	MF		43
1397N	7317E	SEW	1998		Dolores	28th St	Valley	1885	?	18"	VCP	Crushed and multiple cracks	MF/JP		89
1397N	BSSR	SEW	1998		23rd St	Castro	Diamond	1888	?	15"	VCP	Severe cracks @ 25-70', heavy debris, dip	MF		180
1411N		SEW	1998		Harding Park	Skyline	Zoo					New Sewer			
1413N	6094Q	S&H	1998		Davis (Blk #200	Clay	Washington	1878	?	3x5	BRICK	Bad shape, debris, missing bricks & mortar	RE/JP		167
1413N	BSSR	SEW	1998		Francisco	Stockton	Powell	1876	?	3x5	BRICK	Bad shape 1/2, fairly bad shape 1/2	MF		290
1413N	1453N	SEW	1998		Kearny	Green	Union	1900	?	12/8"	VCP	Crushed & cracked sections	MF	10/98	99
1474N	BSSR	SEW	1998		43rd Ave	Anza St	Balboa MB	1917	?	15"	VCP	Many cracks @ mh b-c exfiltration @ 120' b-c	OL		95
1474N	....N	SEW	1998		08th Av	Fulton	Cabrillo	1907	?	8"	VCP	Numerous cracked sections, collapse			168
1474N	BSSR	SEW	1998		06th Ave	Cabrillo	Balboa	1902	?	12"	VCP	Many cracked sections; sev. open joints., bad ss & mh	MF		133
1474N	BSSR	SEW	1998		06th Ave	Fulton	Cabrillo	1907	?	8"	ISP	Many cracked sections, hole (repair done 1/12/96)	MF		168
1548N	....N	SEW	1998		O'Farrell	Anza Vista	Masonic	1947		15"	VCP	Numerous cracks			140
1548N	BSSR	SEW	1998		Deming	Clayton MB	Uranus	1920		12"	ISP	Ready to collapse	OL		105
1548N		SEW	1998		Iron Alley	Corbett	Clayton	1917	?	15"	VCP	Offsets, roots, Hole invert @ 140' b-c			129
1548N		SEW	1998		Farnsworth	Edgewood	Willard		?	12"	VCP	Severe cracks, stopped @ 83'; recommend lining			67
1579N	1454N	JP/S&H	1998		Illinois	20th St	19th St	1910	?	18"	VCP	Multi cracked, crushed sections b-c; TV'd 60' b-c	TR	5/98	132
1475N	1389N	JP/S&H	1998		Virginia	Coleridge	Mission St	1905	?	16"	VCP	BSSR RECOMMENDED REPLACEMENT			85
1475N	1389N	JP/S&H	1998		Fair St	Coleridge	Mission	1890		12"	VCP	Mult joint offsets,cracks, infiltration, st. depression		1/99	90
1475N	1389N	JP/S&H	1998		Godeus	Coleridge MB	Mission		?	15"	VCP	Cracks/crush @123'-145'; cracks; open joints b-c	MF	1/99	70
1563N	BSSR	SEW	1998		42nd Ave	Geary	Anza	1920	?	8"	VCP	Street depression, collapse; sev. open joints	MF		145
1563N	....N	SEW	1998		Balboa	Arguello	2nd Ave	1907	?	18"	ISP	Multiple cracks			107
1563N	BSSR	SEW	1998		03rd Ave	Balboa	Anza	1908	?	8"	VCP	Many street dep.; many cracks/holes ms/s	MF		158

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1563N		SEW	1998		20th Ave	Fulton	Cabrillo	1915		8"	ISP	Numerous street depressions			135
	98-99 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1477N		1999	201	Hamilton	Dwight	Woolsey	1952		12"	VCP	Cracks; crushed section (needs lining)	RE	1999	60
	1477N		1999	201	Dartmouth	Dwight	Woolsey	1952		12"	VCP	Invert cracks, Open joints (needs lining)	RE	1999	60
	7458E		1999	7	Clay	Jones MB	Taylor	1889	?	12"	?	Offsets, cracks, dip	RE	1999	90
1578N	1668N	JP/S&H	1999		Golden Gate	Polk St	Van Ness	1873		3'x5'	BRICK	Many St. depressions, Rec. by BSSR	MF	6/99	146
1578N	W-2240	JP/WD	1999		Golden Gate	Scott MB	Pierce	1875		14"	ISP/CP	Cement pipe sections, badly crackec	MF	6/99	80
1628N		S&H	1999		Moraga St	17th Ave	18th Ave								
1583N		SEW	1999		Everglade	Gellert	Lake Merced		?	21"	VCP	Easement;collapsed @ 30-40' a -b; exfiltration(line?			49
1583N	....N	SEW	1999		Victoria	Randolph	Brotherhood	1920	?	12"	ISP	Open break @112-115', cont. cracks, mh b-c			163
1583N	.......N	SEW	1999		Revere	Griffith	Hawes MB	1930		8"	VCP	Many severe cracks/crushed mh b-c	RE		70
1583N		SEW	1999		Bridgeview	Topeka	Thornton	1941		12"	VCP	Many cracks & ss problems, invert break			185
1395N		SEW	1999		Sacramento	Grant	Kearny	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			274
1395N		SEW	1999		Larkin	Pine	Bush	1875	?	3x5	BRICK	Bad shape, many loose bricks			208
1395N	1453N	SEW	1999		Sacramento	Sansome	Battery	1908		12"	ISP	Many cracks, crushed sections, debris	MF	10/98	80
1395N	....N	SEW	1999		Pine	Polk	Larkin	1880	?	3x5	BRICK	Fairly bad shape (230'), st. depression			280
START FY 99-00															
		SEW	1999		Cesar Chavez (A	Bryant	York		?	12"	VCP	Many cracks and collapsed sections			60
		SEW	1999		Folsom	Bessie	Precita	1890	?	16"	VCP	Collapsed sections, severe offsets,open ss, fast flow			39
	....N	SEW	1999		Larkin	Grove	Hayes	1915		18"	VCP	TV'd 190', collapsed, dip, debris			92
		SEW	1999		Winding Way	Prague	Xing	1915	?	8"	VCP	Collapsed & crushed pipe, exfiltration			30
1585N	BSSR	SEW	1999		05th Ave	Balboa	Anza	1908	?	16"	VCP	Severe cracks, depn @ 8-37 c-b, many separated ss	MF		166
1585N		SEW	1999		21st Ave	Clement	California	1902	?	8"	VCP	Severe offsets,Separated ss's, st. depressions			122
1585N	1407N	SEW	1999		California	Parker	Maple	1900	?	16"	VCP	Severe open joints, st. depression; Lining rec.	MF	1/1/00	30
1586N	.....N	SEW	1999		Geary Bl. S. Side	Lyon	Baker	1879		18"	VCP	Severe multi cracks, fast flow, begin to collapse	MF		151
1586N	.....N	SEW	1999		Geary Bl. S. Side	Baker	Broderick	1879	?	18"	VCP	Multi cracks, roots, fast flow	MF		138
1586N	1732N	SEW	1999		Turk	Broderick	Divisadero	1881		16"	ISP	Cracks, collapsed section	MF	7/99	152
	99-00 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
1586N	1732N	SEW	1999		Eddy	Pierce	Steiner	1875		3x5	BRICK	Bad shape (50'), rest needs plastering	MF		280
1586N	1732N	SEW	1999		Eddy	Steiner	Fillmore	1875		3'x5'	BRICK	Bad shape, missing bricks, mortar crown & walls; dirt	MF	7/99	153
1586N		SEW	2000		Elm	Scott MB	Pierce	1908	?	15"	ISP	Egg shape cracks & offsets			55
1587N		SEW	2000		07th Ave	Moraga	Lincoln	1890	?	3'x5'	Conc/Br	Fairly bad shape; Install spray-on mortar lining.			100
1587N	....N	SEW	2000		Kirkham	6th Ave MB	7th Ave	1906		18"	VCP	43 foot run with cracks throughout			107
1590N	7291E	SEW	2000		Ocean	San Leandro	San Fernando	1913		15"	VCP	Many severe cracks @ 1-90' a-b	MUNI	4/99	40
1590N	7291E	SEW	2000		Ocean	San Fernando	Junipero Serra	1913		18"	VCP	Severe Offsets & many cracked sections	MUNI	4/99	40
1590N	7291E	SEW	2000		Ocean	Pinehurst	Manor	1913		18"	VCP	Many cracked sections	MUNI	4/99	56
1589N		SEW	2000		Clipper	Douglass	Diamond MB	1962		15"	VCP	No TV Log; Many large cracks invert, exfiltration; fast flow			82
1589N	....N	SEW	2000		Noe	26th St.	Clipper MB	1888		18"	VCP	Cracks throughout, 33' run(debris)			101
1589N	BSSR	SEW	2000		Fair Oaks	22nd St	23rd St	1878		15"	ISP	Submerged, pipe coming apart. Rec by PUC	MF		144
1589N		SEW	2000		Kingston	Mission	San Jose	1910	?	12"	VCP	Many cracks , dip, size changed to 6"			40
1588N		SEW	2000		Joost	Acadia	Brompton	1926	?	12"	ISP	Many open joints, infiltration, street depresions			150
1588N	6680E	S&H	2000		Alemany	Prentiss	Putnam		?	12"	VCP	Badly crushed pipe	MF		110
START FY 00-01															
1588N	BSSR	SEW	2000		Mt Vernon	Delano	Cayuga	1927		12"	VCP	Crushed sections @ 88-103' a-b; st. depressior	MF		81

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1588N		SEW	2000		Kensington	Merced	Claremont	1915		12"	VCP	Replace mh a-b, otherwise fair condition			100
1602N	BSSR	SEW	2000		Minna	6th St	Russ	1908	?	18"	VCP	Cracked invert @ 76-78' c-d, st depressions	MF		112
1602N	....N	SEW	2000		02nd St	Brannan	Townsend	1890	?	18"	VCP	Many cracks / replace lower 1/2 block			160
1602N		SEW	2000		Howard	01st St	Fremont	1880	?	3'x5'	BRICK	Bad shape, needs cleaning, plaster and bricks	MF		100
1605N	BSSR	SEW	2000		Sacramento	Spruce	Maple	1890	?	8"	ISP	Many seaprated ss's; infiltration	MF		110
1605N	BSSR	SEW	2000		Pierce	Green MB	Union	1885		18"	VCP	May collapse @219'-238', 0-110' replaced	MF		96
1605N	....N	SEW	2000		Wilmot	Webster	Fillmore	1900	?	10"	ISP/CP	Multiple extensive cracks/ cement pipe			120
1629N	1734N	SEW	2000	398	Union	Hyde	Larkin	1900	?	12"/18"	ISP	Crushed invert; multiple cracks, exfiltration	MF	7/99	115
1629N	......N	SEW	2000		Union	Hyde	Leavenworth	1900	?	8"/15"	ISP	3pt cracks, errosion of cement pipe sections, hole	OL	1/99	51
		SEW	2000		Union	Divisadero	Broderick	1885	?	8"/12"	VCP	Cracks/collapse, offsets, open joints		done 4/95	125
	......N	SEW	2000		Union	Jones St	Taylor St	1900		16"	CEM	Many sections collapsed, fast flow, rat	MF	7/99	130
1629N		SEW	2000	208	Kearny	Filbert	Union	1900	?	15"	VCP	Severe offsets, crushed sections, exfiltration			78
1630N	....N	SEW	2000		Polk	Greenwich MB	Filbert	1890	?	10"/18"	VCP	Continuous cracks, offsets			109
1630N		SEW	2000	199	Francisco	Polk	Van Ness	1914		12"	VCP	Many offsets & cracks; fast flow; lining recommended			50
1630N		SEW	2000		Quincy	Pine	California	1900	?	15"	VCP	Many severe cracks, breaks			84
	00-01 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
1630N	....N	SEW	1999		Sacramento	Taylor	Mason	1875		16"	ISP	Many cracks, open joint			138
1631N		SEW	1999	383	04th Avenue	Cabrillo	Balboa	1908	?	8"	VCP	Street depressions, separated ss's, open breaks			166
1631N		SEW	1999	400	10th Ave	Clement MB	Geary	1912	?	8"	ISP	Separated ss's, st depressions, low spots, exfiltration			
1631N	......N	SEW	1999		Anza	9th Avenue	10th Avenue	1907		8"	VCP	Many separated side sewers, exfiltration	MF	1/00	55
1631N	......N	S &H	1999	366	Cabrillo St	6th Ave	7th Ave	1908	?	8"	VCP	Severe open breaks, street depressions	MF		63
1632N	......N	SEW	1999		Post	Lyon	Baker	1900		18"	VCP	ss separated ; hole invert 233-239' a-b, offses, fast flov	MF	1/01	146
1632N	BSSR	SEW	1999		Grove	Baker	Broderick	1890		16"	ISP	Severe offsets, cracks; crushed section	OL		119
1632N		SEW	1999		Potomac St	Waller St	End South	1930	?	8"	VCP	Mult cracks, separated ss, infiltrtion, st. depn			79
1633N		SEW	1999		Greenwich	Webster	Fillmore								
1633N		SEW	1999		Precita South	Coso	Emmet Pl								
		SEW	2001	210	Precita South	Treat	Harrison	1900	?	16"	ISP	Multi cracks, loosing shape, fast flow, rat			
		SEW	2001	210	Precita South	Harrison	Alabama	1900	?	16"/18"	ISP	Many cracks, ss open @ 79' & 148' a-b, rat, replace a-b			
		SEW	2001	211	Pacific	Walnut	Laurel	1900	?	15"/12"	VCP	Cracks and open joints, street depressions, fast flow			
	......N	SEW	2001	402	Clement	27th Ave	26th Ave	1908	?	15"	ISP	Offset joints, many cracked sections			
START FY 01-02															
		SEW	2001	402	3rd St	4th St MB	16th St	1911		12"	VCP	Many cracked sections, collapse @ 27' b-a			
		SEW	2001		Hayes	Larkin	Polk	1890	?	3x5	BRICK	Bad shape, severe sags, missing bricks,bulging			190
	BSSR	SEW	2001		Sterling	I-80 ramp	Bryant	1900	?	12"	CEM	Multi cracks; ready to collapse; Rec. lining	MO	10/98	56
	BSSR	SEW	2001		Jones	Bernard	Pacific	1906	?	12"	VCP	Multiple cracked & collapsed sections	MF	n/a	40
	....N	SEW	2001		Bryant	7th St	Gilbert	1876	?	3x5	BRICK	Bad shape, cracks on crown, ready to cave in	MF		119
	....N	SEW	2001		Townsend	7th St Mb	8th St Mb	1921		12"	VCP	Dips, Cracks, Crushed			167
		SEW	2001		Esmt blk #4315/	Minnesota	3rd St	1949		12"	VCP	Several severe cracks & collapses			145
		SEW	2001		Esmt Blk #4317	Indiana	Minnesota	1949		12"	VCP	Severe multiple cracks			74
		SEW	2001		22nd Ave	Irving	Lincoln	1910	?	18"	VCP	Many active street depressions.			190
		SEW	2001		Folsom	18th St MB	17th St	1946		15"	VCP	Cont cracks 55-130', depression 157' b-c			145
	....N	SEW	2001		Rincon	Bay Bridge	Bryant	1917	?	12"	VCP	Collapsed			70
	....N	SEW	2001		Harrison	8th St	7th St	1880	?	3x5	BRICK	Missing mortar, loose bricks, out of rounc			550

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST YEAR	TAP E #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
	.....N	SEW	2001		Mission	13th St	14th St	1875	?	3'x5'	Brick	Bad shape, crown sagging, ready to collapse	MF		205
	....N	SEW	2001		08th St	Market	Intersection	?		15"	VCP	Cracked sects. replace (a-b) across Marke	RE		50
	01-02 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1727N	SEW	2002		Leavenworth	Washington	Jackson	1900	?	16"	VCP	Many cracks; invert break	MF	7/99	68
	....N	SEW	2002		Leavenworth	Greenwich	Lombard	1890	?	16"	VCP	Crushed Pipe, Numerous Cracks			110
	....N	SEW	2002		Geary	Mason	Powell	1880		3x5	BRICK	Bad shape, crown buckled, mortar, bricks missing	MF		115
	....N	SEW	2002		Jones	Filbert	Lombard	1919		12"	VCP	Numerous Cracks			213
	....N	SEW	2002		Buchanan	Greenwich	Lombard St	1887		18"	VCP	Cracks, offsets, open joints			120
			2002		Stonestown Trestle Removal							Trestle is an attractive nuisance			286
			2002		Chinatown Alleys(3)										150
	BSSR	SEW	2002		South Hill	Prague	Geneva	1915		8"	ISP	Broken sections, cracks	MF/OL		60
	....N	SEW	2002		Washburn	Howard	Mission	1900	?	3x5	BRICK	Fairly bad shape, bricks, broken s/s			350
	BSSR	SEW	2002		Bayshore(W Sid	Cortland	Oakdale	1928		12"	VCP	Many bad cracks & breaks	MF		93
START FY 02-03															
		SEW	2002		Esmt Block#113	End North	Anza	1935		8"	VCP	Many separated ss's from main, exfiltration			75
		SEW	2002		City View Way	Skyview	Knollview	1951		8"	VCP	Street depressions; crushed, open joints, exfiltration, fast flow			57
		SEW	2002		19th St	Collingwood	Castro	1887		18"	ISP	Open joints, bad cracks			90
		SEW	2002		O'Shaughnessy	Portola	Del Vale MB	1939		15"	VCP	Badly cracked, no tv log, sewer lining recommended		paved '96	70
		SEW	2002		Capp	21st St	20th St	1874	?	15"	CEM	Cement pipe, cracks			145
		SEW	2002		Liberty	Guerrero	Valencia	1875		15"	VCP/CP	SS discont'd @173', cracked sections			150
		SEW	2002		37th Ave	Balboa St	Cabrillo St	1920	?	18"	ISP	Offsets, several cracked sections, fast flow			207
		SEW	2002		Folsom	Precita	Army MB	1890	?	16"	VCP	Severe offsets, open invert, exfiltration, fast flow			49
		SEW	2002		Ashbury	Waller	Haight	1890		18"	VCP	Open joints, cracks; Replace Haig-Ash int.; fast flow			111
	BSSR	SEW	2002	208	Walter	Duboce	14th St	1890	?	8"	VCP	Many open breaks, separated ss, exfiltration	OL		148
		SEW	2002		Cole	Carl	Frederick	1888		3'x5'	BRICK	Bad shape			96
		SEW	2002	199	Pacific Ave	Presidio	Walnut	1900	?	12"	VCP	Crushed sections, bad side sewer, fast flow			112
		SEW	2002	398	26th Street	San Jose	Valencia	1889	?	15"	VCP	Open breaks, separated ss's, fast flow			64
	02-03 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	1453N	SEW	2003		Kearny	Maiden Ln	Geary	1875	?	3'x5'	Brick	Bad shape, crown sagging, missing bricks	RE	7/98	77
	BSSR	SEW	2003		Moraga	23rd Ave	22nd Ave	1926		12"	ISP		MF		77
		SEW	2003		Lawton	21st Ave	23rd Ave	1925		15"/21"	VCP				177
		SEW	2003	382	11th Ave	Irving	Lincoln	1903	?	10"/12"	VCP	Many active street depressions, severe offsets,ss problems			
		SEW	2003		21st Ave	Moraga	Lawton	1925		15"	ISP				190
		SEW	2003		Russia	Madrid	Lisbon	1907	?	16"	VCP	Cracks, larghe street depression'			
1394N		SEW	hold		Kirkham	21st Ave	26th Ave					New Auxiliary Sewer 12"? VCP			216
				208	Morris	Harrison	Bryant	1935	?	12"	VCP	Cracks, offsets, dip	OL	1999	
												TOTAL PRIOTITY 2 PROJECTS=			**37,386**
												TOTAL EMERGENCY, ACCELERATED, & PRIOTITY 1 PROJECTS=			**$8,475**
												PRIORITY 3 PLANNED PROJECTS (not detailed)=			**$6,900**
												GRAND TOTAL=			**######**

SF
P85.93
:2
4/8/99(?)

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 410 (4/8/99 ?)

~~March 11, 1999~~ ← ?

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Jean To	554-8298
James Walsh	554-8272

Street Construction Coordination Center

Cynthia Chono	554-6196
Joe Norris	554-8274

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Berhane Gaime	554-6201
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

Alla Rykov	557-9971

PUC UEB

Henry Anderson	648-6882
Mohammad Rohgadai	554-1852

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

Karen Kubick	550-2971

Redevelopment Agency

(Representative not present)

Caltrans

Dean Drablos	330-6537
Bahman Zarechian	510-286-4425

Caltrans Public Information

(Representative not present)

Pacific Bell

(Representative not present)

Pacific Gas & Electric

(Representative not present)

S F Thermal

(Representative not present)

Allstar / Metro Media

(Representative not present)

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

(Representative not present)

RCN

Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500 x-3346
Lowell Volk	863-8500 x-4428

Underground Construction

(Representative not present)

DOCUMENTS DEPT.
JUN 03 1999
SAN FRANCISCO
PUBLIC LIBRARY

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 410

1. The members introduced themselves around the table.

2. The March 11, 1998 Minutes were approved.

3. X-1104 Monthly Report

Ms. Chono reported that SCCC is looking at electronic distribution for X-1104 reports, as requested by some utilities. We will be canvassing for opinions, or interested parties can Call Ms Chono.

4. SFWD Reservoir Inlet Piping

Ms. Kubick discussed the forthcoming project near Laguna Honda. SFWD is upgrading its disinfection methods, which will require new pipelines and pump stations:

- Pump Station at Clarendon and Laguna Honda Blvd., with a pipeline up Clarendon to the Summit Reservoir and to Stanford Hts. Work is projected to begin in November of 1999 and continue until November of 2000.

- Pump Station at Merced Manor with a pipeline to the Sutro Reservoir. The project will be divided into two or three contracts, to begin in November of 2000 and last two years.

Mr Drablos noted that the pipeline in Sloat Blvd will require a Caltrans permit.

Ms Chono asked if these projects were part of a larger program. Ms Kubick replied that they are part of a 16 year program in which SFWD is still evaluating some of the routing. Ms Chono added that we will need to find and use opportunities for coordination.

See **Attachment A.**

5. New Business

Mr Drablos introduced his new supervisor, Mr Zarechian, who is replacing Mr Franklin due to Mr Franklin's recent promotion.

Ms Chono announced that Mr Troyan has accepted a position as City Engineer for Los Angeles effective the end of April. Selection of a successor is still in progress. Ms Chow has accepted a position with the San Jose Airport, also as of the end of April. Until her replacement has been selected, clearances and the like should be addressed to Mr Norris.

There was some discussion of the relative purposes of CULCOP and the SCCC meetings, which appear to involve the same people and the same issues. We will discuss this, and a possible new site for CULCOP, at the May 13 meeting. See **Attachment B**.

The next meeting will be at 10:00 am Thursday, June 10, 1999, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

Attachment A

SFWD Projects

CITY AND COUNTY OF SAN FRANCISCO
PUBLIC UTILITIES COMMISSION

SAN FRANCISCO WATER DEPARTMENT
CITY DISTRIBUTION DIVISION

CULCOP Meeting
April 8, 1999 - 10am

SFPUC Items

1. Pipelines from Clarendon to Summit and Stanford Heights Reservoirs
    a) Construction Schedule 11/99 – 11/00
    b) Moratorium issues on Laguna Honda
        i) Dewey St. to Merced St. will be available November 1999.
        ii) Idora St. to Portola St. will be available September 1999.
        iii) Balceta Ave. to Iodora St. will be available September 2000.

2. Pipeline from Central Pump Station to Sutro Reservoir
    a) Construction Schedule 11/00 – 8/02
    (2-phases)
    b) No identified moratorium issues

SFPUC Contacts:

Karen Kubick, PM	(415) 550-2971
Mohammad Kohgadai, PE	(415) 554-1852

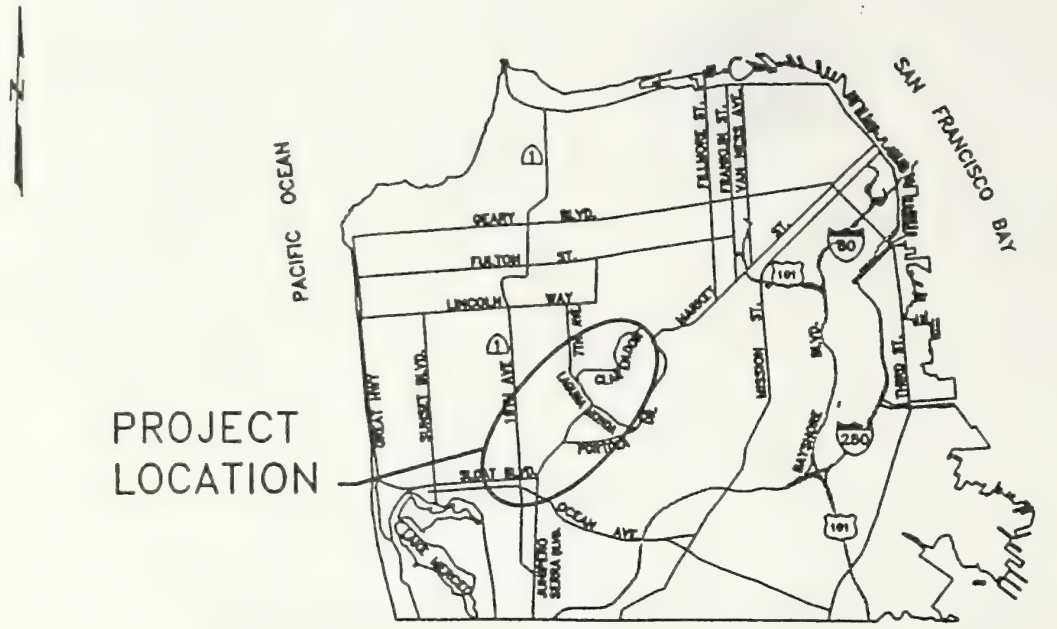
PACIFIC OCEAN
SAN FRANCISCO BAY
PROJECT LOCATION
N
GEARY BLVD.
FULTON ST.
LINCOLN WAY
SLOAT BLVD.
OCEAN AVE.
PORTOLA DR.
LAGUNA HONDA
CLARENDON
7TH AVE
19TH AVE.
SUNSET BLVD.
GREAT HWY
JUNIPERO SERRA BLVD.
LAKE MERCED
MARKET ST.
MISSION ST.
BAYSHORE BLVD.
THIRD ST.
FILLMORE ST.
FRANKLIN ST.
VAN NESS AVE.
1
101
80
280

VICINITY MAP

NOT TO SCALE

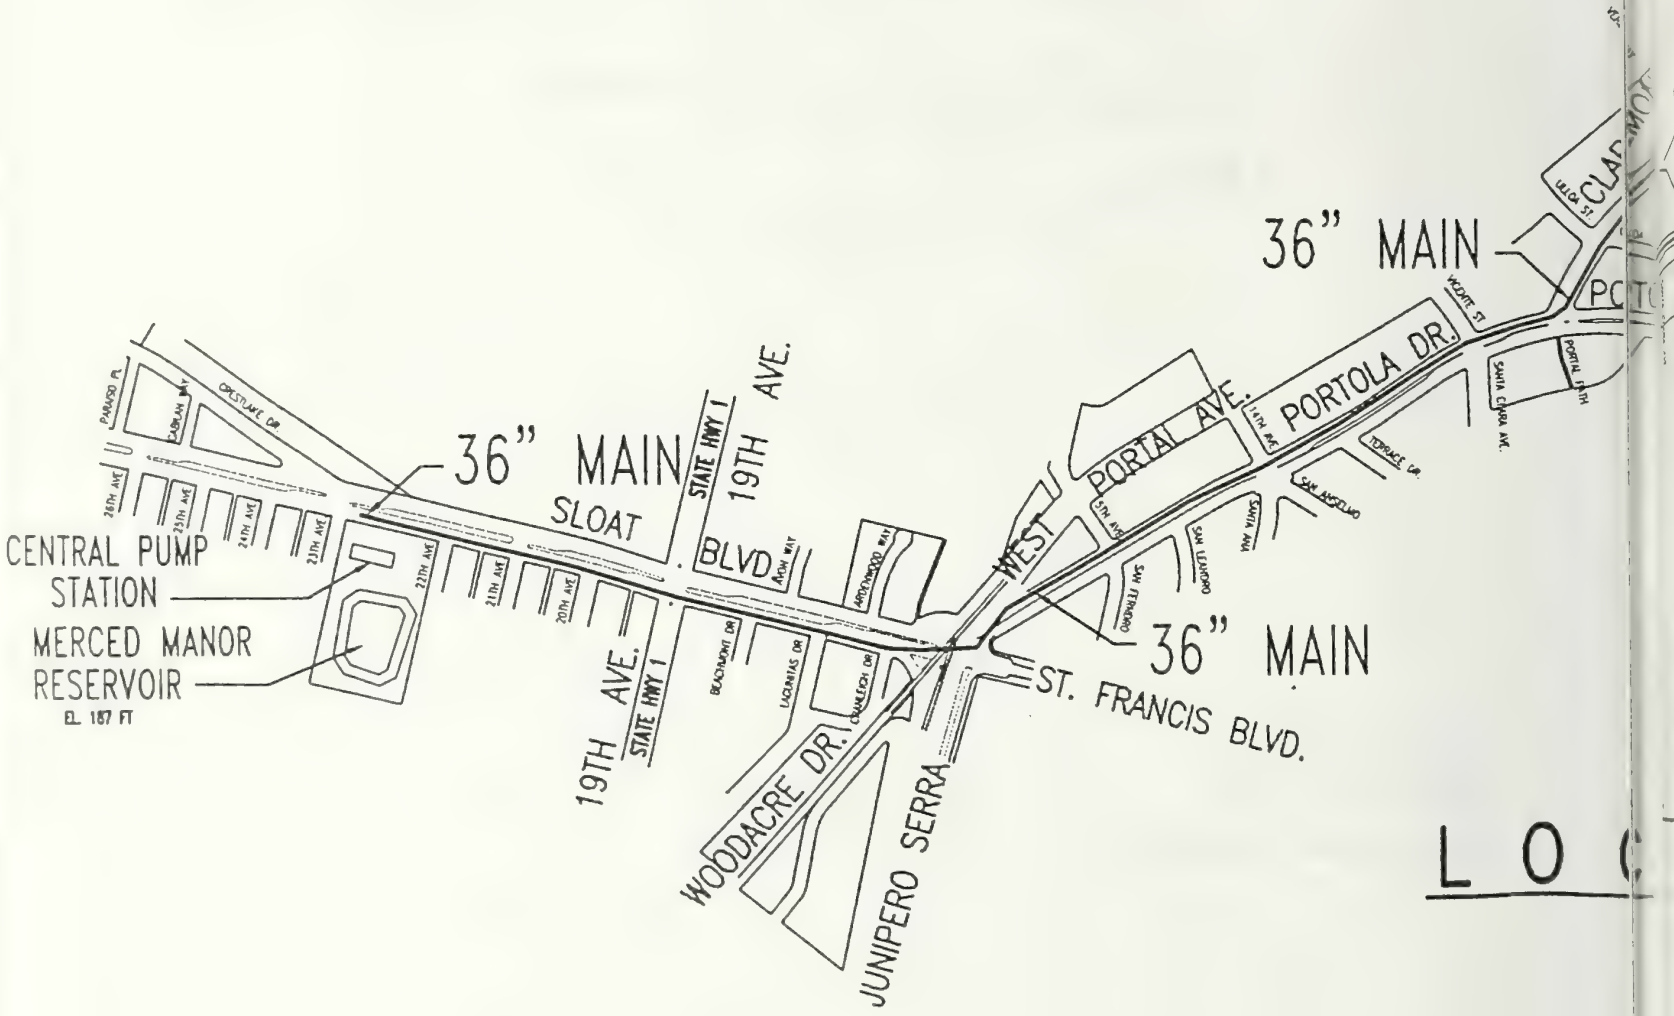
N
36" MAIN
36" MAIN
36" MAIN
CENTRAL PUMP STATION
MERCED MANOR RESERVOIR
EL 187 FT
SLOAT BLVD
19TH AVE.
STATE HWY 1
19TH AVE.
STATE HWY 1
PORTAL AVE.
PORTOLA DR.
WEST
ST. FRANCIS BLVD.
WOODACRE DR.
JUNIPERO SERRA
PARAISO PL.
CRESTLAKE DR.
CAPITAL WAY
26TH AVE
25TH AVE
24TH AVE
23TH AVE
22TH AVE
21TH AVE
20TH AVE
BEACHMONT DR
LAGUNITAS DR
CRAGMONT DR
ASHWOOD WAY
ARDENWOOD WAY
SAN FERNANDO
SAN LEANDRO
SANTA ANA
SAN ANSELMO
TERRACE DR.
SANTA CLARA AVE.
PORTOLA PATH
VICENTE ST.
14TH AVE.
5TH AVE
ULLOA ST.
CLAR
POT

LOC

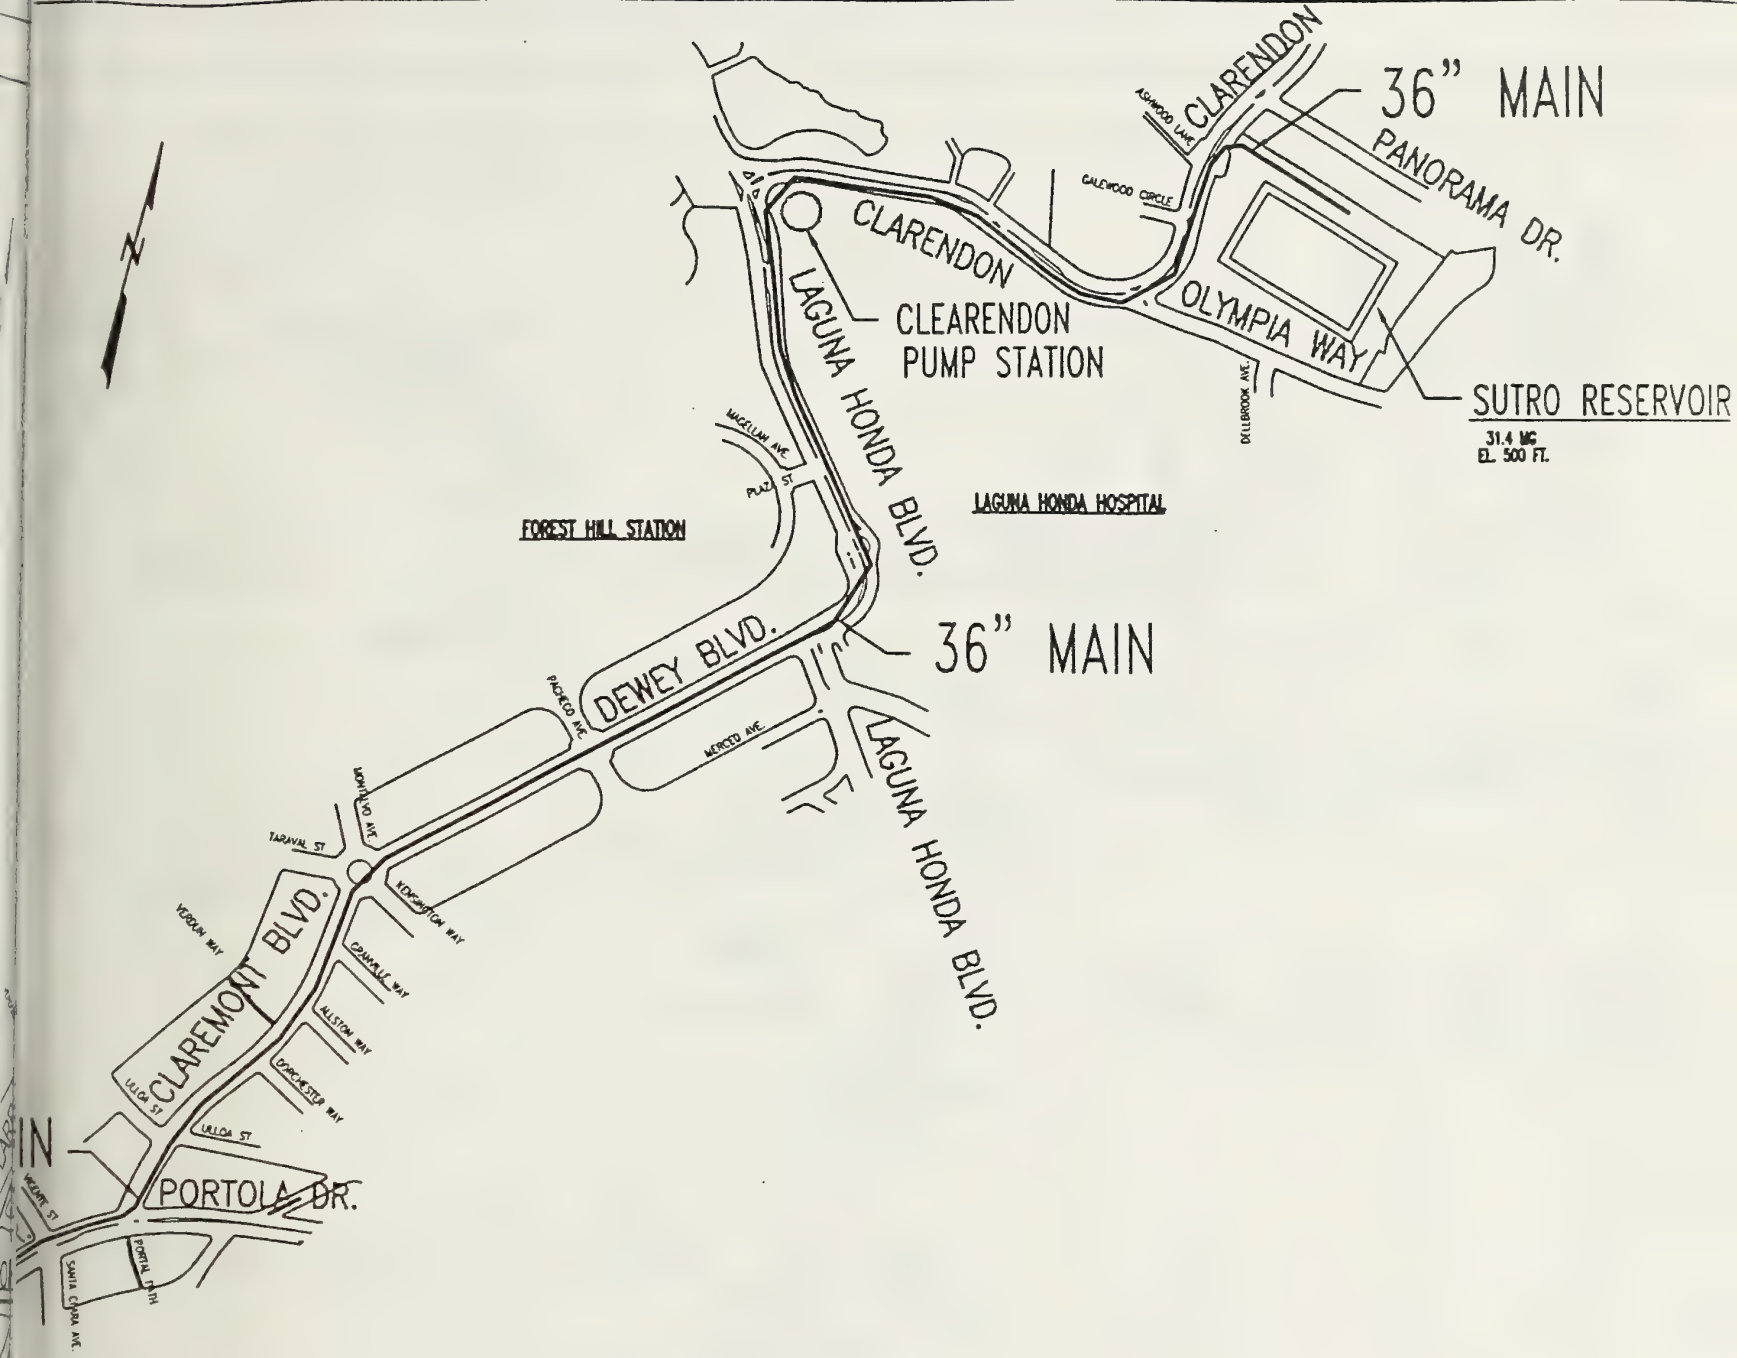
36" MAIN
CLARENDON
ASHWOOD LANE
PANORAMA DR.
GALEWOOD CIRCLE
CLARENDON
CLEARENDON PUMP STATION
OLYMPIA WAY
DELLBROOK AVE.
SUTRO RESERVOIR
31.4 MG
EL. 500 FT.
LAGUNA HONDA BLVD.
MAGELLAN AVE.
PLAZA ST
FOREST HILL STATION
LAGUNA HONDA HOSPITAL
36" MAIN
DEWEY BLVD.
PACHECO AVE.
MERCED AVE.
LAGUNA HONDA BLVD.
MONTALVO AVE.
TARAVAL ST
KENSINGTON WAY
VERDUN WAY
CLAREMONT BLVD.
GRANVILLE WAY
ALLSTON WAY
DORCHESTER WAY
ULLOA ST
ULLOA ST
IN
VICENTE ST
PORTOLA DR.
PORTAL PATH
SANTA CLARA AVE.

LOCATION MAP

NOT TO SCALE

36" MAIN INSTALLATION IN
SUTRO RESERVOIR INLET AND OUTLET

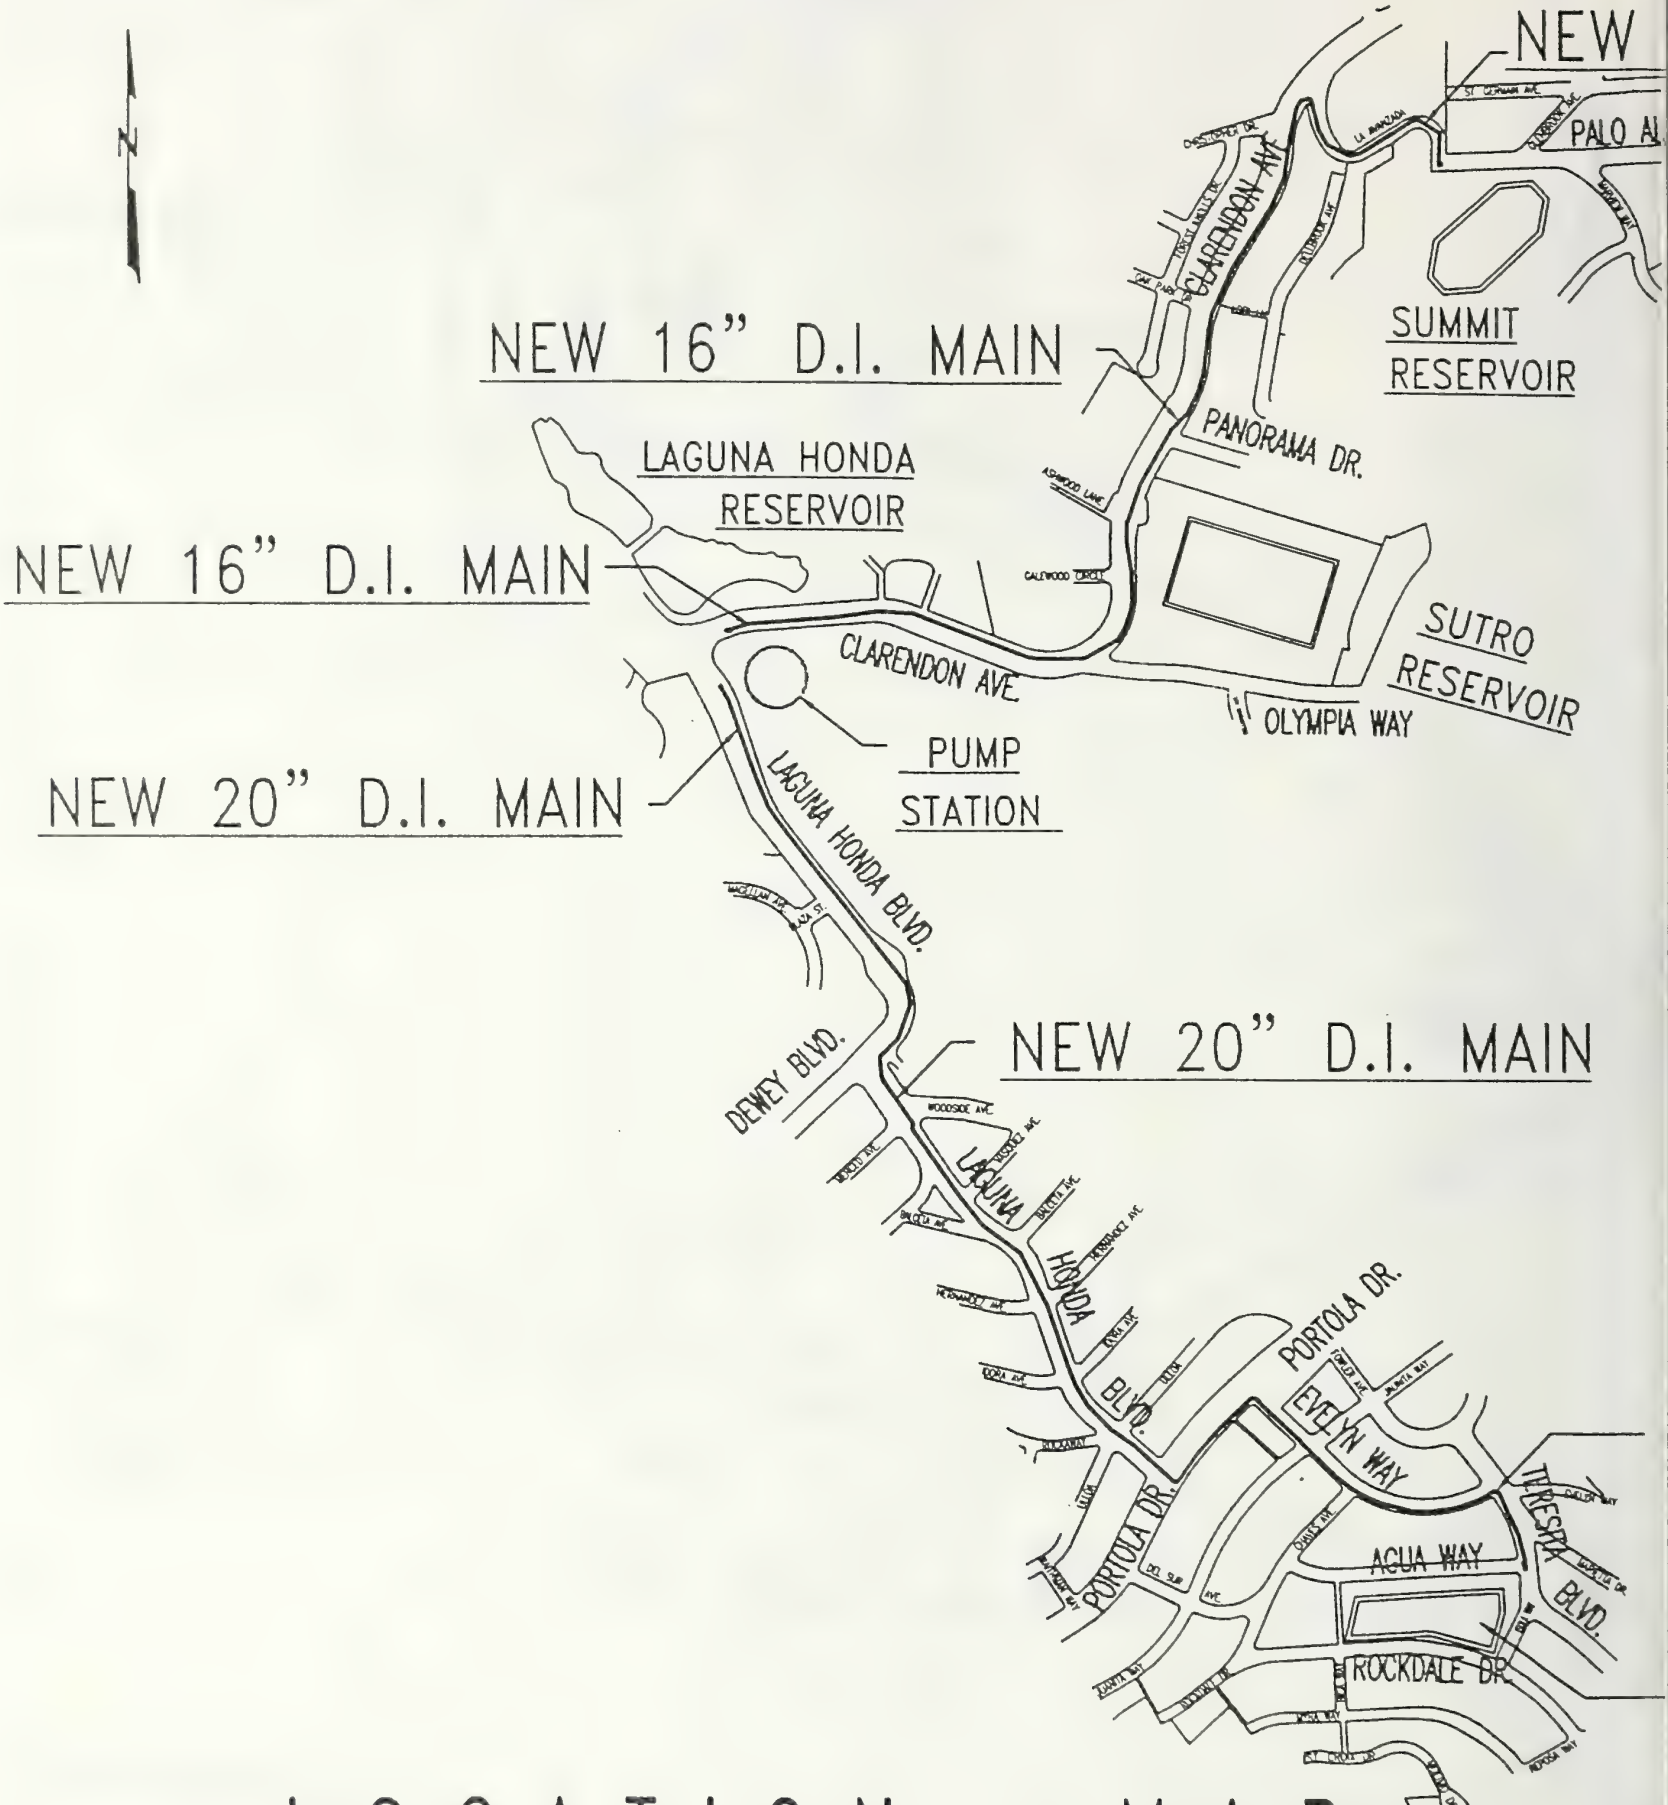
N
NEW 1
PALO AL
ST. GERMAIN AVE.
LA AVANZADA
CHRISTOPHER DR.
FOREST KNOLLS DR.
OAK PARK DR.
CLARENDON AVE.
DELLBROOK AVE.
SUMMIT RESERVOIR
NEW 16" D.I. MAIN
PANORAMA DR.
ASHWOOD LANE
LAGUNA HONDA RESERVOIR
NEW 16" D.I. MAIN
CLARENDON AVE.
SUTRO RESERVOIR
OLYMPIA WAY
PUMP STATION
NEW 20" D.I. MAIN
LAGUNA HONDA BLVD.
DEWEY BLVD.
NEW 20" D.I. MAIN
WOODSIDE AVE.
VASQUEZ AVE.
BALCETA AVE.
HERNANDEZ AVE.
LAGUNA HONDA BLVD.
DORA AVE.
ULLOA
ROCKAWAY
PORTOLA DR.
EVELYN WAY
FOWLER AVE.
JUANITA WAY
PORTOLA DR.
DEL SUR AVE.
AGUA WAY
TERESITA BLVD.
ROCKDALE DR.
MESA WAY
ST. CROIX DR.

LOCATION MAP

NOT TO SCALE

\LARRY\MAP100

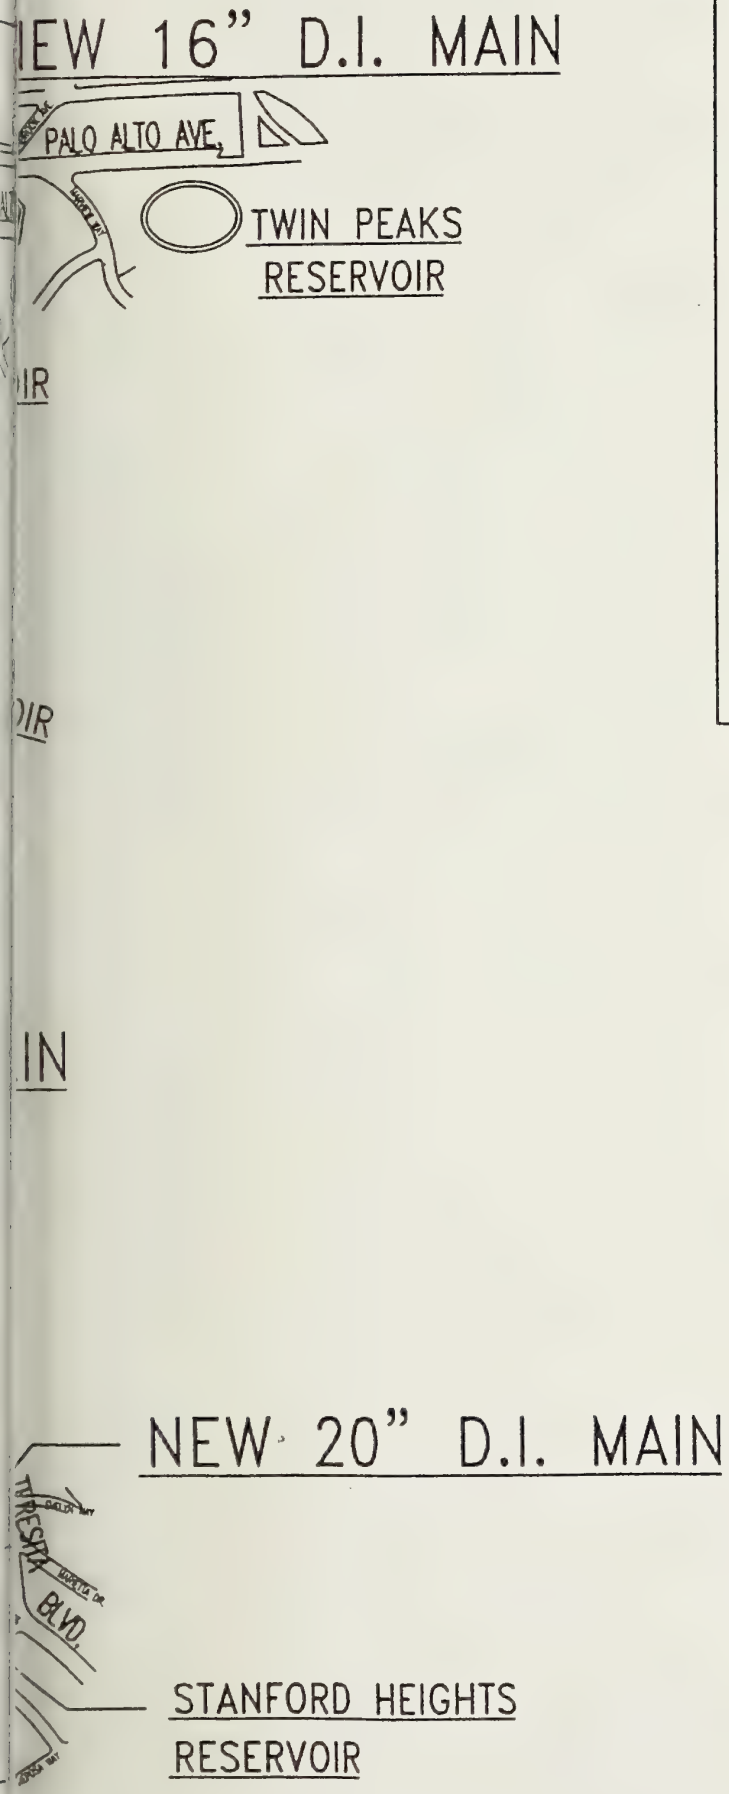
EW 16" D.I. MAIN
PALO ALTO AVE.
TWIN PEAKS RESERVOIR
IR
IR
IN
NEW 20" D.I. MAIN
TERESITA BLVD.
STANFORD HEIGHTS RESERVOIR

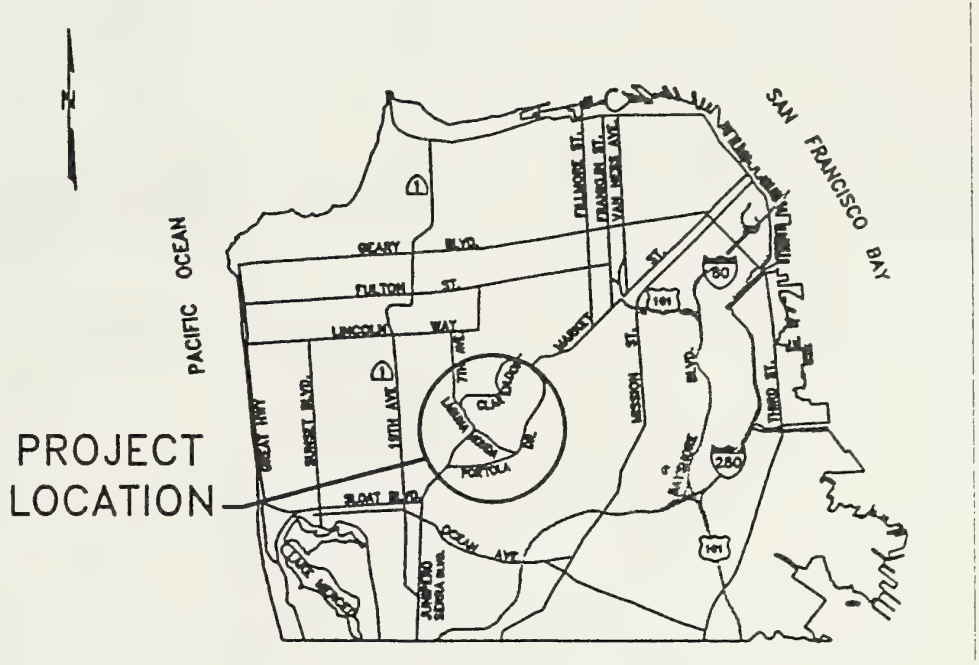
N
PACIFIC OCEAN
SAN FRANCISCO BAY
PROJECT LOCATION
GEARY BLVD.
FULTON ST.
LINCOLN WAY
GREAT HWY
SUNSET BLVD.
19TH AVE.
SLOAT BLVD.
OCEAN AVE.
MARKET ST.
MISSION ST.
FILLMORE ST.
FRANKLIN ST.
VAN NESS AVE.
THIRD ST.
PORTOLA DR.
LAGUNA HONDA
CLARENDON
JUNIPERO SERRA BLVD.
LAKE MERCED
BAYSHORE BLVD.
1
80
101
280

VICINITY MAP

NOT TO SCALE

CLARENDON PUMP STATION AND PIPELINES
TO STANFORD HEIGHTS AND SUMMIT RESERVOIRS

Attachment B.

CULCOP / SCCC Roles and Formats

CULCOP and SCCC

The CULCOP and SCCC meeting forums are both mandated by Ordinance to discuss coordination of work in the City's streets. So far, they appear to cover the same topics and to involve the same people, which is redundant. We need to clarify the purview for each forum and the persons who should attend each.

SCCC has the stated purpose of attempting an ideal of "invisible construction" in the streets, in the sense of minimal disruption to users and residents, by coordinating schedules at the program level to reduce the frequency and shorten the duration of projects in each block. The original purpose of CULCOP was to facilitate cost-effective paving by avoiding digups in newly paved streets. and has evolved to facilitate mutual cooperation among all entities working in the streets, by resolving project-level conflicts. It has also been a means of disseminating other information such as Code changes. The distinction between program level and project level should help to differentiate the topics and attendance between the two forums.

For example, the motive driving the previous "clearance" model for paving was that we are Federally mandated to use a pavement management system based on cost-effective maintenance. For that purpose, timing is critical, since a delay of a few years can mean much higher cost because the method of maintenance has escalated. The same is true of any infrastructure maintenance program. Mutual accommodation must allow for the cost escalation associated with deferred maintenance. It must also consider each project globally, from concept through budgeting, design, procurement, and contracting process, as well as scope and duration of the work itself. Clearance / coordination is then an SCCC matter, while the usual hiccups and surprises during construction belong with CULCOP.

The shift from pavement driven to project driven coordination in CULCOP has not been reflected in the nomenclature and format of the Status Report. We no longer focus on "clearing" streets for paving, and instead have moved to "coordinating" work in each block to comply with the Excavation code's five year horizon, with paving as the last activity in a multi-project site. The current wave of telco installations has increased the number of entities to coordinate. The need to retrieve several of our infrastructure systems at (or past) the end of their useful life has increased the pace of work for the affected agencies. The distinction between sequenced and joint projects needs to be reflected. Displaying that information usefully within a reasonable page count will be difficult. Perhaps we can devise an electronic format which everyone can easily use.

SF
285.93
#1
5/13/99

City and County of San Francisco **Department of Public Works**
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Agenda

Location:	1680 Mission, 4th floor conference room
Date:	Thursday, May 13, 1999 10am to 11:30am.
Subject:	Committee Meeting 411- Coordination of Street Construction

1.	Introduction	
2.	Approval of Minutes for March 11th Meeting	
3.	X1104 Monthly Report	Cynthia Chono
4.	RCN System Presentation	Sieg Weber
5.	CULCOP / SCCC Roles and Formats	All
6.	Other New Business	All

Next Meeting: 2nd Thursday of Each Month
Thursday June 10, 1999 at 10:00 A. M.
Conference Room
1680 Mission Street, 4th Floor

DOCUMENTS DEPT.
JUN 0 3 1999
SAN FRANCISCO
PUBLIC LIBRARY

06-03-99A10:57 RCVD

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-8274, at leaStreet72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-8274.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 1680 Mission Street, the Fourth Floor Conference Room. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L on Mission Street; # 42 on Van Ness Avenue;
   #26 on Valencia Street; #71 on Noriega Street; #9 on Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 410

March 11, 1999 ?

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Jean To	554-8298
James Walsh	554-8272

Street Construction Coordination Center

Cynthia Chono	554-6196
Joe Norris	554-8274

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Berhane Gaime	554-6201
Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

Alla Rykov	557-9971

PUC UEB

Henry Anderson	648-6882
Mohammad Rohgadai	554-1852

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

Karen Kubick	550-2971

Redevelopment Agency

(Representative not present)

Caltrans

Dean Drablos	330-6537
Bahman Zarechian	510-286-4425

Caltrans Public Information

(Representative not present)

Pacific Bell

(Representative not present)

Pacific Gas & Electric

(Representative not present)

S F Thermal

(Representative not present)

Allstar / Metro Media

(Representative not present)

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

(Representative not present)

RCN

Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500 x-3346
Lowell Volk	863-8500 x-4428

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 410

1. The members introduced themselves around the table.

2. The March 11, 1998 Minutes were approved.

3. X-1104 Monthly Report

Ms. Chono reported that SCCC is looking at electronic distribution for X-1104 reports, as requested by some utilities. We will be canvassing for opinions, or interested parties can Call Ms Chono.

4. SFWD Reservoir Inlet Piping

Ms. Kubick discussed the forthcoming project near Laguna Honda. SFWD is upgrading its disinfection methods, which will require new pipelines and pump stations:

- Pump Station at Clarendon and Laguna Honda Blvd., with a pipeline up Clarendon to the Summit Reservoir and to Stanford Hts. Work is projected to begin in November of 1999 and continue until November of 2000.

- Pump Station at Merced Manor with a pipeline to the Sutro Reservoir. The project will be divided into two or three contracts, to begin in November of 2000 and last two years.

Mr Drablos noted that the pipeline in Sloat Blvd will require a Caltrans permit.

Ms Chono asked if these projects were part of a larger program. Ms Kubick replied that they are part of a 16 year program in which SFWD is still evaluating some of the routing. Ms Chono added that we will need to find and use opportunities for coordination.

See **Attachment A**.

5. New Business

Mr Drablos introduced his new supervisor, Mr Zarechian, who is replacing Mr Franklin due to Mr Franklin's recent promotion.

Ms Chono announced that Mr Troyan has accepted a position as City Engineer for Los Angeles effective the end of April. Selection of a successor is still in progress. Ms Chow has accepted a position with the San Jose Airport, also as of the end of April. Until her replacement has been selected, clearances and the like should be addressed to Mr Norris.

There was some discussion of the relative purposes of CULCOP and the SCCC meetings, which appear to involve the same people and the same issues. We will discuss this, and a possible new site for CULCOP, at the May 13 meeting. See **Attachment B**.

The next meeting will be at 10:00 am Thursday, June 10, 1999, the second Thursday of the month, in the fourth floor conference room at 1680 Mission Street.

Attachment A

SFWD Projects

CITY AND COUNTY OF SAN FRANCISCO
PUBLIC UTILITIES COMMISSION

SAN FRANCISCO WATER DEPARTMENT
CITY DISTRIBUTION DIVISION

CULCOP Meeting
April 8, 1999 - 10am

SFPUC Items

1. Pipelines from Clarendon to Summit and Stanford Heights Reservoirs
    a) Construction Schedule 11/99 – 11/00
    b) Moratorium issues on Laguna Honda
        i) Dewey St. to Merced St. will be available November 1999.
        ii) Idora St. to Portola St. will be available September 1999.
        iii) Balceta Ave. to Iodora St. will be available September 2000.

2. Pipeline from Central Pump Station to Sutro Reservoir
    a) Construction Schedule 11/00 – 8/02
    (2-phases)
    b) No identified moratorium issues

SFPUC Contacts:

Karen Kubick, PM	(415) 550-2971
Mohammad Kohgadai, PE	(415) 554-1852

1990 NEWCOMB AVENUE, SAN FRANCISCO, CA 94124-1671 TEL: (415) 550-2971 / FAX (415) 920-4016

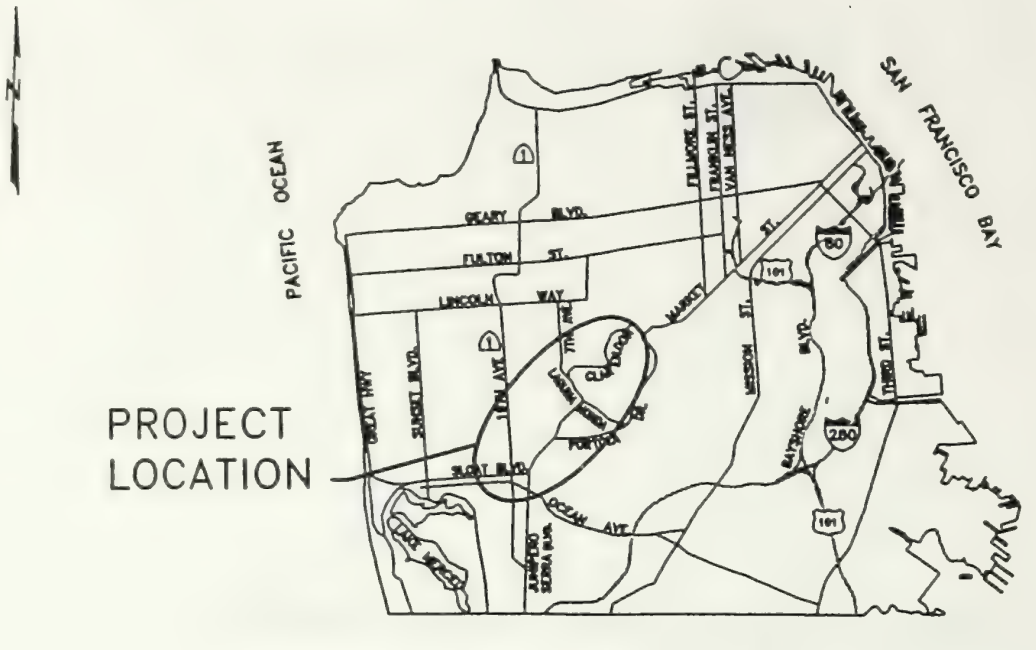
N
PACIFIC OCEAN
SAN FRANCISCO BAY
PROJECT LOCATION
GEARY BLVD.
FULTON ST.
LINCOLN WAY
GREAT HWY
SUNSET BLVD.
19TH AVE.
7TH AVE.
CLARENDON
LAGUNA HONDA
PORTOLA DR.
SLOAT BLVD.
OCEAN AVE.
JUNIPERO SERRA BLVD.
LAKE MERCED
MARKET ST.
MISSION ST.
FILLMORE ST.
FRANKLIN ST.
VAN NESS AVE.
BAYSHORE BLVD.
THIRD ST.
1
80
101
280

VICINITY MAP

NOT TO SCALE

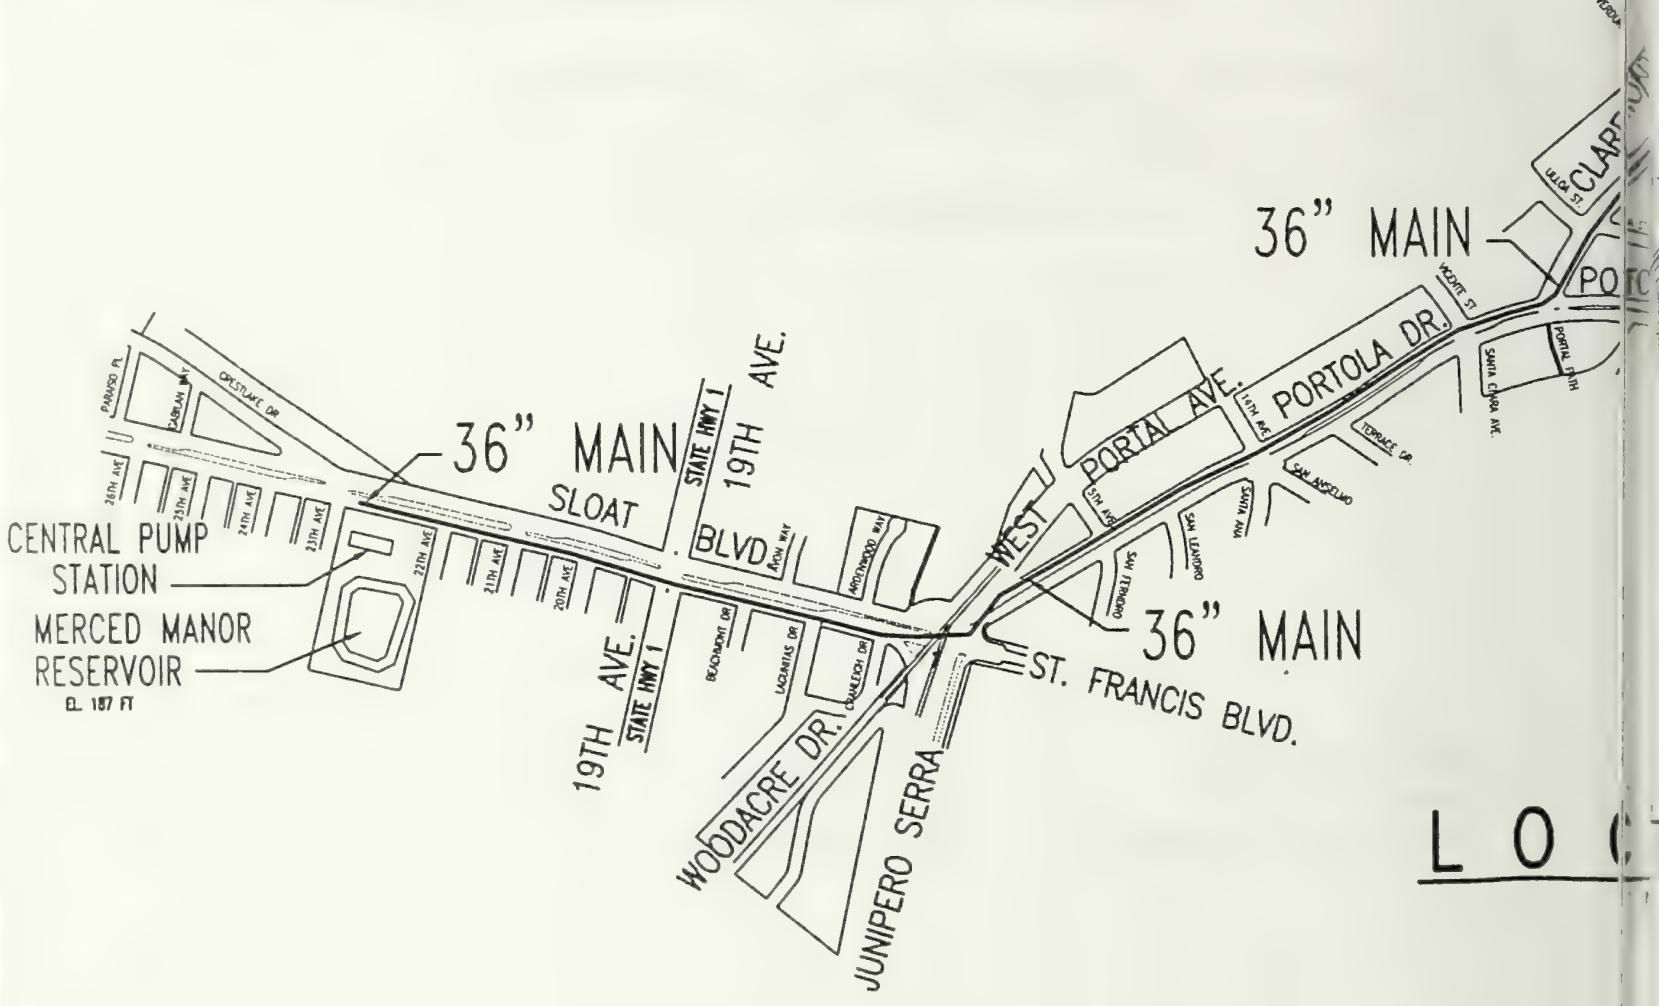
36" MAIN
36" MAIN
36" MAIN
CENTRAL PUMP STATION
MERCED MANOR RESERVOIR
EL. 187 FT
SLOAT BLVD
19TH AVE.
STATE HWY 1
19TH AVE.
STATE HWY 1
PARAISO PL.
CRESTLAKE DR
26TH AVE
25TH AVE
24TH AVE
23RD AVE
22ND AVE
21ST AVE
20TH AVE
BEACHMONT DR
LAGUNITAS DR
CHARLEIGH DR
AVON WAY
ARDENWOOD WAY
WEST PORTAL AVE.
PORTOLA DR.
ST. FRANCIS BLVD.
WOODACRE DR.
JUNIPERO SERRA
SAN FERNANDO
SAN LEANDRO
SANTA ANA
SAN ANSELMO
TERRACE DR.
SANTA CLARA AVE.
VICENTE ST
ULLOA ST
CLAR
POR

L O C

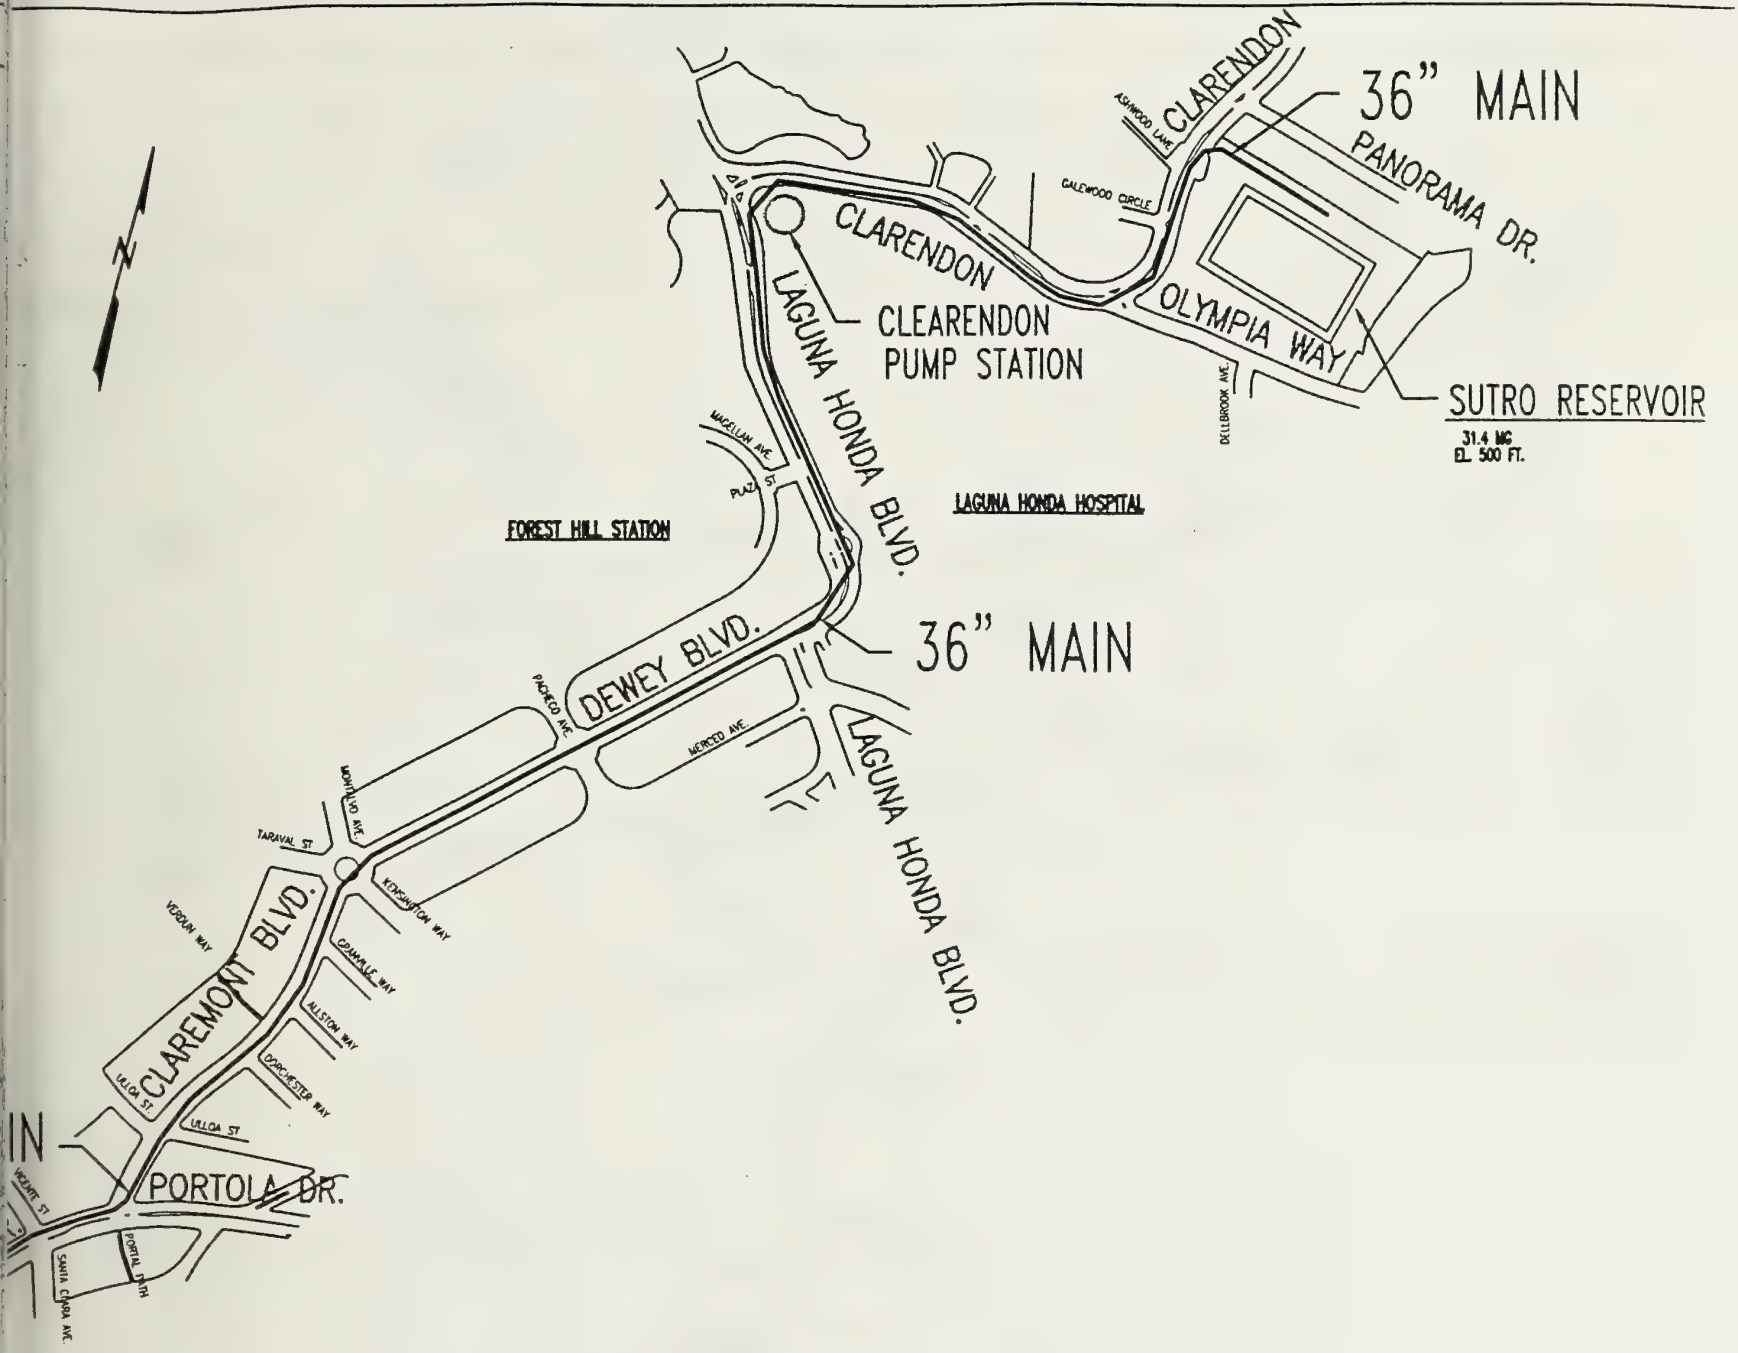
N
CLARENDON
ASHWOOD LANE
36" MAIN
PANORAMA DR.
GALEWOOD CIRCLE
CLARENDON
OLYMPIA WAY
CLEARENDON PUMP STATION
SUTRO RESERVOIR
31.4 MG
EL. 500 FT.
DELLBROOK AVE.
LAGUNA HONDA BLVD.
MAGELLAN AVE.
PLAZA ST
FOREST HILL STATION
LAGUNA HONDA HOSPITAL
36" MAIN
DEWEY BLVD.
PACHECO AVE.
MERCED AVE.
LAGUNA HONDA BLVD.
MONTALVO AVE.
TARAVAL ST
KENSINGTON WAY
VERDUN WAY
CLAREMONT BLVD.
GRANVILLE WAY
ALLSTON WAY
DORCHESTER WAY
ULLOA ST.
ULLOA ST
IN
PORTOLA DR.
VICENTE ST
PORTAL PATH
SANTA CLARA AVE.

LOCATION MAP

NOT TO SCALE

36" MAIN INSTALLATION IN
SUTRO RESERVOIR INLET AND OUTLET

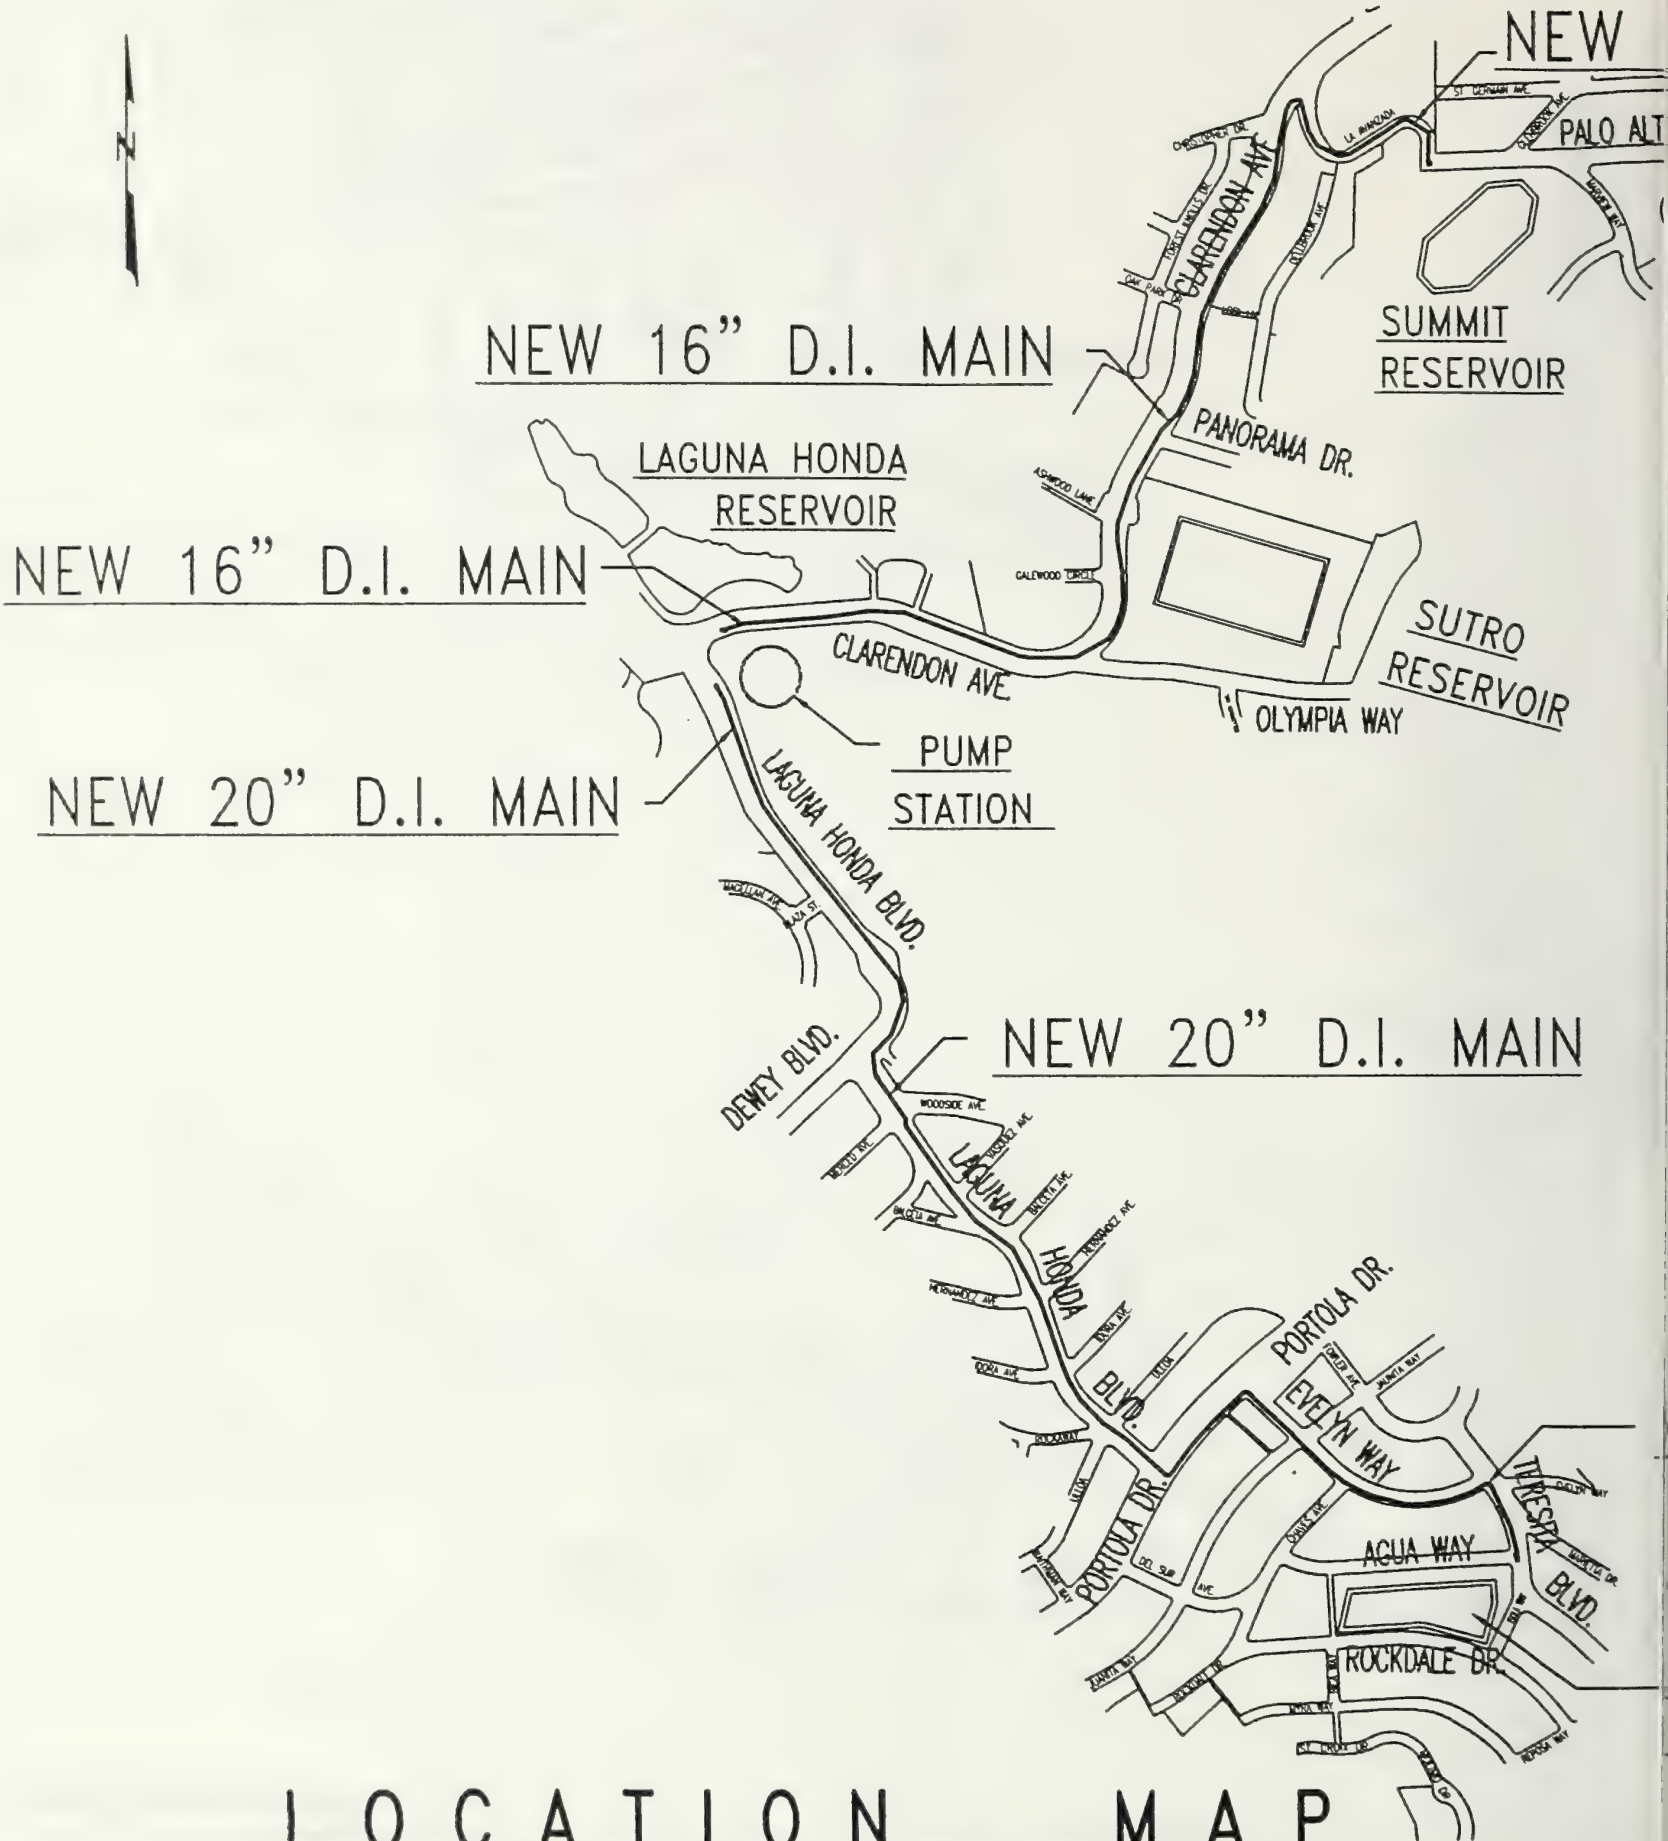
N
NEW
ST. GERMAIN AVE.
PALO ALTO
LA AVANZADA
CLARENDON AVE.
SUMMIT RESERVOIR
NEW 16" D.I. MAIN
PANORAMA DR.
LAGUNA HONDA RESERVOIR
NEW 16" D.I. MAIN
GALEWOOD CIRCLE
SUTRO RESERVOIR
CLARENDON AVE.
OLYMPIA WAY
PUMP STATION
NEW 20" D.I. MAIN
LAGUNA HONDA BLVD.
DEWEY BLVD.
NEW 20" D.I. MAIN
WOODSIDE AVE.
LAGUNA HONDA BLVD.
PORTOLA DR.
EVELYN WAY
PORTOLA DR.
AGUA WAY
TERESITA BLVD.
ROCKDALE DR.

L O C A T I O N   M A P

NOT TO SCALE

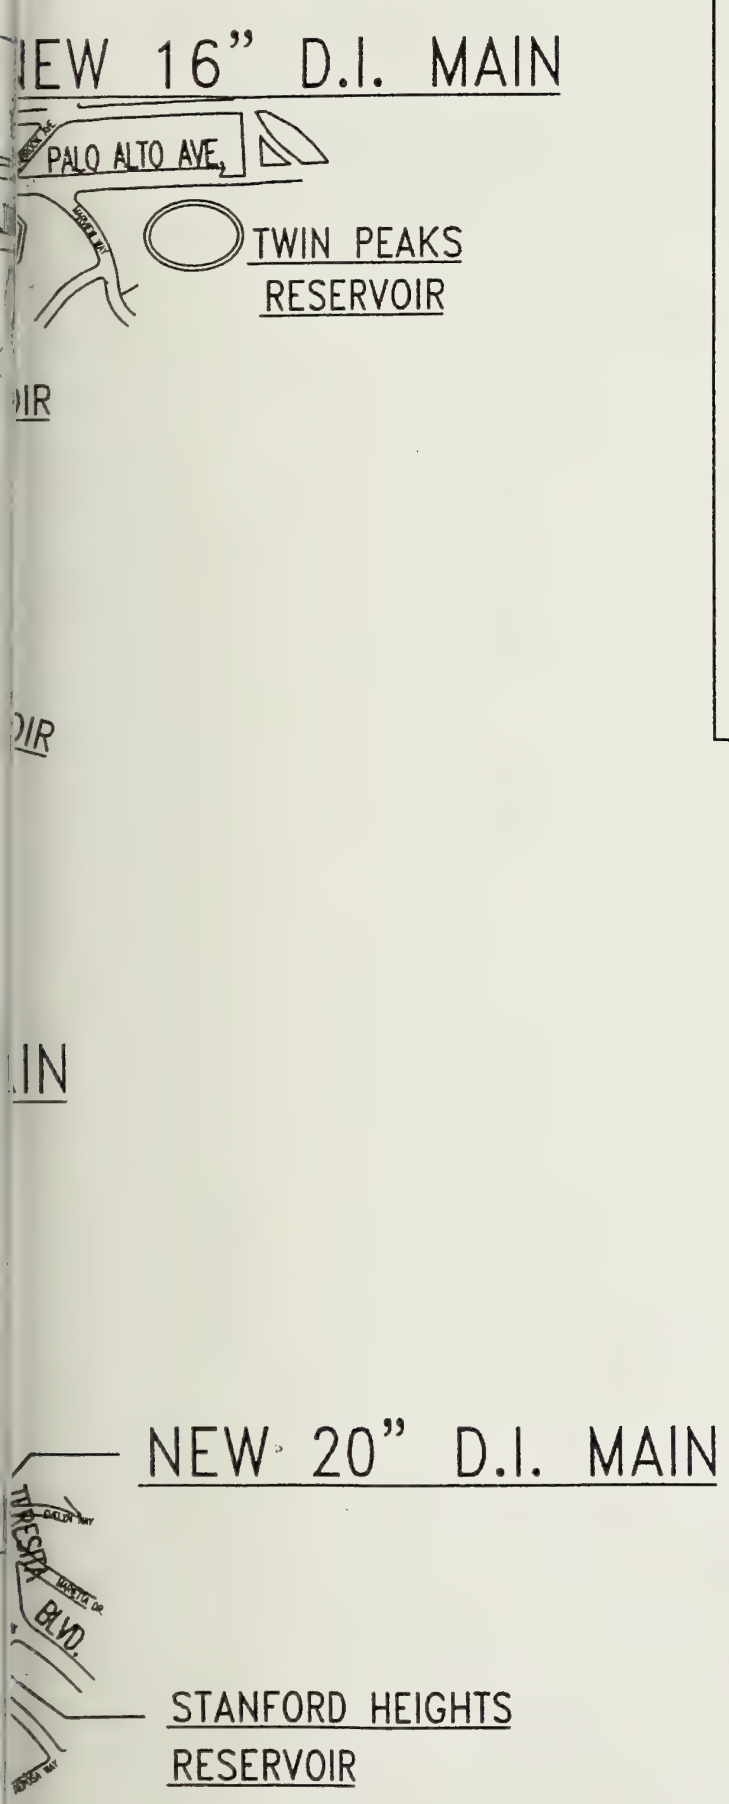
NEW 16" D.I. MAIN
PALO ALTO AVE.
TWIN PEAKS RESERVOIR
IR
IR
IN
NEW 20" D.I. MAIN
TERESITA BLVD.
STANFORD HEIGHTS RESERVOIR

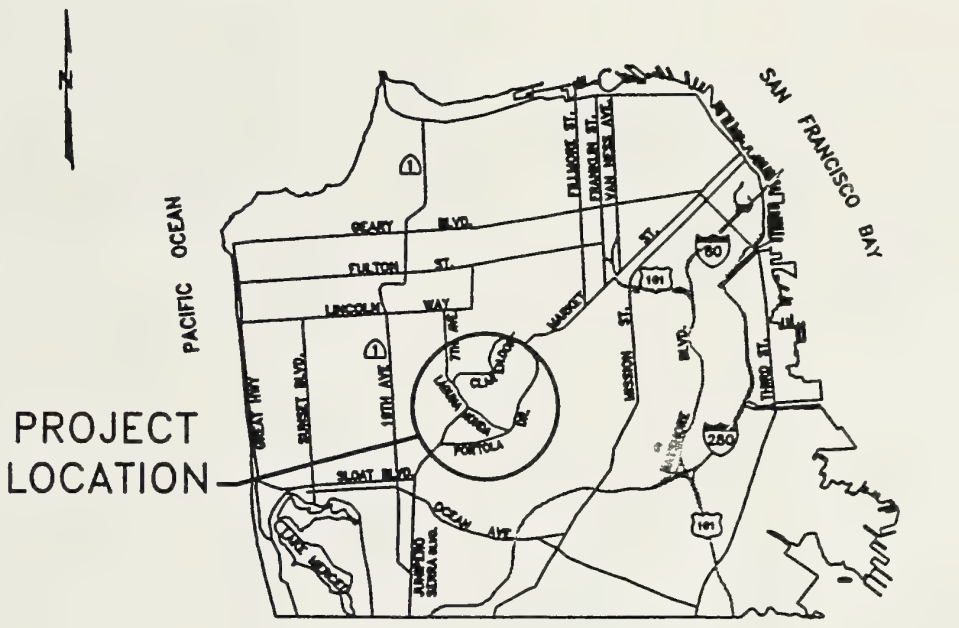
PACIFIC OCEAN
SAN FRANCISCO BAY
N
PROJECT LOCATION
GEARY BLVD.
FULTON ST.
LINCOLN WAY
SLOAT BLVD.
OCEAN AVE.
GREAT HWY
SUNSET BLVD.
19TH AVE.
JUNIPERO SERRA BLVD.
LAKE MERCED
7TH AVE.
LAGUNA HONDA
CLARENDON
PORTOLA DR.
MARKET ST.
FILLMORE ST.
FRANKLIN ST.
VAN NESS AVE.
MISSION ST.
BAYSHORE BLVD.
THIRD ST.
1
1
80
101
101
280

VICINITY MAP

NOT TO SCALE

CLARENDON PUMP STATION AND PIPELINES
TO STANFORD HEIGHTS AND SUMMIT RESERVOIRS

Attachment B.

CULCOP / SCCC Roles and Formats

CULCOP and SCCC

The CULCOP and SCCC meeting forums are both mandated by Ordinance to discuss coordination of work in the City's streets. So far, they appear to cover the same topics and to involve the same people, which is redundant. We need to clarify the purview for each forum and the persons who should attend each.

SCCC has the stated purpose of attempting an ideal of "invisible construction" in the streets, in the sense of minimal disruption to users and residents, by coordinating schedules at the program level to reduce the frequency and shorten the duration of projects in each block. The original purpose of CULCOP was to facilitate cost-effective paving by avoiding digups in newly paved streets. and has evolved to facilitate mutual cooperation among all entities working in the streets, by resolving project-level conflicts. It has also been a means of disseminating other information such as Code changes. The distinction between program level and project level should help to differentiate the topics and attendance between the two forums.

For example, the motive driving the previous "clearance" model for paving was that we are Federally mandated to use a pavement management system based on cost-effective maintenance. For that purpose, timing is critical, since a delay of a few years can mean much higher cost because the method of maintenance has escalated. The same is true of any infrastructure maintenance program. Mutual accommodation must allow for the cost escalation associated with deferred maintenance. It must also consider each project globally, from concept through budgeting, design, procurement, and contracting process, as well as scope and duration of the work itself. Clearance / coordination is then an SCCC matter, while the usual hiccups and surprises during construction belong with CULCOP.

The shift from pavement driven to project driven coordination in CULCOP has not been reflected in the nomenclature and format of the Status Report. We no longer focus on "clearing" streets for paving, and instead have moved to "coordinating" work in each block to comply with the Excavation code's five year horizon, with paving as the last activity in a multi-project site. The current wave of telco installations has increased the number of entities to coordinate. The need to retrieve several of our infrastructure systems at (or past) the end of their useful life has increased the pace of work for the affected agencies. The distinction between sequenced and joint projects needs to be reflected. Displaying that information usefully within a reasonable page count will be difficult. Perhaps we can devise an electronic format which everyone can easily use.

1999 UPCOMING TEMPORARY STREET CLOSURES FOR SPECIAL EVENTS Query

Event Name	Start Date	End Date	Type	Location	Status
Film Shoot "Nash Bridges"	4/14/99	4/14/99	Film	Clementina: 8th to Sumner; Sumner: Clementina to Ho	4/12/99
CCAC Grand Opening	4/15/99	4/16/99	private	8th St: Irwin to Hooper	2/25/99
Film Shoot "Nash Bridges"	4/15/99	4/15/99	Film	Clementina: 8th to Sumner; Sumner: Clementina to Ho	4/12/99
CCAC Grand Opening	4/16/99	4/17/99	private	8th St: Irwin to Hooper	2/25/99
SF YMCA Community Cup	4/17/99	4/17/99	Athletic	Steuart: west side parking & traffic lane only	2/25/99
YMCA Community Cup Eve	4/17/99	4/17/99	Athletic	Steuart (west side parking lane and 1 lane of traffic only	2/25/99
Cherry Blossom Festival	4/17/99	4/18/99	Fair	Pos:Lag to Flm, Web: Gea to Sut	3/26/99
SF Inter. Triathlon	4/18/99	4/18/99	Athletic	Various (NW portion of SF)	canceled
SF Inter. Film Fest.	4/19/99	5/9/99	Film	Post: Flm to Web. 3 parking meters only	3/11/99
SF Inter. Film Fest.	4/22/99	4/28/99	Film	Castro: 17th to 18th Sts., 2 parking meters only	3/11/99
Cherry Blossom Festival	4/24/99	4/25/99	Fair	Pos:Lag to Flm;	3/25/99
Rally for Mumia Abu-Jamal	4/24/99	4/24/99	Rally	C.Goodlett Way & Civic Center Plaza	Disapproved
March for Mumia Abu-Jama	4/24/99	4/24/99	March	Dolores Park to Civic Center	permit by PD
Tante Marie's 20th Annivers	4/25/99	4/25/99	Private	Francisco: Stockton to Bellair	
Neighborhood Block Party	4/25/99	4/25/99	Block	Filbert: Divisadero to Broderick	3/11/99
California Mille	4/25/99	4/26/99		Mason: Ca to Sac	12/17/98
Cherry Blossom Parade	4/25/99	4/25/99	Parade	Civic Center to Polk to Post	permitted by PD
Postrio Rest. 10th Annivers	4/27/99	4/27/99	Corporat	Post (diamond lane): Taylor to Mason	4/8/99

Event Name	Start Date	End Date	Type	Location	Status
Southern Exposure Fund R	5/1/99	5/2/99	Block	Alabama: 17th and Mariposa	4/8/99
Cameron Carnival	5/1/99	5/1/99	Fair	Joice: Sacramento to Clay	2/25/99
Neighborhood Block Party	5/1/99	5/1/99	Block	Brentwood: Hazelwood to Valdez	3/25/99
Cinco De Mayo Celebration	5/1/99	5/3/99	Celebrat	Various Location in Civic Center Area	4/8/99
Cinco De Mayo Parade	5/2/99	5/2/99	Parade	24th & Bryant to 14th & Harrison	Permit by PD
SF Inter. Film Fest	5/6/99	5/6/99	Film	Castro: 17th to 18th Sts., 2 parking meters only	3/11/99
First Baptist Church Block	5/8/99	5/8/99	Block	Weller: Octavia to Laguna	3/25/99
School May Fair	5/8/99	5/8/99	Block	North Point: Scott to Divisadero	3/25/99
Mission Library Gran Reope	5/8/99	5/8/99	Block	Bartlett: 24th to 25th	3/25/99
Asian Art Museum Ground	5/8/99	5/8/99	Civic	Fulton: Larkin to Hyde	2/25/99
Trap Door's Beach Party	5/13/99	5/16/99	Corporat	Scott (west side parking lane): Lom to Chs	4/8/99
Neighborhood Block Party	5/15/99	5/15/99	Block	Mars: 17th to Corbett	3/11/99
Bay to Breakers	5/16/99	5/16/99	Athletic	Various Locations	1/28/99
AIDS Candlelight Vigil & Ma	5/16/99	5/16/99	Parade	Mkt & Castro to Market to City Hall	permit by PD
Young President's Organiza	5/21/99	5/21/99	Shuttle	Stockton(parking lanes): Pine to CA; Parking lane closu	3/25/99
Neighborhood Block Party	5/22/99	5/22/99	Block	Ulloa: Sydney Way to Laguna Honda Blvd.	3/11/99
Young President's Organiza	5/22/99	5/22/99	Shuttle	Stockton(parking lanes): Pine to CA, Parking lane closu	3/25/99
KFOG Kaboom	5/22/99	5/22/99	Celebrat	Embarcadero: Harrison to Townsend	
Young President's Organiza	5/23/99	5/23/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/24/99	5/24/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99

Event Name	Start Date	End Date	Type	Location	Status
Young President's Organiza	5/25/99	5/25/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/26/99	5/26/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/27/99	5/27/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Young President's Organiza	5/28/99	5/28/99	Shuttle	Stockton(parking lanes only): Pine to CA; Parking lane	3/25/99
Carnaval	5/29/99	5/30/99	Fair	Har: 16th to 22nd, etc	2/25/99
Carnaval Parade	5/30/99	5/30/99	Parade	24th: Bry to Mis; Mission: 24th to 14th; 14th: Mis to Har	permitted by PD
Black & White Ball	6/3/99	6/3/99	Civic	Various Parking Lanes in Civic Center area	2/25/99
Black & White Ball	6/3/99	6/7/99	civic	Fulton: Larkin to Hyde	2/25/99
Black & White Ball	6/4/99	6/4/99	civic	Various Parking Lanes in Civic Center Area	2/25/99
Black & White Ball	6/5/99	6/6/99	civic	Various Streets in Civic Center Area	2/25/99
Escape From Alcatraz	6/5/99	6/5/99	Athletic	Marina Blvd (1 lane only): Scott to Lyon	7/23/98
Escape From Alcatraz	6/5/99	6/5/99	Athletic	NW portion of SF, Various Locations	7/23/98
SPCA Animal WingDing	6/5/99	6/6/99	Fair	Alabama:15 to 16; Florida:16 to Tre; Treat:Har to 15th	12/17/98
Union Street Arts Festival	6/5/99	6/6/99	Fair	Union: Gou to Stn, etc	12/17/98
Cyberbuss	6/5/99	6/6/99	Block	Griffith: Revere to Quesada	4/8/99
Black & White Ball	6/5/99	6/6/99	civic	Grove: Van Ness to Franklin	2/25/99
PBS Broadcasting Display	6/5/99	6/9/99	Display	Ellis (most most northerly parking lane & traffic lane onl	4/8/99
CA Aids Ride	6/6/99	6/6/99	Athletic	Various, no street closures involved	No permit required
SPCA Animal WingDing	6/6/99	6/6/99	Fair	Alabama:16 to 17; Florida:16 to 17	12/17/98
Statuto Race	6/6/99	6/6/99	Athletic	Stockton: Union to Filbert	

Event Name	Start Date	End Date	Type	Location	Status
Fiesta Filipina	6/9/99	6/14/99	Fair	Grove: Larkin to Polk	
Fiesta Filipina	6/11/99	6/14/99	Fair	Larkin: Hayes to McAllister; Grove: Larkin to Hyde	
North Beach Festival	6/12/99	6/13/99	Fair	Grant:Col to Fil,Green: Col to Gra; Vallejo:Col to Gra	2/11/99
Haight Street Fair	6/13/99	6/13/99	Fair	Haight:Masonic to Stanyan, etc	11/13/98
Gay & Lesbian Film Festivi	6/15/99	6/28/99	Festival	Eureka Valley Lot #1 behind the Castro Theater	
Gay & Lesbian Film Festiva	6/15/99	6/28/99	Festival	Eureka Valley Parking Lot #1 (behind Castro Theater)	
Juneteenth Parade	6/19/99	6/19/99	Parade	Panhandle to Ellis & Scott	permit by SFPD
Juneteenth	6/19/99	6/20/99	Fair	Pierce: Ellis to O'Farrell; O'Farrell: Pierce to Scott	
X Games Street Luge	6/22/99	6/29/99	Athletic	Pt. Lobos: 45th to Great Hwy; Great Hwy: Pt. Lobos to	
Extreme Games	6/23/99	7/3/99	Athletic	Pier 30-32	permit by Port
X Games Street Luge	6/24/99	6/28/99	Athletic	Alta Mar: Seal Rock Dr. to Pt. Lobos	
NASCAR Rally	6/24/99	6/24/99		Leavenworth: Chestnut to Greenwich; Lombard: Hyde t	Disapproved
Gay Pride Celebration	6/25/99	6/28/99	Fair	Civic Center Area	1/28/99
Pink Saturday	6/26/99	6/27/99	Civic	Castro: 19th to Mkt; 18th: Cwd to Hfd	
Gay Pride Parade	6/27/99	6/27/99	Parade	Market: 2nd to Civic Center	permit by PD
Tall Ships	7/2/99	7/5/99		Wharf Area	
Chronicle's 4th of July	7/3/99	7/5/99	Fair	Jefferson: Hyde to Terminus	12/17/98
Jazz & All That Art on Fillm	7/3/99	7/4/99	Fair	Fillmore: Geary to McAllister etc.	Disapproved
Upper Fillmore Jazz Fest. E	7/3/99	7/4/99	Fair	Fillmore: Geary to Eddy; Gea: Web to Stn etc	
Fillmore Street Jazz Festiva	7/3/99	7/4/99	Fair	Fillmore: Jackson to Post, etc	2/11/99

Event Name	Start Date	End Date	Type	Location	Status
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Van Ness: North Pt. To Muni Pier	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Embarcadero: Pow to Tay	12/17/98
Chronicle's 4th of July	7/4/99	7/5/99	Firewks	Jefferson: Hyde to Taylor	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	Wharf Area	12/17/98
Chronicle's 4th of July	7/4/99	7/4/99	Firewks	N/B Embarcadero: Bwd to Bay	12/17/98
SOMAfest	7/10/99	7/10/99	Fair	Harriet: Howard to Folsom	
SF Chronicle Marathon	7/11/99	7/11/99	Athletic	Various City Wide	2/25/99
Third Street Fair	7/17/99	7/18/99	Fair	3rd St.:Cargo to Evans	1/14/99
Blues & Art on the Bay	9/4/99	9/6/99	Fair	Treasure Island	permit by T. Island
Opera Gala	9/11/99	9/11/99	Civic		
Fest. Of Culinary Arts	9/11/99	9/12/99	Fair	Polk: Eddy to MCA; Turk: Van to Lar	
Chinatown Moon Festival	9/17/99	9/19/99	Fair	Grant: Cal to Pac	
Alcatraz Triathlon XIX	9/18/99	9/18/99	Athletic	Marina Blvd (1 lane only): Lag to Buc	10/22/98
Annual March of Witness	9/26/99	9/26/99	March	Powell: Broadway to Vallejo	3/25/99
Eagle Tavern Closure	9/26/99	9/26/99	Fair	12th St: Harrison to Folsom	
Folsom Street Fair	9/26/99	9/26/99	Fair	Folsom: 7th to 12th etc.	
Blessing of the Animals	10/2/99	10/2/99	Block	Golden Gate: Leavenworth to Jones	
Bridge to Bridge	10/3/99	10/3/99	Athletic	Various: Ferry Bldg to Presidio	1/28/99
Page Street Fair	10/9/99	10/9/99	Fair	Page: Franklin to Gough	3/25/99
Page Street Fair	10/10/99	10/10/99	Fair	Page: Franklin to Gough	3/25/99

Event Name	Start Date	End Date	Type	Location	Status
West Portal Fair	10/23/99	10/24/99	Fair	West Portal: Ulloa to 15th Sts.	
Champion Run for Children	10/24/99	10/24/99	Athletic	McAllister: Polk to Larkin	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Various Lane Closures	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Dr. Carleton Goodlett Place	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Sanchez: Duboce to Market	3/11/99
Champion Run for Children	10/24/99	10/24/99	Athletic	Larkin: McA to Gro; Hyde: McA to Grove; Grove: Hyd to	3/11/99
Run to the Far Side XV	11/28/99	11/28/99	Athletic	Oak: Stanyan to Broderick; Fell: Stanyan to Broderick,	3/11/99
Corporate Event	12/3/99	12/4/99	Corporat	Fern: Van Ness to Polk	4/8/99

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, Architect, AIA, Director

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

UNDERGROUND PLANNING MEETING

MEETING DATE: April 6, 1999

PRESENT:

Tom Trimbur	-DPW/BSM	(554-6167)	Lowell Volk, Jr	-TCI	(863-8500)
Louis Victorio	-TCI	(863-8500)	Cindy Vowell	-PacBell	(542-9095)
John Giusti	-DHIC	(863-7500)	John Fadeff	DPW/BSM	(554-5830)

DISCUSSION:

A. PROJECT STATUS

1. UGD 318 - DOLORES HEIGHTS DISTRICT

PHASE 2 – Because the trench is being redesigned, all the utilities will need to sign-off on Form B again. Construction to begin in May/June.

2. UGD 310 - PRESIDIO HEIGHTS

PHASE 2 – Electrical system should be energized in a month. PacBell pulling cable and will then begin splicing which takes months.

California St. – Project out to bid. RCN included in the joint trench.

3. UGD 320 - BREWSTER/JOY

PacBell has completed work on the "Freeway phone". PacBell has wrecked out their facilities. PG&E will be pulling poles.

4. UGD 321 - INDIANA STREET/ISLAIS CREEK & UGD 323 - CESAR CHAVEZ

1601 Indiana work completed; PG&E to cut over this week. The City to contact CALTRAIN/Joint Powers Board regarding approvals for receiving utilities underground. Overhead facilities removed from over freeway. PG&E reported that the boxes along Chavez may need to be adjusted by more than 3 inches. When curbs are poured, utilities will know how much adjustment is required; if more than 3 inches, adjustment will take some time. PG&E is reviewing grading information provided by City. There is also a billboard which has overhead service and a communications line crossing Chavez which may be a City emergency line (PacBell says it's not theirs).

5. UGD 324 - DUBOCE AVENUE

Nothing new to report.

6. UGD 311 - CORBETT AVENUE - PEMBERTON STAIRWAY

Project is still on hold.

7. UGD 335 - UPPER FOLSOM

Substructure work nearing completion.

8. UGD 322 - Alpine Terrace/Museum Way

City has chosen a light for the next few neighborhood projects and should have light locations by the end of April or mid-May.

9. UGD 327 - INNER SUNSET

Streetlight design is proceeding.

10. UGD 338 - Ocean Avenue

Another community meeting, with City department heads, to be held on 12 April. Ms. Healy had sent out an e-mail requesting cost estimates from the various utilities. Mr. Trimbur reiterated that request. PacBell reported that their costs would be minimal, in the range of $75,000.

11. UGD 339 – Bernal South Slope (Banks/Chapman)

Mr. Trimbur indicated that Mr. Burbank requested that Ms. Healy re-examine schedule per his e-mail.

B. OTHER BUSINESS

1. Mr. Trimbur introduced the Central Freeway replacement project which, at this time, is being planned as an at-grade boulevard north of Market Street. The project will follow the Octavia from Market to Hayes. If the project moves forward the City would most likely want to underground the utilities in conjunction with the other work. Gas replacement is scheduled for 1999-2000 and should be incorporated into the underground work if possible.
2. Mr. Trimbur to contact RCN and request their presence at monthly meetings.

THE NEXT MEETING WILL BE HELD ON TUESDAY, 4 May 1999, AT 9:00 A.M. AT 875 STEVENSON STREET, ROOM 460, BSM CONFERENCE ROOM.

cc: All Attendees
CULCOP - through Joe Norris
Kris Kilgore - BSM
Hin Lok Kung - BOE
Jack Donohoe - DTIS
Barbara Moy - BSM
Manfred Wong - CWP
Lynn Bunim - PacTel
Norman Chan - BOE
Dee Lemmon - BLHP
Lesley Wong - BOE/S&H
Patricia Healy - PG&E
Naoki Kaku - BOE S&H
José Saldaña – PG&E
Amy Chow - PDS
Charles Yu - BOE/S&H
Amy Powell- DHIC
Brian Christiansen - Duboce
Carlos DeAnda - PG&E
Lynn Nakasato - BOE/S&H
Cynthia Chono - BSM
Ray Yamagishi - BLHP
Tom Flahavan - DET
Joe Ovadia - PMD
Kathy Devine - PG&E
Louis Victorio – TCI
Scot Burbank - BOE/PMD
Sieg Weber – RCN
John Katz - MUNI
Sam Lauter - PG&E
Carol Finucane - BOE
Don Stroh - DHIC
Brian Gatter - BOE/Landscape
Terry Bouey - TCI
Dave Bradley - PG&E
Joe Marino - DHIC
Terry Elisaia - DET
Naoki Kaku - BOE
Richard Hong - PG&E
Ben Cruz – BOE
Carlos DeAnda – PG&E
Patrick Rivera – BOE/PMD

C:\My Documents\meet49~1 doc

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

UTILITY COORDINATION REPORT

for April 1, 1999 to April 31, 1999

Notice of Intent and Request for Information Issued (NOI):	**Date**
1637N - Chestnut/Union/Pacific/Harriet Sewer Replacement	4/13/99
1701N - Seventh Street Pavement Renovation (Revise)	4/27/99

Final Preliminary Plans Issued (LOT):	
1668N - Golden Gate Avenue Pavement Renovation	4/13/99
1785N - Taber Place/Gough Street Sewer Replacement	4/19/99
1587N - 7th Avenue and Kirkham Street Sewer Replacement	4/20/99
1583N - Everglade/Victoria/Revere/Bridge View Sewer Replacement	4/23/99
7458E - Clay Street Pavement Renovation	4/26/99

State of California:

Other:

"IMPROVING THE QUALITY OFLIFE IN SAN FRANCISCO" We are dedicted individuals committed to teamwork, custormer service and continuous improvement in partnership with the community

Customer Service *Teamwork* *Continuous Improvement*

S:\PD\UTILITYL\RPTS\CULCOP\UT0499.doc

Projects in Progress (NOI)

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
----N	Greg Cruz	554-8268	Various Locations, Construction of Curb Ramps - STPL-5934(030)	Pav	09/04/1997
1048N	Gene Handa	554-8341	Sunnydale Sewer Improvements	SW	07/03/1996
1076N	Arlen Ung	554-8263	West End Utilities	Pav	08/11/1997
1100N	Martha Ketterer	554-8296	Ecker Street, Mission Street to Elim Alley	Pav	01/08/1996
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements Locations #306 & 309	UG	02/15/1998
1145N	Naoki Kaku	554-8246	Bernal Heights Street Improvement, Banks/Chapman Area	Pav	12/02/1996
1202N	Linda Leong	648-6882	North Point Plant Improvement, Phase II	Pav	01/30/1996
1218N	Cliff Wong	554-8339	Market , Larkin and Harrison Streets Sewer Replacement	SW	03/29/1996
1243N	Ronald Cheng	558-4049	Marina Seawall and Roadway Improvement	Pav	04/12/1996
1277N(1)	Laarni Camerino	554-8256	Var Loc: As Needed Paving - McAllister, Polk, Grove & Van Ness Avenue	Pav	08/17/1998
1277N(2)	Pak Choi	554-8283	Various Locations: As Needed Paving - Stockton (Post to Market Street)	Pav	08/17/1998
1277N(3)	Greg Cruz	554-8268	Var Loc - As Needed Pav: Lake Merced from Skyline Blvd. To John Muir Drive	PAV	09/28/1998
1285N	Brian Gatter	554-8292	Pioneer Park Renovation – Telegraph Hill Stairways	Pav	11/14/1997
1294N	Leon Louie	558-4070	Fourth Street Bridge Fender Repair Project	Str	12/18/1996
1330N	Wallis Lee	554-8344	2nd / 9th Streets Sewer Abandonment Project	SW	06/27/1997
1349N	Saed Toloui	558-4084	12th Avenue/Quintara Street, Stairway Construction	Str	02/07/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	12/02/1996
1381N	Patrick Riviera	558-4045	Martin Luther King Utilities	Pav	09/12/1997
1385N	Laarni Camerino	554-8256	Various Locations: Concrete Street Reconstruction - Stillings Ave from Teresita to Congo	PAV	07/10/1998
1389N	Pak Choi	554-8283	Mission Street Pavement Renovation	Pav	06/13/1997
1395N	Cliff Wong	554-8339	Sacramento/ Larkin/ Pine Streets Sewer Replacement	SW	04/10/1998
1407N	Narciso Paderanga Jr.	554-8258	California Street Pavement Renovation, STP-17	Pav	02/13/1997
1415N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	Str	07/31/1997
1421N	Clifford Wong	554-8339	Green Street Sewer Replacement - Columbus Avenue to Powell Street	SW	01/17/1997
1423N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	SR	07/31/1997
1432N	Gene Handa	554-8341	Post Street Sewer Replacement	SW	02/07/1997
1459N	Narciso Paderanga, Jr.	554-8258	Fillmore Street Pavement Renovation and Muni Underground Ductbank System	Pav	08/29/1997
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	11/10/1997
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SR	09/30/1997
1549N	Thomas Won	554-8275	Ocean/Victoria/Everglade Sewer Replacement	SW	09/23/1997
1573N	Wallis Lee	554-8344	5th Street & Harrison Sewer Replacement	SW	02/17/1998
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	04/13/1998
1588N	Thomas Won	554-8275	Joost Ave/Alemany Blvd/Mt. Vernon Ave/Kensington Way Sewer Replacement	SW	12/22/1998
1590N	Thomas Won	554-8275	Ocean Avenue Sewer Replacement (Joint Venture with MUNI)	SW	07/13/1998
1605N	Bryan Dessaure	554-8299	Sacramento/Pierce/Wilmot Streets Sewer Replacement	SW	06/07/1998
1626N	Thomas Won	554-8275	4th/5th Ave/Stanyan St (easement) / Paris Street Sewer Replacement	SW	10/22/1998
1628N	Jean To	554-8298	Moraga Street Sewer Replacement: 17th to 18th Avenues	SW	09/16/1998
1629N	Peter Cheng	554-8348	Union/Kearny Streets Sewer Replacement	SW	10/28/1998
1637N	Cliff Wong	554-8339	Chestnut/Union/Pacific/Harriet Sewer Replacement	SW	05/21/1999
1653N	Uday Prasad	558-4061	Demolition of North Beach Garage at 763 Vallejo Street	Str	09/15/1997
1655N	Lesley Wong	554-8252	Cezar Chavez Improvements Phase 2		07/27/1998
1667N	Lesley Wong	554-8252	Fourth Street Sidewalk Widening Project - Phase 2	Pav	03/10/1998
1674N	Joe Haas	558-4539	1680 Mission Street Secondary Power Source	SDV	05/27/1998
1678N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Street Reconstruction No. 15	Pav	04/13/1998
1680N	Lesley Wong	554-8252	Great Highway and Point Lobos Pavement Renovation	Pav	05/13/1998
1701N	Laarni Camerino	554-8256	Seventh Street Pavement Renovation	Pav	08/24/1998
1724N	Laarni Camerino	554-8256	Various Locations: As Needed Paving - 2nd St. between Townsend & King Streets	Pav	07/10/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	10/28/1998
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	10/05/1998
1735N	Naoki Kaku	554-8246	Various Locations: Bayview District Pavement Renovation	PAV	10/13/1998
1748N	Carol Finucane	558-4581	Mid-Market Public Improvements		10/05/1998
1755N	David Pang	554-8278	Oak Street Pavement Renovation	PAV	02/02/1999
1759N	Pak Choi	554-8283	Mission Street Pavement Renovation Phase 2	PAV	12/30/1998
1765N	Thinh Nguyen	558-4554	Kearny/Vallejo to Green Streets AWSS Replacement		03/22/1999
1784N	Thomas Won	554-8275	Leavenworth Street Sewer Replacement (CW-231)	PAV	04/08/1999

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
1791N	Peter Cheng	554-8348	3rd Street Sewer System Improvement Phase III	SW	05/10/1999
1978N	Gary Fleming	558-4539	Upgrade Pressure Reducing Stations, Various Locations		04/02/1999
1984N	Naoki Kaku	554-8246	Van Ness Pedestrian Safety Improvements	PAV	03/17/1999
6618E	Leon L. Louie	558-4070	Seismic Retrofit of Third Street Bridge	Str	08/31/1997
6618N	Frank Piruzmand	558-4081	3rd Street Bridge Rehabilitation & Retrofit	Str	03/30/1998
7291E	Lynn Fong	554-8269	K-Line Rail Replacement & Ocean Avenue Improvements	Pav	11/03/1997
7381E	Fernando Cisneros	554-8278	Hunter's Point Naval Shipyard Infrastructure Backbone Phase I	Pav	11/25/1996
7416E	Deirdre Appel	558-4556	Golden Gate Park Reservoir and Pump Station		08/07/1998
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	12/22/1998
N	Linda DeBolt	554-8265	Surface Streets Improvement Project	Pav	02/06/1998

Projects in Progress (NOI)

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
----N	09/04/1997		08/07/1997	11/09/1998	10/20/1997	08/20/1997			09/04/1997
1048N	07/03/1996	Mar-99	07/11/1996	06/17/1996		07/16/1996			07/14/1996
1076N	08/11/1997	Jul-98	07/17/1997			07/23/1997	07/18/1997	07/29/1997	08/26/1997
1100N	01/08/1996	May-98		05/14/1996		12/18/1995			02/16/1996
1109K	02/15/1998		12/30/1997	04/27/1998	01/21/1998	01/09/1998	12/30/1997	01/09/1998	01/13/1998
1145N	12/02/1996	Nov-98	11/08/1996			12/03/1996			12/07/1996
1202N	01/30/1996	18-Nov-97		01/29/1996				01/16/1996	
1218N	03/29/1996	On hold	03/22/1996			03/20/1996	03/01/1996		
1243N	04/12/1996		03/29/1996				03/25/1996	03/19/1996	04/23/1996
1277N(1)	08/17/1998			07/24/1998	08/19/1998	07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(2)	08/17/1998			07/24/1998		07/31/1998	07/24/1998	10/13/1998	08/03/1998
1277N(3)	09/28/1998		09/08/1998	09/10/1998	11/02/1998	09/09/1998	09/04/1998	09/23/1998	09/17/1998
1285N	11/14/1997	Jul-98	10/21/1997	04/13/1998		10/24/1997	10/16/1997	10/20/1997	11/06/1997
1294N	12/18/1996	May-98	10/25/1996	03/19/1997		10/18/1996		10/09/1996	12/07/1996
1330N	06/27/1997	Apr-98	06/16/1997	06/17/1997		06/17/1997	06/16/1997		
1349N	02/07/1997	Apr-98	01/09/1997			03/27/1997	01/10/1997	01/24/1997	02/07/1997
1374N	12/02/1996		11/08/1996	02/24/1997		12/03/1996			12/07/1996
1381N	09/12/1997		08/18/1997			08/22/1997	08/18/1997	10/29/1997	09/15/1997
1385N	07/10/1998		06/12/1998	07/10/1998		06/22/1998	06/18/1998	07/17/1998	06/23/1998
1389N	06/13/1997	May-98	05/28/1997	06/02/1997			06/05/1997	05/28/1997	06/03/1997
1395N	04/10/1998			04/27/1998	04/17/1998	06/02/1998	04/08/1998	04/13/1998	04/20/1998
1407N	02/13/1997	On hold	01/17/1997			01/21/1997	01/15/1997	01/27/1997	02/18/1997
1415N	07/31/1997	Sep-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997	07/22/1997	07/28/1997
1421N	01/17/1997	Jan-98	01/09/1997	01/06/1997		01/23/1997	01/02/1997		02/07/1997
1423N	07/31/1997	Nov-98	07/16/1997		07/10/1997	07/18/1997	07/08/1997		07/28/1997
1432N	02/07/1997	Jun-98		02/20/1997		02/11/1997	01/23/1997		02/18/1997
1459N	08/29/1997	May-98	08/05/1997	12/22/1997	10/20/1997	08/07/1997	08/01/1997		09/05/1997
1474N	11/10/1997	Jul-98	10/21/1997	06/17/1998	10/16/1997	10/24/1997	10/16/1997		11/06/1997
1548N	09/30/1997		09/08/1997	04/13/1998	09/24/1997	09/19/1997	09/09/1997		09/30/1997
1549N	09/23/1997					09/19/1997	09/11/1997		09/30/1997
1573N	02/17/1998		01/23/1998	06/17/1998	01/23/1998	02/12/1998	01/23/1998		02/12/1998
1585N	04/13/1998		04/29/1998	04/30/1998	04/15/1998	05/12/1998	04/09/1998	04/13/1998	04/23/1998
1588N	12/22/1998		03/17/1999	02/22/1999		12/02/1998	12/01/1998		12/09/1998
1590N	07/13/1998			07/13/1998		06/19/1998	06/18/1998	07/16/1998	06/23/1998
1605N	06/07/1998		05/11/1998	05/15/1998	05/11/1998	05/13/1998	05/11/1998		05/20/1998
1626N	10/22/1998		10/16/1998	11/12/1998			10/06/1998		10/15/1998
1628N	09/16/1998		09/14/1998	09/10/1998	09/10/1998	09/10/1998	09/10/1998	09/15/1998	09/17/1998
1629N	10/28/1998			11/12/1998		10/02/1998	10/01/1998	10/09/1998	10/13/1998
1637N	05/21/1999		04/21/1999			04/20/1999	04/20/1999	04/20/1999	05/03/1999
1653N	09/15/1997		09/02/1997	09/09/1997		09/02/1997		09/09/1997	09/10/1997
1655N	07/27/1998		07/01/1998		07/06/1998		06/29/1998		07/20/1998
1667N	03/10/1998		02/20/1998		02/20/1998		02/20/1998	03/13/1998	03/05/1998
1674N	05/27/1998		05/15/1998		05/26/1998	05/22/1998	05/19/1998	06/02/1998	06/09/1998
1678N	04/13/1998								
1680N	05/13/1998		04/27/1998	06/02/1998	05/11/1998	05/26/1998		04/22/1998	05/06/1998
1701N	08/24/1998		07/29/1998	09/02/1998		08/04/1998	07/24/1998	10/15/1998	08/13/1998
1724N	07/10/1998		06/22/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	06/22/1998	06/23/1998
1727N	10/28/1998		10/02/1998	11/06/1998		10/02/1998	10/01/1998	09/30/1998	10/13/1998
1732N	10/05/1998		09/14/1998	11/06/1998	11/02/1998	09/22/1998	09/11/1998	10/15/1998	09/25/1998
1735N	10/13/1998		09/14/1998	11/06/1998		09/22/1998	09/15/1998	09/25/1998	09/25/1998
1748N	10/05/1998		09/14/1998	11/06/1998		09/22/1998	09/14/1998	10/13/1998	09/25/1998
1755N	02/02/1999			02/22/1999		01/08/1999		01/14/1999	02/05/1999
1759N	12/30/1998		11/23/1998		12/27/1998	12/10/1998			12/09/1998
1765N	03/22/1999		03/12/1999	03/17/1999		03/23/1999	03/10/1999	03/11/1999	04/12/1999
1784N	04/08/1999		03/29/1999				03/30/1999		04/21/1999

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1791N	05/10/1999		04/08/1999			04/22/1999	04/08/1999		04/21/1999
1978N	04/02/1999		03/12/1999			03/12/1999	03/12/1999	03/11/1999	04/12/1999
1984N	03/17/1999		02/08/1999			02/18/1999	02/03/1999	02/12/1999	02/05/1999
6618E	08/31/1997	Dec-98	07/16/1997		07/15/1997	07/18/1997	07/24/1997	07/28/1997	08/26/1997
6618N	03/30/1998		03/25/1998	03/23/1998		03/23/1998	03/24/1998	03/17/1998	03/30/1998
7291E	11/03/1997		10/21/1997	06/02/1998		10/24/1997	10/08/1997	10/09/1997	10/14/1997
7381E	11/25/1996		10/31/1996			11/13/1996	11/01/1996	10/30/1996	12/07/1996
7416E	08/07/1998		07/17/1998	07/10/1998		06/30/1998	07/13/1998	07/09/1998	07/29/1998
7458E	12/22/1998		11/25/1998	02/22/1999		12/10/1998	12/01/1998		12/10/1998
N	02/06/1998		01/08/1998		01/23/1998	05/13/1998	01/08/1998	03/09/1998	01/26/1998

Projects in Progress (NOI)

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
----N	09/04/1997	08/26/1997	11/24/1998		08/19/1997		09/30/1997	09/30/1997
1048N	07/03/1996	06/18/1996	06/25/1996	07/16/1996	07/01/1996	06/21/1996		
1076N	08/11/1997	07/28/1997			08/04/1997	07/28/1997	07/28/1997	07/28/1997
1100N	01/08/1996	12/11/1995	12/21/1995	12/11/1995	12/28/1995	12/08/1995		
1109K	02/15/1998		01/14/1998		01/15/1998		01/27/1998	01/27/1998
1145N	12/02/1996	12/07/1996	12/02/1996		11/25/1996	12/03/1996	12/03/1996	12/03/1996
1202N	01/30/1996			01/18/1996	02/02/1996	01/18/1996		
1218N	03/29/1996	03/14/1996		03/14/1996	03/18/1996	03/18/1996		
1243N	04/12/1996	03/27/1996		04/15/1996	03/25/1996	04/02/1996		
1277N(1)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998			
1277N(2)	08/17/1998	07/23/1998	08/04/1998	11/09/1998	07/31/1998	07/31/1998	08/13/1998	08/13/1998
1277N(3)	09/28/1998	09/09/1998	09/04/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1285N	11/14/1997	11/07/1997		02/11/1998	10/24/1997	10/17/1997	11/25/1997	11/25/1997
1294N	12/18/1996	10/24/1996		11/07/1996	10/28/1996	11/19/1996		
1330N	06/27/1997	07/01/1997		07/09/1997	06/27/1997	06/12/1997	07/10/1997	07/10/1997
1349N	02/07/1997	01/17/1997	01/22/1997	03/17/1997		01/13/1997	02/05/1997	02/05/1997
1374N	12/02/1996	11/07/1996			11/25/1996	11/07/1996	12/02/1996	12/02/1996
1381N	09/12/1997	08/26/1997			08/21/1997			09/24/1997
1385N	07/10/1998	06/15/1998	06/23/1998		06/25/1998	10/08/1998	07/29/1998	07/29/1998
1389N	06/13/1997	05/29/1997			05/23/1997	06/11/1997	05/23/1997	05/23/1997
1395N	04/10/1998	04/13/1998	01/05/1999		04/22/1998	04/13/1998		05/14/1998
1407N	02/13/1997	02/24/1997	04/17/1997	03/19/1997	01/23/1997	02/03/1997	02/05/1997	02/05/1997
1415N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1421N	01/17/1997	01/10/1997		01/29/1997	02/19/1997	12/30/1996	01/22/1997	01/22/1997
1423N	07/31/1997	07/16/1997			07/15/1997	07/28/1997	07/28/1997	07/28/1997
1432N	02/07/1997	02/24/1997	02/10/1997	03/18/1997	01/31/1997	01/22/1997	02/24/1997	02/24/1997
1459N	08/29/1997	08/05/1997			08/13/1997		09/24/1997	09/24/1997
1474N	11/10/1997	11/07/1997			10/23/1997	10/14/1997	11/25/1997	11/25/1997
1548N	09/30/1997	09/12/1997			09/15/1997	09/29/1997	10/09/1997	10/09/1997
1549N	09/23/1997	09/24/1997			09/17/1997	09/15/1997	10/09/1997	10/09/1997
1573N	02/17/1998	01/26/1998	03/30/1998			01/22/1998		02/12/1998
1585N	04/13/1998	04/13/1998			04/30/1998	04/13/1998	06/25/1998	06/25/1998
1588N	12/22/1998	12/01/1998			12/02/1998			01/12/1999
1590N	07/13/1998	06/17/1998	08/04/1998		06/29/1998	10/08/1998	07/29/1998	07/29/1998
1605N	06/07/1998	05/12/1998				05/15/1998	06/25/1998	06/25/1998
1626N	10/22/1998	10/06/1998		11/09/1998	10/13/1998			01/12/1999
1628N	09/16/1998	09/10/1998	09/08/1998	11/09/1998	09/11/1998	09/10/1998	11/12/1998	11/12/1998
1629N	10/28/1998	10/06/1998		11/09/1998	10/08/1998		11/12/1998	11/12/1998
1637N	05/21/1999	04/23/1999			04/26/1999			
1653N	09/15/1997	09/12/1997			09/08/1997	09/04/1997	09/24/1997	09/24/1997
1655N	07/27/1998	07/01/1998			07/02/1998	07/01/1998	07/29/1998	07/29/1998
1667N	03/10/1998	02/20/1998			02/27/1998			
1674N	05/27/1998	05/18/1998	05/19/1998		06/02/1998	05/14/1998	07/09/1998	07/09/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998	05/13/1998		04/30/1998		06/25/1998	06/25/1998
1701N	08/24/1998	07/24/1998	08/24/1998	11/09/1998	08/04/1998		08/13/1998	08/13/1998
1724N	07/10/1998	06/15/1998	06/23/1998		06/23/1998	10/08/1998	07/09/1998	07/09/1998
1727N	10/28/1998	10/02/1998		11/09/1998	10/13/1998			01/12/1999
1732N	10/05/1998	09/17/1998		11/09/1998	09/28/1998	09/11/1998		11/12/1998
1735N	10/13/1998	09/18/1998		11/09/1998	09/18/1998	09/09/1998		11/12/1998
1748N	10/05/1998	09/18/1998		11/09/1998	09/24/1998	09/11/1998		11/12/1998
1755N	02/02/1999	01/05/1999			12/30/1998			
1759N	12/30/1998	12/01/1998	11/23/1998		12/14/1998			12/01/1998
1765N	03/22/1999		03/17/1999		03/16/1999			
1784N	04/08/1999	03/30/1999	03/31/1999		04/07/1999			

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1791N	05/10/1999	04/07/1999	04/07/1999		04/09/1999			
1978N	04/02/1999	03/16/1999	03/17/1999		03/16/1999			
1984N	03/17/1999	02/08/1999			02/09/1999			
6618E	08/31/1997	07/16/1997		07/30/1997	07/24/1997	07/28/1997	08/21/1997	08/21/1997
6618N	03/30/1998	03/25/1998			04/01/1998		05/14/1998	
7291E	11/03/1997	10/29/1997			10/20/1997		11/10/1997	11/10/1997
7381E	11/25/1996	11/06/1996	11/05/1996	11/14/1996	11/08/1996	12/18/1996	12/02/1996	12/02/1996
7416E	08/07/1998	07/13/1998		11/09/1998	07/20/1998	07/01/1998		07/29/1998
7458E	12/22/1998	11/25/1998	12/14/1998		12/15/1998			12/01/1998
N	02/06/1998	06/22/1998			01/26/1998	10/08/1998		02/12/1998

Projects in Progress (NOI)

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
----N	09/04/1997	08/12/1997		08/08/1997	08/13/1997	08/08/1997	08/08/1997	08/26/1997
1048N	07/03/1996		06/26/1996	07/01/1996		06/25/1996	07/03/1996	07/01/1996
1076N	08/11/1997	07/24/1997		07/24/1997	07/29/1997	08/08/1997	07/22/1997	08/15/1997
1100N	01/08/1996		12/20/1995	01/03/1996	12/14/1995	12/18/1995	12/27/1995	12/20/1995
1109K	02/15/1998	01/07/1998		01/14/1998	01/14/1998	05/20/1998	01/21/1998	01/21/1998
1145N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1202N	01/30/1996		01/16/1996	01/19/1996	01/31/1996	01/17/1996		02/06/1996
1218N	03/29/1996				03/12/1996	03/05/1996	03/27/1996	03/07/1996
1243N	04/12/1996		03/25/1996		03/27/1996	03/22/1996	03/27/1996	03/21/1996
1277N(1)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(2)	08/17/1998	07/21/1998		07/31/1998	07/29/1998	07/23/1998		08/04/1998
1277N(3)	09/28/1998	09/03/1998		09/15/1998	09/17/1998		01/11/1999	09/17/1998
1285N	11/14/1997	10/20/1997	10/28/1997	10/27/1997	10/23/1997	11/18/1997	11/10/1997	11/13/1997
1294N	12/18/1996		10/25/1996	10/25/1996	10/31/1996		12/02/1996	10/24/1996
1330N	06/27/1997	06/16/1997	07/02/1997	06/23/1997	06/23/1997	07/11/1997	08/08/1997	07/02/1997
1349N	02/07/1997	01/13/1997	01/13/1997	01/21/1997	02/12/1997	02/27/1997		01/22/1997
1374N	12/02/1996		11/13/1996	11/14/1996	11/20/1996	12/14/1996	12/02/1996	11/19/1996
1381N	09/12/1997	08/15/1997		08/22/1997	08/22/1997	11/18/1997		08/26/1997
1385N	07/10/1998	06/15/1998		06/23/1998	06/19/1998		04/13/1999	06/29/1998
1389N	06/13/1997	05/19/1997	05/29/1997	05/21/1997	05/23/1997	05/29/1997	06/26/1997	06/06/1997
1395N	04/10/1998	04/13/1998	04/28/1998	04/17/1998	04/14/1998			04/15/1998
1407N	02/13/1997	01/17/1997	01/15/1997	01/24/1997	02/12/1997	02/27/1997	02/24/1997	01/22/1997
1415N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1421N	01/17/1997	01/07/1997	01/06/1997		02/18/1997	02/27/1997		01/22/1997
1423N	07/31/1997	07/08/1997		07/11/1997	07/14/1997		07/09/1997	07/18/1997
1432N	02/07/1997	01/27/1997	01/27/1997	01/29/1997	02/12/1997	02/27/1997		01/30/1997
1459N	08/29/1997	08/05/1997		08/06/1997	08/12/1997	08/08/1997	11/10/1997	08/26/1997
1474N	11/10/1997	10/20/1997		10/21/1997	10/22/1997	11/18/1997	11/10/1997	11/13/1997
1548N	09/30/1997	09/19/1997		09/12/1997	09/12/1997	09/24/1997	09/11/1997	09/22/1997
1549N	09/23/1997	09/12/1997		09/18/1997	09/16/1997	09/24/1997	09/19/1997	09/22/1997
1573N	02/17/1998	01/26/1998		02/12/1998	02/12/1998			02/20/1998
1585N	04/13/1998	04/13/1998	04/28/1998	04/20/1998	04/28/1998	05/20/1998		04/28/1998
1588N	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
1590N	07/13/1998	06/15/1998		07/08/1998	06/19/1998		01/11/1999	07/07/1998
1605N	06/07/1998	05/13/1998		05/19/1998	05/20/1998	05/20/1998		06/02/1998
1626N	10/22/1998	10/05/1998			10/15/1998		01/07/1999	10/15/1998
1628N	09/16/1998	09/08/1998	09/08/1998	09/15/1998	09/17/1998	09/16/1998	09/17/1998	09/17/1998
1629N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1637N	05/21/1999	04/15/1999	04/19/1999	05/03/1999	04/26/1999			04/28/1999
1653N	09/15/1997	09/02/1997		09/08/1997	09/12/1997		09/15/1997	09/22/1997
1655N	07/27/1998	06/29/1998	07/20/1998	07/10/1998	07/15/1998	07/29/1998	01/11/1999	07/15/1998
1667N	03/10/1998	02/20/1998		02/20/1998	02/20/1998			02/20/1998
1674N	05/27/1998	05/19/1998			06/03/1998	05/20/1998		06/11/1998
1678N	04/13/1998							
1680N	05/13/1998	04/20/1998		05/06/1998	05/06/1998	06/02/1998		05/11/1998
1701N	08/24/1998	07/24/1998		08/04/1998	08/03/1998	07/24/1998	01/11/1999	
1724N	07/10/1998	06/22/1998		06/23/1998	06/19/1998		04/14/1999	06/29/1998
1727N	10/28/1998	10/01/1998		10/07/1998	10/06/1998			10/15/1998
1732N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/30/1998
1735N	10/13/1998	09/11/1998		09/22/1998	09/17/1998		01/07/1999	09/24/1998
1748N	10/05/1998	09/11/1998		09/22/1998	09/17/1998		01/11/1999	09/30/1998
1755N	02/02/1999		12/28/1998	01/14/1999	01/05/1999		01/12/1999	01/07/1999
1759N	12/30/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/14/1998
1765N	03/22/1999	03/11/1999	03/23/1999	03/17/1999	03/12/1999		03/15/1999	03/23/1999
1784N	04/08/1999	03/31/1999	03/31/1999	04/08/1999	04/07/1999		04/13/1999	04/09/1999

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1791N	05/10/1999	03/31/1999	04/06/1999	04/08/1999	04/07/1999		04/13/1999	04/13/1999
1978N	04/02/1999	03/11/1999	03/23/1999	03/17/1999	03/12/1999		03/15/1999	03/26/1999
1984N	03/17/1999	02/04/1999	02/05/1999	02/10/1999	02/17/1999		03/15/1999	02/10/1999
6618E	08/31/1997	07/17/1997		07/21/1997	07/18/1997	03/24/1998	07/16/1997	07/18/1997
6618N	03/30/1998	03/26/1998	04/02/1998	04/02/1998		03/24/1998	04/01/1998	04/03/1998
7291E	11/03/1997	10/09/1997	10/16/1997	10/10/1997	10/15/1997	11/19/1997	11/10/1997	10/16/1997
7381E	11/25/1996	01/10/1997	11/13/1996	11/13/1996	11/07/1996		12/02/1996	11/19/1996
7416E	08/07/1998	07/21/1998		07/20/1998	07/20/1998		01/11/1999	07/31/1998
7458E	12/22/1998	12/01/1998	12/01/1998	12/10/1998	12/10/1998		01/07/1999	12/04/1998
N	02/06/1998	02/10/1998	01/16/1998	01/14/1998	01/21/1997	02/10/1998	01/21/1998	01/21/1998

Projects in Progress (LOT)

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1001H	Paul Travis	557-4631	911/OES Emergency Communications Center		12/06/1996
1034N	Ed Choy	554-8284	Chinatown Alleyway Improvements Phase 1 Commercial, Cordelia and Ross	STR	03/26/1999
1036N	Lesley Wong	554-8252	Fourth Street Pavement Renovation	Pav	05/28/1997
1077N	Steve Bui	554-8298	Bowling Green Drive Contract	SW	09/30/1997
1091N	Ed Choy	554-8284	Various Locations South of Market Removal & Pavement Renovation	Pav	04/30/1997
1106N	Steve Bui	554-8298	Western Presidio Drainage Improvements (NOI/LOT)	SW	05/16/1997
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements, Various Locations	UG	04/28/1997
1109N	Linda DeBolt	554-8265	Cesar Chavez (Army) Street Widening	Pav	12/27/1996
1133N	Ellaine Taraya	554-8245	Fulton Street Roadway Widening	Pav	10/27/1997
1155N	E. Ho/Bhula Patel	554-8324	Grant/Chestnut Street Sewer Replacements	SW	10/21/1998
1195N	Gyee Yang	558-4553	Market and Steuart Streets, AWSS Relocation	AWSS	07/20/1996
1208K	Joe Haas	558-4539	San Francisco General Hospital Underground Storage Tank Replacement	UG	03/09/1998
1223W	Lesley Wong	554-8252	Islais Creek, Street Improvements	Pav	04/30/1997
1245N	Wallis Lee	554-8344	Yosemite/Egbert Sewer Enlargment Project (formerly 3180W)	SW	11/27/1996
1253N	Iqbal Dhapa	554-8337	Twelfth Street (SR)	SW	05/16/1997
1254N	Cliff Wong	554-8339	Eleventh Street Sewer Replacement - Harrison St. to Folsom St.	SW	05/23/1997
1272N	Steve Bui	554-8298	Illinois-Cesar Chavez (Army) Streets Sewer Construction	SW	08/08/1997
1322N	Lesley Wong	554-8252	Cabrillo Street, 9th and 16th Avenues Pavement Renovation	Pav	03/11/1997
1362N	Edward Choy	554-8284	Various Locations SOMA Street District Track Removal & Pavement Renovation Phase	PAV	03/22/1999
1373N	Ken Chu	554-8388	Lower Great Highway, 46th, and 48th Avenues, Pavement Renovation	Pav	09/15/1997
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	05/28/1997
1392N	Birgit Chase	554-8336	Bayshore Blvd. - U.S. 101 Off-Ramp...Sewer Repl. (1108N)	Pav & SW	02/28/1997
1393N	Thomas Won	554-8275	Bush/Kearny/Post Streets Sewer Replacement	SW	10/24/1997
1396N	Peter Cheng	554-8348	Sutter/Fell/Broederick Streets Sewer Replacement	SW	05/12/1997
1397N	Bhula Patel	554-8324	Douglass/Dolores/Ord/23rd/28th Streets, Sewer Replacement	SW	10/17/1997
1408N	Naoki Kaku	554-8246	Geneva Avenue, Pavement Renovation	Pav	02/06/1998
1409N	Pak Choi	554-8283	Sutter Street Pavement Renovation STP-19	Pav	03/25/1999
1411N	Peter Cheng	554-8348	Harding Park SR	SW	11/14/1997
1413N	Iqbal Dhapa	554-8337	Davis/Kearny/Francisco Streets Sewer Replacement	SW	06/25/1997
1414N	Thomas Won	554-8275	Treat / 22nd Streets Sewer Replacement	SW	02/28/1997
1426N	Ting He	554-8338	Dore/Valencia/Clinton Park SR	SW	12/08/1997
1433N	Peter Cheng	554-8348	Shotwell Street Sewer Replacement - Army Street to 26th St	SW	11/07/1997
1440N	Pak Choi	554-8283	Various Locations Concrete Street Reconstruction No. 13	Pav	02/06/1998
1453N	Naoki Kaku	554-8246	Montgomery, Kearny, & Sacramento, Pavement Renovation	Pav	02/06/1998
1454N	Ed Choy	554-8284	Potrero Hill District Track Removal and Pavement Renovation, Phase 3	SW	04/27/1998
1460N	Birgit Chase	554-8336	Church / Folsom / Harper Streets Sewer Replacement	SW	10/22/1997
1461N	Iqbal Dhapa	554-8337	Mason / Pine / Leavenworth Streets and Meacham Place Sewer Replacement	SW	03/06/1998
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	06/22/1998
1475N	Birgit Chase	554-8336	Virginia / Fair Avenues/Godeus Street SR	SW	12/24/1997
1477N	Lynn Fong	554-8269	Various Locations Concrete Street Pavement Renovation No. 14	Pav	11/09/1998
1488N	Peter Cheng	554-8348	24th Ave/California Street Sewer Replacement (1452N)	SW	06/20/1997
1491N	Peter Cheng	554-8348	Pacific Ave. Sewer Replacement - Grant Ave. to Stockton St.	SW	09/25/1997
1519N	Pak Choi	554-8283	Bus Bulb Improvement Project Phase 1	Pav	01/23/1998
1528N	Iqbal Dhapa	554-8337	501 Laguna Honda Boulevard Easement Sewer Replacement	SW	08/25/1997
1547N	Peter Cheng	554-8348	33rd Ave/Lyon Street/Molimo Dr SR	SW	01/16/1998
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SW	01/09/1998
1550N	Bhula Patel	554-8324	Day/Congo/Marston/Cuvier SR	SW	01/30/1998
1562N	Birgit Chase	554-8336	Broadway/Bryant/22nd/Sonoma Streets Sewer Replacement	SW	06/26/1998
1563N	Iqbal Dhapa	554-8337	Balboa St. and 3rd/20th/42nd Avenues Sewer Replacement	SW	06/25/1998
1566N	Peter Cheng	554-8243	Fillmore Street SR	SW	12/19/1997
1569N	Peter Cheng	554-8348	Dolores Street/Block 7044 Easement Sewer Replacement	SW	06/12/1998
1578N	Jean To	554-8329	Golden Gate Ave. Sewer Replacement-Polk St/Van Ness & Pierce/Scott Sts	SW	03/10/1998
1579N	Jean To	554-8329	Illinois Street Sewer Replacement-20th to 19th Street		04/17/1998
1583N	Thomas Won	554-8275	Everglade/ Victoria/ Revere/ Bridge View Sewer Replacement	SW	05/14/1999
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	09/15/1998

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1586N	Jean To	437-7012	Geary, Eddy, Elm and Turk Sewer Replacement	SW	10/20/1998
1587N	Jean To	554-8298	7th Avenue and Kirkham Street Sewer Replacement	SW	05/20/1999
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	01/22/1999
1602N	Jean To	437-7012	Howard, Minna and 2nd Streets Sewer Replacement	SW	11/09/1998
1603N	Jean To	554-8270	Broad Street, Capitol to Plymouth Avenue Sewer Replacement	SW	07/10/1998
1606N	Jean To	554-8348	Cayuga/Laurel/Rondel and Douglass Sewer Replacement	SW	10/29/1998
1630N	Birgit Chase	554-8336	Polk/Francisco/Quincy/Sacramento Streets Sewer Replacement	SW	06/04/1999
1631N	Jean To	554-8298	4th/10th Ave/Anza/Cabrillo Streets Sewer Replacement	SW	02/16/1999
1632N	Bhula Patel	554-8324	Post, Grove and Potomac Streets Sewer Replacement	SW	04/06/1999
1645N	Peter Cheng	554-8348	Third Street Sewer System Improvement Phase II	SW	02/24/1999
1668N	Laarni Camerino	554-8388	Golden Gate Avenue Pavement Renovation	Pav	04/27/1999
1687N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 15	Pav	08/31/1998
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	03/22/1999
1729N	Narciso Paderanga, Jr.	558-8258	Brotherhood Way & Font Boulevard Pavement Renovation	Pav	03/25/1999
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	02/24/1999
1734N	Dimitrios Stavrakis	554-8271	Franklin/Greenwich and Union Streets Pavement Renovation	PAV	04/08/1999
1765N	Thinh Nguyen	558-4554	Kearny/Vallejo to Green Streets AWSS Replacement		03/22/1999
1785N	Peter Cheng	554-8343	Taber Place/Gough Street Sewer Replacement	SW	05/20/1999
6094Q	Deanna Calleros	554-8266	Mid Embarcadero Surface Rdwy and F-Line Extension	Pav	06/27/1997
7090E	Thinh Nguyen	558-4554	Various Locations Motorized Valves Contract #2	AWSS	03/19/1998
7437E	Laarni Camerino	554-8256	Howard, Folsom & Hawthorne Streets (SR)	SW	08/29/1997
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	02/24/1999
7474E	Peter Cheng	554-8348	Pine/California/Delancey Streets SR	SW	11/26/1997

Project in Progress (LOT)

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1001H	12/06/1996		12/03/1996	01/22/1997		12/05/1996		11/25/1996	12/16/1996
1034N	03/26/1999		03/17/1999					03/18/1999	04/21/1999
1036N	05/28/1997	Apr-98	05/15/1997	06/30/1997		05/09/1997	05/14/1997		
1077N	09/30/1997	Apr-98	09/08/1997	06/26/1998		09/24/1997	09/09/1997		09/05/1997
1091N	04/30/1997	15-Sep-97	04/04/1997	05/13/1997				04/11/1997	04/28/1997
1106N	05/16/1997	3-Nov-97	05/06/1997	05/13/1997		05/12/1997	05/06/1997		06/03/1997
1109K	04/28/1997		04/14/1997			04/16/1997		04/22/1997	05/08/1997
1109N	12/27/1996	Jun-98	12/05/1996				12/03/1996		02/07/1997
1133N	10/27/1997	May-98	10/21/1997		10/16/1997		10/10/1997		10/21/1997
1155N	10/21/1998		10/16/1998	11/09/1998		10/07/1998	10/06/1998		10/15/1998
1195N	07/20/1996						07/08/1996		
1208K	03/09/1998		03/24/1998	03/05/1998		03/18/1998	03/05/1998	03/12/1998	03/24/1998
1223W	04/30/1997	Jun-98	04/14/1997	05/13/1997		04/16/1997	04/21/1997		05/14/1997
1245N	11/27/1996		11/08/1996	02/24/1997					12/07/1996
1253N	05/16/1997	Apr-98	04/28/1997	05/13/1997		05/05/1997	04/29/1997		05/12/1997
1254N	05/23/1997	Jul-98	04/28/1997	05/13/1997		04/23/1997	04/22/1997		05/12/1997
1272N	08/08/1997	Jun-98	07/29/1997	06/15/1998		07/28/1997	07/28/1997		
1322N	03/11/1997	May-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997	02/14/1997	02/27/1997
1362N	03/22/1999		03/12/1999	03/22/1999			03/12/1999	03/19/1999	03/16/1999
1373N	09/15/1997	May-98	08/26/1997	04/22/1998			08/22/1997	08/28/1997	09/10/1997
1374N	05/28/1997	May-98	05/01/1997				04/30/1997	05/12/1997	05/14/1997
1392N	02/28/1997		02/20/1997				02/19/1997		02/27/1997
1393N	10/24/1997		10/21/1997	05/19/1998		10/15/1997	10/08/1997		10/21/1997
1396N	05/12/1997	May-98	05/01/1997			05/28/1997			05/12/1997
1397N	10/17/1997		09/26/1997		10/20/1997	10/01/1997	09/26/1997		10/14/1997
1408N	02/06/1998	Jun-98	01/08/1998	04/22/1998	01/20/1998		01/08/1998	03/05/1998	01/21/1998
1409N	03/25/1999		03/09/1999			03/11/1999	02/16/1999	03/18/1999	03/11/1999
1411N	11/14/1997	Jul-98	10/23/1997			11/05/1997	10/24/1997		11/04/1997
1413N	06/25/1997	Jun-98	06/16/1997	06/17/1997		06/11/1997			07/11/1997
1414N	02/28/1997	Jul-98	02/20/1997	02/20/1997		02/18/1997	02/19/1997		02/28/1997
1426N	12/08/1997	Sep-98	12/04/1997		12/03/1997	12/10/1997	12/03/1997		12/17/1997
1433N	11/07/1997	Jun-98	10/21/1997			10/24/1997	10/16/1997		11/13/1997
1440N	02/06/1998	Apr-98	01/08/1998	01/09/1998	01/20/1998	01/27/1998	01/08/1998		01/21/1998
1453N	02/06/1998	Jul-98	01/08/1998				01/08/1998	03/09/1998	01/26/1998
1454N	04/27/1998		04/27/1998			04/20/1998	04/16/1998	04/23/1998	07/09/1998
1460N	10/22/1997		10/21/1997			10/24/1997	10/10/1997		10/21/1997
1461N	03/06/1998	Jul-98	02/20/1998	04/02/1998			02/20/1998		
1474N	06/22/1998	Jul-98	06/03/1998	06/17/1998	06/02/1998	06/09/1998		06/02/1998	06/03/1998
1475N	12/24/1997		12/12/1997		01/20/1998	01/06/1998	12/15/1997		
1477N	11/09/1998	Jun-98	10/16/1998	11/12/1998	11/02/1998		10/16/1998	11/20/1998	10/20/1998
1488N	06/20/1997	Apr-98	06/09/1997			06/04/1997	06/03/1997		06/16/1997
1491N	09/25/1997	May-98	09/18/1997	06/30/1997		09/24/1997	09/16/1997		
1519N	01/23/1998	Jun-98	12/30/1997				12/30/1997	01/09/1998	01/26/1998
1528N	08/25/1997	Mar-98	08/20/1997		10/03/1997		08/21/1997		09/08/1997
1547N	01/16/1998		12/15/1997		01/20/1998	01/06/1998	12/17/1997		12/23/1997
1548N	01/09/1998		12/22/1997	04/13/1998	12/30/1997	01/09/1998	12/29/1997		01/06/1998
1550N	01/30/1998				01/20/1998	02/12/1998	01/14/1998		02/12/1998
1562N	06/26/1998		06/22/1998		06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1563N	06/25/1998		06/19/1998	07/10/1998	06/17/1998	06/22/1998	06/18/1998	07/16/1998	07/09/1998
1566N	12/19/1997		12/12/1997	12/19/1997	12/17/1997	12/17/1997	12/15/1997		
1569N	06/12/1998		05/15/1998	06/12/1998	06/17/1998	06/09/1998	05/19/1998	06/02/1998	06/09/1998
1578N	03/10/1998		03/24/1998	06/30/1998	03/09/1998		03/09/1998	03/11/1998	03/24/1998
1579N	04/17/1998			05/15/1998		04/14/1998	04/13/1998	04/13/1998	04/23/1998
1583N	05/14/1999		04/30/1999	05/05/1999			05/03/1999	05/03/1999	
1585N	09/15/1998		09/08/1998	09/02/1998	09/10/1998	09/17/1998	09/01/1998	09/21/1998	09/08/1998

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1586N	10/20/1998		10/02/1998	11/06/1998	11/02/1998			10/09/1998	10/13/1998
1587N	05/20/1999		04/28/1999				04/23/1999		
1589N	01/22/1999		12/23/1998	02/22/1999			12/29/1998	12/17/1998	01/26/1999
1602N	11/09/1998		10/16/1998				10/16/1998	10/13/1998	10/20/1998
1603N	07/10/1998		06/19/1998	07/10/1998		06/22/1998	06/18/1998	07/16/1998	06/23/1998
1606N	10/29/1998		10/02/1998	11/09/1998	11/09/1998		10/06/1998	10/13/1998	10/13/1998
1630N	06/04/1999								
1631N	02/16/1999		01/19/1999					01/14/1999	02/05/1999
1632N	04/06/1999		03/09/1999	03/17/1999	03/05/1999		03/02/1999		
1645N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/19/1999	02/24/1999
1668N	04/27/1999	Sep-98	04/21/1999				04/20/1999	04/21/1999	
1687N	08/31/1998		08/12/1998	11/06/1998	08/05/1998	08/12/1998	08/03/1998	08/03/1998	08/13/1998
1727N	03/22/1999		03/12/1999	05/05/1999			03/12/1999	03/17/1999	04/09/1999
1729N	03/25/1999		03/12/1999	03/02/1999			02/16/1999	02/24/1999	03/10/1999
1732N	02/24/1999		01/12/1999	01/13/1999			01/13/1999	01/20/1999	02/05/1999
1734N	04/08/1999		03/29/1999				03/26/1999	03/26/1999	04/21/1999
1765N	03/22/1999			03/17/1999			03/11/1999		04/09/1999
1785N	05/20/1999		04/28/1999				04/23/1999		
6094Q	06/27/1997	07/98							
7090E	03/19/1998		03/24/1998	04/22/1998				03/18/1998	
7437E	08/29/1997	Jul-98	08/05/1997	04/13/1998		08/08/1997	08/06/1997	09/23/1997	09/04/1997
7458E	02/24/1999		01/19/1999				01/13/1999	01/21/1999	03/04/1999
7474E	11/26/1997		11/19/1997			12/04/1997	11/20/1997		12/10/1997

Project in Progress (LOT)

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1001H	12/06/1996	12/30/1996	01/22/1997		12/05/1996	12/03/1996	12/06/1996	12/06/1996
1034N	03/26/1999	03/16/1999	03/26/1999		03/26/1999			
1036N	05/28/1997	05/23/1997				06/04/1997	06/12/1997	
1077N	09/30/1997	09/24/1997			10/07/1997		11/10/1997	01/27/1998
1091N	04/30/1997					04/14/1997	05/23/1997	05/23/1997
1106N	05/16/1997	05/20/1997			05/19/1997	05/13/1997	05/19/1997	05/19/1997
1109K	04/28/1997					04/22/1997	09/24/1997	09/04/1998
1109N	12/27/1996	12/14/1996	01/29/1997	01/09/1997			06/23/1997	
1133N	10/27/1997	10/16/1997			10/20/1997	10/17/1997	11/10/1997	11/10/1997
1155N	10/21/1998	10/06/1998		11/09/1998	10/13/1998			
1195N	07/20/1996			08/02/1996		07/23/1996		
1208K	03/09/1998	03/05/1998	03/30/1998		03/10/1998		05/14/1998	
1223W	04/30/1997	04/18/1997	04/17/1997			04/25/1997	05/23/1997	03/06/1998
1245N	11/27/1996			12/02/1996	12/05/1996	11/08/1996	04/15/1997	04/15/1997
1253N	05/16/1997	05/20/1997		05/14/1997		04/29/1997	05/16/1997	05/16/1997
1254N	05/23/1997	04/28/1997				04/24/1997	06/12/1997	
1272N	08/08/1997	08/05/1997			10/07/1997	07/30/1997	09/24/1997	09/24/1997
1322N	03/11/1997	03/11/1997	04/21/1997	03/25/1997		03/03/1997	04/18/1997	04/18/1997
1362N	03/22/1999	03/17/1999	03/17/1999		03/16/1999			
1373N	09/15/1997	09/12/1997		11/07/1997	10/07/1997		11/10/1997	12/22/1997
1374N	05/28/1997	05/20/1997				04/29/1997	09/24/1997	03/06/1998
1392N	02/28/1997	02/28/1997	04/21/1997	03/18/1997		02/24/1997		
1393N	10/24/1997		10/22/1997		10/14/1997	10/16/1997	11/10/1997	
1396N	05/12/1997			05/14/1997		04/30/1997	06/12/1997	
1397N	10/17/1997	09/30/1997			10/07/1997	09/29/1997	11/10/1997	11/10/1997
1408N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1409N	03/25/1999	02/22/1999	03/08/1999		02/22/1999			
1411N	11/14/1997	11/07/1997			10/29/1997	10/29/1997	12/22/1997	12/22/1997
1413N	06/25/1997				10/07/1997	06/09/1997	06/23/1997	
1414N	02/28/1997		04/17/1997	03/18/1997		02/13/1997	04/15/1997	04/15/1997
1426N	12/08/1997				12/12/1997	12/04/1997		02/20/1998
1433N	11/07/1997	11/07/1997			10/21/1997	10/16/1997	11/25/1997	12/22/1997
1440N	02/06/1998	01/13/1998	03/30/1998		01/14/1998		02/12/1998	
1453N	02/06/1998	01/13/1998			01/14/1998		02/12/1998	
1454N	04/27/1998		04/20/1998		04/23/1998		07/09/1998	07/09/1998
1460N	10/22/1997	10/16/1997			10/20/1997	10/08/1997	11/25/1997	12/22/1997
1461N	03/06/1998	02/20/1998	03/30/1998		02/27/1998		05/14/1998	
1474N	06/22/1998	06/18/1998	06/05/1998		06/03/1998	10/08/1998	07/13/1998	
1475N	12/24/1997		01/14/1998		12/19/1997		01/27/1998	
1477N	11/09/1998	10/15/1998			10/13/1998			12/01/1998
1488N	06/20/1997	06/19/1997			06/09/1997	06/02/1997	08/08/1997	
1491N	09/25/1997	09/24/1997			10/07/1997	09/15/1997	11/10/1997	02/12/1998
1519N	01/23/1998				01/06/1998		02/12/1998	
1528N	08/25/1997	08/26/1997			10/07/1997	08/20/1997	09/26/1997	09/26/1997
1547N	01/16/1998		03/30/1998			12/15/1997	02/12/1998	
1548N	01/09/1998	12/29/1997	01/14/1998		12/29/1997	12/19/1997	02/12/1998	
1550N	01/30/1998		03/30/1998		01/21/1998	01/23/1998	04/07/1998	
1562N	06/26/1998	06/22/1998	06/23/1998		06/19/1998	06/19/1998	09/25/1998	
1563N	06/25/1998	06/22/1998	06/23/1998		06/19/1998	06/16/1998	10/27/1998	
1566N	12/19/1997		01/14/1998		12/19/1997	12/10/1997	02/20/1998	
1569N	06/12/1998	06/08/1998	05/19/1998		05/21/1998	05/15/1998	07/13/1998	

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1578N	03/10/1998	03/11/1998				03/09/1998	05/14/1998	
1579N	04/17/1998	04/20/1998	04/20/1998		04/20/1998			
1583N	05/14/1999	05/05/1999			05/04/1999			
1585N	09/15/1998		08/28/1998	11/09/1998	08/31/1998	09/10/1998	10/27/1998	
1586N	10/20/1998			11/09/1998	10/01/1998			
1587N	05/20/1999				04/30/1999			
1589N	01/22/1999	12/21/1998			12/29/1998			
1602N	11/09/1998	10/15/1998	12/02/1998		10/13/1998			
1603N	07/10/1998	06/17/1998	08/04/1998		06/16/1998	10/08/1998	11/12/1998	
1606N	10/29/1998			11/09/1998	10/13/1998			
1630N	06/04/1999							
1631N	02/16/1999	01/20/1999			01/21/1999			
1632N	04/06/1999	03/02/1999	03/10/1999		03/02/1999			
1645N	02/24/1999	01/25/1999				01/19/1999		
1668N	04/27/1999	04/23/1999			04/21/1999			
1687N	08/31/1998	08/07/1998	08/04/1998	11/09/1998	08/07/1998		10/06/1998	
1727N	03/22/1999	03/16/1999	03/17/1999		03/16/1999			
1729N	03/25/1999	02/22/1999	03/08/1999		02/22/1999			
1732N	02/24/1999	01/20/1999			01/20/1999	01/19/1999	02/01/1999	
1734N	04/08/1999	03/30/1999	03/31/1999		03/29/1999			
1765N	03/22/1999				03/29/1999			
1785N	05/20/1999	04/26/1999			04/30/1999			
6094Q	06/27/1997	09/19/1998			10/07/1997	06/13/1997	09/24/1997	09/24/1997
7090E	03/19/1998		01/05/1999		04/08/1998			
7437E	08/29/1997	08/26/1997			10/07/1997	08/07/1997	09/24/1997	09/24/1997
7458E	02/24/1999	01/20/1999			01/20/1999	01/19/1999		02/01/1999
7474E	11/26/1997				11/25/1997	11/17/1997	02/12/1998	

Projects in Progress (LOT)

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1001H	12/06/1996	12/02/1996	12/02/1996		12/05/1996	12/23/1996	12/02/1996	12/05/1996
1034N	03/26/1999	03/15/1999	03/18/1999		04/07/1999		04/13/1999	03/26/1999
1036N	05/28/1997	05/19/1997	05/21/1997		05/23/1997	05/29/1997		05/28/1997
1077N	09/30/1997	09/19/1997			09/15/1997	09/24/1997	09/11/1997	10/02/1997
1091N	04/30/1997	04/09/1997			04/09/1997	04/14/1997	05/14/1997	04/10/1997
1106N	05/16/1997	05/06/1997		05/13/1997	05/13/1997	05/29/1997	05/14/1997	05/28/1997
1109K	04/28/1997	04/18/1997	04/24/1997	04/24/1997	04/16/1997	04/25/1997	05/14/1997	05/08/1997
1109N	12/27/1996	12/12/1996	01/06/1997		12/16/1996	12/23/1996	12/19/1996	12/10/1996
1133N	10/27/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1155N	10/21/1998	10/05/1998			10/15/1998		01/11/1999	10/15/1998
1195N	07/20/1996		07/17/1996		07/19/1996		07/30/1996	07/15/1996
1208K	03/09/1998	03/06/1998	03/20/1998		03/17/1998		04/08/1998	04/03/1998
1223W	04/30/1997	05/05/1997	04/24/1997		04/16/1997		05/14/1997	04/24/1997
1245N	11/27/1996		11/13/1996		11/20/1996		12/02/1996	11/19/1996
1253N	05/16/1997	05/01/1997			05/02/1997	05/29/1997	05/14/1997	06/03/1998
1254N	05/23/1997	04/29/1997			04/29/1997	05/29/1997	05/14/1997	05/08/1997
1272N	08/08/1997	08/12/1997			08/05/1997	08/08/1997	08/08/1997	08/15/1997
1322N	03/11/1997	02/18/1997			03/13/1997	02/27/1997	04/21/1997	02/20/1997
1362N	03/22/1999	03/11/1999	03/18/1999		03/26/1999		03/15/1999	03/24/1999
1373N	09/15/1997	08/27/1997			09/04/1997	09/24/1997	09/15/1997	09/22/1997
1374N	05/28/1997	05/01/1997			05/06/1997	05/29/1997	05/14/1997	05/08/1997
1392N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1393N	10/24/1997	10/14/1997			10/15/1997	11/18/1997	12/11/1997	10/16/1997
1396N	05/12/1997	05/05/1997			05/13/1997	05/29/1997	05/14/1997	05/28/1997
1397N	10/17/1997	09/26/1997			10/02/1997	11/19/1997		10/16/1997
1408N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1409N	03/25/1999	02/19/1999	02/22/1999		02/23/1999		03/09/1999	03/02/1999
1411N	11/14/1997	10/28/1997	11/13/1997		10/31/1997	11/19/1997	11/10/1997	11/13/1997
1413N	06/25/1997	06/11/1997			06/19/1997	06/10/1997	08/08/1997	06/20/1997
1414N	02/28/1997	02/18/1997			03/13/1997	02/27/1997	02/24/1997	02/20/1997
1426N	12/08/1997	12/03/1997	12/20/1997		12/17/1997	02/12/1998	12/08/1997	12/12/1997
1433N	11/07/1997	10/20/1997	10/28/1997		10/23/1997	11/19/1997	11/10/1997	11/13/1997
1440N	02/06/1998	01/12/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1453N	02/06/1998	01/12/1998			01/14/1998	02/12/1998	01/21/1998	01/21/1998
1454N	04/27/1998	04/20/1998			04/28/1998	05/20/1998		05/11/1998
1460N	10/22/1997	10/16/1997			10/22/1997	11/19/1997	11/10/1997	11/13/1997
1461N	03/06/1998	02/20/1998			02/20/1998	05/20/1998	04/08/1998	02/20/1998
1474N	06/22/1998				06/09/1998		04/13/1999	06/03/1998
1475N	12/24/1997	12/13/1997	12/19/1997		12/19/1997	02/10/1998	12/29/1997	11/29/1908
1477N	11/09/1998	10/08/1998			10/19/1998		01/12/1999	10/27/1998
1488N	06/20/1997	06/04/1997			06/11/1997	07/11/1997	08/08/1997	06/20/1997
1491N	09/25/1997	09/19/1997			09/25/1997	11/19/1997	09/19/1997	09/22/1997
1519N	01/23/1998	01/07/1998			01/14/1998	05/20/1998	01/21/1998	01/21/1998
1528N	08/25/1997	08/22/1997			08/26/1997	08/21/1997	09/15/1997	09/22/1997
1547N	01/16/1998	12/19/1997			12/19/1997		12/29/1997	01/12/1998
1548N	01/09/1998	01/07/1998			01/14/1998	02/12/1998	12/29/1997	01/12/1998
1550N	01/30/1998	01/16/1998			01/21/1998	02/12/1998	01/21/1998	01/21/1998
1562N	06/26/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1563N	06/25/1998	06/17/1998			06/19/1998		01/07/1999	07/07/1998
1566N	12/19/1997	12/13/1997	12/19/1997		12/17/1997	02/10/1998	12/29/1997	01/12/1998
1569N	06/12/1998	05/19/1998			06/03/1998	05/20/1998		06/08/1998
1578N	03/10/1998	03/10/1998			03/17/1998		04/08/1998	04/03/1998
1579N	04/17/1998	04/13/1998	04/28/1998			05/20/1998		04/16/1998
1583N	05/14/1999	04/30/1999	04/30/1999		05/05/1999			05/04/1999
1585N	09/15/1998		08/31/1998		09/15/1998		01/07/1999	09/11/1998

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1586N	10/20/1998	09/28/1998			10/06/1998		01/07/1999	10/15/1998
1587N	05/20/1999	04/26/1999	04/30/1999		04/30/1999			05/03/1999
1589N	01/22/1999	12/11/1998	12/14/1998	12/16/1998	12/17/1998		01/12/1999	01/07/1999
1602N	11/09/1998	10/08/1998			10/19/1998		01/11/1999	10/27/1998
1603N	07/10/1998	06/15/1998			06/19/1998		01/11/1999	07/07/1998
1606N	10/29/1998	10/05/1998			10/06/1998		01/07/1999	10/15/1998
1630N	06/04/1999							
1631N	02/16/1999	01/14/1999			01/26/1999		03/15/1999	02/03/1999
1632N	04/06/1999	10/28/1998	03/02/1999	11/23/1998	03/02/1999		03/09/1999	03/05/1999
1645N	02/24/1999	01/11/1999	01/13/1999		01/19/1999		03/09/1999	01/20/1999
1668N	04/27/1999	04/15/1999	04/19/1999		04/26/1999			04/28/1999
1687N	08/31/1998	08/24/1998			08/13/1998		01/11/1999	08/25/1998
1727N	03/22/1999	03/11/1999	03/18/1999				03/15/1999	03/24/1999
1729N	03/25/1999	02/19/1999	02/22/1999		02/23/1999		03/09/1999	03/02/1999
1732N	02/24/1999	01/11/1999	01/13/1999		01/19/1999		03/09/1999	01/20/1999
1734N	04/08/1999	03/31/1999	03/31/1999		04/07/1999		04/13/1999	04/09/1999
1765N	03/22/1999	03/11/1999	03/23/1999					03/23/1999
1785N	05/20/1999	04/26/1999	04/30/1999		04/30/1999			05/03/1999
6094Q	06/27/1997	06/27/1997			06/12/1997			
7090E	03/19/1998				03/24/1998		04/08/1998	04/03/1998
7437E	08/29/1997	08/06/1997			08/12/1997	08/08/1997	08/08/1997	08/26/1997
7458E	02/24/1999	01/12/1999			01/20/1999		03/09/1999	01/20/1999
7474E	11/26/1997	11/25/1997	12/03/1997		12/01/1997	02/12/1998	12/12/1997	12/12/1997

ME

PR

SCHED

PROP'D

PROJ.

SEWER REPLACEMENT PRIORITY LIST

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S&H	LEAD	SCHED CONST (YEAR)	TAPE #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
		SEW=SEWER											MF=Mill & Fill		
		S&H=STREETS AND HIGHWAYS						?	= Exact year of construction not known				OL=Overlay		
		CON=CONFLICT						***Bold***	= New or revised project				RE=Reconstruction		
									= Under construction				JP=Joint Project		
	CLASS A EMERGENCY PROJECTS														
												CLASS A EMERGENCY =			
	ACCELERATED PROJECTS														
1330N		SEW	1998		09th St	Harrison	McLea Ct MB	1900	?	24"	VCP	Crushed pipe @ 194-208, full of debris,dip			99
1626N		SEW	1999		05th Ave	Irving	Lincoln	1900	?	12"	ISP	Many bad cracks; many street depressions			210
1626N		SEW	1999		04th Ave	Lincoln	Hugo					Many cracks; crushed, street depressions			115
1626N		SEW	1999		Stanyan (west sic	Turk	Anza					Many bad cracks; many street depressions			195
1626N		SEW	1999		Paris	Brazil	Excelsior					Bad cracks; open joints, street depression			115
1362N	BSSR	JP/S&H	1999	188	Kate	End South	Bryant	1900	?	16"	VCP	Severe cracks 162-170' b-a; TV'd 13' b-c, offset	RE	Jul-99	90
1362N	BSSR	JP/S&H	1999	188	Gilbert	End South	Brannan	1900	?	12"	VCP	Cannot TV, flow is too high, sump area	RE	Jul-99	80
1637N		SEW	1999		Chestnut	Fillmore	Steiner	1900		8"	VCP	Open joints, cracks, ss open, collapsed sections			115
1776N			1999		21st Ave.	Ortega	Noreiga	1925		15"	VCP	Offsets, separated joints,holes, street depression.	MF	Jul-99	201
1787N	. . . N		1999		Goettingen	Ward	Ordway	1915	?	8"	ISP	Open ss connections, sand infiltration, pavement sinki	RE		130
1776N	1668N	JP/S&H	2000		Golden Gate	Lyon	Central	1887		16"	ISP	Crushed pipe, offsets, streetfailure	MF	Jul-99	140
1785N	. . . N		1999		Gough	Post	Geary	1911		12"	VCP	Offset joints, cracks, street depressions	RE?		80
1645N	MUNI		1999		03RD ST	EGBERT	FITZGERALD	1900	?	12"	ISP	SEWER ENLARGEMENT	RE		
1645N	MUNI		1999		03RD ST	FITZGERALD	GILMAN	1900	?	8"	ISP	SEWER ENLARGEMENT	RE		
1645N	MUNI		1999		03RD ST	PALOU	QUESADA		?	18"	VCP	SEWER ENLARGEMENT	RE		
1645N	MUNI		1999		03RD ST	QUESADA	REVERE		?	18"	VCP	SEWER ENLARGEMENT	RE		
1645N	BSSR		1999		BAYVIEW	3RD ST	LATOMA	1925		12"	VCP	SEWER ENLARGEMENT	MF		
1645N	BSSR		1999		BAYVIEW	LATONA	POMONA	1925		12"	VCP	SEWER ENLARGEMENT	MF		
1645N	BSSR		1999		BAYVIEW	POMONA	FLORA	1925		12"	VCP	SEWER ENLARGEMENT	MF		
1645N	BSSR		1999		BAYVIEW	FLORA	NEWHALL	1925		12"	VCP	SEWER ENLARGEMENT	MF		
1645N	1735N		1999		EGBERT	JENNINGS	3RD ST	1949		12"	VCP	SEWER ENLARGEMENT	TR		
1645N			1999		KIRKWOOD	MENDELL	3RD ST	1912		10"	VCP	SEWER ENLARGEMENT			
1645N	BSSR		1999		MCKINNON	LANE	MENDELL	1917		12"	VCP	SEWER ENLARGEMENT	MF		
1645N			1999		NEWCOMB	KEITH	LANE	1911	?	12"	ISP	SEWER ENLARGEMENT			
1645N			1999		NEWCOMB	LANE	MENDELL	1908		15"	VCP	SEWER ENLARGEMENT			
1645N			1999		NEWHALL	3RD ST	KIRKWOOD	1890		14"	VCP	SEWER ENLARGEMENT			
1645N			1999		OAKDALE	LANE	MENDELL	1911	?	12"	VCP	SEWER ENLARGEMENT			TOTAL
1645N			1999		OAKDALE	MENDELL	3RD ST	1911	?	12"	VCP	SEWER ENLARGEMENT			2000
1791N					Leland	Delta	Rutland	1913		12"	ISP	SEWER ENLARGEMENT			100
1791N					Inglalls	Shafter	Thomas	1930	?	12"	ISP	SEWER ENLARGEMENT			100
1791N					Keith	Revere	Thomas	1910	?	18"	ISP	SEWER ENLARGEMENT			200
1784N	1727N		1999	W038	Leavenworth	O'Farrell	Ellis	1875	?	3'x5'	BRICK	Fairly bad cind. Missing mortar & brick	MF	Jul-99	200
1784N	1727N		1999	W038	Leavenworth	Ellis	Eddy	1875	?	3'x5'	BRICK	Bad cond. out of shape, missing mortar & brick	MF	Jul-99	200
1633N		SEW	1999		Greenwich	Webster	Fillmore	1889		16"	VCP	Cracks, collapsed section, PUC rec. acc. contract	NO VIDEO		100
1633N	BSSR	SEW	1999		Precita South	Coso	Emmet Pl	1910		15"	VCP	Many severe cracks, breaks PUC rec. acc. contract	MF	May-99	150
1633N	......N	SEW	1999		Clement	21th Ave	22th Ave	1908		12"	VCP	Bad grade, flow blocked, PUC rec. acc. contract	MF	Jul-99	85
1776N			1999		Filbert	Van Ness	Franklin	1900	?	16"	ISP	Cracks, crushed, PUC rec. accel. Contract			100
1787N	1477N		1999	314	Dwight	Goettingen	Brussels	1955		8"	VCP	Many offsets, PUC recommends accel. Contract	RE	Jul-99	100
1630N	....N	SEW	1999		Polk	Greenwich MB	Filbert	1890	?	10"/18"	VCP	Continuous cracks, offsets			110

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST (YEAR)	TAPE #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1630N	BSSR	SEW	1999	199	Francisco	Polk	Van Ness	1914		12"	VCP	Many offsets & cracks; fast flow; lining recommendec	MF		70
1630N		*SEW*	*1999*		*Quincy*	*Pine*	*California*	*1900*	*?*	*15"*	*VCP*	*Many severe cracks, breaks*	*MF*	*May-99*	*90*
				spec 3/17/	*Peabody*	*Sunnydale*	*End*	*1932*		*8"*	*ISP*	*Bad ss's, cracks, exfiltrations, depressions, PUC rec. replacement*			*110*
1588N		*SEW*	*1999*		*Joost*	*Acadia*	*Brompton*	*1926*	*?*	*12"*	*ISP*	*Many open joints, infiltration, street depresions*			*160*
		SEW	*1999*	*W041*	*Hyde*	*Turk*	*Golden Gate*	*1880*	*?*	*3X5*	*BRICK*	*Cracks, sags, missing grout*	*MF*	*Jan-00*	*200*
		SEW	*1999*	*W041*	*Hyde*	*Eddy*	*Turk*	*1880*	*?*	*3X5*	*BRICK*	*Cracks, sags, missing grout*	*MF*	*Jan-00*	*200*
												ACCELERATED PROJECT TOTAL =			**$5,845**
1ST PRIORITY PLANNED PROJECTS: Critical Replacements-Severely collapsed/crushed sewers recommended for immediate replacement															
1461N	BSSR	SEW	1998		Mason	Ellis St.	Eddy St.	1880	?	3x5	BRICK	Severly deformed crown,missing bricks	OL	Oct-01	110
1461N	....N	SEW	1998		Pine	Hyde	Leavenworth	1880	?	3x5	BRICK	Fairly bad shape (oval), 3 broken s/s			280
1461N	1727N	SEW	1998		Leavenworth	O'Farrell	Geary	1900	?	3x5	BRICK	Bad shape	MF	Jul-99	230
1461N		SEW	1998		Meacham	Post	End: South		?	8"	VCP	Severe cracks and damaged ss connections			70
1488N		SEW	1998		California	10th Ave	11th Ave	1900	?	8"	VCP	St. depression; crushed / collapsed			80
1488N		SEW	1998		24th Ave	California	Clement MB	1907		8"	ISP	Cracks, breaks, dip, street depressions			80
1550N		SEW	1998		Day St	Dolores	San Jose	1888		18"	ISP	Collapsed pipe			80
1550N		SEW	1998		Congo	Monterey	Hearst	1910	?	12"	VCP	Multiple cracks, st dep @ 147-159' b-c, infiltration			80
1550N	BSSR	SEW	1998		Congo	Melrose	Mangels	1910		8"	VCP	Many cracks over the block	MF	Sep-00	70
1550N	BSSR	SEW	1998		Marston	Circular	Edna	1910		8"	ISP	Many severe cracks	MF		120
1550N	BSSR	SEW	1998		Cuvier	Bosworth MB (m	Mirando (mhE)	1902		15"	VCP	Multiple cracks & egg shape @ 64-140' d-e	MF		90
1550N		SEW	1998		28th St	Noe	East Xing	1900	?	15"	VCP	Bad open joints @20-50'			50
1562N	....N	SEW	1999		Broadway	Taylor	Himmelmann	1952		16"	VCP	Collapsed & Crushed	RE	Jan-99	70
1562N	....N	SEW	1999		Broadway	Florence	Taylor	1900	?	12"	VCP	Crushed invert, mult cracks	RE	Jan-99	70
1562N	1727N	SEW	1999		Broadway(N Sid	Cyrus Pl	Hyde MB	1952		21"	VCP	Mult cracks, ready to collapse a-b	MF	Jul-99	60
1562N	....N	SEW	1999		Bryant	18th St	19th St	1889		14"	VCP	Many cracks; pipe collapses	MF	Jul-01	120
1562N	1562N	SEW	1999		Sonoma	Union	Green		?	12/15"	VCP	Crushed,broken pipe, ready to collapse	MF	Feb-99	90
1606N	BSSR	SEW	1999	211	Douglass	23rd St	Elizabeth	1890	?	15"	VCP	Severe offsets, separated ss's, st depn	OL	Nov-99	111
1606N		SEW	1999	397	Cayuga	Seneca	Junior Terr	1939		8"	VCP	Many offsets, large street depressions, infiltration			60
1606N		SEW	1999	sp1001	Laurel	Washington	Jackson	1900	?	12"	CP	Multiple severe offsets, street depressions			90
1606N		SEW	1999	sp2001	Rondel Pl	End S(17th St)	16th St	1890	?	12"	ISP	Crushed, multi-cracked sections, severe offsets			140
1155N		SEW	1999		Chestnut	Culebra	Polk	1913		12"	ISP	Numerous Cracks, Collapsed Pipe			70
1155N		SEW	1999		Chestnut	Powell	Stockton	1890		16"	CEM	Cracks, invert erosion			140
1155N	....N	SEW	1999		Grant	Chestnut	Francisco	1918	?	14"	VCP	Offsets, Crushed Pipe, Debris	RE		110
1776N	1409N		1999	ec11/19/	Sutter	Van Ness	Polk	1880		3'x5'	BRICK	Bad shape, bulging, lots of bricks missing,	MF	Jan-00	190
1785N	BSSR		1999		Taber	Jack London	3 rd St.	?		12"	VCP	Bad shape, seperated ss's, depressions, crushed	MF	Oct-00	99
1784N	1727N		1999		Leavenworth	Clay	Sacramento	1875		12"/16"	VCP	Collapsed and cracked m/s	MF	Jul-99	99
1155N	....N	SEW	1999		Grant	Greenwich	Lombard	1918	?	16"	VCP	Cracks, Dip, Cement Pipe	MF	Jan-98	110
1635N		SEW	1999		Market S. Side	9th Street	10th Street	1878		3x5	BRICK	Ready to collapse			350
1635N	....N	SEW	1999		Larkin	Golden Gate	McAllister	1874		18"	VCP	Collapsed, continuous cracks	MF		120
	....N	SEW	2000	210	Eugenia	Prospect	Coleridge	1920	?	12"	ISP	Severe offsets, breaks, bad ss, rat, street depressions	MF		70
			2000		Bertita	Seneca	end			8"	VCP	Street collapsing (field check) several bad sections			70
							NOTE: Projects with estimates rounded to 100k have not been finalized and will be revised after sizing.								
												PRIORITY 1 (Planned Projects) TOTAL =			**$3,509**
2ND PRIORITY PLANNED PROJECTS: Severely cracked/crushed sewers to be replaced on a normal contract schedule.															

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST (YEAR)	TAPE #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1254N	....N	SEW	1999		11th St	Folsom	Harrison	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			360
1393N	....N	SEW	1999		Bush	Kearny	Montgomery	1880	?	3x5	BRICK	Fairly bad shape,bricks, plastering		Jul-01	260
1393N	....N	SEW	1999		Bush	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, crown sagging		Jul-01	120
1393N	1453N	SEW	1999		Kearny	Sutter	Bush	1890	?	3x5	BRICK	Fairly bad shape, loose bricks	RE	Apr-99	220
1393N	1453N	SEW	1999		Kearny	Sutter	Post	1875	?	3x5	BRICK	Bad shape, debris, crown sagging	RE	Apr-99	90
1393N	....N	SEW	1999		Post	Grant	Kearny	1880	?	3x5	BRICK	Bad shape, missing & loose bricks	MF	Aug-99	280
1393N	....N	SEW	2000		Sutter	Montgomery	Intersection	1876	?	3x5	BRICK	Intersection in bad shape	MF	Jan-01	50
1397N	7207E	SEW	1999		23rd St	Castro	Diamond	1888	?	15"	VCP	Severe cracks @ 25-70', heavy debris, dip	MF		190
1397N	7317E	SEW	1999		Dolores	28th St	Valley	1885	?	18"	VCP	Crushed and multiple cracks	MF/JP		99
1397N	....N	SEW	1999		Ord	Corbett	Market	1900	?	15"	VCP	Cracks, cracked invert, severe offsets	MF		60
1411N		SEW	1999		Harding Park	Skyline	Zoo					New Sewer			100
1413N	1756N	S&H	1998		Davis (Blk #200	Clay	Washington	1878	?	3x5	BRICK	Bad shape, debris, missing bricks & mortar	MF	Jan-04	180
1413N	BSSR	SEW	1998		Francisco	Stockton	Powell	1876	?	3x5	BRICK	Bad shape 1/2, fairly bad shape 1/2	MF	Oct-00	290
1413N	1453N	SEW	1998		Kearny	Green	Union	1900	?	12/8"	VCP	Crushed & cracked sections	RE	Apr-99	110
1474N	BSSR	SEW	1998		06th Ave	Cabrillo	Balboa	1902	?	12"	VCP	Many cracked sections; sev. open joints., bad ss & mh	MF		140
1474N	BSSR	SEW	1998		06th Ave	Fulton	Cabrillo	1907	?	8"	ISP	Many cracked sections, hole (repair done 1/12/96)	MF		170
1474N	....N	SEW	1998		08th Av	Fulton	Cabrillo	1907	?	8"	VCP	Numerous cracked sections, collapse			170
1474N	BSSR	SEW	1998		43rd Ave	Anza St	Balboa MB	1917	?	15"	VCP	Many cracks @ mh b-c exfiltration @ 120' b-c	OL	Aug-00	90
1475N	1389N	JP/S&H	1998		Fair St	Coleridge	Mission	1890		12"	VCP	Mult joint offsets,cracks, infiltration, st. depression	MF	Mar-99	99
1475N	1389N	JP/S&H	1998		Godeus	Coleridge MB	Mission		?	15"	VCP	Cracks/crush @123'-145'; cracks; open joints b-c	MF	Mar-99	80
1475N	1389N	JP/S&H	1998		Virginia	Coleridge	Mission St	1905	?	16"	VCP	BSSR RECOMMENDED REPLACEMENT	MF	Mar-99	90
1548N	BSSR	SEW	1998		Deming	Clayton MB	Uranus	1920		12"	ISP	Ready to collapse	OL		105
1548N		SEW	1998		Farnsworth	Edgewood	Willard		?	12"	VCP	Severe cracks, stopped @ 83'; recommend lining			80
1548N		SEW	1998		Iron Alley	Corbett	Clayton	1917	?	15"	VCP	Offsets, roots, Hole invert @ 140' b-c			130
1548N	....N	SEW	1998		O'Farrell	Anza Vista	Masonic	1947		15"	VCP	Numerous cracks			150
1563N	BSSR	SEW	1999		03rd Ave	Balboa	Anza	1908	?	8"	VCP	Many street dep.; many cracks/holes ms/ss	MF		160
1563N		SEW	1999		20th Ave	Fulton	Cabrillo	1915		8"	ISP	Numerous street depressions			140
1563N	BSSR	SEW	1999		42nd Ave	Geary	Anza	1920	?	8"	VCP	Street depression, collapse; sev. open joints	MF		150
1563N	....N	SEW	1999		Balboa	Arguello	2nd Ave	1907	?	18"	ISP	Multiple cracks			120
1579N	1454N	JP/S&H	1998		Illinois	20th St	19th St	1910	?	18"	VCP	Multi cracked, crushed sections b-c; TV'd 60' b-c	TR	Jan-99	130
1603N		SEW	1999		Broad	Capitol	Plymouth	1910	?	8"	ISP	Many depressions, complaints, MUNI track replmt			220
	98-99 REMAINING SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $1.0 MILLION)														1,000
1395N		SEW	1999		Larkin	Pine	Bush	1875	?	3x5	BRICK	Bad shape, many loose bricks			220
1395N	....N	SEW	1999		Pine	Polk	Larkin	1880	?	3x5	BRICK	Fairly bad shape (230'), st. depression			280
1395N		SEW	1999		Sacramento	Grant	Kearny	1880	?	3x5	BRICK	Bad shape; missing & loose bricks			280
1395N	1453N	SEW	1999		Sacramento	Sansome	Battery	1908		12"	ISP	Many cracks, crushed sections, debris	MF	Oct-98	90
1578N	1668N	JP/S&H	1999		Golden Gate	Polk St	Van Ness	1873		3'x5'	BRICK	Many St. depressions, Rec. by BSSR	MF	Jan-00	150
1578N	1668N	JP/WD	1999		Golden Gate	Scott MB	Pierce	1875		14"	ISP/CP	Cement pipe sections, badly cracked	MF	Jan-00	80
1583N		SEW	1999		Bridgeview	Topeka	Thornton	1941		12"	VCP	Many cracks & ss problems, invert break			180
1583N		SEW	1999		Everglade	Gellert	Lake Merced		?	21"	VCP	Easement;collapsed @ 30-40' a -b; exfiltration(line?)			49
1583N	7381E	SEW	1999		Revere	Griffith	Hawes MB	1930		8"	VCP	Many severe cracks/crushed mh b-c	MF	Jan-04	70
1583N	....N	SEW	1999		Victoria	Randolph	Brotherhood	1920	?	12"	ISP	Open break @112-115', cont. cracks, mh b-c			160
1628N	1687N	S&H	1999		Moraga St	17th Ave	18th Ave						RE	Oct-99	100
1777N	7458E	JP/S&H	1999	7	Clay	Jones MB	Taylor	1889	?	12"	?	Offsets, cracks, dip	RE	Jul-99	90
1787N	1477N		1999	201	Dartmouth	Dwight	Woolsey	1952		12"	VCP	Invert cracks, Open joints (needs lining)	RE	Jul-99	70
1787N	1477N		1999	201	Hamilton	Dwight	Woolsey	1952		12"	VCP	Cracks; crushed section (needs lining)	RE	Jul-99	70

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST (YEAR)	TAPE #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
START FY 99-00															
1585N	BSSR	SEW	1999		05th Ave	Balboa	Anza	1908	?	16"	VCP	Severe cracks, depn @ 8-37 c-b, many separated ss	MF		170
1585N		SEW	1999		21st Ave	Clement	California	1902	?	8"	VCP	Severe offsets,Separated ss's, st. depressions			130
1585N	1407N	SEW	1999		California	Parker	Maple	1900	?	16"	VCP	Severe open joints, st. depression; Lining rec.	MF	Jan-00	50
1586N	.....N	SEW	1999		Geary Bl. S. Side	Lyon	Baker	1879		18"	VCP	Severe multi cracks, fast flow, begin to collapse	MF	Jan-99	160
1586N	.....N	SEW	1999		Geary Bl. S. Side	Baker	Broderick	1879	?	18"	VCP	Multi cracks, roots, fast flow	MF	Jan-99	150
1586N	1732N	JP/SEW	1999		Turk	Broderick	Divisadero	1881		16"	ISP	Cracks, collapsed section	MF	Jul-99	160
1635N	....N	SEW	1999		Larkin	Grove	Hayes	1915		18"	VCP	TV'd 190', collapsed, dip, debris			110
		SEW	1999		Cesar Chavez (A	Bryant	York		?	12"	VCP	Many cracks and collapsed sections			70
		SEW	1999		Folsom	Bessie	Precita	1890	?	16"	VCP	Collapsed sections, severe offsets,open ss, fast flow			50
	....N	SEW	1999		Winding Way	Prague	Xing	1915	?	8"	VCP	Collapsed & crushed pipe, exfiltration	RE		30
99-00 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)															4,000
1586N	1732N	SEW	1999		Eddy	Pierce	Steiner	1875		3x5	BRICK	Bad shape (50'), rest needs plastering	MF	Jul-99	280
1586N	1732N	SEW	1999		Eddy	Steiner	Fillmore	1875		3'x5'	BRICK	Bad shape, missing bricks, mortar crown & walls; dirt	MF	Jul-99	170
1586N		SEW	2000		Elm	Scott MB	Pierce	1908	?	15"	ISP	Egg shape cracks & offsets			60
1587N		SEW	2000		07th Ave	Moraga	Lincoln	1890	?	3'x5'	Conc/Br	Fairly bad shape; Install spray-on mortar lining.			130
1587N	....N	SEW	2000		Kirkham	6th Ave MB	7th Ave	1906		18"	VCP	43 foot run with cracks throughout			120
1590N	7291E	SEW	2000		Ocean	San Leandro	San Fernando	1913		15"	VCP	Many severe cracks @ 1-90' a-b	MO	Apr-99	50
1590N	7291E	SEW	2000		Ocean	San Fernando	Junipero Serra	1913		18"	VCP	Severe Offsets & many cracked sections	MO	Apr-99	50
1590N	7291E	SEW	2000		Ocean	Pinehurst	Manor	1913		18"	VCP	Many cracked sections	MO	Apr-99	60
1589N		SEW	2000		Clipper	Douglass	Diamond MB	1962		15"	VCP	No TV Log; Many large cracks invert, exfiltration; fast flow			90
1589N	....N	SEW	2000		Noe	26th St.	Clipper MB	1888		18"	VCP	Cracks throughout, 33' run(debris)			110
1589N	1589N	SEW	2000		Fair Oaks	22nd St	23rd St	1878		15"	ISP	Submerged, pipe coming apart. Rec by PUC	MF	May-99	150
1589N	1589N	SEW	2000		Kingston	Mission	San Jose	1910	?	12"	VCP	Many cracks , dip, size changed to 6"	MF	May-99	50
1588N	6680E	SEW	2000		Alemany	Prentiss	Putnam		?	12"	VCP	Badly crushed pipe	MF		120
START FY 00-01															
1588N	BSSR	SEW	2000		Kensington	Merced	Claremont	1915		12"	VCP	Replace mh a-b, otherwise fair condition	MF	Jul-00	80
1588N	BSSR	SEW	2000		Mt Vernon	Delano	Cayuga	1927		12"	VCP	Crushed sections @ 88-103' a-b; st. depression	MF	May-01	90
1602N	....N	SEW	2000		02nd St	Brannan	Townsend	1890	?	18"	VCP	Many cracks / replace lower 1/2 block			170
1602N	....N	SEW	2000		Howard	01st St	Fremont	1880	?	3'x5'	BRICK	Bad shape, needs cleaning, plaster and bricks	MF		140
1602N	BSSR	SEW	2000		Minna	6th St	Russ	1908	?	18"	VCP	Cracked invert @ 76-78' c-d, st depressions	MF	Oct-01	120
1605N	BSSR	SEW	2000		Pierce	Green MB	Union	1885		18"	VCP	May collapse @219'-238', 0-110' replaced	MF	Sep-01	99
1605N	BSSR	SEW	2000		Sacramento	Spruce	Maple	1890	?	8"	ISP	Many seaprated ss's; infiltration	MF	Aug-00	120
1605N	....N	SEW	2000		Wilmot	Webster	Fillmore	1900	?	10"	ISP/CP	Multiple extensive cracks/ cement pipe			130
1629N	...N	JP/SEW	2000	208	Kearny	Filbert	Union	1900	?	15"	VCP	Severe offsets, crushed sections, exfiltration			90
1629N	1734N	JP/SEW	2000	398	Union	Hyde	Larkin	1900	?	12"/18"	ISP	Crushed invert; multiple cracks, exfiltration	MF	Jan-99	120
1629N	......N	JP/SEW	2000		Union	Hyde	Leavenworth	1900	?	8"/15"	ISP	3pt cracks, errosion of cement pipe sections, hole	OL	Jan-99	70
1629N	......N	SEW	2000		Union	Jones St	Taylor St	1900		16"	CEM	Many sections collapsed, fast flow, rat	MF	Jan-99	130
00-01 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)															4,000
1630N	1630N	SEW	2000		Sacramento	Taylor	Mason	1875		16"	ISP	Many cracks, open joint	MF	May-99	150
1631N		SEW	2000	383	04th Avenue	Cabrillo	Balboa	1908	?	8"	VCP	Street depressions, separated ss's, open breaks			180
1631N	BSSR	SEW	2000	400	10th Ave	Clement MB	Geary	1912	?	8"	ISP	Separated ss's, st depressions, low spots, exfiltration	MF	Aug-01	100
1631N	......N	SEW	2000		Anza	9th Avenue	10th Avenue	1907		8"	VCP	Many separated side sewers, exfiltration	MF	Jul-01	80
1631N	1322N	S &H	2000	366	Cabrillo St	6th Ave	7th Ave	1908	?	8"	VCP	Severe open breaks, street depressions	MF	Sep-98	80
1632N	BSSR	SEW	2000		Grove	Baker	Broderick	1890		16"	ISP	Severe offsets, cracks; crushed section	OL		130
1632N	......N	SEW	2000		Post	Lyon	Baker	1900		18"	VCP	ss separated ; hole invert 233-239' a-b, offses, fast flov	MF	Aug-01	150

SEWER REPLACEMENT PRIORITY LIST

JOB SEW	NO. S & H	LEAD	SCHED CONST (YEAR)	TAPE #	STREET	FROM	TO	YEAR CONST		SIZE	MAT	REVIEWER'S COMMENTS	TYPE PAVE	PROP'D PAVE DATE	PROJ. COST (000)
1632N		SEW	2000		Potomac St	Waller St	End South	1930	?	8"	VCP	Mult cracks, separated ss, infiltrtion, st. depn			80
1776N	1409N		2000	W038	Sutter	Buchanan	Webster	1875		3'x5'	BRICK	Bad cond. Offsets, MS Wall collapsed	MF	Jan-00	230
1784N	1727N	SEW	2000		Leavenworth	Washington	Jackson	1900	?	16"	VCP	Many cracks; invert break	MF	Jul-99	80
1784N	....N	SEW	2000		Leavenworth	Greenwich	Lombard	1890	?	16"	VCP	Crushed Pipe, Numerous Cracks			120
1796N	1385N	SEW	2000		Stillings	Malta	Congo	?		12"	VCP	Many open s/s conn., cracked section	RE	Jul-99	80
1796N	BSSR	SEW	2000		Prague	South Hill	Geneva	1915		8"	ISP	Broken sections, cracks	MF/OL		70
1796N		SEW	2000		Russia	Madrid	Lisbon	1907	?	16"	VCP	Cracks, larghe street depression'			100
			2000	W038	2nd St	Folsom	Howard	1880		3'x5'	BRICK	Bad shape. Crown sagging			210
	1407N		2000	219	California	Commenwealth	Cherry	1900		16"	VCP	Severe cracks in short block	MF	Jan-00	80
			2001	219	Capp St.	19th St.	20th St.	?		18	CEM	Cement pipe, open ss connections, active depressions			180
	......N	SEW	2001	402	Clement	27th Ave	26th Ave	1908	?	15"	ISP	Offset joints, many cracked sections	MF	Jul-01	99
	...N		2000	217	Geary Blvd.	Blake	Cook	?		16	RCP	Multiple cracks throughout	MF	Jan-99	90
			2000	197	Masonic	Page	Haight	1890		16"	VCP	Cracks, crushed; offset/open joints, depressions			110
	1215N		2000	W-017	McAllister	Steiner	Fillmore	1869		3x5	BRICK	Bad shape, crown,sidewall bulging;loose,missing bricl	MF	Jan-00	230
	1755N		2000		Oak St.	Webster	Buchanan	1877		12	ISP	Many severe offsets, crushed section.	MF	**May-00**	110
		SEW	2001	211	Pacific	Walnut	Laurel	1900	?	15"/12"	VCP	Cracks and open joints, street depressions, fast flow			120
	BSSR	SEW	2001	210	Precita South	Treat	Harrison	1900	?	16"	ISP	Multi cracks, loosing shape, fast flow, rat	MF	May-01	90
	BSSR	SEW	2001	210	Precita South	Harrison	Alabama	1900	?	16"/18"	ISP	Many cracks, ss open @ 79' & 148' a-b, rat, replace a-	MF	May-01	90
		SEW	2000		Union	Divisadero	Broderick	1885	?	8"/12"	VCP	Cracks/collapse, offsets, open joints		done 4/95	130
START FY 01-02															
	....N	SEW	2001		08th St	Market	Intersection	?		15"	VCP	Cracked sects. replace (a-b) across Market	RE		60
		SEW	2001		22nd Ave	Irving	Lincoln	1910	?	18"	VCP	Many active street depressions.			199
	....N	SEW	2001		Bryant	7th St	Gilbert	1876	?	3x5	BRICK	Bad shape, cracks on crown, ready to cave in	MF	Nov-00	120
		SEW	2001		Folsom	18th St MB	17th St	1946		15"	VCP	Cont cracks 55-130', depression 157' b-c			140
	....N	SEW	2001		Harrison	8th St	7th St	1880	?	3x5	BRICK	Missing mortar, loose bricks, out of round			550
		SEW	2001		Hayes	Larkin	Polk	1890	?	3x5	BRICK	Bad shape, severe sags, missing bricks,bulging			201
	BSSR	SEW	2001		Jones	Bernard	Pacific	1906	?	12"	VCP	Multiple cracked & collapsed sections	MF	n/a	50
	.....N	SEW	2001		Mission	13th St	14th St	1875	?	3'x5'	Brick	Bad shape, crown sagging, ready to collapse	MF		220
	....N	SEW	2001		Rincon	Bay Bridge	Bryant	1917	?	12"	VCP	Collapsed			70
	BSSR	SEW	2001		Sterling	I-80 ramp	Bryant	1900	?	12"	CEM	Multi cracks; ready to collapse; Rec. lining	MO	Oct-98	60
	....N	SEW	2001		Townsend	7th St Mb	8th St Mb	1921		12"	VCP	Dips, Cracks, Crushed		Oct-01	170
		SEW	2001		Esmt blk #4315/	Minnesota	3rd St	1949		12"	VCP	Several severe cracks & collapses			150
		SEW	2001		Esmt Blk #4317	Indiana	Minnesota	1949		12"	VCP	Severe multiple cracks			90
				W-040	***Turk***	***Polk***	***Larkin***	***1873***		***3x5***	***BRICK***	***Bad MHb, St collapse heavy debris,cracks, bricks loose, bulging***			***190***
	01-02 SEWER EMERGENCIES AND ACCELERATED PROJECTS (ESTIMATED COST $4.0 MILLION)														4,000
	....N	SEW	2002		Geary	Mason	Powell	1880		3x5	BRICK	Bad shape, crown buckled, mortar, bricks missing	MF	Jul-01	120
	....N	SEW	2002		Jones	Filbert	Lombard	1919		12"	VCP	Numerous Cracks			220
	....N	SEW	2002		Buchanan	Greenwich	Lombard St	1887		18"	VCP	Cracks, offsets, open joints			130
			2002		Stonestown Trestle Removal							Trestle is an attractive nuisance			299
			2002		Chinatown Alleys(3)										150
	....N	SEW	2002		Washburn	Howard	Mission	1900	?	3x5	BRICK	Fairly bad shape, bricks, broken s/s			350
	BSSR	SEW	2002		Bayshore(W Sid	Cortland	Oakdale	1928		12"	VCP	Many bad cracks & breaks	MF		110
START FY 02-03															
		SEW	2002		Esmt Block#113	End North	Anza	1935		8"	VCP	Many separated ss's from main, exfiltration			90
		SEW	2002		City View Way	Skyview	Knollview	1951		8"	VCP	Street depressions; crushed, open joints, exfiltration, fast flow			70

SF
P85.
*2
51.3

SF
P85.93
#2
5/13/99

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

DOCUMENTS DEPT.
JUN 03 1999
SAN FRANCISCO
PUBLIC LIBRARY

MINUTES OF MEETING NO. 411
May 13, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4046
Eric Kjelsberg	558-4012
Joe Ovadia	558-4004
Gilbert Tang	554-8264
Jean To	554-8298
James Walsh	554-8272

Street Construction Coordination Center

Cynthia Chono	554-6196
Nancy Lynch	554-5870
Mauricio Monsalve	554-8261
Joe Norris	554-8274
Jerry Tsai	554-8261

Bureau of Street and Sewer Repair

Niles McDonald	695-2100

Bureau of Street Use Management

Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326
Carl Shorter	554-2322
Peter Woo	554-2320

MUNI Engineering/DDC

(Representative not present)

PUC Sewers

Henry Anderson	648-6882
Lorenzo Hale	695-2096
Joe Herrera	695-2096

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

Thinh Nguyen	550-4916

Redevelopment Agency

(Representative not present)

Caltrans

Dean Drablos	330-6537
Don Manning	557-4022

Caltrans Public Information

(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric

Kathy Devine	695-3492

S F Thermal

(Representative not present)

Allstar / Metro Media

(Representative not present)

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

(Representative not present)

RCN

Jim Coppedge	650-794-2755
Brian Heckman	650-794-2735
Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500 x-3346

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 411

1. The members introduced themselves around the table. Ms. Chono introduced herself as the new Manager for the Street Construction Coordination Center.

2. The April 8, 1998 Minutes were approved.

3. Meeting Agenda

Ms. Chono proposed changes to the agenda format for regular monthly meetings. See also discussion for a special meeting in June, at the end of these minutes.

For the present, meetings will consist of:

Project Updates
    Under Construction
    Proposed and new

Improvement Issues
    Updating process (housekeeping, etc)
    Clearance or coordination dates (eg, what the date actually means)

New Business

4. X-1104

Ms. Chono noted that the X-1104 process is part of the Mayor's push to improve user-friendliness in the street system, by addressing paving and other defects. It is one of the enforcement devices for the Excavation Code. It should be an improvement issue, both for CULCOP and for each agency. For example, its success depends on each agency's designating one responsible person to receive notices and initiate their response.

5. Paving Projects

Mr. Ovadia distributed a list of streets for the forthcoming as-needed paving contract at the May 3 SCCC meeting. The contract was advertised last Saturday. PG&E and Pac Bell have project scheduling conflicts in some of the streets.

The as-needed list is a subset of a 120-street list for needed clearances for BSSR paving to begin on July 1. It consists of streets with no 5-year projects or clearance dates in the present Status Report.

There was discussion of the 120 street list as a departure from, or addition to, the usual clearance process, which would be confusing and require redundant effort of agencies with already-stretched staffs. While the paving program is being pressed by the Mayor for a faster pace, the agencies should not have to respond more than once for each block. The reason for asking clearances after we have the 5-year programs is that the 5-year programs may not always be current and that they do not capture all activity. It might be possible to clear automatically in areas where an agency will definitely not be active.

Note that coordination must be in time as well as place. For example, we need to avoid timing two nearby projects that would divert traffic into each other's sites.

New Paving Contracts: The Mayor has required DPW to pave Franklin between McAllister and Market, and Geary between Gough and Webster, this year. If there are scheduling conflicts, the affected agency should discuss them with Mr. Primeau.

6. RCN Program

Mr. Weber discussed RCN's plans for installations in the Bay Area. "RCN" stands for "Residential Communication Networks", which describes their scope and marketing aim. RCN has been active on the east coast for four or five years installing fiber optics multiplex systems. They are currently the seventh largest ISP in the US. They intend to service the communities from San Francisco to San Jose and will have their five year plan available soon. They intend to install a service node for sets of not more than 200 homes each, with individual connections from there using coax cable pending fiber availability. More information is available at RCN.com.

Given the wide scope, there will be many opportunities for coordinated or joint work, which RCN is exploring.

Mr. Weber also introduced Mr. Heckman and Mr. Coppedge, who will be representing RCN locally.

Mr. Drablos noted that some parts of the installation may need Caltrans permits, for which RCN can call Mr. Drablos.

7. Port Construction

Mr. Zeller announced that a new ferry terminal at the north side of entrance to China Basin will require four new piles in the water. Any utilities with underwater cables in the area should notify him.

8. DPT Issues

Mr. Woo introduced three areas of concern to DPT:

Traffic Signal Detector Loops

There have been many cases, such as Allstar work at Fifth and Howard, where traffic signal loop detectors or, in this case, the red light camera detector, were cut and the damage not reported. Since detector loops are always installed in saw-cuts after paving, they are always visible where present, whether USA-marked or not. If they are damaged by construction, only the traffic signal shop (550-2736) is authorized to replace them.

Ms. Chono noted that all installations should be USA marked, visible or not. The presence of side sewers, for instance, is also obvious given the vent cover and the convention of placing mains on the street center line. We should not expect contractors to know about any unmarked facility. Looped intersections could be included in the electronic permit alert.

Mr. Broady will give a presentation about loop detectors, how to recognize them and how to protect them, at a forthcoming meeting.

Traffic striping and messages

Any painted striping or messages on the pavement that are disturbed by construction activity must be promptly restored. This is a public safety issue. It applies whether the damage was at the actual excavation or in a staging area or in any other way connected to the excavator's physical presence. The latest version of the Blue book requires notification of the DPT Paint Shop (Mr Shorter at 554-2322), for restoration by DPT. Contrary to past practice, the excavator may not do the restoration.

The latest permit format gives square footage and approximate location but no dimensions that would indicate likely damage. Note that the lines on the diagram do not guarantee the limits of the impact on the ground. The proper time to involve DPT is at the walk-through of the site upon completion of work. This is especially important when an agency has to import an out of town contractor who does not know the local rules.

Blue Book Rules

There have been incidents of crews adversely affecting traffic by working into restricted hours or improperly managing lane closures. For non-emergency work, the scheduling must allow time for dealing with unexpected factors, such that the work is not still in progress when it is time to leave. This includes manhole openings. Likewise, the rules about lane closures apply beyond the particular block. A utility recently worked in two adjacent blocks of Bush Street, with lane closures in compliance for each block, but the closures were on opposite sides of the street from one to the other, which still disrupted traffic in the way the rules were intended to avoid. Traffic impact must be addressed for the project, not separately block by block.

9. Electronic Permit Recognition

Ms. Chono presented Mr. Nguyen with a placque in recognition of the Water Department's being the first to use the electronic permitting system.

Special June Meeting

CULCOP has been evolving over several years from a device to facilitate the paving program to a forum to improve public service through project-driven rather than pavement-driven coordination. Recent legislation and the increased pace of street construction have accelerated that development and led to forming the new Street Construction Coordination Center (SCCC). However, the format of the Status Report still reflects the original pavement-driven model, and the mandate for separate SCCC meetings has raised questions about the mission of CULCOP in the new environment. We will begin to address such questions at the special meeting at 8:30 am, June 10, 1999, before the regular monthly CULCOP meeting which will begin half an hour later than usual, at 10:30 am, to accommodate it. We ask that each agency send one person to the special meeting, prepared to discuss current needs and possible solutions on the way to clarifying what the mission of CULCOP is today in terms of shared practical business needs and how we can fulfill that mission to everyone's advantage.

The next meeting will be at 10:00 am Thursday, June 8, 1999, the second Thursday of the month, at **875 Stevenson St, Rm 410**

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

SF
P85.93
#1
6/10/99
Special

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Location: **875 Stevenson St, Rm 410**

Date: **Thursday, June 10, 1999 8:30 to 10:30 am.**

Subject: **SPECIAL MEETING: FUTURE OF CULCOP — MISSION AND GOALS**

1.	Refreshments	All
2.	Welcome and Introductions	All
3.	Purpose of Meeting and Review Agenda	Ms. Chono
4.	Evolution of CULCOP Original Mandate – See Attached Code Extract Development and Realignment New Environment and Legislation The New Ballgame	Mr. Norris
5.	CULCOP Mission and Goals	All (Please send ONE representative per agency)

DOCUMENTS DEPT.

JUN 0 3 1999

SAN FRANCISCO
PUBLIC LIBRARY

06-03-99A10:56 RCVD

San Francisco Administrative Code

Article VII

STREET UTILITIES COORDINATING COMMITTEE AND CITIZENS ADVISORY COMMITTEE FOR STREET UTILITY CONSTRUCTION

SEC. 5.60. STREET UTILITIES COORDINATING COMMITTEE. There is hereby established a committee to be known as the Street Utilities Coordinating Committee consisting of the Director of Public Works, who is to act as chair; a representative from the Department of City Planning; a representative from the Citizens Advisory Committee to the Street Utilities Coordinating Committee who shall be selected by the Chief Administrative Officer of the City and County from those members of the above committee representing citizen input only and not from any utility or city department; and one senior management representative from each of the following: San Francisco Water Department; Pacific Gas and Electric Company, Gas Division; Pacific Gas and Electric Company, Electric Division; Pacific Telephone Co.; Western Union; and Television Signal Corporation. (Added by Ord. 273-74, App. 6/6/74)

SEC. 5.61 STREET UTILITIES COORDINATING COMMITTEE — MEETINGS. Places, dates, and times of meetings shall be as prescribed by the chair. (Added by Ord. 273-74, App. 6/6/74)

SEC. 5.62 STREET UTILITIES COORDINATING COMMITTEE — DUTIES. This committee shall be charged with the responsibility of formulating policy as it affects the use of public streets by public and private utilities, such as overall traffic regulations during utility construction or maintenance; utility advance planning, and other means to insure minimum disruption and inconvenience to the general public using the surface of the streets; utility joint trenches; utility tunnels; and condition of trench repairs. (Added by Ord. 273-74, App. 6/6/74)

SEC. 5.63 STREET UTILITIES COORDINATING COMMITTEE — SUBCOMMITTEES. There are hereby established two subcommittees to the Street Utility Coordinating Committee as follows:

(a) Committee for Utility Liaison on Construction and Other Projects (CULCOP). This subcommittee shall consist of staff level personnel from the Bureau of Engineering of the Department of Public Works; San Francisco Water Department; Hetch Hetchy Water and Power System; Municipal Railway; San Francisco Fire Department; Pacific Gas and Electric Company, Gas Division; Pacific Gas and Electric Company, Electric Division; Pacific Telephone Company; Western Union; and the Television Signal Corporation. The chair shall be a representative of the Bureau of Engineering as designated by the City Engineer. Meetings shall be monthly at a time and place designated by the chair. The duties of this subcommittee shall be to work out scheduling of utility work that is connected with Department of Public Works projects and plan the utilities undergrounding construction program.

Committee for Planning Utility Construction Program. This subcommittee shall consist of representatives of the Department of Public Works; San Francisco Water Department; Hetch Hetchy Water and Power System; Municipal Railway; San Francisco Police Department; Pacific Gas and Electric Company, Gas Division; Pacific Gas and Electric Company, Electric Division; Pacific Telephone Company; Western Union; and the Television Signal Corporation. The chair shall be a representative of the Department of Public Works as designated by the Director of Public Works. Meetings shall be at the call of the chair. This subcommittee shall be responsible for detailed planning of a 12 months construction program of all street utilities, exclusive of Department of Public works projects which are financed wholly or in part by gas tax or ad valorem funds and utilities undergrounding program, including traffic regulations during utility construction or maintenance, and other duties as assigned by the Street Utilities Coordinating Committee. The Director of Public Works shall transmit to private utility companies and to said subcommittee a list of approved gas tax and ad valorem projects, as soon as such projects are approved by the Board of Supervisors. (Added by Ord. 273-74, App. 6/6/74)

SEC. 5.64. CITIZENS ADVISORY COMMITTEE FOR STREET UTILITY CONSTRUCTION. There is hereby established a committee to be known as the Citizens Advisory Committee for Street Utility Construction consisting of 21 members to be appointed by the Chief Administrative Officer as follows: one representative from each of the following: Department of Public Works; Police Department; Water Department; Municipal Railway; Pacific Gas and Electric Company, Gas Division; Pacific Gas and electric Company, Electric Division; Pacific Telephone Company; Western Union; Television Signal Corporation; San Francisco Planning and Urban Renewal Association; Greater San Francisco Chamber of Commerce; San Francisco Council of District Merchants Association; Associated General Contractors of California; organized labor; Downtown Association; and six members selected from neighborhood organizations representing the various neighborhoods within the city. The committee shall elect a chair from the membership thereof. Any member may delegate an alternate within his or her respective organization to represent him or her at any meeting of the committee in the member's absence. Vacancies on the committee shall be filled by the Chief Administrative Officer in the manner herein provided for the appointment of the original members. (Added by Ord. 273-74, App. 6/6/74)

SEC. 5.64. CITIZENS ADVISORY COMMITTEE FOR STREET UTILITY CONSTRUCTION — MEETINGS. Places, dates, and times of meetings shall be as prescribed by the chair. (Added by Ord. 273-74, App. 6/6/74)

SEC. 5.64. CITIZENS ADVISORY COMMITTEE FOR STREET UTILITY CONSTRUCTION — DUTIES. The duties of the committee shall be to secure citizens' input concerning general problems relating to the use of any digging-up of streets and sidewalks by utility companies or city departments, and to recommend to the Street Utilities Coordinating Committee ways and means to alleviate these problems. (Added by Ord. 273-74, App. 6/6/74)

SF
85
#2
6/10
Spec

SF Utility Liaison on Construction

SF
P85.93
#2
6/10/99
Special

MINUTES OF SPECIAL MEETING

June 10, 1999

ATTENDANCE:

Department of Public Works		
Bureau of Engineering		
	Gilbert Tang	554-8264
	Ryan Cayabyab	554-8307
Street Construction Coordination Center		
	Cynthia Chono	554-6196
	Nancy Lynch	554-5870
	Mauricio Monsalve	554-8261
	Joe Norris	554-8274
	Scott Northrup	
	Jerry Tsai	554-8261
Bureau of Street and Sewer Repair		
	Niles McDonald	695-2100
Bureau of Street Use Management		
	Tom Trimbur	554-6161
Bureau of Construction Management		
	(Representative not present)	
Department of Parking and Traffic		
	Scott Broady	554-2326
MUNI Engineering/DDC		
	Carlos Carrillo	554-9286
	Charles Kascal	557-9983
PUC Sewers		
	Henry Anderson	648-6882
San Francisco Port Authority		
	(Representative not present)	
San Francisco Water Department		
	Thinh Nguyen	550-4916
San Francisco Fire Department AWSS		
	Mike Nara	558-3557
Redevelopment Agency		
	(Representative not present)	
Caltrans		
	Dean Drablos	330-6537
Caltrans Public Information		
	(Representative not present)	
Pacific Bell		
	Cindy Vowell	542-9095
Pacific Gas & Electric		
	Kathy Devine	695-3492

S F Thermal		
	(Representative not present)	
Allstar / Metro Media		
	Nick Araujo	431-2510
AT&T		
	(Representative not present)	
BDI		
	(Representative not present)	
GST		
	(Representative not present)	
ICG		
	(Representative not present)	
Level 3 Communications		
	Dom Filardo	408-523-9096
MFN		
	(Representative not present)	
RCN		
	Brian Heckman	650-794-2735
TCG		
	(Representative not present)	
TCI		
	Terry Bouey	863-8500
Underground Construction		
	Andrew McManus	882-1553

DOCUMENTS DEPT.
JUL 08 1999
SAN FRANCISCO
PUBLIC LIBRARY

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF SPECIAL MEETING

I. The members introduced themselves around the table.

Ms Chono and Mr Norris discussed the historical process that brought us from an uncoordinated beginning with few standards and minimal records to the present in which public health and safety, high work volume in limited space, and the large number of players have forced us to develop elaborate coordination, construction standards, and record keeping. The existing Administrative Code, last updated in 1974, requires a monthly meeting of DPW and other agencies active in street construction to coordinate schedules. The City's Pavement Management System, inaugurated in the mid-1980s and supplemented with the Stick Map, prompted the introduction of the Status Report as a device to "clear" streets for paving and avoid digups in new pavement. Use of the Stick Map, in the context of developing GIS and generalized Infrastructure Management, has encouraged a broader model for program-driven rather than pavement-driven coordination. The new Excavation Code is the latest move in the same direction, in which paving is one among many IMS programs and in many cases logically follows from other agencies' projects.

The current issue is what to coordinate at which point in the process. Broadly, street work falls into two categories:

- **IMS generated** work addresses the scenario in which the condition of a segment in a system reaches an ideal, cost-effective time for maintenance. The IMS, properly conducted, can project in advance for a window of opportunity, typically several years wide, during which the optimum maintenance will be effective. The actual work will occupy only a small segment of that time. Within the window, the schedule is arbitrary and could be adjusted without problems. Where more than one such window falls onto the same block, the coordination is straightforward if both show up early enough. Actual commitment of resources to a schedule comes later, when the known potential conflicts are already resolved. Note that each agency will need to verify the need to do each site before publication, not after everyone else has responded.

- **Customer demand** is less predictable at a block-sized level of resolution, although it should be possible to detect major changes earlier than is now usual. Lead time should normally be proportional to price tag, so that a large hotel, for instance, might appear on the screen comparably to a main replacement if we can devise ways to capture the early signs. For smaller projects showing up later, the cost should be less and the adjustments by the customer should be more easily made, such as by stubbing ahead of another project and then hooking up later.

By the time actual construction occurs, the coordination should be at the level of support and work around, or adjustment of castings, rather than rescheduling.

Viewing the process as a whole, we could have SCCC doing the program-level windows and CULCOP doing the project-level adjustments.

Mr Monsalve reviewed the current clearance process as an introduction to a discussion of members' issues and suggestions.

Ms Devine raised a set of questions about the timeliness of clearance information and of its proper use. For example, how long is a date considered valid after its face value? How does a member rescind clearance when the situation changes? How much lag is appropriate between the all-cleared date and start of construction?

Mr Anderson noted that the cost per block for paving is commonly much less than for utilities such as sewers that have been expected to accommodate it, rather than the other way around.

Several members suggested that the 5 year horizon is not a matter of one size fits all; different systems have different conveyor belt speeds.

Ms Lynch noted that relevant street activity includes more than actual construction; it must account for site developments and major events such as the Moscone expansion, the ballpark construction and then games, or the Bay to Breakers.

From discussion, a set of criteria emerged that need to be addressed for coordination:

- ✓ Public health and safety
- ✓ "Just-in-time" infrastructure maintenance
- ✓ Concurrent events in the neighborhood
- ✓ Whether to schedule towards matching or missing construction dates
- ✓ New construction vs routine IMS
- ✓ Appropriate decision makers involved for each phase

Regarding the last point, if SCCC looks ahead and CULCOP looks at the moment, we are talking about two different layers of management, according to authority to decide relevant issues on the spot.

Mr Anderson suggested the names of the two forums should reflect their respective functions better than "SCCC" and "CULCOP" do. Mr McManus proposed three segments for the process: SCCC for the big picture looking ahead, CULCOP for generic details and frequently raised issues, and the precontract conference for site-specific matters.

Ms Devine suggested arranging the paperwork to reflect the actual process, with attention to when each transmittal captures what information for what purpose. This has been confusing throughout the process. Also, who calls a conflict-resolution meeting? Ms

Chono responded that each player is responsible for proactively addressing whatever they need to have addressed, while SCCC tracks the process and provides the forum.

In summary, Ms Chono noted that the term “SCCC” has been used to refer both to the organization within DPW and to the meeting forum. In reality, the two meetings implement two subsets of the SCCC function. The scope and attendance of each should relate to their respective aspects of the larger picture.

C. CLEARANCE (SCCC)

- GET A LIST OF CANDIDATES FROM PAVING MANAGER
- CHECKS CLEARED BLOCKS, PROJECTS, 5YR FROM DATABASE
- SEND TO UTILITIES FOR CLEARANCE
- PUT INTO DATABASE UTILITIES RESPOND
- SEND FINAL CLEARED LIST TO PAVING MANAGER

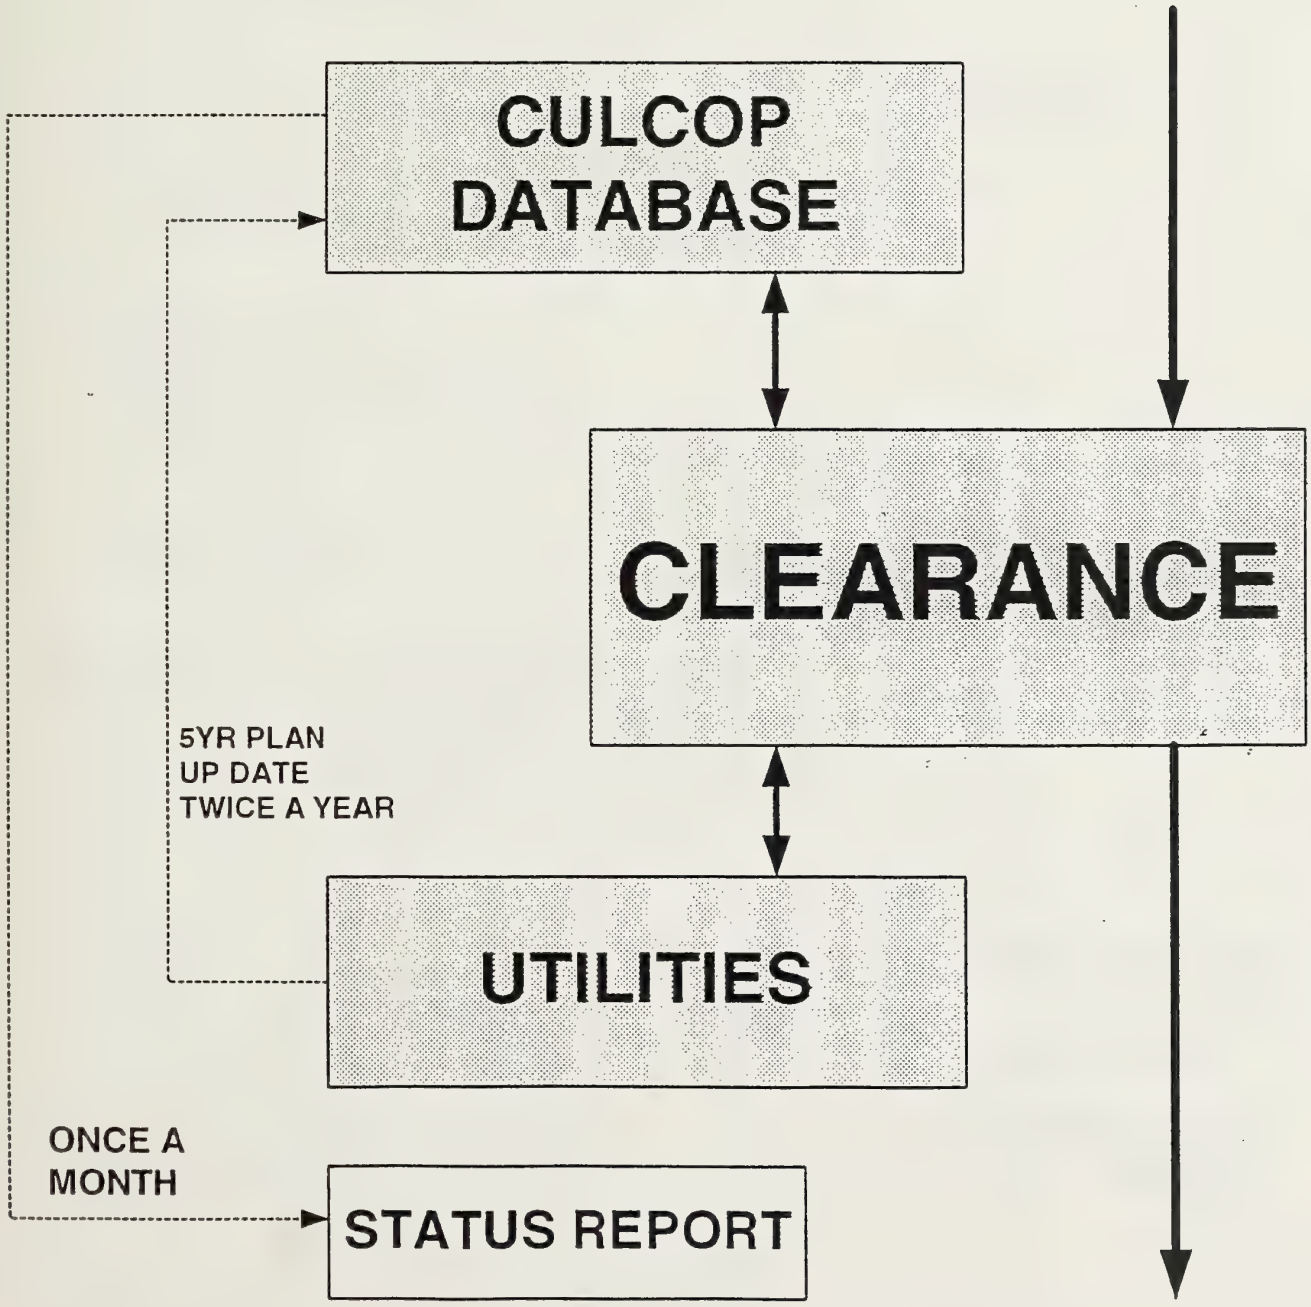
CULCOP DATABASE

CLEARANCE

5YR PLAN
UP DATE
TWICE A YEAR

UTILITIES

ONCE A
MONTH

STATUS REPORT

City and County of San Francisco **Department of Public Works**

Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Agenda

SF
P85.93
#1
6/10/99

Location: **875 Stevenson St, Rm 410 — Note changed location**

Date: Thursday June 10, 1999 **10:30 to 12:00 noon** following special meeting

Subject: Committee Meeting 412- Coordination of Street Construction

1) Introduction	
2) Approval of Minutes for May 13th Meeting	
3) X1104 Monthly Report	Cynthia Chono
4) Project Updates Under Construction New	Any
5) Improvement Issues Data updates / housekeeping Clearance / Coordination (what question does a date answer?)	All
6) Other New Business	All

Next Meeting: 2nd Thursday of Each Month
Thursday July 8, 1999 at 10:00 A. M.
875 Stevenson St, Rm 410

DOCUMENTS DEPT.
JUN 03 1999
SAN FRANCISCO
PUBLIC LIBRARY

06-03-99A10:57 RCVD

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-8274, at leaStreet72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-8274.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 875 Stevenson St, Rm 410. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L on Mission Street; # 42 on Van Ness Avenue;
   #26 on Valencia Street; #71 on Noriega Street; #9 on Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 411

May 13, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Scot Burbank	558-4046
Eric Kjelsberg	558-4012
Joe Ovadia	558-4004
Gilbert Tang	554-8264
Jean To	554-8298
James Walsh	554-8272

Street Construction Coordination Center

Cynthia Chono	554-6196
Nancy Lynch	554-5870
Mauricio Monsalve	554-8261
Joe Norris	554-8274
Jerry Tsai	554-8261

Bureau of Street and Sewer Repair

Niles McDonald	695-2100

Bureau of Street Use Management

Tom Trimbur	554-6161

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326
Carl Shorter	554-2322
Peter Woo	554-2320

MUNI Engineering/DDC

(Representative not present)

PUC Sewers

Henry Anderson	648-6882
Lorenzo Hale	695-2096
Joe Herrera	695-2096

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

Thinh Nguyen	550-4916

Redevelopment Agency

(Representative not present)

Caltrans

Dean Drablos	330-6537
Don Manning	557-4022

Caltrans Public Information

(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric

Kathy Devine	695-3492

S F Thermal

(Representative not present)

Allstar / Metro Media

(Representative not present)

AT&T

(Representative not present)

BDI

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MFN

(Representative not present)

RCN

Jim Coppedge	650-794-2755
Brian Heckman	650-794-2735
Sieg Weber	650-794-2696

TCG

(Representative not present)

TCI

Louis Victorio	863-8500 x-3346

Underground Construction

(Representative not present)

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 411

1. The members introduced themselves around the table. Ms. Chono introduced herself as the new Manager for the Street Construction Coordination Center.

2. The April 8, 1998 Minutes were approved.

3. Meeting Agenda

Ms. Chono proposed changes to the agenda format for regular monthly meetings. See also discussion for a special meeting in June, at the end of these minutes.

For the present, meetings will consist of:

Project Updates
- Under Construction
- Proposed and new

Improvement Issues
- Updating process (housekeeping, etc)
- Clearance or coordination dates (eg, what the date actually means)

New Business

4. X-1104

Ms. Chono noted that the X-1104 process is part of the Mayor's push to improve user-friendliness in the street system, by addressing paving and other defects. It is one of the enforcement devices for the Excavation Code. It should be an improvement issue, both for CULCOP and for each agency. For example, its success depends on each agency's designating one responsible person to receive notices and initiate their response.

5. Paving Projects

Mr. Ovadia distributed a list of streets for the forthcoming as-needed paving contract at the May 3 SCCC meeting. The contract was advertised last Saturday. PG&E and Pac Bell have project scheduling conflicts in some of the streets.

The as-needed list is a subset of a 120-street list for needed clearances for BSSR paving to begin on July 1. It consists of streets with no 5-year projects or clearance dates in the present Status Report.

There was discussion of the 120 street list as a departure from, or addition to, the usual clearance process, which would be confusing and require redundant effort of agencies with already-stretched staffs. While the paving program is being pressed by the Mayor for a faster pace, the agencies should not have to respond more than once for each block. The reason for asking clearances after we have the 5-year programs is that the 5-year programs may not always be current and that they do not capture all activity. It might be possible to clear automatically in areas where an agency will definitely not be active.

Note that coordination must be in time as well as place. For example, we need to avoid timing two nearby projects that would divert traffic into each other's sites.

New Paving Contracts: The Mayor has required DPW to pave Franklin between McAllister and Market, and Geary between Gough and Webster, this year. If there are scheduling conflicts, the affected agency should discuss them with Mr. Primeau.

6. RCN Program

Mr. Weber discussed RCN's plans for installations in the Bay Area. "RCN" stands for "Residential Communication Networks", which describes their scope and marketing aim. RCN has been active on the east coast for four or five years installing fiber optics multiplex systems. They are currently the seventh largest ISP in the US. They intend to service the communities from San Francisco to San Jose and will have their five year plan available soon. They intend to install a service node for sets of not more than 200 homes each, with individual connections from there using coax cable pending fiber availability. More information is available at RCN.com.

Given the wide scope, there will be many opportunities for coordinated or joint work, which RCN is exploring.

Mr. Weber also introduced Mr. Heckman and Mr. Coppedge, who will be representing RCN locally.

Mr. Drablos noted that some parts of the installation may need Caltrans permits, for which RCN can call Mr. Drablos.

7. Port Construction

Mr. Zeller announced that a new ferry terminal at the north side of entrance to China Basin will require four new piles in the water. Any utilities with underwater cables in the area should notify him.

8. DPT Issues

Mr. Woo introduced three areas of concern to DPT:

Traffic Signal Detector Loops

There have been many cases, such as Allstar work at Fifth and Howard, where traffic signal loop detectors or, in this case, the red light camera detector, were cut and the damage not reported. Since detector loops are always installed in saw-cuts after paving, they are always visible where present, whether USA-marked or not. If they are damaged by construction, only the traffic signal shop (550-2736) is authorized to replace them.

Ms. Chono noted that all installations should be USA marked, visible or not. The presence of side sewers, for instance, is also obvious given the vent cover and the convention of placing mains on the street center line. We should not expect contractors to know about any unmarked facility. Looped intersections could be included in the electronic permit alert.

Mr. Broady will give a presentation about loop detectors, how to recognize them and how to protect them, at a forthcoming meeting.

Traffic striping and messages

Any painted striping or messages on the pavement that are disturbed by construction activity must be promptly restored. This is a public safety issue. It applies whether the damage was at the actual excavation or in a staging area or in any other way connected to the excavator's physical presence. The latest version of the Blue book requires notification of the DPT Paint Shop (Mr Shorter at 554-2322), for restoration by DPT. Contrary to past practice, the excavator may not do the restoration.

The latest permit format gives square footage and approximate location but no dimensions that would indicate likely damage. Note that the lines on the diagram do not guarantee the limits of the impact on the ground. The proper time to involve DPT is at the walk-through of the site upon completion of work. This is especially important when an agency has to import an out of town contractor who does not know the local rules.

Blue Book Rules

There have been incidents of crews adversely affecting traffic by working into restricted hours or improperly managing lane closures. For non-emergency work, the scheduling must allow time for dealing with unexpected factors, such that the work is not still in progress when it is time to leave. This includes manhole openings. Likewise, the rules about lane closures apply beyond the particular block. A utility recently worked in two adjacent blocks of Bush Street, with lane closures in compliance for each block, but the closures were on opposite sides of the street from one to the other, which still disrupted traffic in the way the rules were intended to avoid. Traffic impact must be addressed for the project, not separately block by block.

9. Electronic Permit Recognition

Ms. Chono presented Mr. Nguyen with a placque in recognition of the Water Department's being the first to use the electronic permitting system.

Special June Meeting

CULCOP has been evolving over several years from a device to facilitate the paving program to a forum to improve public service through project-driven rather than pavement-driven coordination. Recent legislation and the increased pace of street construction have accelerated that development and led to forming the new Street Construction Coordination Center (SCCC). However, the format of the Status Report still reflects the original pavement-driven model, and the mandate for separate SCCC meetings has raised questions about the mission of CULCOP in the new environment. We will begin to address such questions at the special meeting at 8:30 am, June 10, 1999, before the regular monthly CULCOP meeting which will begin half an hour later than usual, at 10:30 am, to accommodate it. We ask that each agency send one person to the special meeting, prepared to discuss current needs and possible solutions on the way to clarifying what the mission of CULCOP is today in terms of shared practical business needs and how we can fulfill that mission to everyone's advantage.

The next meeting will be at 10:00 am Thursday, June 8, 1999, the second Thursday of the month, at **875 Stevenson St, Rm 410**

P25.93
#2
6/10/99

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

DOCUMENTS DEPT.
JUL 08 1999
SAN FRANCISCO
PUBLIC LIBRARY

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 412
June 10, 1999

ATTENDANCE:

Department of Public Works		
	Bureau of Engineering	
	Eric Kjelsberg	558-4012
	Joe Ovadia	558-4004
	Gilbert Tang	554-8264
	Ryan Cayabyab	554-8307
	Street Construction Coordination Center	
	Cynthia Chono	554-6196
	Nancy Lynch	554-5870
	Mauricio Monsalve	554-8261
	Scott Northrup	
	Joe Norris	554-8274
	Jerry Tsai	554-8261
	Bureau of Street and Sewer Repair	
	Niles McDonald	695-2100
	Bureau of Street Use Management	
	Tom Trimbur	554-6161
	Bureau of Construction Management	
	(Representative not present)	
Department of Parking and Traffic		
	Scott Broady	554-2326
MUNI Engineering/DDC		
	Carlos E Carrillo	554-9286
	Charles Kascal	557-9983
	Ed Viray	554-1838
PUC Sewers		
	(Representative not present)	
San Francisco Port Authority		
	(Representative not present)	
San Francisco Water Department		
	Thinh Nguyen	550-4916
Redevelopment Agency		
	(Representative not present)	

Caltrans		
	Dean Drablos	330-6537
Caltrans Public Information		
	Veronica Faisant	495-5895
Pacific Bell		
	Cindy Vowell	542-9095
Pacific Gas & Electric		
	Kathy Devine	695-3492
S F Thermal		
	(Representative not present)	
Allstar / Metro Media		
	Nick Araujo	431-2510
AT&T		
	(Representative not present)	
BDI		
	(Representative not present)	
GST		
	(Representative not present)	
ICG		
	(Representative not present)	
Level 3 Communications		
	Dom Filando	408-523-9096
MFN		
	(Representative not present)	
RCN		
	Brian Heckman	650-794-2735
TCGc		
	(Representative not present)	
TCI		
	Louis Victorio	863-8500 x-3346
	Lowell Volk. Jr	863-8500 x-3346
Underground Construction		
	Andrew McManus	882-1553

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 412

1. The members introduced themselves around the table.

2. The May 13, 1998 Minutes were approved.

3. Meeting Agenda

Ms. Chono proposed changes to the agenda format for regular monthly meetings. See also discussion for a special meeting in June, at the end of these minutes.

For the present, meetings will consist of:

Project Updates
  Under Construction
  Proposed and new

Improvement Issues
  Updating process (housekeeping, etc)
  Clearance or coordination dates (eg, what the date actually means)

New Business

4. X-1104

Ms. Chono will drop this item in favor of sending the NOV reports directly to the relevant agencies.

5. Project Updates

Ms Chono noted that SF Thermal has not been attending. Since we anticipate their becoming more active in construction, we need them to be present (eg, the extension in 5th St for the Moscone expansion).

Caltrans Ms Ashe had to be at another meeting. The paving in Richardson Avenue will begin in late June. Ms Faisant distributed brochures about the I-80 seismic upgrade work between 16th St and Yerba Buena Island. A summary is given in Attachment A.

Mr Norris noted that the City's accelerated paving, as well as other street construction in the South of Market area, could require coordination with the Caltrans work where it affects surface streets at on and off ramps or involves land closures. Ms Chono added that the 3rd and 4th St bridges will also be refitted during this time, the ballpark construction will be underway, heavy truck permit routing will be altered because of closed streets, and there will be major activities at Moscone and other sites, all of which will need to be part of the planning. This will require global thinking for everyone who intends to work in the area.

MUNI Mr Viray, the Project Engineer, discussed plans to upgrade trolley wiring for the 6 (Parnassus) and 7 (Haight) bus lines. This will involve underground duct lines, the substation for the N Line, and poles along the routes. A sketch and summary are given in Attachment B. Muni and PG&E are negotiating schedule coordination for this and the gas main replacement and undergrounding in 9th Ave.

Mission Bay Risk Management Plan Mr Trimbur reported that he had just received information regarding the Regional Water Quality Board's mandatory standards for dust control, ground water impact, and the like for an area that includes the Mission Bay development project, effective this month. This affects all property owners in the area, including the City, for any excavations such as utility work. Mr Trimbur will report next month on the details and on the effect, if any, on the Excavation Code.

Events Ms Chono reminded members to be alert for crowd-drawing events such as the Sony Center opening and local street fairs, especially during summer, in the South of Market area.

6. Improvement Issues

Ms Devine gave a summary of the Special Meeting that had preceded this one (see minutes), regarding the history, mandate, and current status for the CULCOP and SCCC meeting forums and their distinction.

Ms Chono opened a discussion of the CULCOP "clearance" process. The status quo is based on a unilateral pavement-driven model that has been evolving towards a multi-lateral project-driven process. We need to clarify our current situation and optimize the program to fit. Ms Chono solicited issues from the members for future discussion:

- ✓ Pavement projections and demands need to be realistic
- ✓ Some requests for clearance have been redundant
- ✓ Status Report information must be accurate
- ✓ Stale information is an issue (eg, five year old clearances)
- ✓ Clarify the purpose and need for the NOI/LOT procedure
- ✓ What exactly is the question that the 5 year plan info is answering?
- ✓ How do we un-clear when the situation changes?
- ✓ Are there better ways to share data, such as a Web site?
- ✓ We need to clarify our terms
- ✓ What does a clearance date mean?
- ✓ Better tracking for notices to raise castings

The next meeting will be at 10:00 am Thursday, July 8 1999, the second Thursday of the month, at **875 Stevenson St, Rm 410**

Attachment A

I-80 Seismic Retrofit

Caltrans I-80 Seismic Retrofit

Segment	Schedule	Impact
Yerba Buena Island	Viaduct: Summer 1998 to Fall 1999 Tunnel: Fall 1999 to Summer 2000	Daily lane closures during off-peak hours
West Span	Piers and anchorage: Spring 1998 to Fall 2001 Towers and superstructure: through 2003	Noise and lane closures during off-peak hours. Night closures on some weekends
West approach (anchorage to 5th St)	Fall 2000 to Fall 2006	Lane closures on some weekends for demolition. Loss of 4000 parking spaces
Bayshore viaduct (4th St to 16th St)	Spring 1999 to Summer 2002	Noise and vibration from pile driving. Loss of 1500 parking spaces.
Central freeway	Retrofit: Summer 1996 to Fall 1999 Prop E: ER 1/99 to Spring 2000 Design Spring 2000 to Summer 2002 Construction Summer 2002 to Summer 2004	To be determined

Attachment B.

Muni #6 and #7 Bus Line Upgrades

6 Parnassus and 7 Haight
Trolley Overhead Reconstruction

Scope of Work

1) Reconstruct the existing overhead contact system — entire 6 and 7 routes west of Market Street
2) Construct underground duct banks with feeder cables — 9th Ave from the substation to Ortega; Ortega from 9th Ave to 10th Ave; 10th Ave from Ortega to Quintara
3) Rehabilitate 'N' substation building (9th Ave near Judah)
4) Replace or add street lights, and combine trolley and street light poles

Schedule

CER	January 1999	through October 1999
Detail design	October 1999	through December 2000
Construction	January 2001	through January 2002
Closeout	January 2002	through April 2002

CF

PR

7/

SF
P85.93
#3
7/8/99

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

DOCUMENTS DEPT.
AUG 1 1 1999
SAN FRANCISCO PUBLIC LIBRARY

MINUTES OF MEETING NO. 413
July 8, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Eric Kjelsberg	558-4012
Joe Ovadia	558-4004

Street Construction Coordination Center

Cynthia Chono	554-6196
Nancy Lynch	554-5870
Mauricio Monsalve	554-5882
Joe Norris	554-5881

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Chris McDaniels	850-5865

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

John Fong	554-1875
Charles Kascal	557-9983

PUC Sewers

(Representative not present)

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

(Representative not present)

Redevelopment Agency

(Representative not present)

Caltrans

Karen Ashe	557-7052
Dean Drablos	330-6537

Caltrans Public Information

(Representative not present)

Pacific Bell

(Representative not present)

Pacific Gas & Electric

Kathy Devine	695-3492

S F Thermal

Ben Stout	777-3415

AGS

Ed Slintak	777-2166

Allstar

(Representative not present)

AT&T

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MCI WorldCom

Don Beckermann	408-975-2244

MFN

(Representative not present)

RCN

Brian Heckman	650-794-2735

TCG

(Representative not present)

TCI

(Representative not present)

Underground Construction

(Representative not present)

Moscone Expansion

John Esposito	538-1830
Ray Fong	978-5902
Roberto Lombardi	978-5912
Joyce Oishi	978-5903
Amit Wadhwa	543-9344

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 413

1. The members introduced themselves around the table.

2. The June 10, 1999 Minutes were approved.

3. Project Updates

Paving Work has started on the joint SFWD/DPT/Paving project in Howard and Folsom Sts. Working hours have been moved to night and weekends to ease traffic congestion. SF Thermal will be in Hawthorne St. for another two months. We are watching for congestion and event impacts.

Work has started on Mission St. south of Cesar Chavez.

The 3rd St. Bridge will be closed for about 100 days beginning July 19, and is expected to be open again in time for the ballpark opening.

MUNI Mr. John Fong discussed plans for the light rail storage and maintenance facility at the former Western Pacific property bounded by 25th St., Illinois, and Cesar Chavez. Muni is now finishing conceptual design. Mr. Slintak distributed a fact sheet (see **Attachment A**). The center will require extensive new utility services and relocations. There will also be provision for future development of a 13 acre Port parcel to the east. Details will be presented when the design is nearer completion.

Moscone Center Expansion Following up on the presentation at the October 1997 meeting, Mr. Ray Fong and Ms. Joyce Oishi discussed plans to construct an 800 thousand sq ft extension to the Moscone Center at 4th and Howard, on the site of the Chevy's restaurant, Holland Ct. (to be vacated), and adjacent parking lot. The first contract, for demolition and excavation, is ready to award. The second, for construction, is expected to begin in spring of 2000 and end in time for opening in February 2002. SF Thermal will extend their steam service from 5th and Jessie to 5th and Minna, crossing Mission either at 5th or at Mint depending on the outcome of studies now in process. They expect to begin trenching in May of 2000. The sidewalk and parking lane on the north side of Howard will be closed, and the trailers will be placed on Howard near 5th. The project includes paving in Minna, 4th, and Howard.

4. Improvement Issues

Ms. Chono announced that we hope to begin distributing the Status Report on our Web site beginning as early as August, instead of the paper report. We plan to give a presentation at the next meeting. Please let us have your response about needs and preferences.

Mr. Ovadia asked if the Web version would allow interactive updates. Ms. Chono replied that we intend to provide that feature eventually, but for now it will be read-only. The interactive feature would have to be controlled, in something like the same way as electronic permitting.

Mr. Heckman asked if we could issue a contact list by name and function. We can, and we also need to update the contacts given at the beginning of the Status Report. We would like to add everyone's email address as well. See **Attachment B**.

The next meeting will be at 10:00 am Thursday, August 12, 1999, the second Thursday of the month, at **875 Stevenson St, Rm 410**

Attachment A

Muni Light Rail Facility

07/08/99

MUNI METRO EAST

CULCOP MEETING

DATE: 7/8/99
LOCATION: 875 STEVENSON ST., ROOM 410
TIME: 10 AM

PROJECT DESCRIPTION:

MUNI Metro East LRV Maintenance and Operations Facility

Location

The project site is located in San Francisco, west of the North Container Terminal (Pier 80), on a 5.3 hectare (approximately 13.0 acres) parcel of land, one block east of 3rd Street, bounded on the north by 25th Street, Cesar Chavez to the south, Illinois Street to the west and future Lousiana Street to the east. An existing building located on the southeast corner of the same block with the project site will remain and is not a part of the ME facility.

The site is on the western portion of an abandoned Western Pacific rail yard which is being transferred to the Port of San Francisco. The land is gently sloped from northwest to southeast at approximately 0.2%. There are several abandoned short tracks at the intersections of 25th and Illinois Streets and at Cesar Chavez and Illinois Streets. The main north-south Union Pacific (UP) freight track on Illinois Street to remain is located in the westerly portion of Illinois Street. The proposed LRV lines will cross the UP track at these two intersections.

Project Schedule

The project is scheduled to begin detailed design September 1, 1999 with design to be completed by January 2001. The construction is anticipated to be accomplished in at least two contract packages. The first contract, anticipated to begin April 2000 and lasting up to one year, will include a soil densification program, earthwork, and possibly some utility construction. The main construction contract is scheduled to begin work in April 2001 with completion expected in July 2003.

LRT Connections

The Metro Muni East Operation and Maintenance Facility is connected to the 3rd Street light rail alignment via a double track on 25th Street which is the primary train access to the project site. A secondary connection to the 3rd Street light rail system is on the south site of the facility via Cesar Chavez Street.

Utility Work

No existing utilities are present on site. Utilities on existing streets that are in conflict with the track alignment will be relocated.

Site utilities such as sewer and water are designed to handle possible future expansion of the facility to accommodate storage of a total of 100 LRVs.

Combined Sewer: Site storm water collection and roof runoff will be combined with the subdrains and buildings sanitary sewer laterals prior to leaving the site and gravity discharged into the 66-in. city sewer main (under construction by others) at the tie-in point located at the intersection of Cesar Chavez and Illinois Streets.

The sanitary and storm drain system will be separated from the industrial waste system as required by regulation and codes. Proper pre-treatment including oil/grease separation will be provided for the industrial waste prior to discharge. Industrial waste drains will be provided in all areas where oily wastes are likely to enter the drainage system.

Water: Site water supply for fire, domestic and irrigation purposes will be tied in to the existing main on 25th Street in the north and 12-in. main on Cesar Chavez Street in the south. Fire protection system will be designed to meet the San Francisco Fire Department and Port requirements. It is anticipated that the existing 8-inch main in 25th Street will require relocation away from the track alignments. An upsizing of the line to 12-inch may be warranted to better serve the Metro East facility and the future improvement of the remaining 13-acres of the Western Pacific site.

Electrical and Gas: Supply for the site electrical and gas demands will be connected to the existing PG&E systems on the adjacent public streets. Two or three electrical substations are planned on the site to provide overhead catenary power for the shops buildings, storage yard, and a portion of the Third Street line. Main gas connection is anticipated from 25th Street, the existing main may need to be upgraded back to Third Street to supply the required volumes for Metro East and the future improvements.

Communications: All communication lines such as telephone, data, cable, etc. will be connected to existing systems supplied by appropriate utility companies

Attachment B

CULCOP Contact List

Please review the list and correct or update as necessary. As noted in the Minutes, the list should serve as a guide to the appropriate contact persons at each agency, such as for NOI responses or 5 year plan information. Please add any missing information, including email addresses, to the space provided between the lines.

CULCOP MAILING LIST

05-Aug-99

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
		Walters	D.	949 Presidio Avenue	Rm. 217	San Francisco	CA 94115			
A T & T		Perez	W.	2200 Jerrold Avenue		San Francisco	CA 94124	282-7825	282-8124	
A T & T	**Government Affairs**	Crayton	L.	795 Folsom Street	Rm. 210	San Francisco	CA 94107	442-2416	442-2074	
A T & T Communications		Wilemon	M.	521 Second Street	Rm. 500	Santa Rosa	CA 95401			
A. Ruiz Construction Co.		Hurtado		1615 Cortland Avenue		San Francisco	CA 94110			
All Star Telecom, Inc.		Lowrie	J.	3346 Arden Road		Hayward	CA 94545	510-782-0900	510-928-3909	
All Star Telecom, Inc.		McKee	M.	3346 Arden Road		Hayward	CA 94545	510-782-0900	510-928-3909	
All Star Telecom, Inc.		Stames	T.	3346 Arden Road		Hayward	CA 94545	510-782-0900	510-928-3909	
All Star Telecom, Inc.	**(Construction trailer)**	Araujo	N.	700 16th Street		San Francisco	CA 94107	431-2510		
Annuzzi Concrete		Annuzzi	M.	85 Elmira Street		San Francisco	CA 94124	468-2795	468-0303	
BDI		Hayes	C.	1790 Yosemite		San Francisco	CA 94124			
BDI		Shepherd	C.	1790 Yosemite		San Francisco	CA 94124	671-2150		
BDI	**Business Development**	McDonald	L.	1790 Yosemite		San Francisco	CA 94124	671-2150	671-2156	
Brooks Fiber Comms		Aguilar	L.	464 Oakmead Parkway		Sunnyvale	CA 94086	415-286-4222		
Caltrans		Manning	D.	325 San Bruno Ave		San Francisco	CA 94103	557-4022		
Caltrans		Zarechian	B.	P O Box 23660		Oakland	CA 94623-0660	510-286-4425	510-286-4712	
Caltrans	**District Director**	Yahata	H.	P O Box 23660		Oakland	CA 94623-0660	510-286-4444		
Caltrans	**Maintenance Permits**	Drablos	D.	380 Foster City Blvd		Foster City	CA 94404	330-6537	330-6537	
Caltrans	**Public Information**	Faisant	V.	833 Market Street	Ste 607	San Francisco	CA 94103-1814	495-5895	495-6097	
Caltrans	**Resident Engineer**	Ashe	K.	840 Brannan Street		San Francisco	CA 94103	557-7052	557-7776	
Catellus	**Mixed Use Group, LLC**	Day	D.	255 Channel St		San Francisco	CA 94107	974-3767	974-3724	
Controller	**ISD**	Harrington	E.	875 Stevenson St	Rm. 235	San Francisco	CA 94103	554-7500		
Core Metro Construction		Shelton	K.	2330 Four Seasons Ct		San Jose	CA 95131			
De Young Museum	**75 Tea Garden Dr**	Hartman	J.	Golden Gate Park		San Francisco	CA 941??			
Department of Electricity	**Public Safety**	Donohoe	J.	901 Rankin Street		San Francisco	CA 94124	550-2724	550-2728	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department of Electricity	**Public Safety**	Weiner	F.	901 Rankin Street		San Francisco	CA 94124	550-2724	550-2728	
Department of Electricity	**Telecommunicati**	Derouen	J.	901 Rankin Street		San Francisco	CA 94124	550-2724	550-2728	
Department Public Works	**Assistant to DPW Director**	Arias	O.	City Hall	Rm 340	San Francisco	CA 94103	554-6922	554-6944	
Department Public Works	**Asst to the Director**	Cisneros	F.	1 Dr Carlton Goodlett Pl.	Rm 348	San Francisco	CA 94102			
Department Public Works	**BCM Public Affairs**	Adams	W.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8387	554-8218	
Department Public Works	**BCM Public Affairs**	Lee	F.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8387	554-8218	
Department Public Works	**BOE Asst Deputy Director**	How	K.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8204	554-8203	
Department Public Works	**BOE Civil Engineering**	Wong	N.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8282	554-8243	
Department Public Works	**BOE Disability**	Skaff	R.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8212	554-8203	
Department Public Works	**BOE Electrical**	Kung	H.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4593	558-4053	
Department Public Works	**BOE Genl Engineering**	Manager		30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4516	558-4053	
Department Public Works	**BOE Hydraulics**	Cayabyab	R.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8298	554-8308	
Department Public Works	**BOE Hydraulics**	Chan	N.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8355	554-8308	
Department Public Works	**BOE Hydraulics**	Dhapa	I.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8337	554-8308	
Department Public Works	**BOE Hydraulics**	Law	PT	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8347	554-8308	
Department Public Works	**BOE Hydraulics**	Omokaro	E.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8320	554-8308	
Department Public Works	**BOE Hydraulics**	To	J.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8338	554-8308	
Department Public Works	**BOE Hydraulics**	Walsh	J.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8272	554-8243	
Department Public Works	**BOE Landscape**	Hom	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8303	554-8308	
Department Public Works	**BOE Landscape**	Thomas	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		554-8308	
Department Public Works	**BOE Maintenance**	Lolacono	J.	750 Phelps Street	#850	San Francisco	CA 94124	648-6882	550-9316	
Department Public Works	**BOE Mechanical / AWSS**	Yang	G.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4552	558-4053	
Department Public Works	**BOE Project Management**	Burbank	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4046	558-4032	scot m burbank DPW
Department Public Works	**BOE Project Management**	Chia	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8200	554-8203	
Department Public Works	**BOE Project Management**	Kjelsberg	E.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		558-4032	
Department Public Works	**BOE Project Management**	O'Sullivan	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4047		
Department Public Works	**BOE Project Management**	Ovadia	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4004	554-8203	
Department Public Works	**BOE Project Management**	Rivera	P	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		558-4032	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department Public Works	**BOE Project Management**	Valdes	C.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		554-8203	
Department Public Works	**BOE Streets & Highways**	Choi	P.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8283	554-8243	
Department Public Works	**BOE Streets & Highways**	Choy	E.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8284	554-8243	
Department Public Works	**BOE Streets & Highways**	Kaku	N.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8246	554-8243	
Department Public Works	**BOE Streets & Highways**	Louie	V.	1680 Mission Street	3rd Flr	San Francisco	CA 94103	554-8282	554-8243	
Department Public Works	**BOE Streets & Highways**	Paderanga	N.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8258	554-8243	
Department Public Works	**BOE Streets & Highways**	Stavrakis	D.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8271	554-8243	
Department Public Works	**BOE Streets & Highways**	Tang	G.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8283	554-8243	
Department Public Works	**BOE Streets & Highways**	Wong	L.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8252	554-8243	
Department Public Works	**BOE Streets & Highways**	Yu	C.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8280	554-8243	
Department Public Works	**BOE Structural**	Yee	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4050	558-4053	
Department Public Works	**BSSR Asphalt Plant**	Curran	J.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6672	821-0572	
Department Public Works	**BSSR Asphalt Plant**	Galli	P.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6672	821-0572	
Department Public Works	**BSSR Asphalt Plant**	McDonald	N.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6673	821-0572	
Department Public Works	**BSSR Asphalt Plant**	Roberts	K.	2323 Cesar Chavez St		San Francisco	CA 94124	695-	821-0572	
Department Public Works	**BSSR Asphalt Plant**	Wong	C.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6673	821-0572	
Department Public Works	**BSSR Superintendent**	Cunningham	R.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2090	695-2097	
Department Public Works	**Bureau Construction Mgt**	Yim	N.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8227	554-8218	
Department Public Works	**Bureau of Street Repair**	Olson	M.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2086	695-2097	
Department Public Works	**Bureau Street Cleaning**	Busher	J.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2141	695-2175	
Department Public Works	**Chief Bur Constr Mgt**	Eng	D.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8216	554-8218	
Department Public Works	**Chief, Bur of Engineering**	Munakata	D.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4517	558-4519	
Department Public Works	**Claims**	Casey	F.	875 Stevenson St	Rm. 420	San Francisco	CA 94103	554-5827	554-5843	
Department Public Works	**DDE / City Engineer**	Kelly	H.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4522	554-8203	
Department Public Works	**Deputy Dir Operations**	Devaughn	M.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2100	695-2001	
Department Public Works	**Director**	Primeau	M.	City Hall	Rm 340	San Francisco	CA 94103	554-6920	554-6944	
Department Public Works	**Director's Chief of Staff**	Alfaro	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94103	554-6929	554-6940	
Department Public Works	**Director's Office**	Moore	G.	City Hall	Rm 340	San Francisco	CA 94103			

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department Public Works	OGDS Program Director	White	G.	30 Van Ness Avenue	4th Flr.	San Francisco	CA 94102	557-4741	557-4745	
Department Public Works	Public Affairs	Mamak	A.	City Hall	Rm 340	San Francisco	CA 94103	558-4045	558-4519	
Department Public Works	Public Affairs	McDowell	W.	City Hall	Rm 340	San Francisco	CA 94103	558-4045	558-4519	
Department Public Works	Public Affairs	Pitcher	A.	425 Mason Street	4th Flr.	San Francisco	CA 94102	923-2475		
Department Public Works	Public Affairs	Wong	A.	City Hall	Rm 340	San Francisco	CA 94103	558-4043	558-4519	
Department Public Works	Street Const Coord Center	Chono	C.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6196	554-6161	
Department Public Works	Street Const Coord Center	Duff	S.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5804	554-6161	
Department Public Works	Street Const Coord Center	Lynch	N.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5870	554-6161	
Department Public Works	Street Const Coord Center	Mingaracal	C.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5880	554-6161	
Department Public Works	Street Const Coord Center	Monsalve	M.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5882	554-6161	
Department Public Works	Street Const Coord Center	Norris	J.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5881	554-6161	
Department Public Works	Street Const Coord Center	Sugawara	S.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5848	554-6161	
Department Public Works	Street Use & Mapping	Casey	M.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5851	554-6161	
Department Public Works	Street Use & Mapping	Elsner	N.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6199	554-6161	
Department Public Works	Street Use & Mapping	Escalona	M.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5814	554-6161	
Department Public Works	Street Use & Mapping	Ferreira	C.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6192	554-6161	
Department Public Works	Street Use & Mapping	Gulbengay	H.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5860	554-6161	
Department Public Works	Street Use & Mapping	Hansen	A.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5861	554-6161	
Department Public Works	Street Use & Mapping	Kilgore	K.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6209	554-6161	
Department Public Works	Street Use & Mapping	Kimp	C.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5870	554-6161	
Department Public Works	Street Use & Mapping	Kuo Hoo	W.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5863	554-6161	
Department Public Works	Street Use & Mapping	Lee	A.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5861	554-6161	
Department Public Works	Street Use & Mapping	Lopez	R.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6201	554-6161	
Department Public Works	Street Use & Mapping	Moy	B.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5800	554-5843	
Department Public Works	Street Use & Mapping	Naizghi	E.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6198	554-6161	
Department Public Works	Street Use & Mapping	Quan	R.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6196	554-6161	
Department Public Works	Street Use & Mapping	Sanford	R.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5849	554-6161	
Department Public Works	Street Use & Mapping	Trimbur	T.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6167	554-6161	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department Public Works	**Street Use & Mapping**	Troyan	T.	1660 Mission Street	1st Flr.	San Francisco	CA 94103	558-6060	558-6401	
Department Public Works	**Street Use & Mapping**	Wilburn	A.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5838	554-6161	
Department Public Works	**Urban Forestry**	Baker	M.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2162	695-2175	
Dept Parking & Traffic	**Bicycle Program**	Tannen	P.	25 Van Ness Avenue		San Francisco	CA 94102	554-2396		
Dept Parking & Traffic	**Executive Director**	Sunshine	S.	25 Van Ness Avenue	Ste. 410	San Francisco	CA 94102	554-9835	554-9834	
Dept Parking & Traffic	**Paint Division**	Collins	E.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4097	
Dept Parking & Traffic	**Paint Division**	Danich	M.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4079	
Dept Parking & Traffic	**Paint Division**	Jacobs	J.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4079	
Dept Parking & Traffic	**Paint Division**	Pickens	C.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4079	
Dept Parking & Traffic	**PCO Enforcement**	James	H.	505 - 7th Street		San Francisco	CA 94103			
Dept Parking & Traffic	**PCO Enforcement**	Novello	A.	505 - 7th Street		San Francisco	CA 94103			
Dept Parking & Traffic	**Traffic Engineering**	Broady	S.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2326	554-2352	
Dept Parking & Traffic	**Traffic Engineering**	Jindal	R.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2330	554-2333	
Dept Parking & Traffic	**Traffic Engineering**	Kroll	J.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102			
Dept Parking & Traffic	**Traffic Engineering**	Quan	H.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2319	554-2352	
Dept Parking & Traffic	**Traffic Engineering**	Woo	P.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2320	554-2352	
Dept Parking & Traffic	**Traffic Sign Shop**	Shop Manager		1999 Bryant Street		San Francisco	CA 94110	554-9780	431-7140	
Dept Public Transportation	**Dep Dir Capital Resources**			1155 Market Street	5th Flr.	San Francisco	CA 94103	554-0757	554-1837	
Dept Public Transportation	**Deputy Dir Operations**	Mason	R.	949 Presidio Avenue		San Francisco	CA 94115	923-6252	923-6255	
Dept Public Transportation	**Director**	Burns	J.	949 Presidio Avenue		San Francisco	CA 94115	923-6212	923-6218	
Dept Public Transportation	**MUNI Capital Projects**	Kascal	C.	1390 Market Street	Ste 401	San Francisco	CA 94102-5402	557-9983	554-1837	
Dept Public Transportation	**MUNI Capital Projects**	Rykov	A.	1145 Market Street	6th Flr.	San Francisco	CA 94103	554-1824	554-1837	
Dept Public Transportation	**Muni Engineering**	O'Neill	J.	949 Presidio Avenue		San Francisco	CA 94115	923-6380	923-6325	
Dept Public Transportation	**Muni Planning Section**	Straus	P.	949 Presidio Avenue		San Francisco	CA 94115	923-6100		
Dept Public Transportation	**Senior Project Mgr**	Chee	D.	1155 Market Street	5th Flr.	San Francisco	CA 94103	554-1823	554-3176	
Dresser Arela	**Construction Inc**	Dresser	D.	3940 Valley Avenue		Pleasanton	CA 94566-4733	925-485-1711	925-485-1715	
E. Mitchell, Inc.		Michael	B.	1580 Indiana Street		San Francisco	CA 94107	826-2930		
Electric Lightwave Inc.		Guenther	R.	5013 Sunrise Hills Drive		Fair Oaks	CA 95628			

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Fluor Daniel Telecom		Pratt	D.	395 Oyster Point Blv	Ste 321	So. San Francisco	CA 94080	650-742-4416	650-742-4368	
Focal Communications		Ung	T.	200 North Lasalle	Ste. 800	Chicago	Il 60601	312-895-8320		
Francis Construction Co.		Francis	L.	28 Second Street	Rm 300	San Francisco	CA 94107			
Government Information	Agendas	Main Library			5th Flr.	San Francisco	CA 94102			
GST Telecom		Bradshaw	G.	4317 Thurston Way		Vancouver	WA 98662	707-746-5800		
GST Telecom		Wolf	C.	1340 Treat Blvd	Ste. 100	Walnut Creek	CA	925-280-9540		
ICG Telecommunications		Wright	R.	180 Grand Avenue	Ste.1000	Oakland	CA 94612	510-251-7015	510-251-7037	
ICG Telecommunications	Access Service	Hoerning	B.	180 Grand Avenue	Ste 1000	Oakland	CA 94612	510-769-5737	510-769-5737	
ICG Telecommunications	OSP/ISP Engr	Enea	B.	180 Grand Avenue	Ste 1000	Oakland	CA 94612	510-251-7075	510-251-7037	
IntelCom Group (= ICG?)		Bradshaw	G.	190 Park Ctr Plaza	Ste 100	SanJose	CA 95113	707-746-5800		
IXC Communications		Henley	E.	1122 Capitol of Texas Hw	S.	Austin	TX 78746-6426			
J. Flores Construction Co.		Gleghorn	B.	4229 Mission Street		San Francisco	CA 94112-1519			
K J Woods Construction, Inc		Woods	K.	2718 Pacheco Street		San Francisco	CA 94116			
Level 3 Communications		Shone	R.	14023 Denver West Pk		Golden	CO 80401	882-1553	510-672-1012	
Level 3 Communications		Webb	G.	P O Box 450		Clayton	CA 94517	510-673-0818	510-672-1012	
Mayor's Office	Economic Development	Ayerdi	M.	1 Dr Carlton Goodlett Pl.		San Fancisco	CA 94102			
MCI Metro, Inc.		Dubose	J.	2250 Lakeside Blvd		Richardson	TX 75082	214-918-1977	214-918-1062	
MCI Metro, Inc.		Neely	T.	4618 Campos Lane		Winters	CA 95694	530-795-0615	530-795-0715	
MCI Telecommunications		Rawls	K.	400 International Pk		Richardson	TX 75081	214-918-3248	214-918-3111	
MCI WorldCom		Capurso	M.	1 Front Street	Ste 3060	San Francisco	CA 94111	477-3415	477-3409	mark.w.capurso@wco
MCI WorldCom		Caridi	M.	201 Spear Street 5th Flr	Cb 5158	San Francisco	CA 94105	228-1277		
MCI WorldCom		Slagel	J.	2221 Commerce Avenue	Ste A-1	Concord	CA 94520			
MCI WorldCom	Field Installation Manager	Beckermann	D.	55 South Market	Ste 1250	San Jose	CA 95113-2327	408-975-2244	408-975-2210	don.beckermann@wco
Metromedia Fiber Ntwk		Reid	S.					510-782-0900		
Metromedia Fiber Ntwk		Young	M.	One N Lexington Ave		White Plains	NY 10601	914-421-6700		
Metropolitan Fiber		Gromachey	L.	444 Market Street	Ste.1350	San Francisco	CA 94111	362-3300		
Metropolitan Fiber		Shillington	A.	1200 Landmark Center	Ste 1300	Omaha	NB 68102-1892	402-233-7562	-7650	
Metropolitan Fiber		Zivny	S.	1200 Landmark Center	Ste 1300	Omaha	NB 68102-1892	402-233-7609	-7650	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Metropolitan Fiber	**Operations Support**	Licari	R.	444 Market Street	Ste.1350	San Francisco	CA 94111	362-3300		
MFS Network Technology		Heley	C.	20986 Corsair Blvd		Hayward	CA 94545			
Muni	**Chief Inspector**	Olson	L.	2500 Mariposa Street	Rm 7	San Francisco	CA 94110			
Muni Overhead Lines		Wong	H.	2502 Alemeda Street		San Francisco	CA 94103	554-9201		
Muni Sys Safety & Security	**Director**	Chin	P.	1345 Turk Street		San Francisco	CA 94115			
Nextlink		Bohannon	J.	855 Mission Court		Fremont	CA 94539			
Nextlink California		Shone	R.	1924 Deere Ave		Santa Ana	CA 92705	882-1553		
OSP		Simpson	K.	200 C Mason Circle		Concord	CA 94520	925-680-6822		
P & J Utility Co.		McElroy	A.	435 Brannan Street		San Francisco	CA 94107			
P G & E	**Dir Capital Improvement**	Murray	D.	2180 Harrison Street	2nd Flr.	San Francisco	CA 94110	695-3523	695-3290	
P G & E	**Electrical Department**	Poniente	E.	2180 Harrison Street		San Francisco	CA 94110	695-3539		
P G & E	**Gas Department**	Devine	K.	2180 Harrison Street		San Francisco	CA 94110	695-3394	695-3291	
P G & E	**Gas Department**	Devine	K.	2180 Harrison Street		San Francisco	CA 94110	695-3394	695-3291	
P G & E	**Gas Department**	Dowd	P.	2180 Harrison Street		San Francisco	CA 94110	695-3574	695-3339	JJL6@PGE.COM
P G & E	**Gas Department**	Dowd	P.	2180 Harrison Street		San Francisco	CA 94110	695-3574	695-3339	JJL6@PGE.COM
P G & E	**Gas Department**	Nounou	G.	2180 Harrison Street		San Francisco	CA 94110			
P G & E	**General Constr**	Healy	P.	2180 Harrison Street		San Francisco	CA 94110	695-3394	695-3332	
P G & E	**Service Planning**	Wilson	W.	2180 Harrison Street	2nd Flr.	San Francisco	CA 94110	695-3541	695-3525	
Pacific Bell	**Engineering**	Davey	K.	666 Folsom Street	Rm 1121A	San Francisco	CA 94107	542-9931	957-5973	
Pacific Bell	**Engineering**	Vowell	C.	666 Folsom Street	Rm. 1121	San Francisco	CA 94107	542-9095	957-5973	CVOWELL@tdsi-q.co
Price Technology		Rodriguez	R.	6640 Sierra Lane		Dublin	CA 94568	510-833-8447		
Public Utilities Comm	**Hetch Hetchy Water & Pow**	Lameyse	V.	1401 Bryant Street		San Francisco	CA 94103	695-7223		
Public Utilities Comm	**Hetch Hetchy Water & Pow**	Yamagishi	R.	1155 Market Street	5th Flr.	San Francisco	CA 94103	554-0728	554-1854	
Public Utilities Comm	**Sewer Operations**	Anderson	H.	750 Phelps Street		San Francisco	CA 94124	648-6882	282-5280	
Public Utilities Comm	**Sewer Operations**	Hale	L.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2096		
Public Utilities Comm	**Sewer Operations**	Herrera	J.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2096		
Public Utilities Comm	**Sewer Operations**	O'Neill	C.	2323 Cesar Chavez St		San Francisco	CA 94124			
Public Utilities Comm	**Superintendent WPC**	Keaney	W.	750 Phelps Street		San Francisco	CA 94124			

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Public Utilities Comm	UEB Manager	Quan	M.	1155 Market Street	5th Flr	San Francisco	CA 94103			
Public Utilities Comm	Utility Engineering	Bavishi	K.	1145 Market Street	6th Flr.	San Francisco	CA 94103	554-1884	554-1837	
Public Utilities Comm	Utility Engineering	Hintze	E.	1155 Market Street	4th Flr.	San Francisco	CA 94103	554-0707	554-1854	
Qwest Communications Gp		Berry	M.	555-17th St		Denver	CO 80202	303-312-2832	303-291-1742	
Qwest Communications Gp		Cochran	C.	555-17th St		Denver	CO 80202	303-312-2832	303-291-1742	
RCN		Coppedge	J.	1250 Bayhill Dr	Ste. 200	San Bruno	CA 94066	650-754-2755	650-794-2609	
RCN		Heckman	B.	1250 Bayhill Dr	Ste. 200	San Bruno	CA 94066	650-754-2735	650-794-2609	
RCN	Director of Construction	Weber	S.	1250 Bayhill Dr	Ste. 200	San Bruno	CA 94066	650-754-2696	650-794-2609	
S F Fire Department		Van Dyke	S.	698 Second Street		San Francisco	CA 94107-2015		441-8798	
S F Fire Department	Bur Engr & Water Suppl	Gunn	W.	2245 Jerrold Avenue		San Francisco	CA 94124	558-3557		
S F Fire Department	Facility Renovation Progra	Massetani	G.	698 Second Street		San Francisco	CA 94107-2015			
S F Fire Department	Neighborhood Emerg Resp			698 Second Street		San Francisco	CA 94107-2015		928-3130	
S F Police Department	Dir of Communications	Martin	R.	850 Bryant Street		San Francisco	CA 94102	553-1042	553-1515	
S F Police Department	Director Communications	Nichols	M.	850 Bryant Street		San Francisco	CA 94103	553-1241		
S F Police Department	PLES	Ballentine	J.	850 Bryant Street	Rm 500	San Francisco	CA 94103			
S F Police Department	PLES	Carrington	G.	850 Bryant Street	Rm 500	San Francisco	CA 94103			
S F Port Commision		Zeller	S.	Ferry Building		San Francisco	CA 94111	274-0552	274-0528	
S F Port Commission		Jarrard	C.	Ferry Building		San Francisco	CA 94104	274-0541	274-0528	
S F Redevelopment	Engineering Div	Davis	M.	770 Golden Gate Ave	2nd Flr.	San Francisco	CA 94102	749-2400	749-2525	
S F Redevelopment	Engineering Div	Hapert	D.	770 Golden Gate Ave	2nd Flr.	San Francisco	CA 94102	749-2400	749-2525	
S F Redevelopment	Engineering Div	Hong	W.	770 Golden Gate Ave	2nd Flr.	San Francisco	CA 94102	749-2453	749-2526	
S F Water Department	CDD Engineering	Desai	B.	1990 Newcomb Street	Rm. 112	San Francisco	CA 94124	550-4918	550-4913	
S F Water Department	CDD Engineering	Gapuz-Te	D.	1990 Newcomb Street	Rm. 112	San Francisco	CA 94124	550-4927	550-4913	
S F Water Department	CDD Manager	Flores	A.	1990 Newcomb Street		San Francisco	CA 94124			
S F Water Department	CDD Project Management	Kubick	K.	1990 Newcomb Street		San Francisco	CA 94124	550-2971	550-2980	
S F Water Department	Commercial Division	Flewellen	S.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2526	923-2500	
S F Water Department	Commercial Division	Huie	B.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2523	923-2500	
S F Water Department	Commercial Division	Lew	D.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2520	923-2500	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
S F Water Department	**Distribution Engineering**	Blue	R.	1990 Newcomb Street	Rm. 114	San Francisco	CA 94124	550-4926	550-4913	
S F Water Department	**Distribution Engineering**	Chan	A.	1990 Newcomb Street	Rm. 114	San Francisco	CA 94124	550-4931	550-4913	
S F Water Department	**Distribution Engineering**	Nguyen	T.	1990 Newcomb Street	Rm. 112	San Francisco	CA 94124	550-4916	550-4913	
S F Water Department	**Distribution Engineering**	Poblete	R.	1990 Newcomb Street	Rm. 114	San Francisco	CA 94124	550-4917	550-4913	
S F Water Department	**New Installations**	Evans	G.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2521	923-2500	
S F Water Department	**UEB Construction**	Lee	C.	1990 Newcomb Street		San Francisco	CA 94124	550-4925	550-4913	
S F Water Department	**UEB Construction**	Ronis	J.	1990 Newcomb Street		San Francisco	CA 94124	550-2976	550-4913	
San Francisco Thermal		Judd	G.	460 Jessie Street		San Francisco	CA 94103	771-3415	771-3787	
San Francisco Thermal		Stout	B.	460 Jessie Street		San Francisco	CA 94103	771-3415	771-3787	
Sprint Communications		Freeman	D.	1850 Gateway Drive	4th Flr.	San Mateo	CA 94404-2467	650-513-2545	650-513-2555	
Stacy & Witbeck, Inc.	**E G Construction AJV**	Clemente	R.	290 Toland Street		San Francisco	CA 94124			
TCI of California		Bouey	T.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Callow	M.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Hagerla	R.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Santos	E.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Victorio	L.	2055 Folsom Street		San Francisco	CA 94110	863-8500	252-6302	
Teleport Communications Gp		Wightman	S.	One Bush Street	Ste. 510	San Francisco	CA 94104	276-0083	276-0050	
Teleport Communications Gp	**c/o AT&T**	Leohner	S.	344 - 20th Street	Ste 210	Oakland	CA 94612			
Teleport Communications Gp	**Fiber Resource Engineer**	Sorrels	B.	One Bush Street	Ste. 510	San Francisco	CA 94104	276-0087	276-0050	
Transportation Authority	**Director Congestion Mgt**	Moscovitch	J.	100 Van Ness Avenue	25th Flr	San Francisco	CA 94102	557-6857	557-6858	
Underground Construction		Cook	M.	P O Box 2000		Benicia	CA 94510	707-746-8800	707-746-1314	
Underground Construction		McManus	A.	P O Box 2000		Benicia	CA 94510	707-746-8800	707-746-1314	
Underground Construction		Shone	R.	5145 Industrial Way		Benicia	CA 94511	882-1553		
US SPRINT				P O Box 7501		San Mateo	CA 94403-7501			
World Com		Choo	K.	444 Market Street	Ste 1350	San Francisco	CA 94111	362-0990	394-6705	

SF
REC.
1
8/12

City and County of San Francisco **Department of Public Works**
Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

SF
85.93
1
8/12/99

Location: **875 Stevenson St, Rm 410**

Date: Thursday, August 12, 1999 10:00 to 12:00 noon
Subject: Committee Meeting 414- Coordination of Street Construction

AGENDA

1) Introduction	
2) Approval of Minutes for July 8th Meeting	
3) Project Updates	
a. Paving projects	Joe Ovadia
b. 3rd St Bridge	
c. Caltrans	Karen Ashe
d. Other projects	
e. New projects (starting in next 6 months)	
Fremont/First track removal	Steve O'Sullivan
f. Major events	
4) Improvement Issues	All
Status Report distribution update	
5) Other New Business	All

Next Meeting: 2nd Thursday of Each Month
Thursday September 9, 1999 at 10:00 A. M.
875 Stevenson St, Rm 410

DOCUMENTS DEPT.
AUG 1 1 1999
SAN FRANCISCO
PUBLIC LIBRARY

City and County of San Francisco **Department of Public Works**

Street Construction Coordination Center

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-5881, at least72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-5881.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 875 Stevenson St, Rm 410. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L Mission Street; # 42 Van Ness Avenue;
   #26 Valencia Street; #71 Noriega Street; #9 Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION

AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 413
July 8, 1999

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Eric Kjelsberg	558-4012
Joe Ovadia	558-4004

Street Construction Coordination Center

Cynthia Chono	554-6196
Nancy Lynch	554-5870
Mauricio Monsalve	554-5882
Joe Norris	554-5881

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street Use Management

Chris McDaniels	850-5865

Bureau of Construction Management

(Representative not present)

Department of Parking and Traffic

Scott Broady	554-2326

MUNI Engineering/DDC

John Fong	554-1875
Charles Kascal	557-9983

PUC Sewers

(Representative not present)

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department

(Representative not present)

Redevelopment Agency

(Representative not present)

Caltrans

Karen Ashe	557-7052
Dean Drablos	330-6537

Caltrans Public Information

(Representative not present)

Pacific Bell

(Representative not present)

Pacific Gas & Electric

Kathy Devine	695-3492

S F Thermal

Ben Stout	777-3415

AGS

Ed Slintak	777-2166

Allstar

(Representative not present)

AT&T

(Representative not present)

GST

(Representative not present)

ICG

(Representative not present)

Level 3 Communications

(Representative not present)

MCI WorldCom

Don Beckermann	408-975-2244

MFN

(Representative not present)

RCN

Brian Heckman	650-794-2735

TCG

(Representative not present)

TCI

(Representative not present)

Underground Construction

(Representative not present)

Moscone Expansion

John Esposito	538-1830
Ray Fong	978-5902
Roberto Lombardi	978-5912
Joyce Oishi	978-5903
Amit Wadhwa	543-9344

Committee for Utility Liaison on Construction and Other Projects

MINUTES OF MEETING No. 413

1. The members introduced themselves around the table.

2. The June 10, 1999 Minutes were approved.

3. Project Updates

Paving Work has started on the joint SFWD/DPT/Paving project in Howard and Folsom Sts. Working hours have been moved to night and weekends to ease traffic congestion. SF Thermal will be in Hawthorne St. for another two months. We are watching for congestion and event impacts.

Work has started on Mission St. south of Cesar Chavez.

The 3rd St. Bridge will be closed for about 100 days beginning July 19, and is expected to be open again in time for the ballpark opening.

MUNI Mr. John Fong discussed plans for the light rail storage and maintenance facility at the former Western Pacific property bounded by 25th St., Illinois, and Cesar Chavez. Muni is now finishing conceptual design. Mr. Slintak distributed a fact sheet (see **Attachment A**). The center will require extensive new utility services and relocations. There will also be provision for future development of a 13 acre Port parcel to the east. Details will be presented when the design is nearer completion.

Moscone Center Expansion Following up on the presentation at the October 1997 meeting, Mr. Ray Fong and Ms. Joyce Oishi discussed plans to construct an 800 thousand sq ft extension to the Moscone Center at 4th and Howard, on the site of the Chevy's restaurant, Holland Ct. (to be vacated), and adjacent parking lot. The first contract, for demolition and excavation, is ready to award. The second, for construction, is expected to begin in spring of 2000 and end in time for opening in February 2002. SF Thermal will extend their steam service from 5th and Jessie to 5th and Minna, crossing Mission either at 5th or at Mint depending on the outcome of studies now in process. They expect to begin trenching in May of 2000. The sidewalk and parking lane on the north side of Howard will be closed, and the trailers will be placed on Howard near 5th. The project includes paving in Minna, 4th, and Howard.

4. Improvement Issues

Ms. Chono announced that we hope to begin distributing the Status Report on our Web site beginning as early as August, instead of the paper report. We plan to give a presentation at the next meeting. Please let us have your response about needs and preferences.

Mr. Ovadia asked if the Web version would allow interactive updates. Ms. Chono replied that we intend to provide that feature eventually, but for now it will be read-only. The interactive feature would have to be controlled, in something like the same way as electronic permitting.

Mr. Heckman asked if we could issue a contact list by name and function. We can, and we also need to update the contacts given at the beginning of the Status Report. We would like to add everyone's email address as well. See **Attachment B**.

The next meeting will be at 10:00 am Thursday, August 12, 1999, the second Thursday of the month, at **875 Stevenson St, Rm 410**

Attachment A

Muni Light Rail Facility

MUNI METRO EAST
CULCOP MEETING

DATE: 7/8/99
LOCATION: 875 STEVENSON ST., ROOM 410
TIME: 10 AM

PROJECT DESCRIPTION:

MUNI Metro East LRV Maintenance and Operations Facility

Location

The project site is located in San Francisco, west of the North Container Terminal (Pier 80), on a 5.3 hectare (approximately 13.0 acres) parcel of land, one block east of 3rd Street, bounded on the north by 25th Street, Cesar Chavez to the south, Illinois Street to the west and future Lousiana Street to the east. An existing building located on the southeast corner of the same block with the project site will remain and is not a part of the ME facility.

The site is on the western portion of an abandoned Western Pacific rail yard which is being transferred to the Port of San Francisco. The land is gently sloped from northwest to southeast at approximately 0.2%. There are several abandoned short tracks at the intersections of 25th and Illinois Streets and at Cesar Chavez and Illinois Streets. The main north-south Union Pacific (UP) freight track on Illinois Street to remain is located in the westerly portion of Illinois Street. The proposed LRV lines will cross the UP track at these two intersections.

Project Schedule

The project is scheduled to begin detailed design September 1, 1999 with design to be completed by January 2001. The construction is anticipated to be accomplished in at least two contract packages. The first contract, anticipated to begin April 2000 and lasting up to one year, will include a soil densification program, earthwork, and possibly some utility construction. The main construction contract is scheduled to begin work in April 2001 with completion expected in July 2003.

LRT Connections

The Metro Muni East Operation and Maintenance Facility is connected to the 3rd Street light rail alignment via a double track on 25th Street which is the primary train access to the project site. A secondary connection to the 3rd Street light rail system is on the south site of the facility via Cesar Chavez Street.

Utility Work

No existing utilities are present on site. Utilities on existing streets that are in conflict with the track alignment will be relocated.

Site utilities such as sewer and water are designed to handle possible future expansion of the facility to accommodate storage of a total of 100 LRVs.

Combined Sewer: Site storm water collection and roof runoff will be combined with the subdrains and buildings sanitary sewer laterals prior to leaving the site and gravity discharged into the 66-in. city sewer main (under construction by others) at the tie-in point located at the intersection of Cesar Chavez and Illinois Streets.

The sanitary and storm drain system will be separated from the industrial waste system as required by regulation and codes. Proper pre-treatment including oil/grease separation will be provided for the industrial waste prior to discharge. Industrial waste drains will be provided in all areas where oily wastes are likely to enter the drainage system.

Water: Site water supply for fire, domestic and irrigation purposes will be tied in to the existing main on 25th Street in the north and 12-in. main on Cesar Chavez Street in the south. Fire protection system will be designed to meet the San Francisco Fire Department and Port requirements. It is anticipated that the existing 8-inch main in 25th Street will require relocation away from the track alignments. An upsizing of the line to 12-inch may be warranted to better serve the Metro East facility and the future improvement of the remaining 13-acres of the Western Pacific site.

Electrical and Gas: Supply for the site electrical and gas demands will be connected to the existing PG&E systems on the adjacent public streets. Two or three electrical substations are planned on the site to provide overhead catenary power for the shops buildings, storage yard, and a portion of the Third Street line. Main gas connection is anticipated from 25th Street, the existing main may need to be upgraded back to Third Street to supply the required volumes for Metro East and the future improvements.

Communications: All communication lines such as telephone, data, cable, etc. will be connected to existing systems supplied by appropriate utility companies

Attachment B

CULCOP Contact List

Please review the list and correct or update as necessary. As noted in the Minutes, the list should serve as a guide to the appropriate contact persons at each agency, such as for NOI responses or 5 year plan information. Please add any missing information, including email addresses, to the space provided between the lines.

CULCOP MAILING LIST

05-Aug-99

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
		Walters	D.	949 Presidio Avenue	Rm. 217	San Francisco	CA 94115			
A T & T		Perez	W.	2200 Jerrold Avenue		San Francisco	CA 94124	282-7825	282-8124	
A T & T	Government Affairs	Crayton	L.	795 Folsom Street	Rm. 210	San Francisco	CA 94107	442-2416	442-2074	
A T & T Communications		Wilemon	M.	521 Second Street	Rm. 500	Santa Rosa	CA 95401			
A. Ruiz Construction Co.		Hurtado		1615 Cortland Avenue		San Francisco	CA 94110			
All Star Telecom, Inc.		Lowrie	J.	3346 Arden Road		Hayward	CA 94545	510-782-0900	510-928-3909	
All Star Telecom, Inc.		McKee	M.	3346 Arden Road		Hayward	CA 94545	510-782-0900	510-928-3909	
All Star Telecom, Inc.		Stames	T.	3346 Arden Road		Hayward	CA 94545	510-782-0900	510-928-3909	
All Star Telecom, Inc.	(Construction trailer)	Araujo	N.	700 16th Street		San Francisco	CA 94107	431-2510		
Annuzzi Concrete		Annuzzi	M.	85 Elmira Street		San Francisco	CA 94124	468-2795	468-0303	
BDI		Hayes	C.	1790 Yosemite		San Francisco	CA 94124			
BDI		Shepherd	C.	1790 Yosemite		San Francisco	CA 94124	671-2150		
BDI	Business Development	McDonald	L.	1790 Yosemite		San Francisco	CA 94124	671-2150	671-2156	
Brooks Fiber Comms		Aguilar	L.	464 Oakmead Parkway		Sunnyvale	CA 94086	415-286-4222		
Caltrans		Manning	D.	325 San Bruno Ave		San Francisco	CA 94103	557-4022		
Caltrans		Zarechian	B.	P O Box 23660		Oakland	CA 94623-0660	510-286-4425	510-286-4712	
Caltrans	District Director	Yahata	H.	P O Box 23660		Oakland	CA 94623-0660	510-286-4444		
Caltrans	Maintenance Permits	Drablos	D.	380 Foster City Blvd		Foster City	CA 94404	330-6537	330-6537	
Caltrans	Public Information	Faisant	V.	833 Market Street	Ste 607	San Francisco	CA 94103-1814	495-5895	495-6097	
Caltrans	Resident Engineer	Ashe	K.	840 Brannan Street		San Francisco	CA 94103	557-7052	557-7776	
Catellus	Mixed Use Group, LLC	Day	D.	255 Channel St		San Francisco	CA 94107	974-3767	974-3724	
Controller	ISD	Harrington	E.	875 Stevenson St	Rm. 235	San Francisco	CA 94103	554-7500		
Core Metro Construction		Shelton	K.	2330 Four Seasons Ct		San Jose	CA 95131			
De Young Museum	75 Tea Garden Dr	Hartman	J.	Golden Gate Park		San Francisco	CA 941??			
Department of Electricity	Public Safety	Donohoe	J.	901 Rankin Street		San Francisco	CA 94124	550-2724	550-2728	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department of Electricity	Public Safety	Weiner	F.	901 Rankin Street		San Francisco	CA 94124	550-2724	550-2728	
Department of Electricity	Telecommunicati	Derouen	J.	901 Rankin Street		San Francisco	CA 94124	550-2724	550-2728	
Department Public Works	Assistant to DPW Director	Arias	O.	City Hall	Rm 340	San Francisco	CA 94103	554-6922	554-6944	
Department Public Works	Asst to the Director	Cisneros	F.	1 Dr Carlton Goodlett Pl.	Rm 348	San Francisco	CA 94102			
Department Public Works	BCM Public Affairs	Adams	W.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8387	554-8218	
Department Public Works	BCM Public Affairs	Lee	F.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8387	554-8218	
Department Public Works	BOE Asst Deputy Director	How	K.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8204	554-8203	
Department Public Works	BOE Civil Engineering	Wong	N.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8282	554-8243	
Department Public Works	BOE Disability	Skaff	R.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8212	554-8203	
Department Public Works	BOE Electrical	Kung	H.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4593	558-4053	
Department Public Works	BOE Genl Engineering	Manager		30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4516	558-4053	
Department Public Works	BOE Hydraulics	Cayabyab	R.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8298	554-8308	
Department Public Works	BOE Hydraulics	Chan	N.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8355	554-8308	
Department Public Works	BOE Hydraulics	Dhapa	I.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8337	554-8308	
Department Public Works	BOE Hydraulics	Law	PT	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8347	554-8308	
Department Public Works	BOE Hydraulics	Omokaro	E.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8320	554-8308	
Department Public Works	BOE Hydraulics	To	J.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8338	554-8308	
Department Public Works	BOE Hydraulics	Walsh	J.	1680 Mission Street	2nd Flr.	San Francisco	CA 94103	554-8272	554-8243	
Department Public Works	BOE Landscape	Hom	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8303	554-8308	
Department Public Works	BOE Landscape	Thomas	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		554-8308	
Department Public Works	BOE Maintenance	Loiacono	J.	750 Phelps Street	#850	San Francisco	CA 94124	648-6882	550-9316	
Department Public Works	BOE Mechanical / AWSS	Yang	G.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4552	558-4053	
Department Public Works	BOE Project Management	Burbank	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4046	558-4032	scot m burbank DPW
Department Public Works	BOE Project Management	Chia	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	554-8200	554-8203	
Department Public Works	BOE Project Management	Kjelsberg	E.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		558-4032	
Department Public Works	BOE Project Management	O'Sullivan	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4047		
Department Public Works	BOE Project Management	Ovadia	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4004	554-8203	
Department Public Works	BOE Project Management	Rivera	P	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		558-4032	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department Public Works	BOE Project Management	Valdes	C.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102		554-8203	
Department Public Works	BOE Streets & Highways	Choi	P.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8283	554-8243	
Department Public Works	BOE Streets & Highways	Choy	E.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8284	554-8243	
Department Public Works	BOE Streets & Highways	Kaku	N.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8246	554-8243	
Department Public Works	BOE Streets & Highways	Louie	V.	1680 Mission Street	3rd Flr	San Francisco	CA 94103	554-8282	554-8243	
Department Public Works	BOE Streets & Highways	Paderanga	N.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8258	554-8243	
Department Public Works	BOE Streets & Highways	Stavrakis	D.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8271	554-8243	
Department Public Works	BOE Streets & Highways	Tang	G.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8283	554-8243	
Department Public Works	BOE Streets & Highways	Wong	L.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8252	554-8243	
Department Public Works	BOE Streets & Highways	Yu	C.	1680 Mission Street	3rd Flr.	San Francisco	CA 94103	554-8280	554-8243	
Department Public Works	BOE Structural	Yee	S.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4050	558-4053	
Department Public Works	BSSR Asphalt Plant	Curran	J.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6672	821-0572	
Department Public Works	BSSR Asphalt Plant	Galli	P.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6672	821-0572	
Department Public Works	BSSR Asphalt Plant	McDonald	N.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6673	821-0572	
Department Public Works	BSSR Asphalt Plant	Roberts	K.	2323 Cesar Chavez St		San Francisco	CA 94124	695-	821-0572	
Department Public Works	BSSR Asphalt Plant	Wong	C.	2323 Cesar Chavez St		San Francisco	CA 94124	695-6673	821-0572	
Department Public Works	BSSR Superintendent	Cunningham	R.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2090	695-2097	
Department Public Works	Bureau Construction Mgt	Yim	N.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8227	554-8218	
Department Public Works	Bureau of Street Repair	Olson	M.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2086	695-2097	
Department Public Works	Bureau Street Cleaning	Busher	J.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2141	695-2175	
Department Public Works	Chief Bur Constr Mgt	Eng	D.	1680 Mission Street	4th Flr.	San Francisco	CA 94103	554-8216	554-8218	
Department Public Works	Chief, Bur of Engineering	Munakata	D.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4517	558-4519	
Department Public Works	Claims	Casey	F.	875 Stevenson St	Rm. 420	San Francisco	CA 94103	554-5827	554-5843	
Department Public Works	DDE / City Engineer	Kelly	H.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94102	558-4522	554-8203	
Department Public Works	Deputy Dir Operations	Devaughn	M.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2100	695-2001	
Department Public Works	Director	Primeau	M.	City Hall	Rm 340	San Francisco	CA 94103	554-6920	554-6944	
Department Public Works	Director's Chief of Staff	Alfaro	J.	30 Van Ness Avenue	5th Flr.	San Francisco	CA 94103	554-6929	554-6940	
Department Public Works	Director's Office	Moore	G.	City Hall	Rm 340	San Francisco	CA 94103			

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department Public Works	OGDS Program Director	White	G.	30 Van Ness Avenue	4th Flr.	San Francisco	CA 94102	557-4741	557-4745	
Department Public Works	Public Affairs	Mamak	A.	City Hall	Rm 340	San Francisco	CA 94103	558-4045	558-4519	
Department Public Works	Public Affairs	McDowell	W.	City Hall	Rm 340	San Francisco	CA 94103	558-4045	558-4519	
Department Public Works	Public Affairs	Pitcher	A.	425 Mason Street	4th Flr.	San Francisco	CA 94102	923-2475		
Department Public Works	Public Affairs	Wong	A.	City Hall	Rm 340	San Francisco	CA 94103	558-4043	558-4519	
Department Public Works	Street Const Coord Center	Chono	C.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6196	554-6161	
Department Public Works	Street Const Coord Center	Duff	S.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5804	554-6161	
Department Public Works	Street Const Coord Center	Lynch	N.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5870	554-6161	
Department Public Works	Street Const Coord Center	Mingaracal	C.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5880	554-6161	
Department Public Works	Street Const Coord Center	Monsalve	M.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5882	554-6161	
Department Public Works	Street Const Coord Center	Norris	J.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5881	554-6161	
Department Public Works	Street Const Coord Center	Sugawara	S.	875 Stevenson St	Rm. 410	San Francisco	CA 94103	554-5848	554-6161	
Department Public Works	Street Use & Mapping	Casey	M.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5851	554-6161	
Department Public Works	Street Use & Mapping	Elsner	N.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6199	554-6161	
Department Public Works	Street Use & Mapping	Escalona	M.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5814	554-6161	
Department Public Works	Street Use & Mapping	Ferreira	C.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6192	554-6161	
Department Public Works	Street Use & Mapping	Gulbengay	H.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5860	554-6161	
Department Public Works	Street Use & Mapping	Hansen	A.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5861	554-6161	
Department Public Works	Street Use & Mapping	Kilgore	K.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6209	554-6161	
Department Public Works	Street Use & Mapping	Kimp	C.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5870	554-6161	
Department Public Works	Street Use & Mapping	Kuo Hoo	W.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5863	554-6161	
Department Public Works	Street Use & Mapping	Lee	A.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5861	554-6161	
Department Public Works	Street Use & Mapping	Lopez	R.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6201	554-6161	
Department Public Works	Street Use & Mapping	Moy	B.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5800	554-5843	
Department Public Works	Street Use & Mapping	Naizghi	E.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6198	554-6161	
Department Public Works	Street Use & Mapping	Quan	R.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6196	554-6161	
Department Public Works	Street Use & Mapping	Sanford	R.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5849	554-6161	
Department Public Works	Street Use & Mapping	Trimbur	T.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-6167	554-6161	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Department Public Works	**Street Use & Mapping**	Troyan	T.	1660 Mission Street	1st Flr.	San Francisco	CA 94103	558-6060	558-6401	
Department Public Works	**Street Use & Mapping**	Wilburn	A.	875 Stevenson St	Rm. 460	San Francisco	CA 94103	554-5838	554-6161	
Department Public Works	**Urban Forestry**	Baker	M.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2162	695-2175	
Dept Parking & Traffic	**Bicycle Program**	Tannen	P.	25 Van Ness Avenue		San Francisco	CA 94102	554-2396		
Dept Parking & Traffic	**Executive Director**	Sunshine	S.	25 Van Ness Avenue	Ste. 410	San Francisco	CA 94102	554-9835	554-9834	
Dept Parking & Traffic	**Paint Division**	Collins	E.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4097	
Dept Parking & Traffic	**Paint Division**	Danich	M.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4079	
Dept Parking & Traffic	**Paint Division**	Jacobs	J.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4079	
Dept Parking & Traffic	**Paint Division**	Pickens	C.	80 Charter Oak St		San Francisco	CA 94124	715-4704	715-4079	
Dept Parking & Traffic	**PCO Enforcement**	James	H.	505 - 7th Street		San Francisco	CA 94103			
Dept Parking & Traffic	**PCO Enforcement**	Novello	A.	505 - 7th Street		San Francisco	CA 94103			
Dept Parking & Traffic	**Traffic Engineering**	Broady	S.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2326	554-2352	
Dept Parking & Traffic	**Traffic Engineering**	Jindal	R.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2330	554-2333	
Dept Parking & Traffic	**Traffic Engineering**	Kroll	J.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102			
Dept Parking & Traffic	**Traffic Engineering**	Quan	H.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2319	554-2352	
Dept Parking & Traffic	**Traffic Engineering**	Woo	P.	25 Van Ness Avenue	Ste. 345	San Francisco	CA 94102	554-2320	554-2352	
Dept Parking & Traffic	**Traffic Sign Shop**	Shop Manager		1999 Bryant Street		San Francisco	CA 94110	554-9780	431-7140	
Dept Public Transportation	**Dep Dir Capital Resources**			1155 Market Street	5th Flr.	San Francisco	CA 94103	554-0757	554-1837	
Dept Public Transportation	**Deputy Dir Operations**	Mason	R.	949 Presidio Avenue		San Francisco	CA 94115	923-6252	923-6255	
Dept Public Transportation	**Director**	Burns	J.	949 Presidio Avenue		San Francisco	CA 94115	923-6212	923-6218	
Dept Public Transportation	**MUNI Capital Projects**	Kascal	C.	1390 Market Street	Ste 401	San Francisco	CA 94102-5402	557-9983	554-1837	
Dept Public Transportation	**MUNI Capital Projects**	Rykov	A.	1145 Market Street	6th Flr.	San Francisco	CA 94103	554-1824	554-1837	
Dept Public Transportation	**Muni Engineering**	O'Neill	J.	949 Presidio Avenue		San Francisco	CA 94115	923-6380	923-6325	
Dept Public Transportation	**Muni Planning Section**	Straus	P.	949 Presidio Avenue		San Francisco	CA 94115	923-6100		
Dept Public Transportation	**Senior Project Mgr**	Chee	D.	1155 Market Street	5th Flr.	San Francisco	CA 94103	554-1823	554-3176	
Dresser Arela	**Construction Inc**	Dresser	D.	3940 Valley Avenue		Pleasanton	CA 94566-4733	925-485-1711	925-485-1715	
E. Mitchell, Inc.		Michael	B.	1580 Indiana Street		San Francisco	CA 94107	826-2930		
Electric Lightwave Inc.		Guenther	R.	5013 Sunrise Hills Drive		Fair Oaks	CA 95628			

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Fluor Daniel Telecom		Pratt	D.	395 Oyster Point Blv	Ste 321	So. San Francisco	CA 94080	650-742-4416	650-742-4368	
Focal Communications		Ung	T.	200 North Lasalle	Ste. 800	Chicago	Il 60601	312-895-8320		
Francis Construction Co.		Francis	L.	28 Second Street	Rm 300	San Francisco	CA 94107			
Government Information	Agendas	Main Library			5th Flr.	San Francisco	CA 94102			
GST Telecom		Bradshaw	G.	4317 Thurston Way		Vancouver	WA 98662	707-746-5800		
GST Telecom		Wolf	C.	1340 Treat Blvd	Ste. 100	Walnut Creek	CA	925-280-9540		
ICG Telecommunications		Wright	R.	180 Grand Avenue	Ste.1000	Oakland	CA 94612	510-251-7015	510-251-7037	
ICG Telecommunications	Access Service	Hoerning	B.	180 Grand Avenue	Ste 1000	Oakland	CA 94612	510-769-5737	510-769-5737	
ICG Telecommunications	OSP/ISP Engr	Enea	B.	180 Grand Avenue	Ste 1000	Oakland	CA 94612	510-251-7075	510-251-7037	
IntelCom Group (= ICG?)		Bradshaw	G.	190 Park Ctr Plaza	Ste 100	SanJose	CA 95113	707-746-5800		
IXC Communications		Henley	E.	1122 Capitol of Texas Hw	S.	Austin	TX 78746-6426			
J. Flores Construction Co.		Gleghorn	B.	4229 Mission Street		San Francisco	CA 94112-1519			
K J Woods Construction, Inc		Woods	K.	2718 Pacheco Street		San Francisco	CA 94116			
Level 3 Communications		Shone	R.	14023 Denver West Pk		Golden	CO 80401	882-1553	510-672-1012	
Level 3 Communications		Webb	G.	P O Box 450		Clayton	CA 94517	510-673-0818	510-672-1012	
Mayor's Office	Economic Development	Ayerdi	M.	1 Dr Carlton Goodlett Pl.		San Fancisco	CA 94102			
MCI Metro, Inc.		Dubose	J.	2250 Lakeside Blvd		Richardson	TX 75082	214-918-1977	214-918-1062	
MCI Metro, Inc.		Neely	T.	4618 Campos Lane		Winters	CA 95694	530-795-0615	530-795-0715	
MCI Telecommunications		Rawls	K.	400 International Pk		Richardson	TX 75081	214-918-3248	214-918-3111	
MCI WorldCom		Capurso	M.	1 Front Street	Ste 3060	San Francisco	CA 94111	477-3415	477-3409	mark.w.capurso@wco
MCI WorldCom		Caridi	M.	201 Spear Street 5th Flr	Cb 5158	San Francisco	CA 94105	228-1277		
MCI WorldCom		Slagel	J.	2221 Commerce Avenue	Ste A-1	Concord	CA 94520			
MCI WorldCom	Field Installation Manager	Beckermann	D.	55 South Market	Ste 1250	San Jose	CA 95113-2327	408-975-2244	408-975-2210	don.beckermann@wco
Metromedia Fiber Ntwk		Reid	S.					510-782-0900		
Metromedia Fiber Ntwk		Young	M.	One N Lexington Ave		White Plains	NY 10601	914-421-6700		
Metropolitan Fiber		Gromachey	L.	444 Market Street	Ste.1350	San Francisco	CA 94111	362-3300		
Metropolitan Fiber		Shillington	A.	1200 Landmark Center	Ste 1300	Omaha	NB 68102-1892	402-233-7562	-7650	
Metropolitan Fiber		Zivny	S.	1200 Landmark Center	Ste 1300	Omaha	NB 68102-1892	402-233-7609	-7650	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Metropolitan Fiber	Operations Support	Licari	R.	444 Market Street	Ste.1350	San Francisco	CA 94111	362-3300		
MFS Network Technology		Heley	C.	20986 Corsair Blvd		Hayward	CA 94545			
Muni	Chief Inspector	Olson	L.	2500 Mariposa Street	Rm 7	San Francisco	CA 94110			
Muni Overhead Lines		Wong	H.	2502 Alemeda Street		San Francisco	CA 94103	554-9201		
Muni Sys Safety & Security	Director	Chin	P.	1345 Turk Street		San Francisco	CA 94115			
Nextlink		Bohannon	J.	855 Mission Court		Fremont	CA 94539			
Nextlink California		Shone	R.	1924 Deere Ave		Santa Ana	CA 92705	882-1553		
OSP		Simpson	K.	200 C Mason Circle		Concord	CA 94520	925-680-6822		
P & J Utility Co.		McElroy	A.	435 Brannan Street		San Francisco	CA 94107			
P G & E	Dir Capital Improvement	Murray	D.	2180 Harrison Street	2nd Flr.	San Francisco	CA 94110	695-3523	695-3290	
P G & E	Electrical Department	Poniente	E.	2180 Harrison Street		San Francisco	CA 94110	695-3539		
P G & E	Gas Department	Devine	K.	2180 Harrison Street		San Francisco	CA 94110	695-3394	695-3291	
P G & E	Gas Department	Devine	K.	2180 Harrison Street		San Francisco	CA 94110	695-3394	695-3291	
P G & E	Gas Department	Dowd	P.	2180 Harrison Street		San Francisco	CA 94110	695-3574	695-3339	JJL6@PGE.COM
P G & E	Gas Department	Dowd	P.	2180 Harrison Street		San Francisco	CA 94110	695-3574	695-3339	JJL6@PGE.COM
P G & E	Gas Department	Nounou	G.	2180 Harrison Street		San Francisco	CA 94110			
P G & E	General Constr	Healy	P.	2180 Harrison Street		San Francisco	CA 94110	695-3394	695-3332	
P G & E	Service Planning	Wilson	W.	2180 Harrison Street	2nd Flr.	San Francisco	CA 94110	695-3541	695-3525	
Pacific Bell	Engineering	Davey	K.	666 Folsom Street	Rm 1121A	San Francisco	CA 94107	542-9931	957-5973	
Pacific Bell	Engineering	Vowell	C.	666 Folsom Street	Rm. 1121	San Francisco	CA 94107	542-9095	957-5973	CVOWELL@tdsi-q.co
Price Technology		Rodriguez	R.	6640 Sierra Lane		Dublin	CA 94568	510-833-8447		
Public Utilities Comm	Hetch Hetchy Water & Pow	Lameyse	V.	1401 Bryant Street		San Francisco	CA 94103	695-7223		
Public Utilities Comm	Hetch Hetchy Water & Pow	Yamagishi	R.	1155 Market Street	5th Flr.	San Francisco	CA 94103	554-0728	554-1854	
Public Utilities Comm	Sewer Operations	Anderson	H.	750 Phelps Street		San Francisco	CA 94124	648-6882	282-5280	
Public Utilities Comm	Sewer Operations	Hale	L.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2096		
Public Utilities Comm	Sewer Operations	Herrera	J.	2323 Cesar Chavez St		San Francisco	CA 94124	695-2096		
Public Utilities Comm	Sewer Operations	O'Neill	C.	2323 Cesar Chavez St		San Francisco	CA 94124			
Public Utilities Comm	Superintendent WPC	Keaney	W.	750 Phelps Street		San Francisco	CA 94124			

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
Public Utilities Comm	UEB Manager	Quan	M.	1155 Market Street	5th Flr	San Francisco	CA 94103			
Public Utilities Comm	Utility Engineering	Bavishi	K.	1145 Market Street	6th Flr.	San Francisco	CA 94103	554-1884	554-1837	
Public Utilities Comm	Utility Engineering	Hintze	E.	1155 Market Street	4th Flr.	San Francisco	CA 94103	554-0707	554-1854	
Qwest Communications Gp		Berry	M.	555-17th St		Denver	CO 80202	303-312-2832	303-291-1742	
Qwest Communications Gp		Cochran	C.	555-17th St		Denver	CO 80202	303-312-2832	303-291-1742	
RCN		Coppedge	J.	1250 Bayhill Dr	Ste. 200	San Bruno	CA 94066	650-754-2755	650-794-2609	
RCN		Heckman	B.	1250 Bayhill Dr	Ste. 200	San Bruno	CA 94066	650-754-2735	650-794-2609	
RCN	Director of Construction	Weber	S.	1250 Bayhill Dr	Ste. 200	San Bruno	CA 94066	650-754-2696	650-794-2609	
S F Fire Department		Van Dyke	S.	698 Second Street		San Francisco	CA 94107-2015		441-8798	
S F Fire Department	Bur Engr & Water Suppl	Gunn	W.	2245 Jerrold Avenue		San Francisco	CA 94124	558-3557		
S F Fire Department	Facility Renovation Progra	Massetani	G.	698 Second Street		San Francisco	CA 94107-2015			
S F Fire Department	Neighborhood Emerg Resp			698 Second Street		San Francisco	CA 94107-2015		928-3130	
S F Police Department	Dir of Communications	Martin	R.	850 Bryant Street		San Francisco	CA 94102	553-1042	553-1515	
S F Police Department	Director Communications	Nichols	M.	850 Bryant Street		San Francisco	CA 94103	553-1241		
S F Police Department	PLES	Ballentine	J.	850 Bryant Street	Rm 500	San Francisco	CA 94103			
S F Police Department	PLES	Carrington	G.	850 Bryant Street	Rm 500	San Francisco	CA 94103			
S F Port Commision		Zeller	S.	Ferry Building		San Francisco	CA 94111	274-0552	274-0528	
S F Port Commission		Jarrard	C.	Ferry Building		San Francisco	CA 94104	274-0541	274-0528	
S F Redevelopment	Engineering Div	Davis	M.	770 Golden Gate Ave	2nd Flr.	San Francisco	CA 94102	749-2400	749-2525	
S F Redevelopment	Engineering Div	Hapert	D.	770 Golden Gate Ave	2nd Flr.	San Francisco	CA 94102	749-2400	749-2525	
S F Redevelopment	Engineering Div	Hong	W.	770 Golden Gate Ave	2nd Flr.	San Francisco	CA 94102	749-2453	749-2526	
S F Water Department	CDD Engineering	Desai	B.	1990 Newcomb Street	Rm. 112	San Francisco	CA 94124	550-4918	550-4913	
S F Water Department	CDD Engineering	Gapuz-Te	D.	1990 Newcomb Street	Rm. 112	San Francisco	CA 94124	550-4927	550-4913	
S F Water Department	CDD Manager	Flores	A.	1990 Newcomb Street		San Francisco	CA 94124			
S F Water Department	CDD Project Management	Kubick	K.	1990 Newcomb Street		San Francisco	CA 94124	550-2971	550-2980	
S F Water Department	Commercial Division	Flewellen	S.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2526	923-2500	
S F Water Department	Commercial Division	Huie	B.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2523	923-2500	
S F Water Department	Commercial Division	Lew	D.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2520	923-2500	

ORG	BUR	LNAME	FNAME	ADDR	RMNO	CITY	ZIP	PHONE	FAX	EMAIL
S F Water Department	**Distribution Engineering**	Blue	R.	1990 Newcomb Street	Rm. 114	San Francisco	CA 94124	550-4926	550-4913	
S F Water Department	**Distribution Engineering**	Chan	A.	1990 Newcomb Street	Rm. 114	San Francisco	CA 94124	550-4931	550-4913	
S F Water Department	**Distribution Engineering**	Nguyen	T.	1990 Newcomb Street	Rm. 112	San Francisco	CA 94124	550-4916	550-4913	
S F Water Department	**Distribution Engineering**	Poblete	R.	1990 Newcomb Street	Rm. 114	San Francisco	CA 94124	550-4917	550-4913	
S F Water Department	**New Installations**	Evans	G.	425 Mason Street	1st Flr.	San Francisco	CA 94102	923-2521	923-2500	
S F Water Department	**UEB Construction**	Lee	C.	1990 Newcomb Street		San Francisco	CA 94124	550-4925	550-4913	
S F Water Department	**UEB Construction**	Ronis	J.	1990 Newcomb Street		San Francisco	CA 94124	550-2976	550-4913	
San Francisco Thermal		Judd	G.	460 Jessie Street		San Francisco	CA 94103	771-3415	771-3787	
San Francisco Thermal		Stout	B.	460 Jessie Street		San Francisco	CA 94103	771-3415	771-3787	
Sprint Communications		Freeman	D.	1850 Gateway Drive	4th Flr.	San Mateo	CA 94404-2467	650-513-2545	650-513-2555	
Stacy & Witbeck, Inc.	**E G Construction AJV**	Clemente	R.	290 Toland Street		San Francisco	CA 94124			
TCI of California		Bouey	T.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Callow	M.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Hageria	R.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Santos	E.	2055 Folsom Street		San Francisco	CA 94110	863-8500	863-1659	
TCI of California		Victorio	L.	2055 Folsom Street		San Francisco	CA 94110	863-8500	252-6302	
Teleport Communications Gp		Wightman	S.	One Bush Street	Ste. 510	San Francisco	CA 94104	276-0083	276-0050	
Teleport Communications Gp	**c/o AT&T**	Leohner	S.	344 - 20th Street	Ste 210	Oakland	CA 94612			
Teleport Communications Gp	**Fiber Resource Engineer**	Sorrels	B.	One Bush Street	Ste. 510	San Francisco	CA 94104	276-0087	276-0050	
Transportation Authority	**Director Congestion Mgt**	Moscovitch	J.	100 Van Ness Avenue	25th Flr	San Francisco	CA 94102	557-6857	557-6858	
Underground Construction		Cook	M.	P O Box 2000		Benicia	CA 94510	707-746-8800	707-746-1314	
Underground Construction		McManus	A.	P O Box 2000		Benicia	CA 94510	707-746-8800	707-746-1314	
Underground Construction		Shone	R.	5145 Industrial Way		Benicia	CA 94511	882-1553		
US SPRINT				P O Box 7501		San Mateo	CA 94403-7501			
World Com		Choo	K.	444 Market Street	Ste 1350	San Francisco	CA 94111	362-0990	394-6705	

1999 UPCOMING STREET CLOSURES FOR SPECIAL EVENTS

Start Date	End Date	Event Name	Type	Location	Status
1/4/99	1/5/99	Nash Bridges Film Shoot	Film	Fol (WB only): 11th to 12th	12/29/98
1/5/99	1/5/99	Nash Bridges Film Shoot	Film	Perry: 2nd to 4th (no intersection closures)	12/29/98
1/5/99	1/5/99	Nash Bridges Film Shoot	Film	Zoe: Brannan to Bryant	12/29/98
1/5/99	1/5/99	Reopening of City Hall	Civic	Carleton P. Goodlett Way between Grove & McAllister	12/30/98
1/6/99	1/6/99	Nash Bridges Film Shoot	Film	Perry: 2nd to 4th (no intersection closures)	12/29/98
1/15/99	1/15/99	Nash Bridges Film Shoot	Film	18th:DeHaro to Kansas, etc	1/14/99
1/18/99	1/18/99	MLK Day Parade	Parad	4th & Townsend to 3rd to Market to Grove to Larkin	Permit by PD
1/18/99	1/29/99	SF Ballet Grand Opening	Civic	Fra (E/S parking lane only): Ful to MCA	Withdrawn
1/20/99	1/20/99	Film Shoot "Nash Bridges	Film	Treat: 16th to 17th Sts.	1/19/99
1/23/99	1/24/99	Film Shoot SFO	Film	Lombard (e/b only): Lev to Jones	1/19/99
1/24/99	1/25/99	Film Shoot SFO	Film	Annie:Jess to Mission	1/19/99
1/25/99	1/25/99	Film Shoot "Nash Bridges	Film	9th Ave: Lawton to Noriega; Moraga: 8th to 10th Aves.	1/19/99
1/25/99	1/26/99	SF Ballet Gala	Civic	City Hall	FYI
1/31/99	1/31/99	SF Half Marathon	Athleti	Various: Golden Gate Park area	11/12/98
1/31/99	2/2/99	Film Shoot SFO	Film	Leidesforff: Sac to Com	1/19/99
2/2/99	2/2/99	"Nash Bridges" Film Sho	Film	Broderick: Sac to Cal	canceled
2/2/99	2/3/99	Film Shoot SFO	Film	Waverly: Was to Sac	1/19/99
2/3/99	2/3/99	"Nash Bridges" Film Sho	Film	N.Point: Baker to Broderick; Baker: Beach to Bay	2/1/99
2/3/99	2/4/99	Film Shoot SFO	Film	Maiden Ln: Sto to Gra	1/19/99

Start Date	End Date	Event Name	Type	Location	Status
2/6/99	2/6/99	Shuttle Zones for NADA	Corp.	Grove (parking lanes only): Lar to Pok	2/1/99
2/7/99	2/7/99	Shuttle Zones for NADA	Corp.	Grove (parking lanes only): Lar to Pok	2/1/99
2/8/99	2/8/99	Film Shoot "Nash Bridges	Film	4th St: Berry to 3rd Sts.	2/5/99
2/9/99	2/9/99	Film Shoot "Nash Bridges	Film	Pine (s/s parking lane & 1 lane traffic): Jones to Leavenworth	2/5/99 (xcept 4
2/9/99	2/9/99	Shuttle Zones for NADA	Corp.	Grove (parking lanes only): Lar to Pok	2/1/99
2/9/99	2/9/99	"Nash Bridges" Film Sho	Film	Jones: Pine to Bush	2/1/99
2/12/99	2/14/99	Flower Market Fair	Fair	Gra: Was to Bwd; Pac:Col to Sto	9/24/98
2/13/99	3/1/99	Chinese New Year Carniv	Fair	Walter Lum Place	11/12/98
2/14/99	2/14/99	Parking for Chinese NY C	Privat	9th Ave: Judah to Kirkham	Withdrawn
2/14/99	2/14/99	Vietnamese New Year's	Fair	Ell:Hyd to Pok; Lar:Edy to Ofa	1/14/99
2/15/99	2/15/99	23rd Penny Pitch	Block	Powell: Filbert to Columbus	1/14/99
2/16/99	2/16/99	Shuttle Service for BG Au	Corpo	Grove (parking lanes):Polk to Larkin etc	2/12/99
2/17/99	2/17/99	Shuttle Service for BG Au	Corpo	Grove (parking lanes):Polk to Larkin etc	2/12/99
2/17/99	2/18/99	Corporate Event at Ghira	Corpo	Beach: Pok to Lar; Polk: NPT to Beach	1/14/99
2/19/99	2/19/99	Film Shoot: "Nash Bridge	Film	Francisco: Hyde to Leavenworth	2/18/99
2/19/99	2/19/99	Shuttle Service for BG Au	Corpo	Grove: Larkin to Polk; Grove (south parking lane): Van to Polk etc.	2/12/99
2/21/99	2/21/99	Chinese NY Run	Athleti	Chinatown to Marina Green	1/14/99
2/21/99	2/25/99	Banana Republic Confere	Corpo	Fern (parking lane only): Van Ness to Polk	2/11/99
2/23/99	2/25/99	Banana Republic Confere	Corpo	Van Ness: (E/S parking lane only): Sut to Fern	2/11/99
2/24/99	2/24/99	Banana Republic Confere	Corpo	Sutter (N/S parking lane only): Van Ness to Polk	2/11/99
2/25/99	2/25/99	Film Shoot "Nash Bridges	Film	Laguna: Chestnut to Bay; Francisco: Laguna to Octavia	2/24/99
2/26/99	2/26/99	Live 105 Promo	Prom	Mark Lane: Bush to Harlan	2/24/99
2/26/99	2/26/99	Film Shoot "Nash Bridges	Film	Texas: 18th to 19th Streets	2/24/99

Start Date	End Date	Event Name	Type	Location	Status
2/26/99	2/27/99	TV for Chinese NY Parad	Parad	Post (parking lanes only): Pow to Sto; Stockton (w/s only): Post to Gear	1/28/99
2/26/99	2/28/99	Chinese Community Stre	Fair	Gra:Cla to Bwd; Pac;Sto to Col, etc	9/24/98
2/27/99	2/27/99	Chinese New Year Parad	Parad	Mkt:2nd to Sto; etc	Permit by SFP
3/5/99	3/5/99	Film Shoot "Nash Bridges	Film	Hyde:Bay to Lom; Chestnut: Hyde to Larkin	3/4/99
3/9/99	3/9/99	Film Shoot "Nash Bridges	Film	Hyde:Bay to Lom; Chestnut: Hyde to Larkin	3/4/99
3/11/99	3/11/99	Peugeot Commercial Fil	Film	Taylor: Gre to Pac; Broadway: Mason to Taylor	3/4/99
3/11/99	3/18/99	SF Inter. Asian Amer. Fil		Post (partial southside parking lane only): Fillmore to Webster	2/25/99
3/14/99	3/14/99	St. Patrick's Day Celebrat	Fair	Larkin: Hayes to McAllister	2/11/99
3/14/99	3/14/99	Lion Dance Performance	Block	Waverly: Washington to Clay	2/25/99
3/14/99	3/14/99	St. Patrick's Day Parade	Parad	Market to Civic Center	Permit by SFP
3/14/99	3/14/99	St. Patrick's Day Celebrat	Fair	Fulton: Larkin to Hyde Streets	2/11/99
3/15/99	3/15/99	Film Shoot "Nash Bridges	Film	Montgomery: Jackson to Columbus	3/4/99
3/15/99	3/15/99	Film Shoot "Nash Bridges	Film	Washington: Montgomery & Sansome	3/10/99
3/16/99	3/16/99	Film Shoot "Nash Bridges	Film	Casa Way: Marina to Retiro; Retiro: Rico to Filmore	3/4/99
3/17/99	3/17/99	St. Patrick's Day Celebrat	Block	Front: California to Sacramento	1/28/99
3/17/99	3/17/99	Fiddler' Green St. Patrick'	Celeb	Columbus (3 parking spaces only): N.Point to Beach	3/4/99
3/17/99	3/17/99	St. Patrick's Day at Kells	Block	Jackson St, north side meters #Jac510 & 512 only	3/15/99
3/17/99	3/17/99	O'Reilly's St. Patrick's Da	Celeb	Green (N/S parking lane only): Columbus to Powell	1/28/99
3/21/99	3/21/99	Greek Independence Day	Parad	Valencia & 14th to Civic Center	Permit issued
3/22/99	3/22/99	Film Shoot: "Nash Bridge	Film	Montgomery: Jackson to Columbus	3/4/99
3/23/99	3/23/99	Film Shoot: "Nash Bridge	Film	Francisco: Pow to Mas; Mason: Chs to Fran; Taylor: Lom to Col; Pow: C	3/22/99
3/24/99	3/24/99	Film Shoot: "Nash Bridge	Film	Francisco: Pow to Mas; Mason: Chs to Fran; Taylor: Lom to Col; Pow: C	3/22/99
3/25/99	3/25/99	Film Shoot: "Nash Bridge	Film	Daggett: 7th and 16th Sts.	3/22/99

Start Date	End Date	Event Name	Type	Location	Status
3/27/99	3/27/99	Bench Dedication	Block	Sanchez: 21st to Hill	3/11/99
3/28/99	3/28/99	Houlihan's to Houlihan's	Athleti	Marina Blvd (1 n/b lane only), etc	9/24/99
4/4/99	4/4/99	Sisters of P.I. Birthday Ba	Celeb	Castro: Mkt to 18th	3/1/99, B of Su
4/4/99	4/4/99	Parking for Easter Servic	Privat	Anza: 9th to 10th Avenues	2/11/99
4/4/99	4/4/99	Union Street Easter Cele	Fair	Union: Gough to Fillmore; Webster: Green to Filbert	2/11/99
4/4/99	4/4/99	Union Street Easter Para	Parad	Union: Franklin to Fillmore	Permit issued
4/7/99	4/7/99	Metallica Walk of Fame I		Grove: Larkin to Polk	3/30/99
4/7/99	4/7/99	Film Shoot Nash Bridges	Film	Montgomery: Jackson to Washington	4/2/99
4/10/99	4/10/99	Annual Health Fair	Block	Shotwell: 16th to 17th	3/25/99
4/10/99	4/16/99	Newscapade with Al Neu	Corpo	Fulton: west of the monument to Larkin	3/29/99
4/12/99	4/12/99	Film Shoot "Nash Bridges	Film	Clementina: 8th to Sumner; Sumner: Clementina to How	4/12/99
4/13/99	4/13/99	Film Shoot "Nash Bridges	Film	Clementina: 8th to Sumner; Sumner: Clementina to How	4/12/99
4/14/99	4/14/99	Film Shoot "Nash Bridges	Film	Clementina: 8th to Sumner; Sumner: Clementina to How	4/12/99
4/15/99	4/15/99	Film Shoot "Nash Bridges	Film	Clementina: 8th to Sumner; Sumner: Clementina to How	4/12/99
4/15/99	4/16/99	CCAC Grand Opening	privat	8th St: Irwin to Hooper	2/25/99
4/16/99	4/17/99	CCAC Grand Opening	privat	8th St: Irwin to Hooper	2/25/99
4/17/99	4/17/99	SF YMCA Community Cu	Athleti	Steuart: west side parking & traffic lane only	2/25/99
4/17/99	4/17/99	YMCA Community Cup E	Athleti	Steuart (west side parking lane and 1 lane of traffic only): How to Mis	2/25/99
4/17/99	4/18/99	Cherry Blossom Festival	Fair	Pos:Lag to Flm; Web: Gea to Sut	3/26/99
4/18/99	4/18/99	SF Inter. Triathlon	Athleti	Various (NW portion of SF)	canceled
4/19/99	5/9/99	SF Inter. Film Fest.	Film	Post: Flm to Web. 3 parking meters only ,	3/11/99
4/20/99	4/20/99	Film Shoot "Nash Bridges	Film	Lombard: Col to Tay; Powell: Chestnut to Francisco; Jansen: Lom to G	4/19/99
4/22/99	4/28/99	SF Inter. Film Fest.	Film	Castro: 17th to 18th Sts., 2 parking meters only	3/11/99

Start Date	End Date	Event Name	Type	Location	Status
4/24/99	4/24/99	Rally for Mumia Abu-Jam	Rally	C.Goodlett Way & Civic Center Plaza	Disapproved
4/24/99	4/24/99	March for Mumia Abu-Ja	March	Dolores Park to Civic Center	permit by PD
4/24/99	4/25/99	Cherry Blossom Festival	Fair	Pos:Lag to Flm;	3/25/99
4/25/99	4/25/99	Neighborhood Block Part	Block	Filbert: Divisadero to Broderick	3/11/99
4/25/99	4/25/99	Tante Marie's 20th Anniv	Privat	Francisco: Stockton to Bellair	4/16/99
4/25/99	4/25/99	Cherry Blossom Parade	Parad	Civic Center to Polk to Post	permitted by P
4/25/99	4/26/99	California Mille		Mason: Ca to Sac	12/17/98
4/27/99	4/27/99	Postrio Rest. 10th Annive	Corpo	Post (diamond lane): Taylor to Mason	4/8/99
4/27/99	4/27/99	Film Shoot "Nash Bridges	Film	Taylor: Green to Pacific; Bwd: Mason to westerly terminus	4/26/99
4/30/99	4/30/99	Film Shoot "Nash Bridges	Film	Lombard: Baker to Lyon	4/29/99
5/1/99	5/1/99	Neighborhood Block Part	Block	Brentwood: Hazelwood to Valdez	3/25/99
5/1/99	5/1/99	Cameron Carnival	Fair	Joice: Sacramento to Clay	2/25/99
5/1/99	5/2/99	Southern Exposure Fund	Block	Alabama: 17th and Mariposa	4/8/99
5/1/99	5/3/99	Cinco De Mayo Celebrati	Celeb	Various Location in Civic Center Area	4/8/99
5/2/99	5/2/99	Cinco De Mayo Parade	Parad	24th & Bryant to 14th & Harrison	Permit by PD
5/3/99	5/3/99	Film Shoot "Nash Bridges	Film	Jessie: 4th to 5th; Natoma: 5th to 6th; Mary: How to Mis	4/26/99
5/6/99	5/6/99	SF Inter. Film Fest.	Film	Castro: 17th to 18th Sts., 2 parking meters only	3/11/99
5/8/99	5/8/99	School May Fair	Block	North Point: Scott to Divisadero	3/25/99
5/8/99	5/8/99	First Baptist Church Bloc	Block	Waller: Octavia to Laguna	3/25/99
5/8/99	5/8/99	Asian Art Museum Groun	Civic	Fulton: Larkin to Hyde	2/25/99
5/8/99	5/8/99	Mission Library Gran Reo	Block	Bartlett: 24th to 25th	3/25/99
5/10/99	5/10/99	Film Shoot: Jings Product	Film	Valencia (N/B only): 14th to 15th	5/7/99
5/13/99	5/16/99	Trap Door's Beach Party	Corpo	Scott (west side parking lane): Lom to Chs	4/8/99

Start Date	End Date	Event Name	Type	Location	Status
5/15/99	5/15/99	Neighborhood Block Part	Block	Mars: 17th to Corbett	3/11/99
5/15/99	5/15/99	YWCA	Block	Commercial: Kearny to Grant	5/4/99
5/15/99	5/15/99	Black & White Ball Prome	Block	Fillmore: California to Pine Streets	5/12/99
5/16/99	5/16/99	World Premiere Star War	Grand	Sutter: Van Ness to Polk etc.	5/12/99
5/16/99	5/16/99	AIDS Candlelight Vigil &	Parad	Mkt & Castro to Market to City Hall	permit by PD
5/16/99	5/16/99	Bay to Breakers	Athleti	Various Locations	1/28/99
5/20/99	5/20/99	ILM Commercial Film Sh	Film	Waverly: Clay to Washington	5/19/99
5/21/99	5/21/99	ILM Commercial Film Sh	Film	Minna: New Mont. To 2nd St.	5/19/99
5/21/99	5/21/99	Young President's Organi	Shuttl	Stockton(parking lanes): Pine to CA; Parking lane closures on Pine & C	3/25/99
5/22/99	5/22/99	KFOG Kaboom	Celeb	Embarcadero: Harrison to Townsend	4/22/99
5/22/99	5/22/99	Young President's Organi	Shuttl	Stockton(parking lanes): Pine to CA; Parking lane closures on Pine & C	3/25/99
5/22/99	5/22/99	Neighborhood Block Part	Block	Ulloa: Sydney Way to Laguna Honda Blvd.	3/11/99
5/22/99	5/22/99	Bayview Opera House Fa	Fair	Oakdale: Mendell to 3rd St.	5/13/99
5/22/99	5/22/99	Family Day Celebration	Fair	Oakdale: 3rd to Mendell; Mendell: 3rd to Oakdale	5/13/99
5/23/99	5/23/99	Young President's Organi	Shuttl	Stockton(parking lanes only): Pine to CA; Parking lane closures on Pine	3/25/99
5/23/99	5/23/99	ILM Commercial Film Sh	Film	Front: Mkt to CA; Pine: Mkt to Bat	5/19/99
5/24/99	5/24/99	Young President's Organi	Shuttl	Stockton(parking lanes only): Pine to CA; Parking lane closures on Pine	3/25/99
5/25/99	5/25/99	Young President's Organi	Shuttl	Stockton(parking lanes only): Pine to CA; Parking lane closures on Pine	3/25/99
5/26/99	5/26/99	Young President's Organi	Shuttl	Stockton(parking lanes only): Pine to CA; Parking lane closures on Pine	3/25/99
5/27/99	5/27/99	Young President's Organi	Shuttl	Stockton(parking lanes only): Pine to CA; Parking lane closures on Pine	3/25/99
5/28/99	5/28/99	Young President's Organi	Shuttl	Stockton(parking lanes only): Pine to CA; Parking lane closures on Pine	3/25/99
5/29/99	5/30/99	Carnaval	Fair	Har: 16th to 22nd, etc	2/25/99
5/30/99	5/30/99	Carnaval Parade	Parad	24th: Bry to Mis; Mission: 24th to 14th; 14th: Mis to Har	permitted by P

Start Date	End Date	Event Name	Type	Location	Status
6/2/99	6/2/99	Grand Opening Hotel W	Corpo	3rd (lane closure only): How to Mis; How (lane closure only): Haw to 3rd	5/27/99
6/3/99	6/3/99	Black & White Ball	Civic	Various Parking Lanes in Civic Center area	2/25/99
6/3/99	6/7/99	Black & White Ball	civic	Fulton: Larkin to Hyde	2/25/99
6/3/99	6/7/99	Black & White Ball	Civic	Grove: Van Ness to Franklin	5/13/99
6/4/99	6/4/99	Black & White Ball	civic	Various Parking Lanes in Civic Center Area	2/25/99
6/4/99	6/4/99	In the Street Festival	Block	Steiner: Herman to Duboce	5/13/99
6/5/99	6/5/99	Escape From Alcatraz	Athleti	NW portion of SF, Various Locations	7/23/98
6/5/99	6/5/99	Escape From Alcatraz	Athleti	Marina Blvd (1 lane only): Scott to Lyon	7/23/98
6/5/99	6/5/99	Demonstration Against W	Parad	UN Plaza to Dolores Park	permit by PD
6/5/99	6/5/99	In the Street Festival	Block	Ellis: Leavenworth to Hyde	5/13/99
6/5/99	6/5/99	ILM Commercial Film Sh	Film	Sansome: Bush to Pine	6/4/99
6/5/99	6/6/99	Union Street Arts Festival	Fair	Union: Gou to Stn, etc	12/17/98
6/5/99	6/6/99	SPCA Animal WingDing	Fair	Alabama:15 to 16; Florida:16 to Tre; Treat:Har to 15th	12/17/98
6/5/99	6/6/99	Cyberbuss	Block	Griffith: Revere to Quesada	4/8/99
6/5/99	6/6/99	Black & White Ball	civic	Various Streets in Civic Center Area	2/25/99
6/5/99	6/6/99	Black & White Ball	civic	Grove: Van Ness to Franklin	2/25/99
6/5/99	6/9/99	PBS Broadcasting Displa	Displa	Ellis (most most northerly parking lane & traffic lane only): Mason to Tay	4/8/99
6/6/99	6/6/99	CA Aids Ride	Athleti	Various, no street closures involved	No permit requ
6/6/99	6/6/99	SPCA Animal WingDing	Fair	Alabama:16 to 17; Florida:16 to 17	12/17/98
6/6/99	6/6/99	Statuto Race	Athleti	Stockton: Union to Filbert	4/22/99
6/6/99	6/6/99	Hispanic Scholarship Fun	Athleti	Gilman: Giants Dr. to Hunter's Pt. Ex. Etc.	5/13/99
6/6/99	6/6/99	In the Street Festival	Block	Ellis: Leavenworth to Hyde	5/13/99
6/9/99	6/14/99	Fiesta Filipina	Fair	Grove: Larkin to Polk	5/13/99

Start Date	End Date	Event Name	Type	Location	Status
6/10/99	6/10/99	Cocktails on Maiden Lan	Benefi	Maiden Lane: Grant to Kearny	5/27/99
6/11/99	6/14/99	Fiesta Filipina	Fair	Larkin: Hayes to McAllister; Grove: Larkin to Hyde	5/13/99
6/12/99	6/13/99	North Beach Festival	Fair	Grant:Col to Fil;Green: Col to Gra; Vallejo:Col to Gra	2/11/99
6/13/99	6/13/99	Inter. Schools Celebratio		Oak: Gough to Franklin	withdrawn
6/13/99	6/13/99	Haight Street Fair	Fair	Haight:Masonic to Stanyan, etc	11/13/98
6/15/99	6/15/99	Inter. Schools Celebratio		Hickory: Gough to Franklin	5/27/99
6/15/99	6/28/99	Gay & Lesbian Film Festi	Festiv	Eureka Valley Lot #1 behind the Castro Theater	4/22/99
6/16/99	6/16/99	City Bank Film Shoot	Film	Conneticut: 20th to 22nd	6/15/99
6/17/99	6/17/99	City Bank Film Shoot	Film	Conneticut: 20th to 22nd	6/15/99
6/17/99	6/17/99	Nextel Film Commercial	Film	Waverly: Washington to Sacramento	6/15/99
6/19/99	6/19/99	"Do Something" Bike Rid	Athleti	Beach (1 lane only): Laguna to Marina Blvd, Marina (1 lane only): Buc to	5/13/99
6/19/99	6/19/99	Juneteenth Parade	Parad	Panhandle to Ellis & Scott	permit by SFP
6/19/99	6/19/99	City Bank Film Shoot	Film	Bush: Battery to Montgomery	6/15/99
6/19/99	6/20/99	Juneteenth	Fair	Pierce: Ellis to O'Farrell; O'Farrell: Pierce to Scott	4/22/99
6/20/99	6/20/99	Neighborhood block Part	Block	Washington: Scott to Divisadero	5/27/99
6/20/99	6/20/99	City Bank Film Shoot	Film	Bush: Battery to Montgomery	6/15/99
6/23/99	7/3/99	Extreme Games	Athleti	Pier 30-32	permit by Port
6/24/99	6/24/99	NASCAR Rally		Leavenworth: Chestnut to Greenwich; Lombard: Hyde to Jones	Disapproved
6/24/99	6/27/99	X Games Street Luge	Athleti	Alta Mar: Seal Rock Dr. to Pt. Lobos	4/22/99
6/24/99	6/27/99	X Games Street Luge	Athleti	Pt. Lobos: 45th to Great Hwy; Great Hwy: Pt. Lobos to Balboa	4/22/99
6/24/99	7/4/99	ESPN Parking & Shuttle		T.Francois Blvd: 3rd to Mission Rock	6/23/99
6/24/99	7/4/99	Shuttle & X Games Parki	Corp	T. Francois Blvd: 3rd St to Mission Rock	6/23/99
6/25/99	6/25/99	Gr. Opening Tenderloin C		Taylor: Eddy to Ellis Street	6/10/99

Start Date	End Date	Event Name	Type	Location	Status
6/25/99	6/28/99	Gay Pride Celebration	Fair	Civic Center Area	1/28/99
6/26/99	6/26/99	Dyke March Pre-Celebrati	Celeb	Dolores: 18th to 20th Sts.	unpermitted
6/26/99	6/26/99	Dyke March	Parad	Dolores Park to Market & Castro	
6/26/99	6/26/99	Dyke March Celebration	Celeb	Market: Castro to Noe	unpermitted
6/26/99	6/27/99	Pink Saturday	Civic	Castro: 19th to Mkt; 18th: Cwd to Hfd	5/27/99
6/27/99	6/17/99	Nextel Comm. Film Shoot	Film	Waverly: Washington to Sacramento	6/15/99
6/27/99	6/27/99	Gay Pride Parade	Parad	Market: 2nd to Civic Center	permit by PD
6/27/99	6/27/99	Club Townsend Closure		Townsend: 2nd to 3rd	5/13/99
7/2/99	7/5/99	Tall Ships		Wharf Area	
7/3/99	7/4/99	Upper Fillmore Jazz Fest.	Fair	Fillmore: Geary to Eddy; Gea: Web to Stn etc	4/22/99
7/3/99	7/4/99	Jazz & All That Art on Fill	Fair	Fillmore: Geary to McAllister etc.	Disapproved
7/3/99	7/4/99	Fillmore Street Jazz Festi	Fair	Fillmore: Jackson to Post, etc	2/11/99
7/3/99	7/5/99	Chronicle's 4th of July	Fair	Jefferson: Hyde to Terminus	12/17/98
7/4/99	7/4/99	Neighborhood Block Part	Block	26th St.: Sanchez to Noe	6/10/99
7/4/99	7/4/99	Chronicle's 4th of July	Firew	Wharf Area	12/17/98
7/4/99	7/4/99	Neighborhood Block Part	Block	Sylvan: Sloat to Ocean	5/13/99
7/4/99	7/4/99	Chronicle's 4th of July	Firew	Van Ness: North Pt. To Muni Pier	12/17/98
7/4/99	7/4/99	Levis Union Square Conc	Corpo	Post: Powell to Stockson Xcept MUNI	6/23/99
7/4/99	7/4/99	Neighborhood Block Part	Block	Golden Gate: Baker to Lyon	6/23/99
7/4/99	7/4/99	Chronicle's 4th of July	Firew	N/B Embarcadero: Bwd to Bay	12/17/98
7/4/99	7/4/99	Neighborhood Block Part	Block	37th Ave: Kirkham to Lawton	6/10/99
7/4/99	7/5/99	Chronicle's 4th of July	Firew	Jefferson: Hyde to Taylor	12/17/98
7/4/99	7/5/99	Chronicle's 4th of July	Firew	Embarcadero: Pow to Tay	12/17/98

Start Date	End Date	Event Name	Type	Location	Status
7/7/99	7/7/99	Grand Opening Hotel Ser	Corp	Taylor: O'Farrell to Geary	5/13/99
7/10/99	7/10/99	SOMAfest	Fair	Harriet: Howard to Folsom	4/22/99
7/11/99	7/11/99	SF Chronicle Marathon	Athleti	Various City Wide	2/25/99
7/14/99	7/15/99	Bastille Day Celebration	Celeb	Claude Lane: Bush to Sutter	5/27/99
7/14/99	7/15/99	Bastille Day Celebration	Celeb	Belden: Bush to Pine; Kearny to Montgomery	5/13/99
7/17/99	7/17/99	Procession in Celebration	Parad	Gough at Bush to California to Taylor	permit by PD
7/17/99	7/17/99	150th Ann. Of Episcopal		Taylor: Sacramento to California	5/27/99
7/17/99	7/18/99	Third Street Fair	Fair	3rd St.:Cargo to Evans	1/14/99
7/20/99	7/21/99	Private Party	Corp	11th St: Folsom to Harrison	5/13/99
7/24/99	7/24/99	Mt. Zion Church Youth Fe	Block	Baker St: Oak to Page	6/10/99
7/24/99	7/24/99	Obon Odori		Octavia: Pine to Austin	6/10/99
7/25/99	7/25/99	North Beach Jazz Festiva		Telegraph Hill Blvd. Grant to Coit Tower	7/8/99
7/25/99	7/25/99	Up Your Alley Fair	Fair	Dore:Howard to Folsom; Folsom: 9th to 10th	5/13/99
7/25/99	7/25/99	Obon Odori		Octavia: Pine to Bush	6/10/99
7/31/99	8/1/99	Polk Street Festival: Swin	Fair	Polk: Jackson to Bush	5/27/99
8/2/99	8/2/99	Dynamite Films	Film	Montgomery: Green to Vallejo	7/29/99
8/7/99	8/8/99	Nihonmachi Street Fair	Fair	Post: Laguna to Fillmore	6/24/99
8/8/99	8/8/99	Benefit for Tenderloin De		Jones: Bwd to Vallejo; Bwd: Jones to easterly terminus	7/29/99
8/11/99	8/11/99	Chase Corporate Challen	Athlet	Various Locations: Fisherman's Wharf	7/8/99
8/12/99	8/12/99	Macy's Grand Opening	Corp	Geary (parking lane only): Powell to Stockton	7/22/99
8/12/99	8/12/99	Macy's Grand Opening	Corp	Geary(most southerly traffic lane only): Powell to Stockton	7/22/99
8/12/99	8/12/99	49'ers VS San Diego	Footb	Candlestick Park	
8/14/99	8/14/99	Neighborhood Block Part	Block	18th Ave: Vicente to Wawona	7/22/99

Start Date	End Date	Event Name	Type	Location	Status
8/14/99	8/14/99	Glide Community House	Openi	Taylor:Ellis to O'Farrel (1 14' lane will remain open)	7/22/99
8/14/99	8/14/99	Tenderloin Summer Carni	Fair	Jones: Golden Gate to Turk	7/22/99
8/15/99	8/15/99	Glide Communi	Openi	Taylor: Ellis to O'Farrell (1 14 ft. lane open)	7/22/99
8/15/99	8/15/99	Glide Communi	Openi	Ellis: Taylor to Jones	7/22/99
8/19/99	8/19/99	49'ers VS Seattle	Footb	Candlestick Park	
8/21/99	8/21/99	Rescue Mission's Summe		Jones: Eddy to Turk	6/10/99
8/22/99	8/22/99	Perry's 30th Anniversary	Fair	Union: Laguna to Buchanan	5/27/99
8/22/99	8/22/99	BRAVA: Youth Arts Fest	Fair	24th St.: York to Hampshire	6/24/99
8/28/99	8/28/99	Youth Gospel Music Rally		Kirkwood: 3rd to Mendell	7/22/99
9/4/99	9/6/99	Blues & Art on the Bay	Fair	Treasure Island	permit by T. Isl
9/7/99	9/12/99	Opera Grand Opening	Openi	Fulton: Franklin to Gough	7/22/99
9/11/99	9/11/99	Neighborhood Block Part	Block	28th Ave: Irving to Lincoln Way	7/22/99
9/11/99	9/11/99	Opera Gala	Civic		
9/11/99	9/12/99	Fest. Of Culinary Arts	Fair	Polk: Eddy to MCA; Turk: Van to Lar	6/24/99
9/12/99	9/12/99	R&H Wholesale Open Ho		Isis: 12th to 13th Streets	7/22/99
9/12/99	9/12/99	Neighborhood Block Part	Block	Larkin: Greenwich to Lombard	7/22/99
9/12/99	9/12/99	Neighborhood Block Part	Block	Greenwich: Divisadero to Broderrick	7/8/99
9/12/99	9/12/99	150th Anniversary of Con		Montgomery:Jackson to Washington	
9/17/99	9/18/99	Family Harvest Festival	Fair	Union: Battery to Front; Front: Union to Green	7/8/99
9/18/99	9/18/99	Alcatraz Triathlon XIX	Athleti	Marina Blvd (1 lane only): Lag to Buc	10/22/98
9/18/99	9/18/99	Neighborhood Block Part	Block	Chestnut: Broderick to Baker	
9/18/99	9/18/99	Neighborhood Block Part	Block	2nd Ave: Lake to California	7/22/99
9/18/99	9/19/99	Chinatown Moon Festival	Fair	Grant: California to Pacific	5/13/99

Start Date	End Date	Event Name	Type	Location	Status
9/19/99	9/19/99	49'ers VS New Orleans	Footb	Candlestick Park	
9/26/99	9/26/99	Annual March of Witness	March	Powell: Broadway to Vallejo	3/25/99
9/26/99	9/26/99	Folsom Street Fair	Fair	Folsom: 7th to 12th etc.	5/13/99
9/26/99	9/26/99	Eagle Tavern Closure	Fair	12th St: Harrison to Folsom	4/22/99
9/26/99	9/26/99	Glen Park Festival	Fair	Diamond: Bosworth to Chenery; Wilder: Diamond to Carrie	7/8/99
9/26/99	9/26/99	Neighborhood Block Part	Block	Beach: Broderick to Divisadero	7/22/99
10/2/99	10/2/99	Islais Creek Waterfront F	Fair	Various in the Islais Creek area	
10/2/99	10/2/99	Blessing of the Animals	Block	Golden Gate: Leavenworth to Jones	5/13/99
10/3/99	10/3/99	Bridge to Bridge	Athleti	Various: Ferry Bldg to Presidio	1/28/99
10/3/99	10/3/99	49'ers VS Tennessee	Footb	Candlestick Park	
10/3/99	10/3/99	Neighborhood Block Part	Block	23rd St: Castro to Diamond	5/27/99
10/3/99	10/3/99	Castro Street Fair	Fair	Market: Collingwood to Noe; Castro: 19th to Mkt. Etc	5/27/99
10/9/99	10/9/99	Page Street Fair	Fair	Page: Franklin to Gough	3/25/99
10/10/99	10/10/99	Page St. Fair Extension	Block	12th St.: Howard to S.Van Ness	6/10/99
10/10/99	10/10/99	Page Street Fair	Fair	Page: Franklin to Gough	3/25/99
10/10/99	10/10/99	Neighborhood Block Part	Block	Maywood: Ravenwood to Brentwood	7/8/99
10/17/99	10/17/99	49'ers VS Carolina	Footb	Candlestick Park	
10/23/99	10/24/99	West Portal Fair	Fair	West Portal: Ulloa to 15th Sts.	
10/24/99	10/24/99	Champion Run for Childr	Athleti	Dr. Carleton Goodlett Place	3/11/99
10/24/99	10/24/99	Champion Run for Childr	Athleti	Sanchez: Duboce to Market	3/11/99
10/24/99	10/24/99	Champion Run for Childr	Athleti	Various Lane Closures	3/11/99
10/24/99	10/24/99	Champion Run for Childr	Athleti	McAllister: Polk to Larkin	3/11/99
10/24/99	10/24/99	Champion Run for Childr	Athleti	Larkin: McA to Gro; Hyde: McA to Grove; Grove: Hyd to Polk	3/11/99

Start Date	End Date	Event Name	Type	Location	Status
11/7/99	11/7/99	49'ers VS Pittsburgh	Footb	Candlestick Park	
11/20/99	11/20/99	Rescue Mission's Thanks		Jones: Eddy to Turk	6/10/99
11/21/99	11/21/99	49'ers VS St Louis	Footb	Candlestick Park	
11/28/99	11/28/99	Run to the Far Side XV	Athleti	Oak: Stanyan to Broderick; Fell: Stanyan to Broderick, etc.	3/11/99
11/29/99	11/29/99	49'ers VS Green Bay	Footb	Candlestick Park	
12/3/99	12/4/99	Corporate Event	Corpo	Fern: Van Ness to Polk	4/8/99
12/4/99	12/4/99	"Holly Days" at Hamlin Sc		Broadway: Buchanan to Webster	6/24/99
12/12/99	12/12/99	49'ers VS Atlanta	Footb	Candlestick Park	
12/18/99	12/18/99	Rescue Mission's Toy Giv		Jones: Eddy to Turk	6/10/99
12/26/99	12/26/99	49'ers VS Washington	Footb	Candlestick Park	
1/16/00	1/16/00	Millennathon 3.3 Mile	Athlet	Various throughout SF	
1/16/00	1/16/00	Millennathon 21 KM	Athlet	Various throughout SF	
1/16/00	1/16/00	Millennathon 21 Mile	Athlet	Various throughout SF	
1/28/00	1/30/00	Flower Market Fair	Fair	Gra: Bwd to Was; Jac: Sto to Kea; Pac: Sto to Col	
1/30/00	1/30/99	SF Half Marathon	Athleti	Oak & Fell: Stanyan to Baker etc.	6/24/99
2/18/00	2/20/00	Community Street Fair	Fair	Gra: Bwd to Cla; Jac: Sto to Kea; Pac: Sto to Col	
3/26/00	3/26/00	Houlihan's to Houlihan's	Athleti	Marina Blvd (1 lnne only) Lyon to Buchanan; Van Ness: Npoint to Termi	6/24/99
5/27/00	5/27/00	Escape From Alcatraz	Athlet	Pt. Lobos: 48th to Great Hwy	
6/4/00	6/4/00	Statuto Race	Athlet	Stockton:Un to Fil etc.	
6/4/00	6/4/00	CA AIDS Ride	Athlet	Various Locations	no permit requi
6/11/00	6/11/00	Haight Street Fair	Fair	Haight: Stanyan to Masonic etc.	

City and County of San Francisco

Willie Lewis Brown, Jr., Mayor
Mark A. Primeau, Architect, AIA, Director

(415) 554-5800
FAX (415) 554-5843
http://www.sfdpw.com

Department of Public Works
Bureau of Street-Use and Mapping
875 Stevenson Street, Room 460
San Francisco, CA 94103-0942

Barbara L. Moy, Bureau Manager

UNDERGROUND PLANNING MEETING

MEETING DATE: July 6, 1999

PRESENT:

John Fadeff	-DPW/BSM	(554-5830)
Scot Burbank	BOE/PMD	(558-4046)
Carlos DeAnda	-PG&E	(330-2138)
Brian Heckman	-RCN	(650-794-2735)

DISCUSSION:

A. PROJECT STATUS

1. UGD 318 - DOLORES HEIGHTS DISTRICT

PHASE 2 – Final drawings are due in August and construction to begin in September or October.

2. UGD 310 - PRESIDIO HEIGHTS

PHASE 2 – PG&E received streetlight tags, streetlights being lit as system is energized. PG&E to begin customer conversions next week. PG&E to send letter this week indicating that conversions are to begin and requesting that customers complete their work.

California St. – Construction working from Parker toward Arguello. Still in area with gas only; not in area with undergrounding work. 90% of properties converted.

3. UGD 320 - BREWSTER/JOY

Poles out. Construction complete.

4. UGD 321 - INDIANA STREET/ISLAIS CREEK & UGD 323 - CESAR CHAVEZ

All poles removed except the one serving Caltrain. This pole, on the north side of the street, is not in way of City construction project.

5. UGD 324 - DUBOCE AVENUE

No further information on MUNI's construction schedule.

6. UGD 311 - CORBETT AVENUE - PEMBERTON STAIRWAY

Project is still on hold.

7. UGD 335 - UPPER FOLSOM

Substructure work completed. About 8 properties need to be converted. PG&E designing electrical work; cable pulling to begin in August/September.

8. UGD 322 - Alpine Terrace/Museum Way

Electrical estimate complete and composite in process. Construction is expected to begin early September.

9. UGD 327 - INNER SUNSET
Streetlight design is proceeding. Lighting locations will be available by August 13. Construction scheduled to begin in November.

10. UGD 338 - Ocean Avenue
No decision has been made on what will be included in project (bulb outs, "historic" lights, improvements at Phelan Loop).

11. UGD 339 – Bernal South Slope (Banks/Chapman)
PG&E will route along Eugenia instead of Powhatten, which is their current transmission corridor. Streetlight locations still to be determined.

12. UGD 333 - Shotwell/Montezuma
Construction 40% complete. 75% of properties have completed conversion work. PG&E has requested variance from City for paving concrete streets in area.

B. OTHER BUSINESS

1. None.

THE NEXT MEETING WILL BE HELD ON TUESDAY, 3 August 1999, AT 9:00 A.M. AT 875 STEVENSON STREET, ROOM 460, BSM CONFERENCE ROOM.

cc: All Attendees
CULCOP - through Joe Norris
Kris Kilgore - BSM
Hin Lok Kung - BOE
Jack Donohoe - DTIS
Barbara Moy - BSM
Manfred Wong - CWP
Lynn Bunim - PacTel
Norman Chan - BOE
Naoki Kaku – BOE
Lesley Wong - BOE/S&H
Louis Victorio – TCI
Sieg Weber – RCN
Maurice Charley – PG&E
John Katz – MUNI
Charles Yu - BOE/S&H
Amy Powell- DHIC
Brian Christiansen - Duboce
Brian Gatter - BOE/Landscape
Joe Ovadia – PMD
Cynthia Chono - BSM
Ray Yamagishi - BLHP
Tom Flahavan - DET
Scot Burbank - BOE/PMD
Kathy Devine - PG&E
Ben Cruz – BOE
Brian Heckman – RCN
Patrick Rivera – BOE/PMD
Sam Lauter - PG&E
Carol Finucane - BOE
Don Stroh - DHIC
Louis Victorio - TCI
Terry Bouey - TCI
Dave Bradley - PG&E
Joe Marino - DHIC
Terry Elisaia - DET
Naoki Kaku - BOE S&H
Richard Hong - PG&E
Lowell Volk – TCI
Jim Coppedge – RCN

City and County of San Francisco

Department of Public Works
Street Construction Coordination Center

UTILITY COORDINATION REPORT
for July 1, 1999 to July 30, 1999

Notice of Intent and Request for Information Issued (NOI):	**Date**
0101J – Capp/Liberty/Hartford/19th Streets Sewer Replacement (Formerly 1806N)	7/1/99
1767N – Lake Merced Boulevard Roadway Restoration Project	7/29/99

Final Preliminary Plans Issued (LOT):	
1589N – Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	7/23/99
1605N – Sacramento/Pierce/Wilmot Streets Sewer Replacement	6/10/99
1777N – Clay and Sacramento Streets Sewer Replacement	7/1/99
1784N – Leavenworth Street Sewer Replacement	6/2/99
1794N – Peabody Street Sewer Replacement	7/16/99
1701N – Seventh Street Pavement Renovation	7/30/99

State of California:

Other:	
N Line/Miscellaneous Rail Replacement Program (MUNI)	6/24/99

Projects in Progress (NOI)

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
—N	Greg Cruz	554-8268	Various Locations, Construction of Curb Ramps - STPL-5934(030)	Pav	9/4/97
0101J	Philip Louie	437-7045	Capp/Liberty/Hartford/19th Streets Sewer Replacement	SW	8/2/99
0102J	Cliff Wong	554-8339	11th/22nd Avenues Sewer Replacement	SW	9/6/99
1048N	Gene Handa	554-8341	Sunnydale Sewer Improvements	SW	7/3/96
1076N	Arlen Ung	554-8263	West End Utilities	Pav	8/11/97
1100N	Martha Ketterer	554-8296	Ecker Street, Mission Street to Elim Alley	Pav	1/8/96
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements Locations #306 & 309	UG	2/15/98
1145N	Naoki Kaku	554-8246	Bernal Heights Street Improvement, Banks/Chapman Area	Pav	12/2/96
1202N	Linda Leong	648-6882	North Point Plant Improvement, Phase II	Pav	1/30/96
1218N	Cliff Wong	554-8339	Market , Larkin and Harrison Streets Sewer Replacement	SW	3/29/96
1243N	Ronald Cheng	558-4049	Marina Seawall and Roadway Improvement	Pav	4/12/96
1277N(1)	Laarni Camerino	554-8256	Var Loc: As Needed Paving - McAllister, Polk, Grove & Van Ness Avenue	Pav	8/17/98
1277N(2)	Pak Choi	554-8283	Various Locations: As Needed Paving - Stockton (Post to Market Street)	Pav	8/17/98
1277N(3)	Greg Cruz	554-8268	Var Loc - As Needed Pav: Lake Merced from Skyline Blvd. To John Muir Drive	PAV	9/28/98
1285N	Brian Gatter	554-8292	Pioneer Park Renovation -- Telegraph Hill Stairways	Pav	11/14/97
1294N	Leon Louie	558-4070	Fourth Street Bridge Fender Repair Project	Str	12/18/96
1330N	Wallis Lee	554-8344	2nd / 9th Streets Sewer Abandonment Project	SW	6/27/97
1349N	Saed Toloui	558-4084	12th Avenue/Quintara Street, Stairway Construction	Str	2/7/97
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	12/2/96
1381N	Patrick Riviera	558-4045	Martin Luther King Utilities	Pav	9/12/97
1385N	Laarni Camerino	554-8256	Various Locations: Concrete Street Reconstruction - Stillings Ave from Teresita to Congo	PAV	7/10/98
1389N	Pak Choi	554-8283	Mission Street Pavement Renovation	Pav	6/13/97
1395N	Cliff Wong	554-8339	Sacramento/ Larkin/ Pine Streets Sewer Replacement	SW	4/10/98
1407N	Narciso Paderanga Jr.	554-8258	California Street Pavement Renovation, STP-17	Pav	2/13/97
1415N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	Str	7/31/97
1421N	Clifford Wong	554-8339	Green Street Sewer Replacement - Columbus Avenue to Powell Street	SW	1/17/97
1423N	Leon L. Louie	558-4070	Seismic Retrofit of Various Pedestrian Over Crosses	SR	7/31/97
1432N	Gene Handa	554-8341	Post Street Sewer Replacement	SW	2/7/97
1459N	Narciso Paderanga, Jr.	554-8258	Fillmore Street Pavement Renovation and Muni Underground Ductbank System	Pav	8/29/97
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	11/10/97
1477N(A)	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 14	PAV	7/19/99
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SR	9/30/97
1549N	Thomas Won	554-8275	Ocean/Victoria/Everglade Sewer Replacement	SW	9/23/97
1573N	Wallis Lee	554-8344	5th Street & Harrison Sewer Replacement	SW	2/17/98
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	4/13/98
1590N	Thomas Won	554-8275	Ocean Avenue Sewer Replacement (Joint Venture with MUNI)	SW	7/13/98
1626N	Thomas Won	554-8275	4th/5th Ave/Stanyan St (easement) / Paris Street Sewer Replacement	SW	10/22/98
1628N	Jean To	554-8298	Moraga Street Sewer Replacement: 17th to 18th Avenues	SW	9/16/98
1629N	Peter Cheng	554-8348	Union/Kearny Streets Sewer Replacement	SW	10/28/98
1637N	Cliff Wong	554-8339	Chestnut/Union/Pacific/Harriet Sewer Replacement	SW	5/21/99
1653N	Uday Prasad	558-4061	Demolition of North Beach Garage at 763 Vallejo Street	Str	9/15/97
1655N	Lesley Wong	554-8252	Cezar Chavez Improvements Phase 2		7/27/98
1667N	Lesley Wong	554-8252	Fourth Street Sidewalk Widening Project - Phase 2	Pav	3/10/98
1674N	Joe Haas	558-4539	1680 Mission Street Secondary Power Source	SDV	5/27/98
1678N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Street Reconstruction No. 15	Pav	4/13/98
1680N	Lesley Wong	554-8252	Great Highway and Point Lobos Pavement Renovation	Pav	5/13/98
1724N	Laarni Camerino	554-8256	Various Locations: As Needed Paving - 2nd St. between Townsend & King Streets	Pav	7/10/98
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	10/28/98
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	10/5/98
1735N	Naoki Kaku	554-8246	Various Locations: Bayview District Pavement Renovation	PAV	10/13/98
1748N	Carol Finucane	558-4581	Mid-Market Public Improvements		10/5/98
1755N	David Pang	554-8278	Oak Street Pavement Renovation	PAV	2/2/99
1759N	Pak Choi	554-8283	Mission Street Pavement Renovation Phase 2	PAV	12/30/98
1765N	Thinh Nguyen	558-4554	Kearny/Vallejo to Green Streets AWSS Replacement		3/22/99
1767N	Lesley Wong	554-8252	Lake Merced Boulevard Roadway Restoration Project	PAV	8/30/99

PRJ #	Proj. Coord.	Phone #	Project Title	Type	Due Date
1776N	Iqbal Dhapa	554-8337	Sutter/Filbert Streets and Golden Gate Avenue Sewer Replacement	SW	7/6/99
1791N	Peter Cheng	554-8348	3rd Street Sewer System Improvement Phase III	SW	5/10/99
1795N	Birgit Chase	554-8336	Ashbury/California/Geary Blvd/Masonic Avenue Sewer Replacement	SW	6/22/99
1796N	Peter Cheng	554-8348	Stillings Ave/Russia Ave/Bertita and Prague Streets Sewer Replacement	SW	6/15/99
1797N	Birgit Chase	554-8336	Morris/Ritch/Sterling/Rincon Streets Sewer Replacement	SW	7/19/99
1803N	Bryan Dessaure	554-8299	Clay/Jones Streets Sewer Replacement	SW	7/14/99
1806N	Philip Louie	437-7045	Capp/Liberty/Hartford/19th Streets Sewer Replacement	SW	7/23/99
1978N	Gary Fleming	558-4539	Upgrade Pressure Reducing Stations, Various Locations		4/2/99
1984N	Naoki Kaku	554-8246	Van Ness Pedestrian Safety Improvements	PAV	3/17/99
6618E	Leon L. Louie	558-4070	Seismic Retrofit of Third Street Bridge	Str	8/31/97
6618N	Frank Piruzmand	558-4081	3rd Street Bridge Rehabilitation & Retrofit	Str	3/30/98
7291E	Lynn Fong	554-8269	K-Line Rail Replacement & Ocean Avenue Improvements	Pav	11/3/97
7381E	Fernando Cisneros	554-8278	Hunter's Point Naval Shipyard Infrastructure Backbone Phase I	Pav	11/25/96
7416E	Deirdre Appel	558-4556	Golden Gate Park Reservoir and Pump Station		8/7/98
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	12/22/98
N	Linda DeBolt	554-8265	Surface Streets Improvement Project	Pav	2/6/98

Projects in Progress (NOI)

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
---N	9/4/97		8/7/97	11/9/98	10/20/97	8/20/97			9/4/97
0101J	8/2/99		7/22/99			7/22/99	7/12/99	7/26/99	
0102J	9/6/99								
1048N	7/3/96	Mar-99	7/11/96	6/17/96		7/16/96			7/14/96
1076N	8/11/97	Jul-98	7/17/97			7/23/97	7/18/97	7/29/97	8/26/97
1100N	1/8/96	May-98		5/14/96		12/18/95			2/16/96
1109K	2/15/98		12/30/97	4/27/98	1/21/98	1/9/98	12/30/97	1/9/98	1/13/98
1145N	12/2/96	Nov-98	11/8/96			12/3/96			12/7/96
1202N	1/30/96	18-Nov-97		1/29/96				1/16/96	
1218N	3/29/96	On hold	3/22/96			3/20/96	3/1/96		
1243N	4/12/96		3/29/96				3/25/96	3/19/96	4/23/96
1277N(1)	8/17/98			7/24/98	8/19/98	7/31/98	7/24/98	10/13/98	8/3/98
1277N(2)	8/17/98			7/24/98		7/31/98	7/24/98	10/13/98	8/3/98
1277N(3)	9/28/98		9/8/98	9/10/98	11/2/98	9/9/98	9/4/98	9/23/98	9/17/98
1285N	11/14/97	Jul-98	10/21/97	4/13/98		10/24/97	10/16/97	10/20/97	11/6/97
1294N	12/18/96	May-98	10/25/96	3/19/97		10/18/96		10/9/96	12/7/96
1330N	6/27/97	Apr-98	6/16/97	6/17/97		6/17/97	6/16/97		
1349N	2/7/97	Apr-98	1/9/97			3/27/97	1/10/97	1/24/97	2/7/97
1374N	12/2/96		11/8/96	2/24/97		12/3/96			12/7/96
1381N	9/12/97		8/18/97			8/22/97	8/18/97	10/29/97	9/15/97
1385N	7/10/98		6/12/98	7/10/98		6/22/98	6/18/98	7/17/98	6/23/98
1389N	6/13/97	May-98	5/28/97	6/2/97			6/5/97	5/28/97	6/3/97
1395N	4/10/98			4/27/98	4/17/98	6/2/98	4/8/98	4/13/98	4/20/98
1407N	2/13/97	On hold	1/17/97			1/21/97	1/15/97	1/27/97	2/18/97
1415N	7/31/97	Sep-98	7/16/97		7/10/97	7/18/97	7/8/97	7/22/97	7/28/97
1421N	1/17/97	Jan-98	1/9/97	1/6/97		1/23/97	1/2/97		2/7/97
1423N	7/31/97	Nov-98	7/16/97		7/10/97	7/18/97	7/8/97		7/28/97
1432N	2/7/97	Jun-98		2/20/97		2/11/97	1/23/97		2/18/97
1459N	8/29/97	May-98	8/5/97	12/22/97	10/20/97	8/7/97	8/1/97		9/5/97
1474N	11/10/97	Jul-98	10/21/97	6/17/98	10/16/97	10/24/97	10/16/97		11/6/97
1477N(A)	7/19/99		6/21/99				6/22/99	7/23/99	7/22/99
1548N	9/30/97		9/8/97	4/13/98	9/24/97	9/19/97	9/9/97		9/30/97
1549N	9/23/97					9/19/97	9/11/97		9/30/97
1573N	2/17/98		1/23/98	6/17/98	1/23/98	2/12/98	1/23/98		2/12/98
1585N	4/13/98		4/29/98	4/30/98	4/15/98	5/12/98	4/9/98	4/13/98	4/23/98
1590N	7/13/98			7/13/98		6/19/98	6/18/98	7/16/98	6/23/98
1626N	10/22/98		10/16/98	11/12/98			10/6/98		10/15/98
1628N	9/16/98		9/14/98	9/10/98	9/10/98	9/10/98	9/10/98	9/15/98	9/17/98
1629N	10/28/98			11/12/98		10/2/98	10/1/98	10/9/98	10/13/98
1637N	5/21/99		4/21/99			4/20/99	4/20/99	4/20/99	5/3/99
1653N	9/15/97		9/2/97	9/9/97		9/2/97		9/9/97	9/10/97
1655N	7/27/98		7/1/98		7/6/98		6/29/98		7/20/98
1667N	3/10/98		2/20/98		2/20/98		2/20/98	3/13/98	3/5/98
1674N	5/27/98		5/15/98		5/26/98	5/22/98	5/19/98	6/2/98	6/9/98
1678N	4/13/98								
1680N	5/13/98		4/27/98	6/2/98	5/11/98	5/26/98		4/22/98	5/6/98
1724N	7/10/98		6/22/98	7/10/98	6/17/98	6/22/98	6/18/98	6/22/98	6/23/98
1727N	10/28/98		10/2/98	11/6/98		10/2/98	10/1/98	9/30/98	10/13/98
1732N	10/5/98		9/14/98	11/6/98	11/2/98	9/22/98	9/11/98	10/15/98	9/25/98
1735N	10/13/98		9/14/98	11/6/98		9/22/98	9/15/98	9/25/98	9/25/98
1748N	10/5/98		9/14/98	11/6/98		9/22/98	9/14/98	10/13/98	9/25/98
1755N	2/2/99			2/22/99		1/8/99		1/14/99	2/5/99
1759N	12/30/98		11/23/98		12/27/98	12/10/98			12/9/98
1765N	3/22/99		3/12/99	3/17/99		3/23/99	3/10/99	3/11/99	4/12/99
1767N	8/30/99						8/4/99		

PRJ #	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1776N	7/6/99		6/9/99	6/16/99		6/25/99	6/9/99		7/15/99
1791N	5/10/99		4/8/99	5/6/99		4/22/99	4/8/99		4/21/99
1795N	6/22/99		7/22/99	6/4/99		6/8/99	6/14/99	6/2/99	6/18/99
1796N	6/15/99		5/20/99	5/21/99			5/18/99		6/18/99
1797N	7/19/99		6/21/99			6/22/99	6/22/99	7/19/99	7/26/99
1803N	7/14/99		7/22/99	6/21/99			6/16/99		7/22/99
1806N	7/23/99								
1978N	4/2/99		3/12/99	5/5/99		3/12/99	3/12/99	3/11/99	4/12/99
1984N	3/17/99		2/8/99	5/6/99		2/18/99	2/3/99	2/12/99	2/5/99
6618E	8/31/97	Dec-98	7/16/97		7/15/97	7/18/97	7/24/97	7/28/97	8/26/97
6618N	3/30/98		3/25/98	3/23/98		3/23/98	3/24/98	3/17/98	3/30/98
7291E	11/3/97		10/21/97	6/2/98		10/24/97	10/8/97	10/9/97	10/14/97
7381E	11/25/96		10/31/96			11/13/96	11/1/96	10/30/96	12/7/96
7416E	8/7/98		7/17/98	7/10/98		6/30/98	7/13/98	7/9/98	7/29/98
7458E	12/22/98		11/25/98	2/22/99		12/10/98	12/1/98		12/10/98
N	2/6/98		1/8/98		1/23/98	5/13/98	1/8/98	3/9/98	1/26/98

Projects in Progress (NOI)

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
—N	9/4/97	8/26/97	11/24/98		8/19/97		9/30/97	9/30/97
0101J	8/2/99	7/15/99			7/19/99			
0102J	9/6/99							
1048N	7/3/96	6/18/96	6/25/96	7/16/96	7/1/96	6/21/96		
1076N	8/11/97	7/28/97			8/4/97	7/28/97	7/28/97	7/28/97
1100N	1/8/96	12/11/95	12/21/95	12/11/95	12/28/95	12/8/95		
1109K	2/15/98		1/14/98		1/15/98		1/27/98	1/27/98
1145N	12/2/96	12/7/96	12/2/96		11/25/96	12/3/96	12/3/96	12/3/96
1202N	1/30/96			1/18/96	2/2/96	1/18/96		
1218N	3/29/96	3/14/96		3/14/96	3/18/96	3/18/96		
1243N	4/12/96	3/27/96		4/15/96	3/25/96	4/2/96		
1277N(1)	8/17/98	7/23/98	8/4/98	11/9/98	7/31/98			
1277N(2)	8/17/98	7/23/98	8/4/98	11/9/98	7/31/98	7/31/98	8/13/98	8/13/98
1277N(3)	9/28/98	9/9/98	9/4/98	11/9/98	9/11/98	9/10/98	11/12/98	11/12/98
1285N	11/14/97	11/7/97		2/11/98	10/24/97	10/17/97	11/25/97	11/25/97
1294N	12/18/96	10/24/96		11/7/96	10/28/96	11/19/96		
1330N	6/27/97	7/1/97		7/9/97	6/27/97	6/12/97	7/10/97	7/10/97
1349N	2/7/97	1/17/97	1/22/97	3/17/97		1/13/97	2/5/97	2/5/97
1374N	12/2/96	11/7/96			11/25/96	11/7/96	12/2/96	12/2/96
1381N	9/12/97	8/26/97			8/21/97			9/24/97
1385N	7/10/98	6/15/98	6/23/98		6/25/98	10/8/98	7/29/98	7/29/98
1389N	6/13/97	5/29/97			5/23/97	6/11/97	5/23/97	5/23/97
1395N	4/10/98	4/13/98	1/5/99		4/22/98	4/13/98		5/14/98
1407N	2/13/97	2/24/97	4/17/97	3/19/97	1/23/97	2/3/97	2/5/97	2/5/97
1415N	7/31/97	7/16/97			7/15/97	7/28/97	7/28/97	7/28/97
1421N	1/17/97	1/10/97		1/29/97	2/19/97	12/30/96	1/22/97	1/22/97
1423N	7/31/97	7/16/97			7/15/97	7/28/97	7/28/97	7/28/97
1432N	2/7/97	2/24/97	2/10/97	3/18/97	1/31/97	1/22/97	2/24/97	2/24/97
1459N	8/29/97	8/5/97			8/13/97		9/24/97	9/24/97
1474N	11/10/97	11/7/97			10/23/97	10/14/97	11/25/97	11/25/97
1477N(A)	7/19/99				7/1/99			
1548N	9/30/97	9/12/97			9/15/97	9/29/97	10/9/97	10/9/97
1549N	9/23/97	9/24/97			9/17/97	9/15/97	10/9/97	10/9/97
1573N	2/17/98	1/26/98	3/30/98			1/22/98		2/12/98
1585N	4/13/98	4/13/98			4/30/98	4/13/98	6/25/98	6/25/98
1590N	7/13/98	6/17/98	8/4/98		6/29/98	10/8/98	7/29/98	7/29/98
1626N	10/22/98	10/6/98		11/9/98	10/13/98			1/12/99
1628N	9/16/98	9/10/98	9/8/98	11/9/98	9/11/98	9/10/98	11/12/98	11/12/98
1629N	10/28/98	10/6/98		11/9/98	10/8/98		11/12/98	11/12/98
1637N	5/21/99	4/23/99	5/6/99		4/26/99			
1653N	9/15/97	9/12/97			9/8/97	9/4/97	9/24/97	9/24/97
1655N	7/27/98	7/1/98			7/2/98	7/1/98	7/29/98	7/29/98
1667N	3/10/98	2/20/98			2/27/98			
1674N	5/27/98	5/18/98	5/19/98		6/2/98	5/14/98	7/9/98	7/9/98
1678N	4/13/98							
1680N	5/13/98	4/20/98	5/13/98		4/30/98		6/25/98	6/25/98
1724N	7/10/98	6/15/98	6/23/98		6/23/98	10/8/98	7/9/98	7/9/98
1727N	10/28/98	10/2/98		11/9/98	10/13/98			1/12/99
1732N	10/5/98	9/17/98		11/9/98	9/28/98	9/11/98		11/12/98
1735N	10/13/98	9/18/98		11/9/98	9/18/98	9/9/98		11/12/98
1748N	10/5/98	9/18/98		11/9/98	9/24/98	9/11/98		11/12/98
1755N	2/2/99	1/5/99			12/30/98			
1759N	12/30/98	12/1/98	11/23/98		12/14/98			12/1/98
1765N	3/22/99		3/17/99		3/16/99			
1767N	8/30/99							

PRJ #	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1776N	7/6/99	6/14/99	6/14/99		6/18/99			
1791N	5/10/99	4/7/99	4/7/99		4/9/99			
1795N	6/22/99	6/2/99	6/2/99		6/2/99			
1796N	6/15/99	5/20/99	6/2/99		6/2/99			
1797N	7/19/99	6/23/99			7/2/99			
1803N	7/14/99	6/18/99	6/24/99		7/1/99			
1806N	7/23/99							
1978N	4/2/99	3/16/99	3/17/99		3/16/99			
1984N	3/17/99	2/8/99			2/9/99			
6618E	8/31/97	7/16/97		7/30/97	7/24/97	7/28/97	8/21/97	8/21/97
6618N	3/30/98	3/25/98			4/1/98		5/14/98	
7291E	11/3/97	10/29/97			10/20/97		11/10/97	11/10/97
7381E	11/25/96	11/6/96	11/5/96	11/14/96	11/8/96	12/18/96	12/2/96	12/2/96
7416E	8/7/98	7/13/98		11/9/98	7/20/98	7/1/98		7/29/98
7458E	12/22/98	11/25/98	12/14/98		12/15/98			12/1/98
N	2/6/98	6/22/98			1/26/98	10/8/98		2/12/98

Projects in Progress (NOI)

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
—N	9/4/97	8/12/97		8/8/97	8/13/97	8/8/97	8/8/97	8/26/97
0101J	8/2/99	7/7/99	7/6/99	7/12/99	7/15/99		7/22/99	7/19/99
0102J	9/6/99							
1048N	7/3/96		6/26/96	7/1/96		6/25/96	7/3/96	7/1/96
1076N	8/11/97	7/24/97		7/24/97	7/29/97	8/8/97	7/22/97	8/15/97
1100N	1/8/96		12/20/95	1/3/96	12/14/95	12/18/95	12/27/95	12/20/95
1109K	2/15/98	1/7/98		1/14/98	1/14/98	5/20/98	1/21/98	1/21/98
1145N	12/2/96		11/13/96	11/14/96	11/20/96	12/14/96	12/2/96	11/19/96
1202N	1/30/96		1/16/96	1/19/96	1/31/96	1/17/96		2/6/96
1218N	3/29/96				3/12/96	3/5/96	3/27/96	3/7/96
1243N	4/12/96		3/25/96		3/27/96	3/22/96	3/27/96	3/21/96
1277N(1)	8/17/98	7/21/98		7/31/98	7/29/98	7/23/98		8/4/98
1277N(2)	8/17/98	7/21/98		7/31/98	7/29/98	7/23/98		8/4/98
1277N(3)	9/28/98	9/3/98		9/15/98	9/17/98		1/11/99	9/17/98
1285N	11/14/97	10/20/97	10/28/97	10/27/97	10/23/97	11/18/97	11/10/97	11/13/97
1294N	12/18/96		10/25/96	10/25/96	10/31/96		12/2/96	10/24/96
1330N	6/27/97	6/16/97	7/2/97	6/23/97	6/23/97	7/11/97	8/8/97	7/2/97
1349N	2/7/97	1/13/97	1/13/97	1/21/97	2/12/97	2/27/97		1/22/97
1374N	12/2/96		11/13/96	11/14/96	11/20/96	12/14/96	12/2/96	11/19/96
1381N	9/12/97	8/15/97		8/22/97	8/22/97	11/18/97		8/26/97
1385N	7/10/98	6/15/98		6/23/98	6/19/98		4/13/99	6/29/98
1389N	6/13/97	5/19/97	5/29/97	5/21/97	5/23/97	5/29/97	6/26/97	6/6/97
1395N	4/10/98	4/13/98	4/28/98	4/17/98	4/14/98			4/15/98
1407N	2/13/97	1/17/97	1/15/97	1/24/97	2/12/97	2/27/97	2/24/97	1/22/97
1415N	7/31/97	7/8/97		7/11/97	7/14/97		7/9/97	7/18/97
1421N	1/17/97	1/7/97	1/6/97		2/18/97	2/27/97		1/22/97
1423N	7/31/97	7/8/97		7/11/97	7/14/97		7/9/97	7/18/97
1432N	2/7/97	1/27/97	1/27/97	1/29/97	2/12/97	2/27/97		1/30/97
1459N	8/29/97	8/5/97		8/6/97	8/12/97	8/8/97	11/10/97	8/26/97
1474N	11/10/97	10/20/97		10/21/97	10/22/97	11/18/97	11/10/97	11/13/97
1477N(A)	7/19/99	6/21/99	6/21/99	7/1/99	6/24/99		7/22/99	7/1/99
1548N	9/30/97	9/19/97		9/12/97	9/12/97	9/24/97	9/11/97	9/22/97
1549N	9/23/97	9/12/97		9/18/97	9/16/97	9/24/97	9/19/97	9/22/97
1573N	2/17/98	1/26/98		2/12/98	2/12/98			2/20/98
1585N	4/13/98	4/13/98	4/28/98	4/20/98	4/28/98	5/20/98		4/28/98
1590N	7/13/98	6/15/98		7/8/98	6/19/98		1/11/99	7/7/98
1626N	10/22/98	10/5/98			10/15/98		1/7/99	10/15/98
1628N	9/16/98	9/8/98	9/8/98	9/15/98	9/17/98	9/16/98	9/17/98	9/17/98
1629N	10/28/98	10/1/98		10/7/98	10/6/98			10/15/98
1637N	5/21/99	4/15/99	4/19/99	5/3/99	4/26/99			4/28/99
1653N	9/15/97	9/2/97		9/8/97	9/12/97		9/15/97	9/22/97
1655N	7/27/98	6/29/98	7/20/98	7/10/98	7/15/98	7/29/98	1/11/99	7/15/98
1667N	3/10/98	2/20/98		2/20/98	2/20/98			2/20/98
1674N	5/27/98	5/19/98			6/3/98	5/20/98		6/11/98
1678N	4/13/98							
1680N	5/13/98	4/20/98		5/6/98	5/6/98	6/2/98		5/11/98
1724N	7/10/98	6/22/98		6/23/98	6/19/98		4/14/99	6/29/98
1727N	10/28/98	10/1/98		10/7/98	10/6/98			10/15/98
1732N	10/5/98	9/11/98		9/22/98	9/17/98		1/7/99	9/30/98
1735N	10/13/98	9/11/98		9/22/98	9/17/98		1/7/99	9/24/98
1748N	10/5/98	9/11/98		9/22/98	9/17/98		1/11/99	9/30/98
1755N	2/2/99		12/28/98	1/14/99	1/5/99		1/12/99	1/7/99
1759N	12/30/98	12/1/98	12/1/98	12/10/98	12/10/98		1/7/99	12/14/98
1765N	3/22/99	3/11/99	3/23/99	3/17/99	3/12/99		3/15/99	3/23/99
1767N	8/30/99	8/2/99	8/4/99					

PRJ #	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1776N	7/6/99	6/21/99	6/11/99	6/15/99	6/15/99		7/22/99	6/15/99
1791N	5/10/99	3/31/99	4/6/99	4/8/99	4/7/99		4/13/99	4/13/99
1795N	6/22/99			6/4/99	6/15/99		7/22/99	6/4/99
1796N	6/15/99	5/18/99		6/2/99	6/15/99			6/2/99
1797N	7/19/99	6/21/99	6/21/99	7/1/99	6/24/99		7/22/99	7/1/99
1803N	7/14/99	6/21/99	6/21/99	6/22/99	6/24/99		7/22/99	7/1/99
1806N	7/23/99							
1978N	4/2/99	3/11/99	3/23/99	3/17/99	3/12/99		3/15/99	3/26/99
1984N	3/17/99	2/4/99	2/5/99	2/10/99	2/17/99		3/15/99	2/10/99
6618E	8/31/97	7/17/97		7/21/97	7/18/97	3/24/98	7/16/97	7/18/97
6618N	3/30/98	3/26/98	4/2/98	4/2/98		3/24/98	4/1/98	4/3/98
7291E	11/3/97	10/9/97	10/16/97	10/10/97	10/15/97	11/19/97	11/10/97	10/16/97
7381E	11/25/96	1/10/97	11/13/96	11/13/96	11/7/96		12/2/96	11/19/96
7416E	8/7/98	7/21/98		7/20/98	7/20/98		1/11/99	7/31/98
7458E	12/22/98	12/1/98	12/1/98	12/10/98	12/10/98		1/7/99	12/4/98
N	2/6/98	2/10/98	1/16/98	1/14/98	1/21/97	2/10/98	1/21/98	1/21/98

Projects in Progress (LOT)

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1001H	Paul Travis	557-4631	911/OES Emergency Communications Center		12/6/96
1034N	Ed Choy	554-8284	Chinatown Alleyway Improvements Phase 1 Commercial, Cordelia and Ross	STR	3/26/99
1036N	Lesley Wong	554-8252	Fourth Street Pavement Renovation	Pav	5/28/97
1077N	Steve Bui	554-8298	Bowling Green Drive Contract	SW	9/30/97
1091N	Ed Choy	554-8284	Various Locations South of Market Removal & Pavement Renovation	Pav	4/30/97
1106N	Steve Bui	554-8298	Western Presidio Drainage Improvements (NOI/LOT)	SW	5/16/97
1109K	Thinh Nguyen	558-4554	Underground Storage Tank Replacements, Various Locations	UG	4/28/97
1109N	Linda DeBolt	554-8265	Cesar Chavez (Army) Street Widening	Pav	12/27/96
1133N	Ellaine Taraya	554-8245	Fulton Street Roadway Widening	Pav	10/27/97
1155N	E. Ho/Bhula Patel	554-8324	Grant/Chestnut Street Sewer Replacements	SW	10/21/98
1195N	Gyee Yang	558-4553	Market and Steuart Streets, AWSS Relocation	AWSS	7/20/96
1208K	Joe Haas	558-4539	San Francisco General Hospital Underground Storage Tank Replacement	UG	3/9/98
1223W	Lesley Wong	554-8252	Islais Creek, Street Improvements	Pav	4/30/97
1245N	Wallis Lee	554-8344	Yosemite/Egbert Sewer Enlargment Project (formerly 3180W)	SW	11/27/96
1253N	Iqbal Dhapa	554-8337	Twelfth Street (SR)	SW	5/16/97
1254N	Cliff Wong	554-8339	Eleventh Street Sewer Replacement - Harrison St. to Folsom St.	SW	5/23/97
1272N	Steve Bui	554-8298	Illinois-Cesar Chavez (Army) Streets Sewer Construction	SW	8/8/97
1322N	Lesley Wong	554-8252	Cabrillo Street, 9th and 16th Avenues Pavement Renovation	Pav	3/11/97
1362N	Edward Choy	554-8284	Various Locations SOMA Street District Track Removal & Pavement Renovation Phase	PAV	3/22/99
1373N	Ken Chu	554-8388	Lower Great Highway, 46th, and 48th Avenues, Pavement Renovation	Pav	9/15/97
1374N	Naoki Kaku	554-8246	27th/Noe Street Stairway and Sidewalk Construction	Pav	5/28/97
1392N	Birgit Chase	554-8336	Bayshore Blvd. - U.S. 101 Off-Ramp...Sewer Repl. (1108N)	Pav & SW	2/28/97
1393N	Thomas Won	554-8275	Bush/Kearny/Post Streets Sewer Replacement	SW	10/24/97
1396N	Peter Cheng	554-8348	Sutter/Fell/Broederick Streets Sewer Replacement	SW	5/12/97
1397N	Bhula Patel	554-8324	Douglass/Dolores/Ord/23rd/28th Streets, Sewer Replacement	SW	10/17/97
1408N	Naoki Kaku	554-8246	Geneva Avenue, Pavement Renovation	Pav	2/6/98
1409N	Pak Choi	554-8283	Sutter Street Pavement Renovation STP-19	Pav	3/25/99
1411N	Peter Cheng	554-8348	Harding Park SR	SW	11/14/97
1413N	Iqbal Dhapa	554-8337	Davis/Kearny/Francisco Streets Sewer Replacement	SW	6/25/97
1414N	Thomas Won	554-8275	Treat / 22nd Streets Sewer Replacement	SW	2/28/97
1426N	Ting He	554-8338	Dore/Valencia/Clinton Park SR	SW	12/8/97
1433N	Peter Cheng	554-8348	Shotwell Street Sewer Replacement - Army Street to 26th St	SW	11/7/97
1440N	Pak Choi	554-8283	Various Locations Concrete Street Reconstruction No. 13	Pav	2/6/98
1453N	Naoki Kaku	554-8246	Montgomery, Kearny, & Sacramento, Pavement Renovation	Pav	2/6/98
1454N	Ed Choy	554-8284	Potrero Hill District Track Removal and Pavement Renovation, Phase 3	SW	4/27/98
1460N	Birgit Chase	554-8336	Church / Folsom / Harper Streets Sewer Replacement	SW	10/22/97
1461N	Iqbal Dhapa	554-8337	Mason / Pine / Leavenworth Streets and Meacham Place Sewer Replacement	SW	3/6/98
1474N	Iqbal Dhapa	554-8337	6th / 8th / 43rd Avenues Sewer Replacement	SW	6/22/98
1475N	Birgit Chase	554-8336	Virginia / Fair Avenues/Godeus Street SR	SW	12/24/97
1477N(A)	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 14	PAV	7/19/99
1488N	Peter Cheng	554-8348	24th Ave/California Street Sewer Replacement (1452N)	SW	6/20/97
1491N	Peter Cheng	554-8348	Pacific Ave. Sewer Replacement - Grant Ave. to Stockton St.	SW	9/25/97
1519N	Pak Choi	554-8283	Bus Bulb Improvement Project Phase 1	Pav	1/23/98
1528N	Iqbal Dhapa	554-8337	501 Laguna Honda Boulevard Easement Sewer Replacement	SW	8/25/97
1547N	Peter Cheng	554-8348	33rd Ave/Lyon Street/Molimo Dr SR	SW	1/16/98
1548N	Thomas Won	554-8275	O'Farrell/Farnsworth/Iron/Deming SR	SW	1/9/98
1550N	Bhula Patel	554-8324	Day/Congo/Marston/Cuvier SR	SW	1/30/98
1562N	Birgit Chase	554-8336	Broadway/Bryant/22nd/Sonoma Streets Sewer Replacement	SW	6/26/98
1563N	Iqbal Dhapa	554-8337	Balboa St. and 3rd/20th/42nd Avenues Sewer Replacement	SW	6/25/98
1566N	Peter Cheng	554-8243	Fillmore Street SR	SW	12/19/97
1569N	Peter Cheng	554-8348	Dolores Street/Block 7044 Easement Sewer Replacement	SW	6/12/98
1578N	Jean To	554-8329	Golden Gate Ave. Sewer Replacement-Polk St/Van Ness & Pierce/Scott Sts	SW	3/10/98
1579N	Jean To	554-8329	Illinois Street Sewer Replacement-20th to 19th Street		4/17/98
1583N	Thomas Won	554-8275	Everglade/ Victoria/ Revere/ Bridge View Sewer Replacement	SW	5/14/99
1585N	Bryan Dessaure	554-8299	4th Ave/ 5th Ave/ 21st Ave/ California St. Sewer Replacements	SW	9/15/98

PRJ#	Project Coord.	PH #	Project Title	Type	Due Date
1586N	Jean To	437-7012	Geary, Eddy, Elm and Turk Sewer Replacement	SW	10/20/98
1587N	Jean To	554-8298	7th Avenue and Kirkham Street Sewer Replacement	SW	5/20/99
1588N	Thomas Won	554-8275	Joost Ave/Alemany Blvd/Mt. Vernon Ave/Kensington Way Sewer Replacement	SW	12/22/98
1589N	Birgit Chase	554-8336	Clipper/Noe/Fair Oaks/Kingston Streets Sewer Replacement	SW	8/13/99
1602N	Jean To	437-7012	Howard, Minna and 2nd Streets Sewer Replacement	SW	11/9/98
1603N	Jean To	554-8270	Broad Street, Capitol to Plymouth Avenue Sewer Replacement	SW	7/10/98
1605N	Bryan Dessaure	554-8299	Sacramento/Pierce/Wilmot Streets Sewer Replacement	SW	7/9/99
1606N	Jean To	554-8348	Cayuga/Laurel/Rondel and Douglass Sewer Replacement	SW	10/29/98
1630N	Birgit Chase	554-8336	Polk/Francisco/Quincy/Sacramento Streets Sewer Replacement	SW	6/4/99
1631N	Jean To	554-8298	4th/10th Ave/Anza/Cabrillo Streets Sewer Replacement	SW	2/16/99
1632N	Bhula Patel	554-8324	Post, Grove and Potomac Streets Sewer Replacement	SW	4/6/99
1645N	Peter Cheng	554-8348	Third Street Sewer System Improvement Phase II	SW	2/24/99
1668N	Laami Camerino	554-8388	Golden Gate Avenue Pavement Renovation	Pav	4/27/99
1687N	Narciso Paderanga, Jr.	554-8258	Various Locations Concrete Reconstruction No. 15	Pav	8/31/98
1701N	Laami Camerino	554-8256	Seventh Street Pavement Renovation	Pav	8/13/99
1727N	Eric Kjelsberg	554-8277	Broadway/Leavenworth/Taylor Pavement Renovation	Pav	3/22/99
1729N	Narciso Paderanga, Jr.	558-8258	Brotherhood Way & Font Boulevard Pavement Renovation	Pav	3/25/99
1732N	Pak Choi	554-8283	Eddy and Turk Streets Pavement Renovation	PAV	2/24/99
1734N	Dimitrios Stavrakis	554-8271	Franklin/Greenwich and Union Streets Pavement Renovation	PAV	4/8/99
1765N	Thinh Nguyen	558-4554	Kearny/Vallejo to Green Streets AWSS Replacement		3/22/99
1777N	Iqbal Dhapa	554-8337	Clay and Sacramento Streets Sewer Replacement	SW	7/16/99
1784N	Thomas Won	554-8275	Leavenworth Street Sewer Replacement (CW-231)	PAV	6/14/99
1785N	Peter Cheng	554-8343	Taber Place/Gough Street Sewer Replacement	SW	5/17/99
1785N	Peter Cheng	554-8343	Taber Place/Gough Street Sewer Replacement	SW	5/17/99
1794N	Ryan Cayabyab	554-8307	Peabody Street Sewer Replacement	SW	7/30/99
6094Q	Deanna Calleros	554-8266	Mid Embarcadero Surface Rdwy and F-Line Extension	Pav	6/27/97
7090E	Thinh Nguyen	558-4554	Various Locations Motorized Valves Contract #2	AWSS	3/19/98
7437E	Laami Camerino	554-8256	Howard, Folsom & Hawthorne Streets (SR)	SW	8/29/97
7458E	Pak Choi	554-8283	Clay Street Pavement Renovation	PAV	6/3/99
7474E	Peter Cheng	554-8348	Pine/California/Delancey Streets SR	SW	11/26/97

Project in Progress (LOT)

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1001H	12/6/96		12/3/96	1/22/97		12/5/96		11/25/96	12/16/96
1034N	3/26/99		3/17/99					3/18/99	4/21/99
1036N	5/28/97	Apr-98	5/15/97	6/30/97		5/9/97	5/14/97		
1077N	9/30/97	Apr-98	9/8/97	6/26/98		9/24/97	9/9/97		9/5/97
1091N	4/30/97	15-Sep-97	4/4/97	5/13/97				4/11/97	4/28/97
1106N	5/16/97	3-Nov-97	5/6/97	5/13/97		5/12/97	5/6/97		6/3/97
1109K	4/28/97		4/14/97			4/16/97		4/22/97	5/8/97
1109N	12/27/96	Jun-98	12/5/96				12/3/96		2/7/97
1133N	10/27/97	May-98	10/21/97		10/16/97		10/10/97		10/21/97
1155N	10/21/98		10/16/98	11/9/98		10/7/98	10/6/98		10/15/98
1195N	7/20/96						7/8/96		
1208K	3/9/98		3/24/98	3/5/98		3/18/98	3/5/98	3/12/98	3/24/98
1223W	4/30/97	Jun-98	4/14/97	5/13/97		4/16/97	4/21/97		5/14/97
1245N	11/27/96		11/8/96	2/24/97					12/7/96
1253N	5/16/97	Apr-98	4/28/97	5/13/97		5/5/97	4/29/97		5/12/97
1254N	5/23/97	Jul-98	4/28/97	5/13/97		4/23/97	4/22/97		5/12/97
1272N	8/8/97	Jun-98	7/29/97	6/15/98		7/28/97	7/28/97		
1322N	3/11/97	May-98	2/20/97	2/20/97		2/18/97	2/19/97	2/14/97	2/27/97
1362N	3/22/99		3/12/99	3/22/99			3/12/99	3/19/99	3/16/99
1373N	9/15/97	May-98	8/26/97	4/22/98			8/22/97	8/28/97	9/10/97
1374N	5/28/97	May-98	5/1/97				4/30/97	5/12/97	5/14/97
1392N	2/28/97		2/20/97				2/19/97		2/27/97
1393N	10/24/97		10/21/97	5/19/98		10/15/97	10/8/97		10/21/97
1396N	5/12/97	May-98	5/1/97			5/28/97			5/12/97
1397N	10/17/97		9/26/97		10/20/97	10/1/97	9/26/97		10/14/97
1408N	2/6/98	Jun-98	1/8/98	4/22/98	1/20/98		1/8/98	3/5/98	1/21/98
1409N	3/25/99		3/9/99			3/11/99	2/16/99	3/18/99	3/11/99
1411N	11/14/97	Jul-98	10/23/97			11/5/97	10/24/97		11/4/97
1413N	6/25/97	Jun-98	6/16/97	6/17/97		6/11/97			7/11/97
1414N	2/28/97	Jul-98	2/20/97	2/20/97		2/18/97	2/19/97		2/28/97
1426N	12/8/97	Sep-98	12/4/97		12/3/97	12/10/97	12/3/97		12/17/97
1433N	11/7/97	Jun-98	10/21/97			10/24/97	10/16/97		11/13/97
1440N	2/6/98	Apr-98	1/8/98	1/9/98	1/20/98	1/27/98	1/8/98		1/21/98
1453N	2/6/98	Jul-98	1/8/98				1/8/98	3/9/98	1/26/98
1454N	4/27/98		4/27/98			4/20/98	4/16/98	4/23/98	7/9/98
1460N	10/22/97		10/21/97			10/24/97	10/10/97		10/21/97
1461N	3/6/98	Jul-98	2/20/98	4/2/98			2/20/98		
1474N	6/22/98	Jul-98	6/3/98	6/17/98	6/2/98	6/9/98		6/2/98	6/3/98
1475N	12/24/97		12/12/97		1/20/98	1/6/98	12/15/97		
1477N(A)	7/19/99		7/22/99				6/22/99		7/22/99
1488N	6/20/97	Apr-98	6/9/97			6/4/97	6/3/97		6/16/97
1491N	9/25/97	May-98	9/18/97	6/30/97		9/24/97	9/16/97		
1519N	1/23/98	Jun-98	12/30/97				12/30/97	1/9/98	1/26/98
1528N	8/25/97	Mar-98	8/20/97		10/3/97		8/21/97		9/8/97
1547N	1/16/98		12/15/97		1/20/98	1/6/98	12/17/97		12/23/97
1548N	1/9/98		12/22/97	4/13/98	12/30/97	1/9/98	12/29/97		1/6/98
1550N	1/30/98				1/20/98	2/12/98	1/14/98		2/12/98
1562N	6/26/98		6/22/98		6/17/98	6/22/98	6/18/98	7/16/98	7/9/98
1563N	6/25/98		6/19/98	7/10/98	6/17/98	6/22/98	6/18/98	7/16/98	7/9/98
1566N	12/19/97		12/12/97	12/19/97	12/17/97	12/17/97	12/15/97		
1569N	6/12/98		5/15/98	6/12/98	6/17/98	6/9/98	5/19/98	6/2/98	6/9/98
1578N	3/10/98		3/24/98	6/30/98	3/9/98		3/9/98	3/11/98	3/24/98
1579N	4/17/98			5/15/98		4/14/98	4/13/98	4/13/98	4/23/98
1583N	5/14/99		4/30/99	5/5/99			5/3/99	5/3/99	5/17/99
1585N	9/15/98		9/8/98	9/2/98	9/10/98	9/17/98	9/1/98	9/21/98	9/8/98

PRJ#	Due Date	NTP	ATT	BLHP	BSES	DPT	EE(BWPC)	HYD	MCI
1586N	10/20/98		10/2/98	11/6/98	11/2/98			10/9/98	10/13/98
1587N	5/20/99		4/28/99				4/23/99		5/17/99
1588N	12/22/98		7/27/99		7/22/99		7/23/99	7/27/99	
1589N	8/13/99		7/28/99				7/29/99		
1602N	11/9/98		10/16/98				10/16/98	10/13/98	10/20/98
1603N	7/10/98		6/19/98	7/10/98		6/22/98	6/18/98	7/16/98	6/23/98
1605N	7/9/99		6/21/99	6/16/99			6/15/99		7/22/99
1606N	10/29/98		10/2/98	11/9/98	11/9/98		10/6/98	10/13/98	10/13/98
1630N	6/4/99		5/7/99	5/17/99			5/7/99		6/2/99
1631N	2/16/99		1/19/99					1/14/99	2/5/99
1632N	4/6/99		3/9/99	3/17/99	3/5/99		3/2/99		
1645N	2/24/99		1/12/99	1/13/99			1/13/99	1/19/99	2/24/99
1668N	4/27/99	Sep-98	4/21/99	5/21/99			4/20/99	4/21/99	7/26/99
1687N	8/31/98		8/12/98	11/6/98	8/5/98	8/12/98	8/3/98	8/3/98	8/13/98
1701N	8/13/99								
1727N	3/22/99		3/12/99	5/5/99			3/12/99	3/17/99	4/9/99
1729N	3/25/99		3/12/99	5/17/99			2/16/99	2/24/99	3/10/99
1732N	2/24/99		1/12/99	1/13/99			1/13/99	1/20/99	2/5/99
1734N	4/8/99		3/29/99	5/17/99			3/26/99	3/26/99	4/21/99
1765N	3/22/99			3/17/99			3/11/99		4/9/99
1777N	7/16/99		7/22/99				7/12/99		
1784N	6/14/99		6/9/99	6/16/99			6/14/99	6/8/99	7/1/99
1785N	5/17/99		4/28/99				4/23/99		7/1/99
1785N	5/17/99								
1794N	7/30/99		7/22/99						
6094Q	6/27/97	07/98							
7090E	3/19/98		3/24/98	4/22/98				3/18/98	
7437E	8/29/97	Jul-98	8/5/97	4/13/98		8/8/97	8/6/97	9/23/97	9/4/97
7458E	6/3/99		5/7/99	5/17/99			5/7/99		6/2/99
7474E	11/26/97		11/19/97			12/4/97	11/20/97		12/10/97

Project in Progress (LOT)

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1001H	12/6/96	12/30/96	1/22/97		12/ 5/96	12/3/96	12/6/96	12/6/96
1034N	3/26/99	3/16/99	3/26/99		3/26/99			
1036N	5/28/97	5/23/97				6/4/97	6/12/97	
1077N	9/30/97	9/24/97			10/ 7/97		11/10/97	1/27/98
1091N	4/30/97					4/14/97	5/23/97	5/23/97
1106N	5/16/97	5/20/97			5/19/97	5/13/97	5/19/97	5/19/97
1109K	4/28/97					4/22/97	9/24/97	9/4/98
1109N	12/27/96	12/14/96	1/29/97	1/9/97			6/23/97	
1133N	10/27/97	10/16/97			10/20/97	10/17/97	11/10/97	11/10/97
1155N	10/21/98	10/6/98		11/9/98	10/13/98			
1195N	7/20/96			8/2/96		7/23/96		
1208K	3/9/98	3/5/98	3/30/98		3/10/98		5/14/98	
1223W	4/30/97	4/18/97	4/17/97			4/25/97	5/23/97	3/6/98
1245N	11/27/96			12/2/96	12/ 5/96	11/8/96	4/15/97	4/15/97
1253N	5/16/97	5/20/97		5/14/97		4/29/97	5/16/97	5/16/97
1254N	5/23/97	4/28/97				4/24/97	6/12/97	
1272N	8/8/97	8/5/97			10/ 7/97	7/30/97	9/24/97	9/24/97
1322N	3/11/97	3/11/97	4/21/97	3/25/97		3/3/97	4/18/97	4/18/97
1362N	3/22/99	3/17/99	3/17/99		3/16/99			
1373N	9/15/97	9/12/97		11/7/97	10/ 7/97		11/10/97	12/22/97
1374N	5/28/97	5/20/97				4/29/97	9/24/97	3/6/98
1392N	2/28/97	2/28/97	4/21/97	3/18/97		2/24/97		
1393N	10/24/97		10/22/97		10/14/97	10/16/97	11/10/97	
1396N	5/12/97			5/14/97		4/30/97	6/12/97	
1397N	10/17/97	9/30/97			10/ 7/97	9/29/97	11/10/97	11/10/97
1408N	2/6/98	1/13/98	3/30/98		1/14/98		2/12/98	
1409N	3/25/99	2/22/99	3/8/99		2/22/99			
1411N	11/14/97	11/7/97			10/29/97	10/29/97	12/22/97	12/22/97
1413N	6/25/97				10/ 7/97	6/9/97	6/23/97	
1414N	2/28/97		4/17/97	3/18/97		2/13/97	4/15/97	4/15/97
1426N	12/8/97				12/12/97	12/4/97		2/20/98
1433N	11/7/97	11/7/97			10/21/97	10/16/97	11/25/97	12/22/97
1440N	2/6/98	1/13/98	3/30/98		1/14/98		2/12/98	
1453N	2/6/98	1/13/98			1/14/98		2/12/98	
1454N	4/27/98		4/20/98		4/23/98		7/9/98	7/9/98
1460N	10/22/97	10/16/97			10/20/97	10/8/97	11/25/97	12/22/97
1461N	3/6/98	2/20/98	3/30/98		2/27/98		5/14/98	
1474N	6/22/98	6/18/98	6/5/98		6/ 3/98	10/8/98	7/13/98	
1475N	12/24/97		1/14/98		12/19/97		1/27/98	
1477N(A)	7/19/99	6/24/99			7/ 1/99			
1488N	6/20/97	6/19/97			6/ 9/97	6/2/97	8/8/97	
1491N	9/25/97	9/24/97			10/ 7/97	9/15/97	11/10/97	2/12/98
1519N	1/23/98				1/ 6/98		2/12/98	
1528N	8/25/97	8/26/97			10/ 7/97	8/20/97	9/26/97	9/26/97
1547N	1/16/98		3/30/98			12/15/97	2/12/98	
1548N	1/9/98	12/29/97	1/14/98		12/29/97	12/19/97	2/12/98	
1550N	1/30/98		3/30/98		1/21/98	1/23/98	4/7/98	
1562N	6/26/98	6/22/98	6/23/98		6/19/98	6/19/98	9/25/98	
1563N	6/25/98	6/22/98	6/23/98		6/19/98	6/16/98	10/27/98	
1566N	12/19/97		1/14/98		12/19/97	12/10/97	2/20/98	
1569N	6/12/98	6/8/98	5/19/98		5/21/98	5/15/98	7/13/98	

PRJ#	Due Date	MECH	MFS	MUNI	PB	PD	PGE-G	PGE-E
1578N	3/10/98	3/11/98				3/9/98	5/14/98	
1579N	4/17/98	4/20/98	4/20/98		4/20/98			
1583N	5/14/99	5/5/99	5/7/99		5/ 4/99			
1585N	9/15/98		8/28/98	11/9/98	8/31/98	9/10/98	10/27/98	
1586N	10/20/98			11/9/98	10/ 1/98			
1587N	5/20/99	5/12/99	5/7/99		4/30/99			
1588N	12/22/98	7/26/99			7/27/99			
1589N	8/13/99	7/29/99			8/ 2/99			
1602N	11/9/98	10/15/98	12/2/98		10/13/98			
1603N	7/10/98	6/17/98	8/4/98		6/16/98	10/8/98	11/12/98	
1605N	7/9/99	6/18/99	6/24/99		6/18/99			
1606N	10/29/98			11/9/98	10/13/98			
1630N	6/4/99	5/7/99	5/12/99		5/13/99			
1631N	2/16/99	1/20/99			1/21/99			
1632N	4/6/99	3/2/99	3/10/99		3/ 2/99			
1645N	2/24/99	1/25/99				1/19/99		
1668N	4/27/99	4/23/99	5/7/99		4/21/99			
1687N	8/31/98	8/7/98	8/4/98	11/9/98	8/ 7/98		10/6/98	
1701N	8/13/99							
1727N	3/22/99	3/16/99	3/17/99		3/16/99			
1729N	3/25/99	2/22/99	3/8/99		2/22/99			
1732N	2/24/99	1/20/99			1/20/99	1/19/99	2/1/99	
1734N	4/8/99	3/30/99	3/31/99		3/29/99			
1765N	3/22/99				3/29/99			
1777N	7/16/99	7/15/99			7/12/99			
1784N	6/14/99	6/9/99	6/14/99		6/10/99			
1785N	5/17/99	4/26/99	5/7/99		4/30/99			
1785N	5/17/99							
1794N	7/30/99				7/30/99			
6094Q	6/27/97	9/19/98			10/ 7/97	6/13/97	9/24/97	9/24/97
7090E	3/19/98		1/5/99		4/ 8/98			
7437E	8/29/97	8/26/97			10/ 7/97	8/7/97	9/24/97	9/24/97
7458E	6/3/99	5/7/99	5/12/99		5/13/99			
7474E	11/26/97				11/25/97	11/17/97	2/12/98	

Projects in Progress (LOT)

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1001H	12/6/96	12/2/96	12/2/96		12/5/96	12/23/96	12/2/96	12/5/96
1034N	3/26/99	3/15/99	3/18/99		4/7/99		4/13/99	3/26/99
1036N	5/28/97	5/19/97	5/21/97		5/23/97	5/29/97		5/28/97
1077N	9/30/97	9/19/97			9/15/97	9/24/97	9/11/97	10/2/97
1091N	4/30/97	4/9/97			4/9/97	4/14/97	5/14/97	4/10/97
1106N	5/16/97	5/6/97		5/13/97	5/13/97	5/29/97	5/14/97	5/28/97
1109K	4/28/97	4/18/97	4/24/97	4/24/97	4/16/97	4/25/97	5/14/97	5/8/97
1109N	12/27/96	12/12/96	1/6/97		12/16/96	12/23/96	12/19/96	12/10/96
1133N	10/27/97	10/16/97			10/22/97	11/19/97	11/10/97	11/13/97
1155N	10/21/98	10/5/98			10/15/98		1/11/99	10/15/98
1195N	7/20/96		7/17/96		7/19/96		7/30/96	7/15/96
1208K	3/9/98	3/6/98	3/20/98		3/17/98		4/8/98	4/3/98
1223W	4/30/97	5/5/97	4/24/97		4/16/97		5/14/97	4/24/97
1245N	11/27/96		11/13/96		11/20/96		12/2/96	11/19/96
1253N	5/16/97	5/1/97			5/2/97	5/29/97	5/14/97	6/3/98
1254N	5/23/97	4/29/97			4/29/97	5/29/97	5/14/97	5/8/97
1272N	8/8/97	8/12/97			8/5/97	8/8/97	8/8/97	8/15/97
1322N	3/11/97	2/18/97			3/13/97	2/27/97	4/21/97	2/20/97
1362N	3/22/99	3/11/99	3/18/99		3/26/99		3/15/99	3/24/99
1373N	9/15/97	8/27/97			9/4/97	9/24/97	9/15/97	9/22/97
1374N	5/28/97	5/1/97			5/6/97	5/29/97	5/14/97	5/8/97
1392N	2/28/97	2/18/97			3/13/97	2/27/97	2/24/97	2/20/97
1393N	10/24/97	10/14/97			10/15/97	11/18/97	12/11/97	10/16/97
1396N	5/12/97	5/5/97			5/13/97	5/29/97	5/14/97	5/28/97
1397N	10/17/97	9/26/97			10/2/97	11/19/97		10/16/97
1408N	2/6/98	1/12/98			1/14/98	2/12/98	1/21/98	1/21/98
1409N	3/25/99	2/19/99	2/22/99		2/23/99		3/9/99	3/2/99
1411N	11/14/97	10/28/97	11/13/97		10/31/97	11/19/97	11/10/97	11/13/97
1413N	6/25/97	6/11/97			6/19/97	6/10/97	8/8/97	6/20/97
1414N	2/28/97	2/18/97			3/13/97	2/27/97	2/24/97	2/20/97
1426N	12/8/97	12/3/97	12/20/97		12/17/97	2/12/98	12/8/97	12/12/97
1433N	11/7/97	10/20/97	10/28/97		10/23/97	11/19/97	11/10/97	11/13/97
1440N	2/6/98	1/12/98			1/21/98	2/12/98	1/21/98	1/21/98
1453N	2/6/98	1/12/98			1/14/98	2/12/98	1/21/98	1/21/98
1454N	4/27/98	4/20/98			4/28/98	5/20/98		5/11/98
1460N	10/22/97	10/16/97			10/22/97	11/19/97	11/10/97	11/13/97
1461N	3/6/98	2/20/98			2/20/98	5/20/98	4/8/98	2/20/98
1474N	6/22/98				6/9/98		4/13/99	6/3/98
1475N	12/24/97	12/13/97	12/19/97		12/19/97	2/10/98	12/29/97	11/29/1908
1477N(A)	7/19/99		6/21/99	7/1/99			7/22/99	7/1/99
1488N	6/20/97	6/4/97			6/11/97	7/11/97	8/8/97	6/20/97
1491N	9/25/97	9/19/97			9/25/97	11/19/97	9/19/97	9/22/97
1519N	1/23/98	1/7/98			1/14/98	5/20/98	1/21/98	1/21/98
1528N	8/25/97	8/22/97			8/26/97	8/21/97	9/15/97	9/22/97
1547N	1/16/98	12/19/97			12/19/97		12/29/97	1/12/98
1548N	1/9/98	1/7/98			1/14/98	2/12/98	12/29/97	1/12/98
1550N	1/30/98	1/16/98			1/21/98	2/12/98	1/21/98	1/21/98
1562N	6/26/98	6/17/98			6/19/98		1/7/99	7/7/98
1563N	6/25/98	6/17/98			6/19/98		1/7/99	7/7/98
1566N	12/19/97	12/13/97	12/19/97		12/17/97	2/10/98	12/29/97	1/12/98
1569N	6/12/98	5/19/98			6/3/98	5/20/98		6/8/98
1578N	3/10/98	3/10/98			3/17/98		4/8/98	4/3/98
1579N	4/17/98	4/13/98	4/28/98			5/20/98		4/16/98
1583N	5/14/99	4/30/99	4/30/99		5/5/99			5/4/99
1585N	9/15/98		8/31/98		9/15/98		1/7/99	9/11/98

PRJ#	Due Date	PORT	SFT	SFWD	SPRINT	STR	TCG	TCI
1586N	10/20/98	9/28/98			10/6/98		1/7/99	10/15/98
1587N	5/20/99	4/26/99	4/30/99		4/30/99			5/3/99
1588N	12/22/98	7/22/99		12/10/98	7/29/99			7/30/99
1589N	8/13/99	7/29/99			8/2/99			
1602N	11/9/98	10/8/98			10/19/98		1/11/99	10/27/98
1603N	7/10/98	6/15/98			6/19/98		1/11/99	7/7/98
1605N	7/9/99	6/21/99	6/21/99		6/21/99		7/22/99	6/23/99
1606N	10/29/98	10/5/98			10/6/98		1/7/99	10/15/98
1630N	6/4/99		5/11/99		6/2/99			5/19/99
1631N	2/16/99	1/14/99			1/26/99		3/15/99	2/3/99
1632N	4/6/99	10/28/98	3/2/99	11/23/98	3/2/99		3/9/99	3/5/99
1645N	2/24/99	1/11/99	1/13/99		1/19/99		3/9/99	1/20/99
1668N	4/27/99	4/15/99	4/19/99		4/26/99			4/28/99
1687N	8/31/98	8/24/98			8/13/98		1/11/99	8/25/98
1701N	8/13/99	8/4/99						
1727N	3/22/99	3/11/99	3/18/99				3/15/99	3/24/99
1729N	3/25/99	2/19/99	2/22/99		2/23/99		3/9/99	3/2/99
1732N	2/24/99	1/11/99	1/13/99		1/19/99		3/9/99	1/20/99
1734N	4/8/99	3/31/99	3/31/99		4/7/99		4/13/99	4/9/99
1765N	3/22/99	3/11/99	3/23/99					3/23/99
1777N	7/16/99	7/7/99	7/6/99				7/22/99	7/20/99
1784N	6/14/99	6/21/99	6/11/99		6/15/99		7/22/99	6/14/99
1785N	5/17/99	4/26/99	4/30/99		4/30/99			5/3/99
1785N	5/17/99							
1794N	7/30/99	7/22/99	7/22/99		7/27/99		7/22/99	7/28/99
6094Q	6/27/97	6/27/97			6/12/97			
7090E	3/19/98				3/24/98		4/8/98	4/3/98
7437E	8/29/97	8/6/97			8/12/97	8/8/97	8/8/97	8/26/97
7458E	6/3/99		5/11/99		6/2/99			5/19/99
7474E	11/26/97	11/25/97	12/3/97		12/1/97	2/12/98	12/12/97	12/12/97

5
185.93
2
8/10/00

DOCUMENTS DEPT
SEP - 8 2000
SAN FRANCISCO
PUBLIC LIBRARY

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 425

August 10, 2000

ATTENDANCE:

Department of Public Works		
Bureau of Engineering		
	Aenny Chen	558-4055
	Eric Kjelsberg	558-4012
	Ramon Kong	558-4030
	Jean To	554-8298
Street Construction Coordination Center		
	Cynthia Chono	554-6196
	Grace Moore	554-5892
	Joe Norris	554-5881
Bureau of Street and Sewer Repair	**(Representative not present)**	
Bureau of Street-Use & Mapping	**(Representative not present)**	
Bureau of Construction Management		
	Bill Adams	437-7038
Department of Parking and Traffic		
	Philip Louie	554-2322
Hetch Hetchy Water & Power	**(Representative not present)**	
MUNI Engineering / DDC		
	Mark Rudnicki	557-9959
PUC Water Pollution Control	**(Representative not present)**	
San Francisco Port Authority		
	Skip Zeller	274-0552
San Francisco Water Department	**(Representative not present)**	
Redevelopment Agency	**(Representative not present)**	
Caltrans		
	Ron Crump	510-286-7187
	Dean Drablos	510-520-8850
	Ahmad Rahimi	510-622-1664
Caltrans Public Information	**(Representative not present)**	
Pacific Bell		
	Cindy Vowell	542-9095
Pacific Gas & Electric	**(Representative not present)**	
S F Thermal		
	Hank Thompson	777-3415
AGS		
	Steven Nguyen	777-2166 x36
	Ed Slintak	777-2166 x14
Allstar	**(Representative not present)**	
AT&T		
	Louis Victorio	863-8500
BDI	**(Representative not present)**	
Dresser / Areia	**(Representative not present)**	
Fluor / Level 3 Communications		
	Donald Domineck	408-556-1578
GST	**(Representative not present)**	
ICG	**(Representative not present)**	
Looking Glass Networks		
	John Kelly	707-864-5434
MCI WorldCom		
	Pam Brown	408-533-4076
MFS	**(Representative not present)**	
MFN	**(Representative not present)**	
Nextlink	**(Representative not present)**	
RCN		
	Jeff Parson	510-786-9487
TCG	**(Representative not present)**	
Underground Construction	**(Representative not present)**	
Winzler & Kelly (Mission Bay)		
	Mike Kincaid	283-4970
	Jason Ling	283-4970

S:\PD\PAVEMENT\MIN\Culc426.doc

Committee for Utility Liaison on Construction and Other Projects

DOCUMENTS DEPT.

SEP - 8 2000

SAN FRANCISCO
PUBLIC LIBRARY

MINUTES OF MEETING No. 425
August 10, 2000

1. The members introduced themselves around the table.

2. The July 13, 2000 Minutes were approved.

3. Project Updates

Paving Projects Mr. Kong reported that the paving contract on California Street has been advertised; construction has started for Brotherhood and Font; Sutter Street will start in September. Golden Gate Avenue, Mission Street south of Silver, and Lake Merced Boulevard will start work later this year. Ms. Chono noted that 3rd St., Mission, and Ocean Ave. may impact each other's rerouting.

Mr. Adams reported that track removal and paving work begins in a week on Fremont between Market and Howard Streets, fronting the Transbay Terminal, and in January on First St. There may be some impact on traffic exiting I-80 and on traffic flow diverted by the retrofitting project. In response to Ms. Chono's question, Mr. Rahimi said Ms. Ashe is the Caltrans contact person for construction-phase issues there. Mr. Drablos and Mr. Kong asked if sewer work planned for Howard Street would affect the paving; Ms. To said probably not.

Ms. Chono reminded members that the intersection of Mission and Cesar Chavez will be resurfaced soon.

Caltrans Mr. Rahimi noted that he is the Caltrans representative for matters affecting the West Approach project.

4. New Business

Muni Metro East Mr. Rudnicki and Mr. Slintak discussed the present state of Muni's plans for the Metro East Light Rail Maintenance and Operations Facility. There will be two main contracts, one for soil improvement and grading, and one for everything else. The soil improvement will involve compaction of presently unconsolidated fill beginning in October of 2000. Everything else includes the buildings and track layout; extension of 25th Street east from Michigan; construction of Illinois as a roadway, per DPW design, from 25th to Cesar Chavez; an electrical power installation, configuration still being negotiated with PG&E; gas, water, and telecommunications services; and upgrades to the sewer installation. This contract is expected to be bid in July of 2001. The track work needs to be done in time to store expected deliveries of LRVs intended for the 3rd Street line, since other storage facilities are already at capacity. The facility will be expanded later into an additional four acres to the east. Where they are known to be affected, the

utility companies have been contacted, and the contract has milestones for points of impact such as the crossing for the Port's rail line along Illinois St.

Mr. Rudnicki will return periodically for updates. Questions and comments can be directed to Mr. Kascal.

Mission Bay Mr. Kincaid of Winzler & Kelly discussed the current state of the Mission Bay project. Block and building construction will begin along the China Basin channel and at the UC building north of 16th Street. The storm drains in 16th St. will be rebuilt in coordination with the UC development. Ms. Chono pointed out that the crossing of 16th and 3rd Sts. will need attention since the sewers in each are unusually large. Also, since the work begins on the axes and peripheries of the project area, utility impact is immediate. In addition, south of China Basin, the storm and sanitary sewers will be separate systems, which means twice the underground space compared to the combined systems elsewhere. Utilities intending to install their facilities need to join the planning process now, such as by participating in the joint trenching meeting at the Catellus offices on August 18. The street layout will be almost completely changed, except for 3rd and 16th; some will be public thoroughfares accepted by DPW and some will be emergency-accessible landscaped malls and walkways or utility easements. Street design will include allowance for subsidence, such as by using flexible joints for wet lines. Ms. Chono observed that SCCC will need to have detailed information about the layouts and timing so we can fit our permit conditions to the site and time. Mr. Kincaid noted that in some cases, particularly water and AWSS, services will be phased to accommodate both intermediate and final requirements, such as for the UC site.

The project is coordinated with the Light Rail route, which will cross the project area via the 4th St. Bridge, a realigned segment of 4th St. east to 3rd, and down 3rd.

Mr. Zeller asked about plans for soil remediation, particularly oil residues to the southeast. Mr. Kincaid replied that Catellus is still deciding between digging out, damming, or a combination.

Ms. Chono reminded members that any excavation in this area will require inclusion of a health and safety plan for each permit, specifying the location (ie, not a blanket document), for which any departure from the standard document will require approval by the Water Pollution Control Board. In addition, each excavator will be required to receive training in identifying potential archeological sites, particularly in sites that are not now roadways; for this purpose, "excavator" means the people who do the actual work in the field. The archeologist from Catellus will be at the September meeting to discuss this requirement, which will be a condition of each excavation permit issued in this area; members are requested to send their field foremen to that meeting.

Other New Business

Ms. Vowell announced Pacific Bell work on Geary Street that is not yet in the 5 year plan:

Start Oct 2000

Geary Blvd. Funston to Park Presidio Geary Blvd. 27th Ave. to 39th Ave.
Geary Blvd. 39th Ave. to Point Lobos

Start Jan 2001

Geary Blvd. 14th Ave. to 27th Ave.

Ms. To noted that there have been problems with conduit being laid above sewer lines. Mr. Adams has found water lines above the sewer in Alemany near Putnam. Ms. Chono replied that the regulations specify both the minimal 12" horizontal clearance for any two lines, and the prohibition of any parallel line directly above a sewer. Any line placed in violation of the rules can be made to relocate.

Ms. Chono reminded members of the X-Games which will require all construction sites in the area to be cleared of active construction to accommodate the expected crowds.

Please update your records: Due to rotation of duties at DPT, Traffic Engineering Division, Scott Broady (554-2326) has assumed Joern Kroll's previous responsibilities in traffic engineering support for building construction and related projects (sidewalk issues, encroachment permits, overwide driveways). Please inform your staff of this change.

The next meeting will be:

10:00 AM Thursday, September 14, 2000
(the second Thursday of the month)
To accommodate an expected larger than usual attendance, the September meeting will be moved to:

DTIS Resource Room
875 Stevenson St, Fifth Floor

Agenda:

- Third Street Light Rail Project Update
- Guest Speaker: Mission Bay requirement – how to identify potential archeological sites and how to proceed with them. Intended for your field foremen: please have them attend.

TF
P8
#1
n/

City and County of San Francisco

Department of Public Works
Bureau of Street Use and Mapping
Street Construction Coordination Center

85.93
1
/14/00

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION AND OTHER PROJECTS

AGENDA for

Date:	**Thursday, September 14, 2000**
Time:	10:00 am to 12:00 noon
Subject:	Committee Meeting 426- Coordination of Street Construction
Location:	875 Stevenson St, **DTIS Resource Room, Fifth Floor**

1) Introduction

2) Approval of Minutes for August 10 Meeting

3) Old Business

4) Project Updates

a. Paving projects		Joe Ovadia
b. Caltrans		Karen Ashe
c. Project Update	3rd St. Light Rail	Jeff Rogers
d. New projects		
e. Major events	Holiday Construction Moratorium	

5) New Business
   a. Mission Bay Archeological Procedures – how to identify and deal with potential archeological sites, for field supervisors — Allen Pastron, Archeo-tec

6) Improvement Issues
   a. NOI Letters

Next Meeting: 2nd Thursday of Each Month
Thursday October 12, 2000 at 10:00 A. M.
875 Stevenson St, Rm. 400

To be scheduled:

DOCUMENTS DEPT
SEP - 8 2000
SAN FRANCISCO
PUBLIC LIBRARY

Accessible Meeting Information

1. The meeting room is wheelchair accessible. Accessible seating for people with disabilities (including those using wheelchairs) will be available.

2. For American Sign Language interpreters, use of a reader during meeting, or sound enhancements, please contact CULCOP secretary at (415) 554-5881, at least72 hours in advance of need. Late requests will be honored if possible.

3. Following a meeting, minutes are available in large prints or alternative formats. Please call CULCOP secretary at (415) 554-5881.

4. As part of the City's efforts to accommodate people with severe allergies, environmental illnesses, multiple chemical sensitivity, attendees at public meetings are reminded that other attendees may be sensitive to various chemical based products. Please help the City to accommodate these attendees and refrain from wearing perfume or other scented products.

5. The meeting will be held at 875 Stevenson St, Rm 410. Accessible MUNI line serving this location is:

   MUNI Bus Lines: #14, #14L Mission Street; # 42 Van Ness Avenue;
   #26 Valencia Street; #71 Noriega Street; #9 Market Street.
   MUNI Street Cars: K, L, M, N, stops at Van Ness Station.

For further information about MUNI accessible services, call MUNI's Elderly and Handicapped Program at 923-6142, TDD 923-6366.

COMMITTEE FOR UTILITY LIAISON ON CONSTRUCTION
AND OTHER PROJECTS

UTILITY STREET OPENING AND UNDERGROUND CONSTRUCTION PLANNING

MINUTES OF MEETING NO. 425
August 10, 2000

ATTENDANCE:

Department of Public Works

Bureau of Engineering

Aenny Chen	558-4055
Eric Kjelsberg	558-4012
Ramon Kong	558-4030
Jean To	554-8298

Street Construction Coordination Center

Cynthia Chono	554-6196
Grace Moore	554-5892
Joe Norris	554-5881

Bureau of Street and Sewer Repair

(Representative not present)

Bureau of Street-Use & Mapping

(Representative not present)

Bureau of Construction Management

Bill Adams	437-7038

Department of Parking and Traffic

Philip Louie	554-2322

Hetch Hetchy Water & Power
(Representative not present)

MUNI Engineering / DDC

Mark Rudnicki	557-9959

PUC Water Pollution Control
(Representative not present)

San Francisco Port Authority

Skip Zeller	274-0552

San Francisco Water Department
(Representative not present)

Redevelopment Agency
(Representative not present)

Caltrans

Ron Crump	510-286-7187
Dean Drablos	510-520-8850
Ahmad Rahimi	510-622-1664

Caltrans Public Information
(Representative not present)

Pacific Bell

Cindy Vowell	542-9095

Pacific Gas & Electric
(Representative not present)

S F Thermal

Hank Thompson	777-3415

AGS

Steven Nguyen	777-2166 x36
Ed Slintak	777-2166 x14

Allstar
(Representative not present)

AT&T

Louis Victorio	863-8500

BDI
(Representative not present)

Dresser / Arcia
(Representative not present)

Fluor / Level 3 Communications

Donald Domineck	408-556-1578

GST
(Representative not present)

ICG
(Representative not present)

Looking Glass Networks

John Kelly	707-864-5434

MCI WorldCom

Pam Brown	408-533-4076

MFS
(Representative not present)

MFN
(Representative not present)

Nextlink
(Representative not present)

RCN

Jeff Parson	510-786-9487

TCG
(Representative not present)

Underground Construction
(Representative not present)

Winzler & Kelly (Mission Bay)

Mike Kincaid	283-4970
Jason Ling	283-4970

S:\PD\PAVEMENT\MIN\Culc426.doc

DOCUMENTS DEPT
SEP - 8 2000
SAN FRANCISCO
PUBLIC LIBRARY

Committee for Utility Liaison on Construction and Other Projects

DOCUMENTS DEPT.

SEP - 8 2000

SAN FRANCISCO
PUBLIC LIBRARY

MINUTES OF MEETING No. 425
August 10, 2000

1. The members introduced themselves around the table.

2. The July 13, 2000 Minutes were approved.

3. Project Updates

Paving Projects Mr. Kong reported that the paving contract on California Street has been advertised; construction has started for Brotherhood and Font; Sutter Street will start in September. Golden Gate Avenue, Mission Street south of Silver, and Lake Merced Boulevard will start work later this year. Ms. Chono noted that 3rd St., Mission, and Ocean Ave. may impact each other's rerouting.

Mr. Adams reported that track removal and paving work begins in a week on Fremont between Market and Howard Streets, fronting the Transbay Terminal, and in January on First St. There may be some impact on traffic exiting I-80 and on traffic flow diverted by the retrofitting project. In response to Ms. Chono's question, Mr. Rahimi said Ms. Ashe is the Caltrans contact person for construction-phase issues there. Mr. Drablos and Mr. Kong asked if sewer work planned for Howard Street would affect the paving; Ms. To said probably not.

Ms. Chono reminded members that the intersection of Mission and Cesar Chavez will be resurfaced soon.

Caltrans Mr. Rahimi noted that he is the Caltrans representative for matters affecting the West Approach project.

4. New Business

Muni Metro East Mr. Rudnicki and Mr. Slintak discussed the present state of Muni's plans for the Metro East Light Rail Maintenance and Operations Facility. There will be two main contracts, one for soil improvement and grading, and one for everything else. The soil improvement will involve compaction of presently unconsolidated fill beginning in October of 2000. Everything else includes the buildings and track layout; extension of 25th Street east from Michigan; construction of Illinois as a roadway, per DPW design, from 25th to Cesar Chavez; an electrical power installation, configuration still being negotiated with PG&E; gas, water, and telecommunications services; and upgrades to the sewer installation. This contract is expected to be bid in July of 2001. The track work needs to be done in time to store expected deliveries of LRVs intended for the 3rd Street line, since other storage facilities are already at capacity. The facility will be expanded later into an additional four acres to the east. Where they are known to be affected, the utility companies have been contacted, and the contract has milestones for points of impact such as the crossing for the Port's rail line along Illinois St.

Mr. Rudnicki will return periodically for updates. Questions and comments can be directed to Mr. Kascal.

Mission Bay Mr. Kincaid of Winzler & Kelly discussed the current state of the Mission Bay project. Block and building construction will begin along the China Basin channel and at the UC building north of 16th Street. The storm drains in 16th St. will be rebuilt in coordination with the UC development. Ms. Chono pointed out that the crossing of 16th and 3rd Sts. will need attention since the sewers in each are unusually large. Also, since the work begins on the axes and peripheries of the project area, utility impact is immediate. In addition, south of China Basin, the storm and sanitary sewers will be separate systems, which means twice the underground space compared to the combined systems elsewhere. Utilities intending to install their facilities need to join the planning process now, such as by participating in the joint trenching meeting at the Catellus offices on August 18. The street layout will be almost completely changed, except for 3rd and 16th; some will be public thoroughfares accepted by DPW and some will be emergency-accessible landscaped malls and walkways or utility easements. Street design will include allowance for subsidence, such as by using flexible joints for wet lines. Ms. Chono observed that SCCC will need to have detailed information about the layouts and timing so we can fit our permit conditions to the site and time. Mr. Kincaid noted that in some cases, particularly water and AWSS, services will be phased to accommodate both intermediate and final requirements, such as for the UC site.

The project is coordinated with the Light Rail route, which will cross the project area via the 4th St. Bridge, a realigned segment of 4th St. east to 3rd, and down 3rd.

Mr. Zeller asked about plans for soil remediation, particularly oil residues to the southeast. Mr. Kincaid replied that Catellus is still deciding between digging out, damming, or a combination.

Ms. Chono reminded members that any excavation in this area will require inclusion of a health and safety plan for each permit, specifying the location (ie, not a blanket document), for which any departure from the standard document will require approval by the Water Pollution Control Board. In addition, each excavator will be required to receive training in identifying potential archeological sites, particularly in sites that are not now roadways; for this purpose, "excavator" means the people who do the actual work in the field. The archeologist from Catellus will be at the September meeting to discuss this requirement, which will be a condition of each excavation permit issued in this area; members are requested to send their field foremen to that meeting.

Other New Business

Ms. Vowell announced Pacific Bell work on Geary Street that is not yet in the 5 year plan:

Start Oct 2000

Geary Blvd. Funston to Park Presidio Geary Blvd. 27th Ave. to 39th Ave.
Geary Blvd. 39th Ave. to Point Lobos

Start Jan 2001

Geary Blvd. 14th Ave. to 27th Ave.

Ms. To noted that there have been problems with conduit being laid above sewer lines. Mr. Adams has found water lines above the sewer in Alemany near Putnam. Ms. Chono replied that the regulations specify both the minimal 12" horizontal clearance for any two lines, and the prohibition of any parallel line directly above a sewer. Any line placed in violation of the rules can be made to relocate.

Ms. Chono reminded members of the X-Games which will require all construction sites in the area to be cleared of active construction to accommodate the expected crowds.

Please update your records: Due to rotation of duties at DPT, Traffic Engineering Division, Scott Broady (554-2326) has assumed Joern Kroll's previous responsibilities in traffic engineering support for building construction and related projects (sidewalk issues, encroachment permits, overwide driveways). Please inform your staff of this change.

The next meeting will be:

10:00 AM Thursday, September 14, 2000
(the second Thursday of the month)
To accommodate an expected larger than usual attendance, the September meeting will be moved to:

DTIS Resource Room
875 Stevenson St, Fifth Floor

Agenda:
- Third Street Light Rail Project Update
- Guest Speaker: Mission Bay requirement – how to identify potential archeological sites and how to proceed with them. Intended for your field foremen: please have them attend.

HOUCHEN
BINDERY LTD
UTICA/OMAHA NE.
2004
